



# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan



---

Transportation | Water Resources | Land Development | Surveying | Environmental



January 2, 2025

Ms. Monica Reyes  
Texas Commission on Environmental Quality (TCEQ)  
Region 11  
12100 Park 35 Circle, Bldg A, Rm 179  
Austin, TX 78753

Re: JARRELL INDUSTRIAL PARK  
Water Pollution Abatement Plan

Dear Ms. Reyes:

Please find included herein the JARRELL INDUSTRIAL PARK Water Pollution Abatement Plan. This Water Pollution Abatement Plan has been prepared in accordance with the regulations of the Texas Administrative Code (30 TAC 213) and current policies for development over the Edwards Aquifer Recharge Zone.

This Water Pollution Abatement Plan applies to an approximate 6.184 ac (10.78-acre legal limit) site as identified by the project limits. Please review the plan information for the items it is intended to address. If acceptable, please provide a written approval of the plan in order that construction may begin at the earliest opportunity.

Appropriate review fees (\$6,500) and fee application are included. If you have questions or require additional information, please do not hesitate to contact me at your earliest convenience.

Sincerely,  
Pape-Dawson Consulting Engineers, LLC

1 / 3 / 25



Taylor Dawson, P.E.  
Senior Vice President



Attachments

H:\Projects\515\70\00\301 Construction Documents\Documents\Reports\WPAP\241109a1.docx

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

1/3/25



**EDWARDS AQUIFER  
APPLICATION COVER PAGE  
(TCEQ-20705)**

# Texas Commission on Environmental Quality

## Edwards Aquifer Application Cover Page

---

### Our Review of Your Application

**The Edwards Aquifer Program staff conducts an administrative and technical review of all applications. The turnaround time for administrative review can be up to 30 days as outlined in 30 TAC 213.4(e). Generally administrative completeness is determined during the intake meeting or within a few days of receipt. The turnaround time for technical review of an administratively complete Edwards Aquifer application is 90 days as outlined in 30 TAC 213.4(e). Please know that the review and approval time is directly impacted by the quality and completeness of the initial application that is received. In order to conduct a timely review, it is imperative that the information provided in an Edwards Aquifer application include final plans, be accurate, complete, and in compliance with [30 TAC 213](#).**

### Administrative Review

1. [Edwards Aquifer applications](#) must be deemed administratively complete before a technical review can begin. To be considered administratively complete, the application must contain completed forms and attachments, provide the requested information, and meet all the site plan requirements. The submitted application and plan sheets should be final plans. Please submit one full-size set of plan sheets with the original application, and half-size sets with the additional copies.

To ensure that all applicable documents are included in the application, the program has developed tools to guide you and web pages to provide all forms, checklists, and guidance. Please visit the below website for assistance: <http://www.tceq.texas.gov/field/eapp>.

2. This Edwards Aquifer Application Cover Page form (certified by the applicant or agent) must be included in the application and brought to the administrative review meeting.
3. Administrative reviews are scheduled with program staff who will conduct the review. Applicants or their authorized agent should call the appropriate regional office, according to the county in which the project is located, to schedule a review. The average meeting time is one hour.
4. In the meeting, the application is examined for administrative completeness. Deficiencies will be noted by staff and emailed or faxed to the applicant and authorized agent at the end of the meeting, or shortly after. Administrative deficiencies will cause the application to be deemed incomplete and returned.

An appointment should be made to resubmit the application. The application is re-examined to ensure all deficiencies are resolved. The application will only be deemed administratively complete when all administrative deficiencies are addressed.

5. If an application is received by mail, courier service, or otherwise submitted without a review meeting, the administrative review will be conducted within 30 days. The applicant and agent will be contacted with the results of the administrative review. If the application is found to be administratively incomplete, it can be retrieved from the regional office or returned by regular mail. If returned by mail, the regional office may require arrangements for return shipping.
6. If the geologic assessment was completed before October 1, 2004 and the site contains “possibly sensitive” features, the assessment must be updated in accordance with the *Instructions to Geologists* (TCEQ-0585 Instructions).

### Technical Review

1. When an application is deemed administratively complete, the technical review period begins. The regional office will distribute copies of the application to the identified affected city, county, and groundwater conservation district whose jurisdiction includes the subject site. These entities and the public have 30 days to provide comments on the application to the regional office. All comments received are reviewed by TCEQ.
2. A site assessment is usually conducted as part of the technical review, to evaluate the geologic assessment and observe existing site conditions. The site must be accessible to our staff. The site boundaries should be

clearly marked, features identified in the geologic assessment should be flagged, roadways marked and the alignment of the Sewage Collection System and manholes should be staked at the time the application is submitted. If the site is not marked the application may be returned.

3. We evaluate the application for technical completeness and contact the applicant and agent via Notice of Deficiency (NOD) to request additional information and identify technical deficiencies. There are two deficiency response periods available to the applicant. There are 14 days to resolve deficiencies noted in the first NOD. If a second NOD is issued, there is an additional 14 days to resolve deficiencies. If the response to the second notice is not received, is incomplete or inadequate, or provides new information that is incomplete or inadequate, the application must be withdrawn or will be denied. Please note that because the technical review is underway, whether the application is withdrawn or denied **the application fee will be forfeited**.
4. The program has 90 calendar days to complete the technical review of the application. If the application is technically adequate, such that it complies with the Edwards Aquifer rules, and is protective of the Edwards Aquifer during and after construction, an approval letter will be issued. Construction or other regulated activity may not begin until an approval is issued.

### Mid-Review Modifications

It is important to have final site plans prior to beginning the permitting process with TCEQ to avoid delays.

Occasionally, circumstances arise where you may have significant design and/or site plan changes after your Edwards Aquifer application has been deemed administratively complete by TCEQ. This is considered a "Mid-Review Modification". Mid-Review Modifications may require redistribution of an application that includes the proposed modifications for public comment.

If you are proposing a Mid-Review Modification, two options are available:

- If the technical review has begun your application can be denied/withdrawn, your fees will be forfeited, and the plan will have to be resubmitted.
- TCEQ can continue the technical review of the application as it was submitted, and a modification application can be submitted at a later time.

If the application is denied/withdrawn, the resubmitted application will be subject to the administrative and technical review processes and will be treated as a new application. The application will be redistributed to the affected jurisdictions.

Please contact the regional office if you have questions. If your project is located in Williamson, Travis, or Hays County, contact TCEQ's Austin Regional Office at 512-339-2929. If your project is in Comal, Bexar, Medina, Uvalde, or Kinney County, contact TCEQ's San Antonio Regional Office at 210-490-3096

Please fill out all required fields below and submit with your application.

<b>1. Regulated Entity Name:</b>					<b>2. Regulated Entity No.:</b>				
<b>3. Customer Name:</b>					<b>4. Customer No.:</b>				
<b>5. Project Type:</b> (Please circle/check one)	<input checked="" type="radio"/> New	<input type="radio"/> Modification			<input type="radio"/> Extension		<input type="radio"/> Exception		
<b>6. Plan Type:</b> (Please circle/check one)	<input checked="" type="radio"/> WPAP	<input type="radio"/> CZP	<input type="radio"/> SCS	<input type="radio"/> UST	<input type="radio"/> AST	<input type="radio"/> EXP	<input type="radio"/> EXT	<input type="radio"/> Technical Clarification	<input type="radio"/> Optional Enhanced Measures
<b>7. Land Use:</b> (Please circle/check one)	<input type="radio"/> Residential		<input checked="" type="radio"/> Non-residential			<b>8. Site (acres):</b>			
<b>9. Application Fee:</b>				<b>10. Permanent BMP(s):</b>					
<b>11. SCS (Linear Ft.):</b>				<b>12. AST/UST (No. Tanks):</b>					
<b>13. County:</b>				<b>14. Watershed:</b>					

# Application Distribution

Instructions: Use the table below to determine the number of applications required. One original and one copy of the application, plus additional copies (as needed) for each affected incorporated city, county, and groundwater conservation district are required. Linear projects or large projects, which cross into multiple jurisdictions, can require additional copies. Refer to the "Texas Groundwater Conservation Districts within the EAPP Boundaries" map found at:

[http://www.tceq.texas.gov/assets/public/compliance/field\\_ops/eapp/EAPP%20GWCD%20map.pdf](http://www.tceq.texas.gov/assets/public/compliance/field_ops/eapp/EAPP%20GWCD%20map.pdf)

For more detailed boundaries, please contact the conservation district directly.

Austin Region			
County:	Hays	Travis	Williamson
Original (1 req.)	—	—	—
Region (1 req.)	—	—	—
County(ies)	—	—	—
Groundwater Conservation District(s)	___ Edwards Aquifer Authority ___ Barton Springs/ Edwards Aquifer ___ Hays Trinity ___ Plum Creek	___ Barton Springs/ Edwards Aquifer	NA
City(ies) Jurisdiction	___ Austin ___ Buda ___ Dripping Springs ___ Kyle ___ Mountain City ___ San Marcos ___ Wimberley ___ Woodcreek	___ Austin ___ Bee Cave ___ Pflugerville ___ Rollingwood ___ Round Rock ___ Sunset Valley ___ West Lake Hills	___ Austin ___ Cedar Park ___ Florence ___ Georgetown ___ Jerrell ___ Leander ___ Liberty Hill ___ Pflugerville ___ Round Rock

San Antonio Region					
County:	Bexar	Comal	Kinney	Medina	Uvalde
Original (1 req.)	—	—	—	—	—
Region (1 req.)	—	—	—	—	—
County(ies)	—	—	—	—	—
Groundwater Conservation District(s)	___ Edwards Aquifer Authority ___ Trinity-Glen Rose	___ Edwards Aquifer Authority	___ Kinney	___ EAA ___ Medina	___ EAA ___ Uvalde
City(ies) Jurisdiction	___ Castle Hills ___ Fair Oaks Ranch ___ Helotes ___ Hill Country Village ___ Hollywood Park ___ San Antonio (SAWS) ___ Shavano Park	___ Bulverde ___ Fair Oaks Ranch ___ Garden Ridge ___ New Braunfels ___ Schertz	NA	___ San Antonio ETJ (SAWS)	NA

I certify that to the best of my knowledge, that the application is complete and accurate. This application is hereby submitted to TCEQ for administrative review and technical review.

Print Name of Customer/Authorized Agent



1 / 3 / 25

Signature of Customer/Authorized Agent

Date

**\*\*FOR TCEQ INTERNAL USE ONLY\*\***

Date(s) Reviewed:		Date Administratively Complete:	
Received From:		Correct Number of Copies:	
Received By:		Distribution Date:	
EAPP File Number:		Complex:	
Admin. Review(s) (No.):		No. AR Rounds:	
Delinquent Fees (Y/N):		Review Time Spent:	
Lat./Long. Verified:		SOS Customer Verification:	
Agent Authorization Complete/Notarized (Y/N):		Fee Check:	Payable to TCEQ (Y/N):
Core Data Form Complete (Y/N):			Signed (Y/N):
Core Data Form Incomplete Nos.:			Less than 90 days old (Y/N):

**GENERAL INFORMATION  
FORM (TCEQ-0587)**

# General Information Form

## Texas Commission on Environmental Quality

For Regulated Activities on the Edwards Aquifer Recharge and Transition Zones and Relating to 30 TAC §213.4(b) & §213.5(b)(2)(A), (B) Effective June 1, 1999

***To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.***

***Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.***


## Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **General Information Form** is hereby submitted for TCEQ review. The application was prepared by:

Print Name of Customer/Agent: Taylor Dawson, P.E.

Date: 1 / 3 / 25

Signature of Customer/Agent:

  
\_\_\_\_\_

## Project Information

1. Regulated Entity Name: JARRELL INDUSTRIAL PARK
2. County: Williamson
3. Stream Basin: Brazos River
4. Groundwater Conservation District (If applicable): N/A
5. Edwards Aquifer Zone:  
☒ Recharge Zone  
☐ Transition Zone
6. Plan Type:  
☒ WPAP  
☐ SCS

- ☐ Modification  
☐ AST

☐ UST

☐ Exception Request

7. Customer (Applicant):

Contact Person: Barry Cryer

Entity: : JARRELL INDUSTRIAL PARK, LLC

Mailing Address: 7500 Chevy Chase Dr.

City, State: Austin, TX

Zip: 78752

Telephone: 512.971.2833

FAX: \_\_\_\_\_

Email Address: jarrellbusinesspark@gmail.com

8. Agent/Representative (If any):

Contact Person: Taylor Dawson, P.E.

Entity: Pape-Dawson Consulting Engineers, LLC.

Mailing Address: 2000 NW Loop 410

City, State: San Antonio, TX

Zip: 78213

Telephone: (210) 375.9000

FAX: \_\_\_\_\_

Email Address: TaylorDawson@pape-dawson.com

9. Project Location:

☐ The project site is located inside the city limits of \_\_\_\_\_.

☒ The project site is located outside the city limits but inside the ETJ (extra-territorial jurisdiction) of Jarrell.

☐ The project site is not located within any city's limits or ETJ.

10. ☒ The location of the project site is described below. The description provides sufficient detail and clarity so that the TCEQ's Regional staff can easily locate the project and site boundaries for a field investigation.

11000 CR308, Jarrell, TX 76537, which is approx. 0.36 mi southeast of CR307 & CR308 intersection

11. ☒ **Attachment A – Road Map.** A road map showing directions to and the location of the project site is attached. The project location and site boundaries are clearly shown on the map.

12. ☒ **Attachment B - USGS / Edwards Recharge Zone Map.** A copy of the official 7 ½ minute USGS Quadrangle Map (Scale: 1" = 2000') of the Edwards Recharge Zone is attached. The map(s) clearly show:

☒ Project site boundaries.

☒ USGS Quadrangle Name(s).

☒ Boundaries of the Recharge Zone (and Transition Zone, if applicable).

☒ Drainage path from the project site to the boundary of the Recharge Zone.

13. ☒ **The TCEQ must be able to inspect the project site or the application will be returned.**  
Sufficient survey staking is provided on the project to allow TCEQ regional staff to locate

the boundaries and alignment of the regulated activities and the geologic or manmade features noted in the Geologic Assessment.

☒ Survey staking will be completed by this date: completed

14. ☒ **Attachment C – Project Description.** Attached at the end of this form is a detailed narrative description of the proposed project. The project description is consistent throughout the application and contains, at a minimum, the following details:

- ☒ Area of the site
- ☒ Offsite areas
- ☒ Impervious cover
- ☒ Permanent BMP(s)
- ☒ Proposed site use
- ☐ Site history
- ☐ Previous development
- ☐ Area(s) to be demolished

15. Existing project site conditions are noted below:

- ☐ Existing commercial site
- ☒ Existing industrial site
- ☐ Existing residential site
- ☐ Existing paved and/or unpaved roads
- ☐ Undeveloped (Cleared)
- ☐ Undeveloped (Undisturbed/Uncleared)
- ☐ Other: \_\_\_\_\_

### ***Prohibited Activities***

16. ☒ I am aware that the following activities are prohibited on the Recharge Zone and are not proposed for this project:

- (1) Waste disposal wells regulated under 30 TAC Chapter 331 of this title (relating to Underground Injection Control);
- (2) New feedlot/concentrated animal feeding operations, as defined in 30 TAC §213.3;
- (3) Land disposal of Class I wastes, as defined in 30 TAC §335.1;
- (4) The use of sewage holding tanks as parts of organized collection systems; and
- (5) New municipal solid waste landfill facilities required to meet and comply with Type I standards which are defined in §330.41(b), (c), and (d) of this title (relating to Types of Municipal Solid Waste Facilities).
- (6) New municipal and industrial wastewater discharges into or adjacent to water in the state that would create additional pollutant loading.

17. ☐ I am aware that the following activities are prohibited on the Transition Zone and are not proposed for this project:

- (1) Waste disposal wells regulated under 30 TAC Chapter 331 (relating to Underground Injection Control);
- (2) Land disposal of Class I wastes, as defined in 30 TAC §335.1; and
- (3) New municipal solid waste landfill facilities required to meet and comply with Type I standards which are defined in §330.41 (b), (c), and (d) of this title.

### ***Administrative Information***

18. The fee for the plan(s) is based on:

- ☒ For a Water Pollution Abatement Plan or Modification, the total acreage of the site where regulated activities will occur.
- ☐ For an Organized Sewage Collection System Plan or Modification, the total linear footage of all collection system lines.
- ☐ For a UST Facility Plan or Modification or an AST Facility Plan or Modification, the total number of tanks or piping systems.
- ☐ A request for an exception to any substantive portion of the regulations related to the protection of water quality.
- ☐ A request for an extension to a previously approved plan.

19. ☒ Application fees are due and payable at the time the application is filed. If the correct fee is not submitted, the TCEQ is not required to consider the application until the correct fee is submitted. Both the fee and the Edwards Aquifer Fee Form have been sent to the Commission's:


- ☒ TCEQ cashier
- ☐ Austin Regional Office (for projects in Hays, Travis, and Williamson Counties)
- ☐ San Antonio Regional Office (for projects in Bexar, Comal, Kinney, Medina, and Uvalde Counties)

20. ☒ Submit one (1) original and one (1) copy of the application, plus additional copies as needed for each affected incorporated city, groundwater conservation district, and county in which the project will be located. The TCEQ will distribute the additional copies to these jurisdictions. The copies must be submitted to the appropriate regional office.

21. ☒ No person shall commence any regulated activity until the Edwards Aquifer Protection Plan(s) for the activity has been filed with and approved by the Executive Director.

**ATTACHMENT A**

# JARRELL INDUSTRIAL PARK Water Pollution Abatement Plan

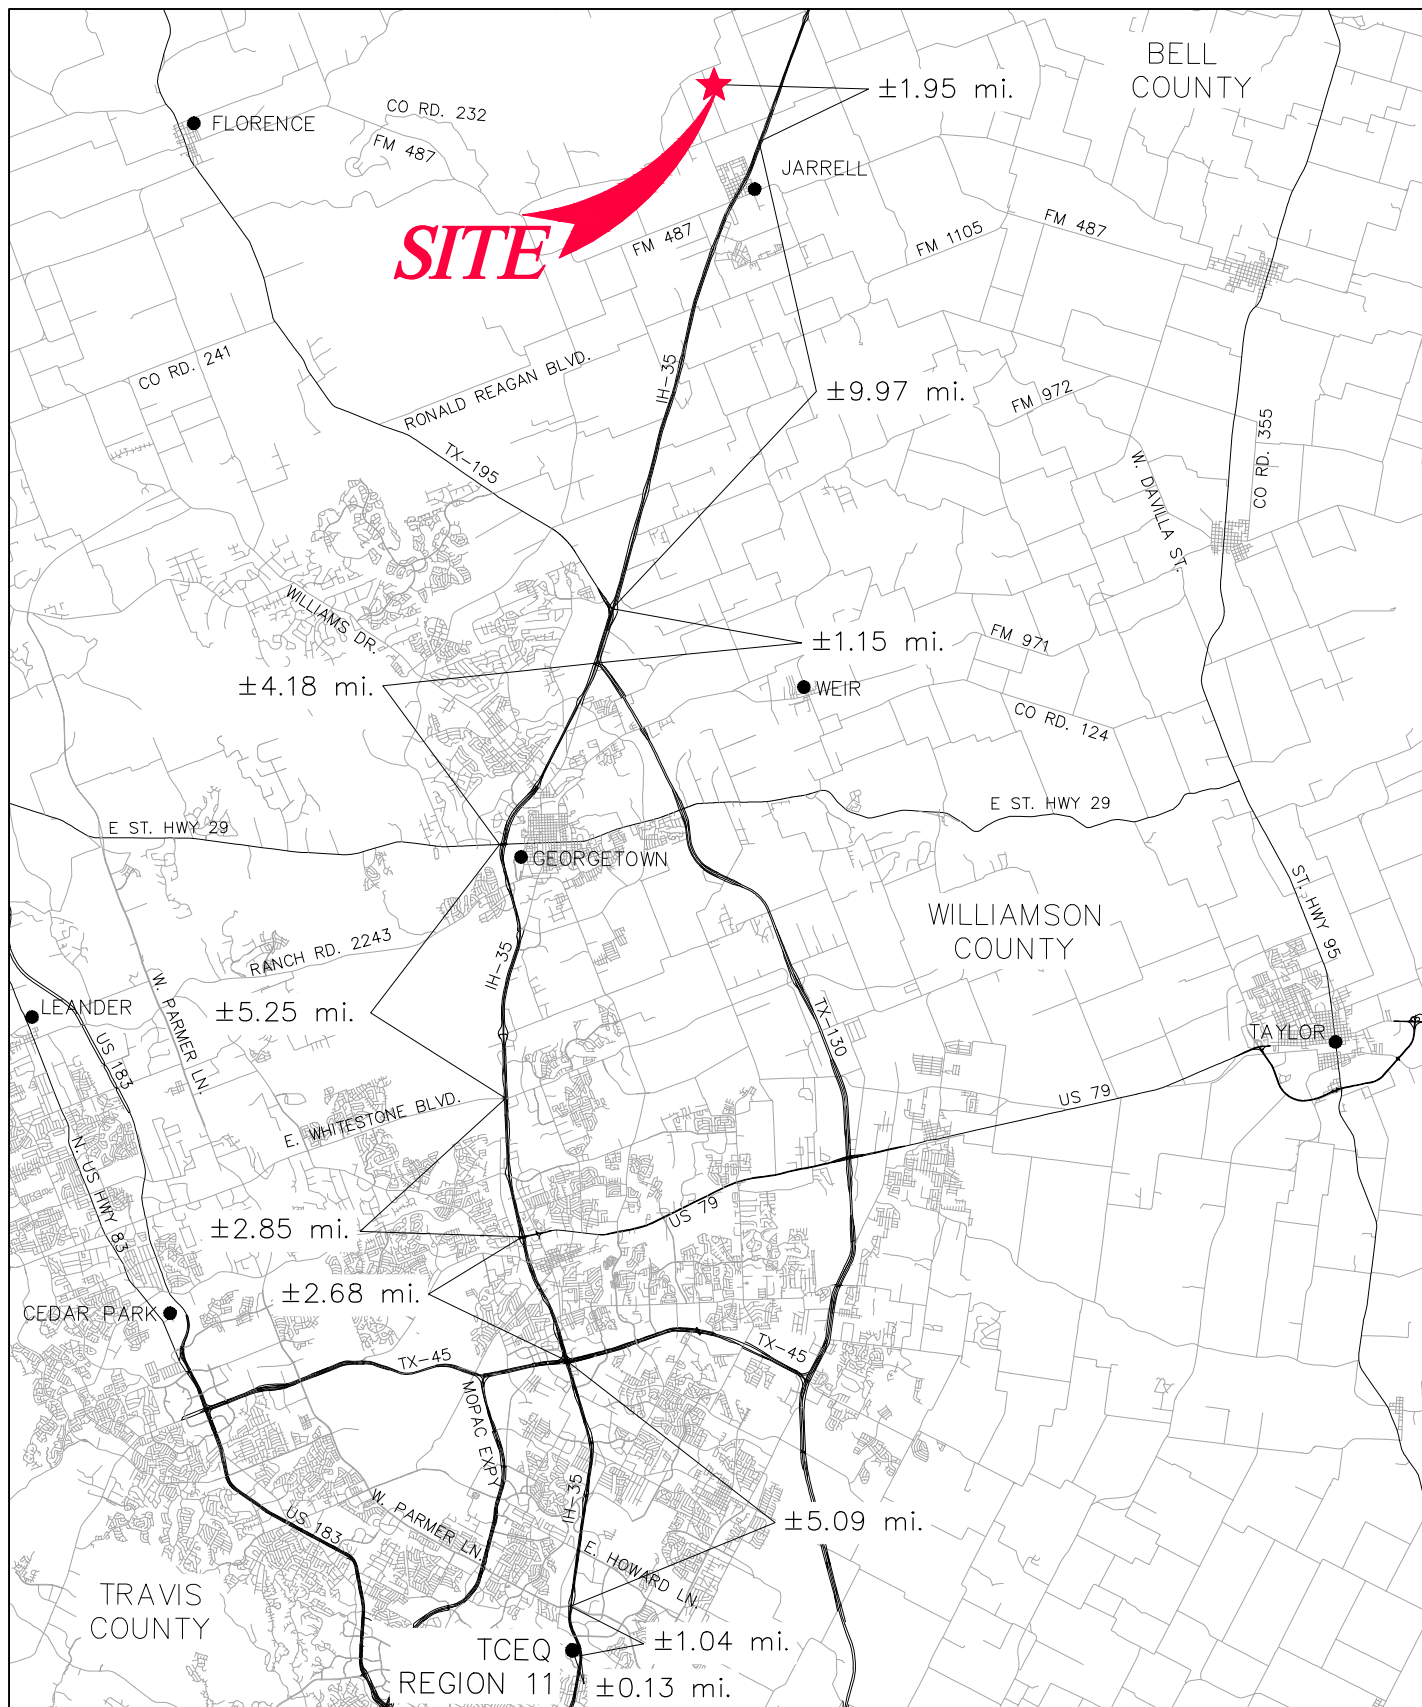


Pape-Dawson Engineers, Inc.


Date: Jan 03, 2025, 10:04am User ID: kherrera  
File: H:\Projects\515\70\00\301 Construction Documents\Exhibits\RM1193310.dwg

ROAD MAP  
ATTACHMENT A


**ATTACHMENT B**

JARRELL INDUSTRIAL PARK  
Water Pollution abatement Plan

  
SCALE: 1" = 2000'

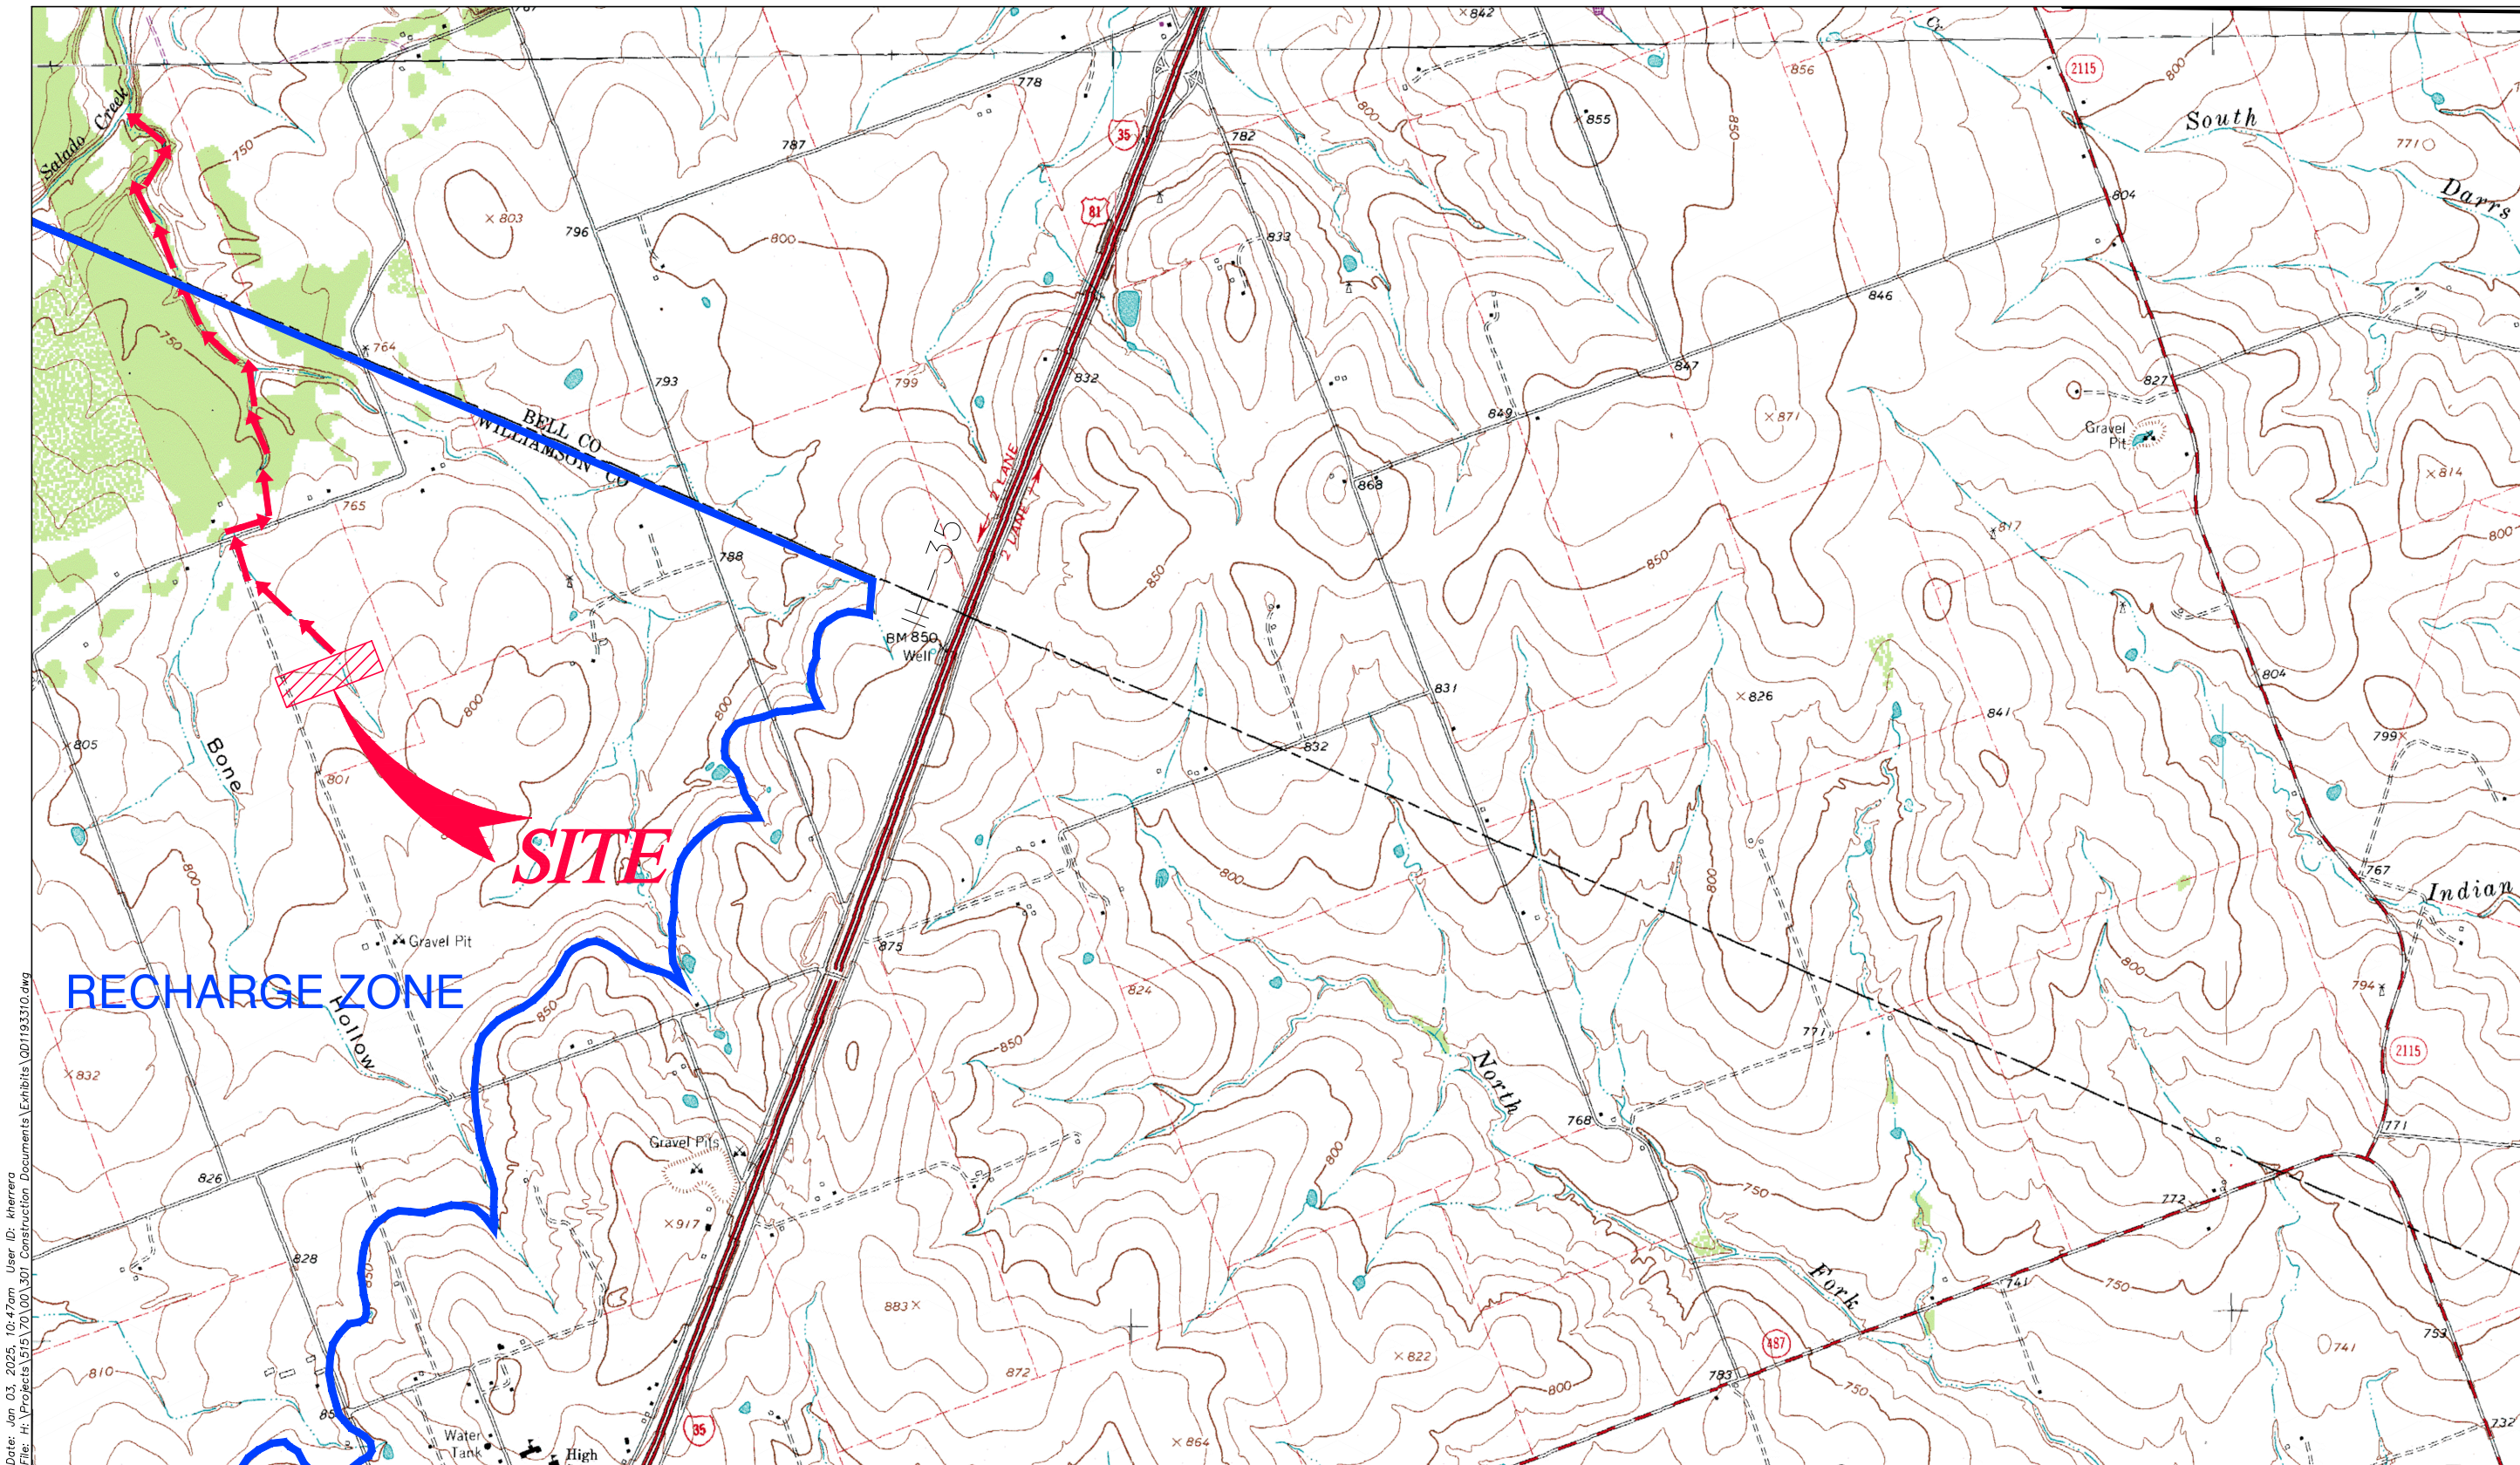

Date: Jan 03, 2025, 10:47am User ID: kherrera  
File: H:\Projects\1515170\00\301 Construction Documents\Exhibits\001193310.dwg

GENERAL LOCATION MAP - JARRELL, TX QUAD  
DRAINAGE FLOW   
Pape-Dawson Engineers, Inc.

USGS QUAD MAP  
ATTACHMENT B

**ATTACHMENT C**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment C – Project Description

Jarrell Industrial Park Water Pollution Abatement Plan (WPAP) proposes the construction of a light industrial business complex on a project limits of 6.184 acres (10.78 legal limits) within the extra territorial jurisdiction of the City of Jarrell, in Williamson County, Texas. The site is located approximately 0.35 mi southeast of CR307/CR308 intersection (1000 CR 308, Jarrell, TX 76537). The site is bound by undeveloped property to the north, south and east. The site is currently developed, and this application is being submitted in response to a Notice of Enforcement due to development without an approved WPAP. The site lies within the Brazos River watershed and does not contain a 100-year floodplain. There were no naturally occurring sensitive geological features identified in the Geologic Assessment.

This WPAP proposes approval of the existing impervious cover for the buildings, drives, and associated hardscapes which is approximately 2.89 acre, or 26.81% of the 10.78 legal limit of the site. Regulated activities consist of clearing, grading, excavation, installation of utilities and drainage improvements, water quality basin construction, construction of buildings and associated parking. The proposed Permanent Best Management Practices (PBMPs) for stormwater treatment is one (1) batch detention basin. Approximately 2.86 acres of impervious cover from the building, parking, and drives will be treated by the basin; leaving 0.03 acres from the driveway flare as overtreatment. Stormwater from upgradient areas will be routed around the site. The proposed Permanent Best Management Practices (PBMPs) for stormwater treatment is designed in accordance with the TCEQ's Technical Guidance Manual (TGM) RG-348 (2005) to remove 80% of the increase in Total Suspended Solids (TSS) from the site.

Wastewater will be disposed of to onsite OSSF services, see attached inspection reports from Williamson County.

**GEOLOGIC ASSESSMENT FORM**  
**(TCEQ-0585)**

# Geologic Assessment

## Texas Commission on Environmental Quality

For Regulated Activities on The Edwards Aquifer Recharge/transition Zones and Relating to 30 TAC §213.5(b)(3), Effective June 1, 1999

**To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.**

**Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.**

## Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. My signature certifies that I am qualified as a geologist as defined by 30 TAC Chapter 213.

Print Name of Geologist: Henry E. Stultz III, P.G.


Telephone: 210-375-9000

Date: October 2, 2024

Fax: 210-375-9090

Representing: Pape-Dawson Engineers, Inc., TBPGE registration number 50351

Signature of Geologist:



Regulated Entity Name: Jarrell Industrial Park WQ Pond

## Project Information

1. Date(s) Geologic Assessment was performed: September 25, 2024

2. Type of Project:

- ☒ WPAP  
☐ SCS

- ☐ AST  
☐ UST

3. Location of Project:

- ☒ Recharge Zone  
☐ Transition Zone  
☐ Contributing Zone within the Transition Zone

4. ☒ **Attachment A - Geologic Assessment Table.** Completed Geologic Assessment Table (Form TCEQ-0585-Table) is attached.
5. ☒ Soil cover on the project site is summarized in the table below and uses the SCS Hydrologic Soil Groups\* (Urban Hydrology for Small Watersheds, Technical Release No. 55, Appendix A, Soil Conservation Service, 1986). If there is more than one soil type on the project site, show each soil type on the site Geologic Map or a separate soils map.

**Table 1 - Soil Units, Infiltration Characteristics and Thickness**

Soil Name	Group*	Thickness(feet)
Denton silty clay, 1 to 3 % slopes (DnB)	D	3-5

*\* Soil Group Definitions (Abbreviated)*

- A. Soils having a high infiltration rate when thoroughly wetted.
- B. Soils having a moderate infiltration rate when thoroughly wetted.
- C. Soils having a slow infiltration rate when thoroughly wetted.
- D. Soils having a very slow infiltration rate when thoroughly wetted.

6. ☒ **Attachment B – Stratigraphic Column.** A stratigraphic column showing formations, members, and thicknesses is attached. The outcropping unit, if present, should be at the top of the stratigraphic column. Otherwise, the uppermost unit should be at the top of the stratigraphic column.
7. ☒ **Attachment C – Site Geology.** A narrative description of the site specific geology including any features identified in the Geologic Assessment Table, a discussion of the potential for fluid movement to the Edwards Aquifer, stratigraphy, structure(s), and karst characteristics is attached.
8. ☒ **Attachment D – Site Geologic Map(s).** The Site Geologic Map must be the same scale as the applicant's Site Plan. The minimum scale is 1": 400'

Applicant's Site Plan Scale: 1" = 50'

Site Geologic Map Scale: 1" = 50'

Site Soils Map Scale (if more than 1 soil type): N/A

9. Method of collecting positional data:

- ☒ Global Positioning System (GPS) technology.
- ☐ Other method(s). Please describe method of data collection: \_\_\_\_\_

10. ☒ The project site and boundaries are clearly shown and labeled on the Site Geologic Map.
11. ☒ Surface geologic units are shown and labeled on the Site Geologic Map.

12. ☒ Geologic or manmade features were discovered on the project site during the field investigation. They are shown and labeled on the Site Geologic Map and are described in the attached Geologic Assessment Table.
- ☐ Geologic or manmade features were not discovered on the project site during the field investigation.
13. ☒ The Recharge Zone boundary is shown and labeled, if appropriate.
14. All known wells (test holes, water, oil, unplugged, capped and/or abandoned, etc.): If applicable, the information must agree with Item No. 20 of the WPAP Application Section.
- ☐ There is \_\_\_\_\_ (#) wells present on the project site and the location is shown and labeled.  
(Check all of the following that apply.)
- ☐ The wells are not in use and have been properly abandoned.
- ☐ The wells are not in use and will be properly abandoned.
- ☐ The wells are in use and comply with 16 TAC Chapter 76.
- ☒ There are no wells or test holes of any kind known to exist on the project site.

### ***Administrative Information***

15. ☒ Submit one (1) original and one (1) copy of the application, plus additional copies as needed for each affected incorporated city, groundwater conservation district, and county in which the project will be located. The TCEQ will distribute the additional copies to these jurisdictions. The copies must be submitted to the appropriate regional office.

**ATTACHMENT A**  
**Geologic Assessment Table**

GEOLOGIC ASSESSMENT TABLE									PROJECT NAME: Jarrell Industrial Park WQ Pond											
LOCATION			FEATURE CHARACTERISTICS											EVALUATION		PHYSICAL SETTING				
1A	1B *	1C*	2A	2B	3	4			5	5A	6	7	8A	8B	9	10		11		12
FEATURE ID	LATITUDE	LONGITUDE	FEATURE TYPE	POINTS	FORMATION	DIMENSIONS (FEET)			TREND (DEGREES)	DOM	DENSITY (NO/FT)	APERTURE (FEET)	INFILL	RELATIVE INFILTRATION RATE	TOTAL	SENSITIVITY		CATCHMENT AREA (ACRES)		TOPOGRAPHY
						X	Y	Z		10						<40	≥40	<1.6	≥1.6	
S-1	30.85487°	-97.61477°	MB	30	Kgt	10	5	5					F,X	5	35	35		X		Hillside
S-2	30.85489°	-97.61471°	MB	30	Kgt	10	5	5					F,X	5	35	35		X		Hillside
S-3	30.85507°	-97.61414°	MB	30	Kgt	10	5	5					F,X	5	35	35		X		Hillside
S-4	30.85510°	-97.61407°	MB	30	Kgt	10	5	5					F,X	5	35	35		X		Hillside
S-5	30.85528°	-97.61347°	MB	30	Kgt	10	5	5					F,X	5	35	35		X		Hillside

\*\* DATUM: NAD 83



2A TYPE	TYPE	2B POINTS
C	Cave	30
SC	Solution cavity	20
SF	Solution-enlarged fracture(s)	20
F	Fault	20
O	Other natural bedrock features	5
MB	Manmade feature in bedrock	30
SW	Swallow hole	30
SH	Sinkhole	20
CD	Non-karst closed depression	5
Z	Zone, clustered or aligned features	30

8A INFILLING	
N	None, exposed bedrock
C	Coarse - cobbles, breakdown, sand, gravel
O	Loose or soft mud or soil, organics, leaves, sticks, dark colors
F	Fines, compacted clay-rich sediment, soil profile, gray or red colors
V	Vegetation. Give details in narrative description
FS	Flowstone, cements, cave deposits
X	Other materials

12 TOPOGRAPHY
Cliff, Hilltop, Hillside, Drainage, Floodplain, Streambed

I have read, I understood, and I have followed the Texas Commission on Environmental Quality's Instructions to Geologists. The information presented here complies with that document and is a true representation of the conditions observed in the field. My signature certifies that I am qualified as a geologist as defined by 30 TAC Chapter 213.

Date October 2, 2024

**ATTACHMENT B**  
**Stratigraphic Column**

JARRELL INDUSTRIAL PARK WQ POND  
Geologic Assessment (TCEQ-0585)

Attachment B – Stratigraphic Column

Period	Epoch	Group	Formation	Member	Thickness	Lithology	Hydro-logic Unit	Hydro-stratigraphic Unit	Hydrologic Function	Porosity	Cavern Development
Cretaceous	Late Cretaceous	Washita	George-town	--	20–30	Reddish-brown, gray to light tan, shaley mudstone and wackestone; commonly contains black dendrites, iron nodules, and iron staining; often fossiliferous with <i>Plesioturrillites brazoensis</i> , <i>Waconella wacoensis</i> common	Edwards Aquifer	I	Confining	MO	None
			Person	Cyclic and marine, undivided	80–90	Pelletal limestone; ranges from chalk to mudstone and miliolid grainstone; thin to massive beds; some crossbedding evident; a packstone containing large caprinids is present near contact with the overlying Georgetown Formations; chert is common as beds and large nodules		II	Aquifer	MO, BU, VUG, BP, FR, CV	Many subsurface; might be associated with earlier karst development
	Leached and collapsed, undivided	70–90		Hard, dense, recrystallized limestone;mudstone, wackestone, packstone, and grainstone; contains chert as beds and large nodules; heavily bioturbated with iron-stained beds; often stromatolitic; <i>Toucasia</i> sp. Often found above contact with the underlying regional dense member; <i>Montastrea roemeriana</i> and oysters rare	III	Aquifer		BU, VUG, FR, BP, BR, CV	Extensive lateral development; large rooms		
		Regional dense		20–24	Dense, shaly limestone; oyster shell mudstone and iron wackestone; wispy iron staining; chert nodules rarer than in the rest of the chert-bearing Edwards Group	IV		Confining	FR, CV	Very few; only vertical fracture enlargement	
	Kainer	Grainstone	40–50	Hard, dense limestone that consists mostly of a tightly cemented miliolid skeletal fragment grainstone; contains interspersed chalky mudstone and wackestone; chert as beds and nodules; crossbedding and ripple marks are common primarily at the contact with the overlying regional dense bed	V	Aquifer		IP, IG, BU, FR, BP, CV	Few		
		Kirsch-berg Evaporite	40–50	Highly altered crystalline limestone and chalky mudstone with occasional grainstone associated with tidal channels; chert as beds and nodules, boxwork molds are common, matrix recrystallized to a coarse grain spar; intervals of collapse breccia and travertine deposits	VI	Aquifer		IG, MO, VUG, FR, BR, CV	Probably extensive cave development		
		Dolomitic	90–120	Hard, dense to granular, dolomitic limestone; chert as beds and nodules (absent in lower 20 ft); <i>Toucasia</i> sp. abundant; lower three-fourths composed of sucrosic dolomites and grainstones with hard, dense limestones interspersed; upper one-fourth composed mostly of hard, dense mudstone, wackestone, packstone, grainstone, and recrystallized dolomites with bioturbated beds	VII	Aquifer		IP, IC, IG, MO, BU, VUG, FR, BP, CV	Cave development as shafts with minor horizontal extent		
		Basal nodular	40–50	Moderately hard, shaly, nodular, burrowed mudstone to miliolid grainstone that also contains dolomite; contains dark, spherical textural features known as black rotund bodies; <i>Ceratostreon texana</i> , <i>Caprina</i> sp., miliolids, and gastropods	VIII	Aquifer, confining unit in areas without caves		IP, MO, BU, BP, FR, CV	Large lateral caves at surface		
	Trinity	Glen Rose Limestone	Upper Glen Rose	0–120 (absent in northern Comal Co.)	Alternating resistant and nonresistant beds of blue shale, nodular marl, and impure, fossiliferous limestone; gray to yellowish gray; stair-step topography; contains two distinct evaporite zones; distinct <i>Corbula</i> sp. bed marks the contact with the underlying lower member of the Glen Rose Limestone; <i>Orbitulina texana</i>	Upper Trinity  Lower confining unit to the Edwards aquifer	Cavernous		Aquifer	MO, BR, BP, FR, CV	Some surface cave development
				Camp Bullis			Confining	BU, BP, FR, occasional CV			
				Upper evaporite			Aquifer	IP, MO, BU, BR			
				Fossil-iferous			Upper	Aquifer	MO, BU, FR, CV		
							Lower	Confining	MO, BU, FR		
				Lower evaporite			Aquifer	IP, MO, BU, BR			

Source: Clark, Golab, and Morris (2016); Cavern development modified from Stein and Ozuna (1995). Porosity types - Fabric selective: IP, interparticle porosity; IG, intergranular porosity; IC, intercrystalline porosity; SH, shelter porosity; MO, moldic porosity; BU, burrowed porosity; FE, fenestral; BP, bedding plane porosity. Not fabric selective: FR, fracture porosity; CH, channel porosity; BR, breccia; VUG, vug porosity; CV, cave porosity.

# **ATTACHMENT C**

## **Site Geology**

# JARRELL INDUSTRIAL PARK WQ POND

## Geologic Assessment

### Attachment C – Site Geology

#### SUMMARY

The Jarrell Industrial Park WQ Pond site is located at 1000 County Rd 308 in the City of Jarrell, Williamson County, Texas.

Based on the results of the field survey conducted in accordance with *Instructions for Geologists for Geologic Assessments in the Edwards Aquifer Recharge/Transition Zones (TCEQ-0585 Instructions)*, no naturally occurring sensitive features were identified on site. No springs or seeps were observed onsite. One stream was observed onsite but was not flowing at the time of the site visit. The overall potential for fluid migration to the Edwards Aquifer for the site is low.

#### SITE GEOLOGY

As observed through review of published sources and through field evidence, the geologic formation which outcrops at the surface within the subject site is the Georgetown (Kgt) formation. The Kgt formation is characterized by reddish-brown to light tan marly limestone. Karst development within the Kgt is uncommon and generally minor.

The predominant trend of faults in the vicinity of the site is approximately N37°E, based on faults identified during the previous mapping of the area.

#### FEATURE DESCRIPTIONS:

A description of the features observed onsite is provided below:

##### Features S-1 through S-5

Features S-1 through S-5 are septic tanks. Due to the non-karst origin and the likelihood that the septic systems are confined to the soil horizon, the probability for rapid infiltration to the aquifer is low.

# JARRELL INDUSTRIAL PARK WQ POND

## Geologic Assessment

### REFERENCES

Collins, E.W., 2005, Geologic map of the west half of the Taylor, Texas, 30 X 60 minute quadrangle: central Texas urban corridor, encompassing Round Rock, Georgetown, Salado, Briggs, Liberty Hill, and Leander: University of Texas at Austin, Bureau of Economic Geology, Miscellaneous Map 43, scale 1:100,000

Nationwide Environmental Title Research, LLC. Historical Aerials, HistoricAerials.com. <https://www.historicaerials.com/viewer>, September 24, 2024.

Soil Survey Staff, Natural Resources Conservation Service, United States Department of Agriculture. Web Soil Survey. <http://websoilsurvey.sc.egov.usda.gov/>, September 24, 2024.

Stein, W.G., and Ozuna, G.B., 1995, Geologic framework and hydrogeologic characteristics of the Edwards Aquifer recharge zone, Bexar County, Texas: U.S. Geological Survey Water-Resources Investigations Report 95-4030, 8 p.

Texas Water Development Board, Wells in TWDB Groundwater Database Viewer, <https://www3.twdb.texas.gov/apps/waterdatainteractive/groundwaterdataviewer>, September 24, 2024.

U.S. Geological Survey, National Water Information System: Mapper, <https://maps.waterdata.usgs.gov/mapper/index.html>, September 24, 2024.

**ATTACHMENT D**  
**Site Geologic Map(s)**

LEGEND

PROJECT LIMITS

EXISTING CONTOUR LINE

100 YEAR FLOODPLAIN

STREAM

GEOLOGIC FORMATIONS

Qal

ALLUVIUM

Kgt

GEORGETOWN

Kef

EAGLE FORD

Kbu

BUDA

Kdr

DEL RIO

Ked

EDWARDS

Kgr

GLEN ROSE

SYMBOLS AND LINES

S-1

POTENTIAL RECHARGE FEATURE

CONTACT, LOCATED APPROXIMATELY

CONTACT, INFERRED

u

FAULT, LOCATED APPROXIMATELY  
(U, DOWNTHROWN SIDE; U, UP-THROWN SIDE)

FAULT, EXTRAPOLATED

FAULT, INFERRED

STRIKE AND DIP OF BEDDING

STRIKE AND DIP OF JOINTS

STRIKE OF VERTICAL JOINTS

CAVE

SOLUTION CAVITY

SOLUTION ENLARGED FRACTURE

SWALLOW HOLE

SINKHOLE

NON-KARST CLOSED DEPRESSION

ZONE

OTHER NATURAL BEDROCK FEATURES

SPRING/SEEP

MB

MAN-MADE FEATURE IN BEDROCK

MB

WATER WELL

SANITARY SEWER LINE

STORM DRAIN LINE

NOTE: THE RECHARGE ZONE BOUNDARY IS NOT WITHIN THE AREA SHOWN ON THIS SHEET. THE SITE IS LOCATED ENTIRELY WITHIN THE RECHARGE ZONE.

NOTE: THE GEOSCIENTIST SEAL HAS BEEN AFFIXED TO THIS SHEET ONLY FOR THE PURPOSES OF GEOLOGIC INFORMATION. ALL OTHER INFORMATION SHOULD BE ACQUIRED FROM THE APPROPRIATE SIGNED AND SEALED CIVIL ENGINEERING DRAWINGS.

NO.	REVISION	DATE

**PAPE-DAWSON ENGINEERS**

SAN ANTONIO | AUSTIN | HOUSTON | FORT WORTH | DALLAS  
2000 NW LOOP 410 | SAN ANTONIO, TX 78213 | 210.375.9000  
TBPCE FIRM REGISTRATION #470 | TBPCE FIRM REGISTRATION #10028800

**JARRELL INDUSTRIAL PARK WQ POND**

CITY OF JARRELL

**SITE GEOLOGIC MAP**

**WATER POLLUTION ABATEMENT PLAN**

PLAT NO.	---
JOB NO.	51570-00
DATE	Sep 2024
DESIGNER	HS
CHECKED	HDJ
DRAWN	HS
SHEET	ATT D

Date: Sep 30, 2024 9:25 AM User: hsalutz  
File: H:\Projects\5157000\ENR\WQ\Attachments\GIS\Working.aprx

THIS DOCUMENT HAS BEEN PRODUCED FROM MATERIAL THAT WAS STORED AND/OR TRANSMITTED ELECTRONICALLY AND MAY HAVE BEEN INADVERTENTLY ALTERED. RELY ONLY ON FINAL HARD-COPY MATERIALS BEARING THE CONSULTANT'S ORIGINAL SIGNATURE AND SEAL. AERIAL IMAGERY PROVIDED BY GOOGLE. © UNLESS OTHERWISE NOTED. Imagery © 2024, CAPCOG Digital Globe, Texas Orthoregistry Program, USDA Farm Service Agency.

**WATER POLLUTION  
ABATEMENT PLAN  
APPLICATION FORM (TCEQ-  
0584)**

# Water Pollution Abatement Plan Application

## Texas Commission on Environmental Quality

for Regulated Activities on the Edwards Aquifer Recharge Zone and Relating to 30 TAC §213.5(b), Effective June 1, 1999

*To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.*

*Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.*

## Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Water Pollution Abatement Plan Application Form** is hereby submitted for TCEQ review and Executive Director approval. The form was prepared by:

Print Name of Customer/Agent: Taylor Dawson, P.E.

Date: 1/3/25

Signature of Customer/Agent:



---

Regulated Entity Name: JARRELL INDUSTRIAL PARK

## Regulated Entity Information

1. The type of project is:

- ☐ Residential: Number of Lots: \_\_\_\_\_
- ☐ Residential: Number of Living Unit Equivalents: \_\_\_\_\_
- ☐ Commercial
- ☒ Industrial
- ☐ Other: \_\_\_\_\_

2. Total site acreage (size of property): 10.78

3. Estimated projected population: 0

4. The amount and type of impervious cover expected after construction are shown below:

**Table 1 - Impervious Cover Table**

Impervious Cover of Proposed Project	Sq. Ft.	Sq. Ft./Acre	Acres
Structures/Rooftops	25,855	$\div 43,560 =$	0.59
Parking	25,247	$\div 43,560 =$	0.58
Other paved surfaces	74,608	$\div 43,560 =$	1.71
Total Impervious Cover	125,710	$\div 43,560 =$	2.89

**Total Impervious Cover 2.89  $\div$  Total Acreage 10.78 X 100 = 26.81% Impervious Cover**

5. ☒ **Attachment A - Factors Affecting Surface Water Quality.** A detailed description of all factors that could affect surface water and groundwater quality that addresses ultimate land use is attached.
6. ☒ Only inert materials as defined by 30 TAC §330.2 will be used as fill material.

### ***For Road Projects Only***

**Complete questions 7 - 12 if this application is exclusively for a road project.**

7. Type of project:

- ☐ TXDOT road project.
- ☐ County road or roads built to county specifications.
- ☐ City thoroughfare or roads to be dedicated to a municipality.
- ☐ Street or road providing access to private driveways.

8. Type of pavement or road surface to be used:

- ☐ Concrete
- ☐ Asphaltic concrete pavement
- ☐ Other: \_\_\_\_\_

9. Length of Right of Way (R.O.W.): \_\_\_\_\_ feet.

Width of R.O.W.: \_\_\_\_\_ feet.

$L \times W =$  \_\_\_\_\_  $\text{Ft}^2 \div 43,560 \text{ Ft}^2/\text{Acre} =$  \_\_\_\_\_ acres.

10. Length of pavement area: \_\_\_\_\_ feet.

Width of pavement area: \_\_\_\_\_ feet.

$L \times W =$  \_\_\_\_\_  $\text{Ft}^2 \div 43,560 \text{ Ft}^2/\text{Acre} =$  \_\_\_\_\_ acres.

Pavement area \_\_\_\_\_ acres  $\div$  R.O.W. area \_\_\_\_\_ acres  $\times 100 =$  \_\_\_\_\_ % impervious cover.

11. ☐ A rest stop will be included in this project.

☐ A rest stop will not be included in this project.

12. ☐ Maintenance and repair of existing roadways that do not require approval from the TCEQ Executive Director. Modifications to existing roadways such as widening roads/adding shoulders totaling more than one-half (1/2) the width of one (1) existing lane require prior approval from the TCEQ.

### ***Stormwater to be generated by the Proposed Project***

13. ☒ **Attachment B - Volume and Character of Stormwater.** A detailed description of the volume (quantity) and character (quality) of the stormwater runoff which is expected to occur from the proposed project is attached. The estimates of stormwater runoff quality and quantity are based on the area and type of impervious cover. Include the runoff coefficient of the site for both pre-construction and post-construction conditions.

### ***Wastewater to be generated by the Proposed Project***

14. The character and volume of wastewater is shown below:

<u>100%</u> Domestic	_____ Gallons/day
_____ % Industrial	_____ Gallons/day
_____ % Commingled	
_____ Gallons/day	
TOTAL gallons/day _____	

15. Wastewater will be disposed of by:

☒ On-Site Sewage Facility (OSSF/Septic Tank):

☒ **Attachment C - Suitability Letter from Authorized Agent.** An on-site sewage facility will be used to treat and dispose of the wastewater from this site. The appropriate licensing authority's (authorized agent) written approval is attached. It states that the land is suitable for the use of private sewage facilities and will meet or exceed the requirements for on-site sewage facilities as specified under 30 TAC Chapter 285 relating to On-site Sewage Facilities.

☒ Each lot in this project/development is at least one (1) acre (43,560 square feet) in size. The system will be designed by a licensed professional engineer or registered sanitarian and installed by a licensed installer in compliance with 30 TAC Chapter 285.

☐ Sewage Collection System (Sewer Lines):

☐ Private service laterals from the wastewater generating facilities will be connected to an existing SCS.

☐ Private service laterals from the wastewater generating facilities will be connected to a proposed SCS.

☐ The SCS was previously submitted on \_\_\_\_\_.

☐ The SCS was submitted with this application.

☐ The SCS will be submitted at a later date. The owner is aware that the SCS may not be installed prior to Executive Director approval.

☐ The sewage collection system will convey the wastewater to the \_\_\_\_\_ (name) Treatment Plant. The treatment facility is:

☐ Existing.

☐ Proposed.

16. ☐ All private service laterals will be inspected as required in 30 TAC §213.5.

## **Site Plan Requirements**

**Items 17 – 28 must be included on the Site Plan.**

17. ☒ The Site Plan must have a minimum scale of 1" = 400'.

Site Plan Scale: 1" = 50'.

18. 100-year floodplain boundaries:

☐ Some part(s) of the project site is located within the 100-year floodplain. The floodplain is shown and labeled.

☒ No part of the project site is located within the 100-year floodplain.

The 100-year floodplain boundaries are based on the following specific (including date of material) sources(s): DFIRM (Digital Flood Insurance Rate Map for Williamson County, Texas and Incorporated Areas) Panel No. 48491C0485F, Dated 12.20.2019

19. ☒ The layout of the development is shown with existing and finished contours at appropriate, but not greater than ten-foot contour intervals. Lots, recreation centers, buildings, roads, open space, etc. are shown on the plan.

☐ The layout of the development is shown with existing contours at appropriate, but not greater than ten-foot intervals. Finished topographic contours will not differ from the existing topographic configuration and are not shown. Lots, recreation centers, buildings, roads, open space, etc. are shown on the site plan.

20. All known wells (oil, water, unplugged, capped and/or abandoned, test holes, etc.):

☒ There are 0 (#) wells present on the project site and the locations are shown and labeled. (Check all of the following that apply)

☐ The wells are not in use and have been properly abandoned.

☐ The wells are not in use and will be properly abandoned.

☐ The wells are in use and comply with 16 TAC §76.

☒ There are no wells or test holes of any kind known to exist on the project site.

21. Geologic or manmade features which are on the site:

☐ All sensitive geologic or manmade features identified in the Geologic Assessment are shown and labeled.

☒ No sensitive geologic or manmade features were identified in the Geologic Assessment.

☐ **Attachment D - Exception to the Required Geologic Assessment.** A request and justification for an exception to a portion of the Geologic Assessment is attached.

- 22. ☒ The drainage patterns and approximate slopes anticipated after major grading activities.
- 23. ☒ Areas of soil disturbance and areas which will not be disturbed.
- 24. ☒ Locations of major structural and nonstructural controls. These are the temporary and permanent best management practices.
- 25. ☒ Locations where soil stabilization practices are expected to occur.
- 26. ☐ Surface waters (including wetlands).  
☒ N/A
- 27. ☐ Locations where stormwater discharges to surface water or sensitive features are to occur.  
☒ There will be no discharges to surface water or sensitive features.
- 28. ☒ Legal boundaries of the site are shown.

### ***Administrative Information***

- 29. ☒ Submit one (1) original and one (1) copy of the application, plus additional copies as needed for each affected incorporated city, groundwater conservation district, and county in which the project will be located. The TCEQ will distribute the additional copies to these jurisdictions. The copies must be submitted to the appropriate regional office.
- 30. ☒ Any modification of this WPAP will require Executive Director approval, prior to construction, and may require submission of a revised application, with appropriate fees.

**ATTACHMENT A**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment A – Factors Affecting Water Quality

Potential sources of pollution that may reasonably be expected to affect the quality of storm water discharges from the site during construction include:

- Soil erosion due to the clearing of the site;
- Oil, grease, fuel and hydraulic fluid contamination from construction equipment and vehicle drippings;
- Hydrocarbons from asphalt paving operations;
- Miscellaneous trash and litter from construction workers and material wrappings;
- Concrete truck washout.
- Potential overflow/spills from portable toilets

Potential sources of pollution that may reasonably be expected to affect the quality of storm water discharges from the site after development include:

- Oil, grease, fuel and hydraulic fluid contamination from vehicle drippings;
- Dirt and dust which may fall off vehicles; and
- Miscellaneous trash and litter.

**ATTACHMENT B**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment B – Volume and Character of Stormwater

Stormwater runoff will increase as a result of this development. For a 25-year storm event, the overall project will generate approximately 32 cfs. The runoff coefficient for the site changes from approximately 80 before development to 90 after development. Values are based on the runoff coefficients per the City of Jarrell Drainage Design Criteria.

**ATTACHMENT C**



## Inspection Report

Inspection Date: 3/16/2022 4:32:29 PM

**Passed**

MES Septic - Charles Morrison Should Contact Williamson County at (512-943-3330) for further information.

Case Number	Work Order Number	Inspection Number
OSSF-2022-4	16509273	12241395
Jurisdiction	Inspection Type	Inspector
Williamson County	Field Inspection	James Lancaster
Customer	Address	Phone
MES Septic - Charles Morrison	1000 CR 308, JARRELL 76537	No Number Provided
Scheduled	Completed	Uploaded
3/16/2022 12:00:00 AM	3/16/2022 4:32:29 PM	3/16/2022 4:32:29 PM

## Details

The information included in this report is also available at  
[MyPermitNow.org](https://MyPermitNow.org)

For more information on accessing your information through MyPermitNow.org's Free Customer Portal, visit [MyPermitNow.org](https://MyPermitNow.org), or contact our support line at 1-866-95-PERMIT (73764)

**Inspection Report**

Inspection Date: 5/23/2022 12:12:46 PM

**Passed**

MES Septic - CJ Morrison Should Contact Williamson County at (512-943-3330) for further information.

Case Number	Work Order Number	Inspection Number
OSSF-2022-45	16804992	12510212
Jurisdiction	Inspection Type	Inspector
Williamson County	Field Inspection	James Lancaster
Customer	Address	Phone
MES Septic - CJ Morrison	1000 CR 308, JARRELL 76537	No Number Provided
Scheduled	Completed	Uploaded
5/23/2022 12:00:00 AM	5/23/2022 12:12:46 PM	5/23/2022 12:12:46 PM

**Details**

Ok to cover and seed. Monitor port needed for final.

The information included in this report is also available at  
**MyPermitNow.org**

For more information on accessing your information through MyPermitNow.org's Free Customer Portal, visit MyPermitNow.org, or contact our support line at 1-866-95-PERMIT (73764)

**TEMPORARY STORMWATER  
SECTION (TCEQ-0602)**

# Temporary Stormwater Section

## Texas Commission on Environmental Quality

for Regulated Activities on the Edwards Aquifer Recharge Zone and Relating to 30 TAC §213.5(b)(4)(A), (B), (D)(I) and (G); Effective June 1, 1999

***To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.***

***Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.***

## Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Temporary Stormwater Section** is hereby submitted for TCEQ review and executive director approval. The application was prepared by:

Print Name of Customer/Agent: Taylor Dawson, P.E.

Date: 1 / 3 / 25

Signature of Customer/Agent:



Regulated Entity Name: JARRELL INDUSTRIAL PARK

## Project Information

### Potential Sources of Contamination

*Examples: Fuel storage and use, chemical storage and use, use of asphaltic products, construction vehicles tracking onto public roads, and existing solid waste.*

1. Fuels for construction equipment and hazardous substances which will be used during construction:

☒ The following fuels and/or hazardous substances will be stored on the site: Construction Staging Area

These fuels and/or hazardous substances will be stored in:

- ☐ Aboveground storage tanks with a cumulative storage capacity of less than 250 gallons will be stored on the site for less than one (1) year.

- ☐ Aboveground storage tanks with a cumulative storage capacity between 250 gallons and 499 gallons will be stored on the site for less than one (1) year.
- ☐ Aboveground storage tanks with a cumulative storage capacity of 500 gallons or more will be stored on the site. An Aboveground Storage Tank Facility Plan application must be submitted to the appropriate regional office of the TCEQ prior to moving the tanks onto the project.
- ☐ Fuels and hazardous substances will not be stored on the site.
- 2. ☒ **Attachment A - Spill Response Actions.** A site specific description of the measures to be taken to contain any spill of hydrocarbons or hazardous substances is attached.
- 3. ☒ Temporary aboveground storage tank systems of 250 gallons or more cumulative storage capacity must be located a minimum horizontal distance of 150 feet from any domestic, industrial, irrigation, or public water supply well, or other sensitive feature.
- 4. ☒ **Attachment B - Potential Sources of Contamination.** A description of any activities or processes which may be a potential source of contamination affecting surface water quality is attached.

### ***Sequence of Construction***

- 5. ☒ **Attachment C - Sequence of Major Activities.** A description of the sequence of major activities which will disturb soils for major portions of the site (grubbing, excavation, grading, utilities, and infrastructure installation) is attached.
  - ☒ For each activity described, an estimate (in acres) of the total area of the site to be disturbed by each activity is given.
  - ☒ For each activity described, include a description of appropriate temporary control measures and the general timing (or sequence) during the construction process that the measures will be implemented.
- 6. ☒ Name the receiving water(s) at or near the site which will be disturbed or which will receive discharges from disturbed areas of the project: Tributary to Bone Hollow Creek

### ***Temporary Best Management Practices (TBMPs)***

*Erosion control examples: tree protection, interceptor swales, level spreaders, outlet stabilization, blankets or matting, mulch, and sod. Sediment control examples: stabilized construction exit, silt fence, filter dikes, rock berms, buffer strips, sediment traps, and sediment basins. Please refer to the Technical Guidance Manual for guidelines and specifications. All structural BMPs must be shown on the site plan.*

- 7. ☒ **Attachment D – Temporary Best Management Practices and Measures.** TBMPs and measures will prevent pollution of surface water, groundwater, and stormwater. The construction-phase BMPs for erosion and sediment controls have been designed to retain sediment on site to the extent practicable. The following information is attached:

- ☒ A description of how BMPs and measures will prevent pollution of surface water, groundwater or stormwater that originates upgradient from the site and flows across the site.
  - ☒ A description of how BMPs and measures will prevent pollution of surface water or groundwater that originates on-site or flows off site, including pollution caused by contaminated stormwater runoff from the site.
  - ☒ A description of how BMPs and measures will prevent pollutants from entering surface streams, sensitive features, or the aquifer.
  - ☒ A description of how, to the maximum extent practicable, BMPs and measures will maintain flow to naturally-occurring sensitive features identified in either the geologic assessment, TCEQ inspections, or during excavation, blasting, or construction.
8. ☒ The temporary sealing of a naturally-occurring sensitive feature which accepts recharge to the Edwards Aquifer as a temporary pollution abatement measure during active construction should be avoided.
- ☐ **Attachment E - Request to Temporarily Seal a Feature.** A request to temporarily seal a feature is attached. The request includes justification as to why no reasonable and practicable alternative exists for each feature.
- ☒ There will be no temporary sealing of naturally-occurring sensitive features on the site.
9. ☒ **Attachment F - Structural Practices.** A description of the structural practices that will be used to divert flows away from exposed soils, to store flows, or to otherwise limit runoff discharge of pollutants from exposed areas of the site is attached. Placement of structural practices in floodplains has been avoided.
10. ☒ **Attachment G - Drainage Area Map.** A drainage area map supporting the following requirements is attached:
- ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin will be provided.
  - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a smaller sediment basin and/or sediment trap(s) will be used.
  - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin or other equivalent controls are not attainable, but other TBMPs and measures will be used in combination to protect down slope and side slope boundaries of the construction area.
  - ☐ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. A smaller sediment basin and/or sediment trap(s) will be used in combination with other erosion and sediment controls within each disturbed drainage area.

- ☒ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. Erosion and sediment controls other than sediment basins or sediment traps within each disturbed drainage area will be used.
11. ☐ **Attachment H - Temporary Sediment Pond(s) Plans and Calculations.** Temporary sediment pond or basin construction plans and design calculations for a proposed temporary BMP or measure have been prepared by or under the direct supervision of a Texas Licensed Professional Engineer. All construction plans and design information must be signed, sealed, and dated by the Texas Licensed Professional Engineer. Construction plans for the proposed temporary BMPs and measures are attached.
- ☒ N/A
12. ☒ **Attachment I - Inspection and Maintenance for BMPs.** A plan for the inspection of each temporary BMP(s) and measure(s) and for their timely maintenance, repairs, and, if necessary, retrofit is attached. A description of the documentation procedures, recordkeeping practices, and inspection frequency are included in the plan and are specific to the site and/or BMP.
13. ☒ All control measures must be properly selected, installed, and maintained in accordance with the manufacturer's specifications and good engineering practices. If periodic inspections by the applicant or the executive director, or other information indicate a control has been used inappropriately, or incorrectly, the applicant must replace or modify the control for site situations.
14. ☒ If sediment escapes the construction site, off-site accumulations of sediment must be removed at a frequency sufficient to minimize offsite impacts to water quality (e.g., fugitive sediment in street being washed into surface streams or sensitive features by the next rain).
15. ☐ Sediment must be removed from sediment traps or sedimentation ponds not later than when design capacity has been reduced by 50%. A permanent stake will be provided that can indicate when the sediment occupies 50% of the basin volume.
16. ☒ Litter, construction debris, and construction chemicals exposed to stormwater shall be prevented from becoming a pollutant source for stormwater discharges (e.g., screening outfalls, picked up daily).

## ***Soil Stabilization Practices***

*Examples: establishment of temporary vegetation, establishment of permanent vegetation, mulching, geotextiles, sod stabilization, vegetative buffer strips, protection of trees, or preservation of mature vegetation.*

17. ☒ **Attachment J - Schedule of Interim and Permanent Soil Stabilization Practices.** A schedule of the interim and permanent soil stabilization practices for the site is attached.

- 18. ☒ Records must be kept at the site of the dates when major grading activities occur, the dates when construction activities temporarily or permanently cease on a portion of the site, and the dates when stabilization measures are initiated.
- 19. ☒ Stabilization practices must be initiated as soon as practicable where construction activities have temporarily or permanently ceased.

### ***Administrative Information***

- 20. ☒ All structural controls will be inspected and maintained according to the submitted and approved operation and maintenance plan for the project.
- 21. ☒ If any geologic or manmade features, such as caves, faults, sinkholes, etc., are discovered, all regulated activities near the feature will be immediately suspended. The appropriate TCEQ Regional Office shall be immediately notified. Regulated activities must cease and not continue until the TCEQ has reviewed and approved the methods proposed to protect the aquifer from any adverse impacts.
- 22. ☒ Silt fences, diversion berms, and other temporary erosion and sediment controls will be constructed and maintained as appropriate to prevent pollutants from entering sensitive features discovered during construction.

**ATTACHMENT A**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment A – Spill Response Actions

In the event of an accidental leak or spill:

- Spill must be contained and cleaned up immediately.
- Spills will not be merely buried or washed with water.
- Contractor shall take action to contain spill. Contractor may use sand or other absorbent material stockpiled on site to absorb spill. Absorbent material should be spread over the spill area to absorb the spilled product.
- In the event of an uncontained discharge the contractor shall utilize onsite equipment to construct berms downgradient of the spill with sand or other absorbent material to contain and absorb the spilled product.
- Spill containment/absorbent materials along with impacted media must be collected and stored in such a way so as not to continue to affect additional media (soil/water). Once the spill has been contained, collected material should be placed on poly or plastic sheeting until removed from the site. The impacted media and cleanup materials should be covered with plastic sheeting and the edges weighed down with paving bricks or other similarly dense objects as the material is being accumulated. This will prevent the impacted media and cleanup materials from becoming airborne in windy conditions or impacting runoff during a rain event. The stockpiled materials should not be located within an area of concentrated runoff such as along a curb line or within a swale.
- Contaminated soils and cleanup materials will be sampled for waste characterization. When the analysis results are known the contaminated soils and cleanup materials will be removed from the site and disposed in a permitted landfill in accordance with applicable regulations.
- The contractor will be required to notify the owner, who will in turn contact TCEQ to notify them in the event of a significant hazardous/reportable quantity spill. Additional notifications as required by the type and amount of spill will be conducted by owner or owner's representative.

In the event of an accidental significant or hazardous spill:

The contractor will be required to report significant or hazardous spills in reportable quantities to:

- Notify the TCEQ by telephone as soon as possible and within 24 hours at 512-339-2929 (Austin) or 210-490-3096 (San Antonio) between 8 AM and 5 PM. After hours, contact the Environmental Release Hotline at 1-800-832-8224. It is the contractor's responsibility to have all emergency phone numbers at the construction site. [https://www.tceq.texas.gov/response/spills/spill\\_rq.html](https://www.tceq.texas.gov/response/spills/spill_rq.html)
- For spills of federal reportable quantities, in conformance with the requirements in 40 CFR parts 110,119, and 302, the contractor should notify the National Response Center at (800) 424-8802.

## JARRELL INDUSTRIAL PARK

### Water Pollution Abatement Plan

- Notification should first be made by telephone and followed up with a written report.
- The services of a spills contractor or a Haz-Mat team should be obtained immediately. Construction personnel should not attempt to clean up until the appropriate and qualified staffs have arrived at the job site.
- Other agencies which may need to be consulted include, but are not limited to, the City Police Department, County Sheriff Office, Fire Departments, etc.
- Contaminated soils will be sampled for waste characterization. When the analysis results are known the contaminated soils will be removed from the site and disposed in a permitted landfill in accordance with applicable regulations.

Additional guidance can be obtained from TCEQ's Technical Guidance Manual (TGM) RG-348 (2005) Section 1.4.16. Contractor shall review this section.

**ATTACHMENT B**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment B – Potential Sources of Contamination

Other potential sources of contamination during construction include:

Potential Source	Preventative Measure
Asphalt products used on this project.	<ul style="list-style-type: none"> <li>After placement of asphalt, emulsion or coatings, the contractor will be responsible for immediate cleanup should an unexpected rain occur. For the duration of the asphalt product curing time, the contractor will maintain standby personnel and equipment to contain any asphalt wash-off should an unexpected rain occur. The contractor will be instructed not to place asphalt products on the ground within 48 hours of a forecasted rain.</li> </ul>
Oil, grease, fuel, and hydraulic fluid contamination from construction equipment and vehicle dripping.	<ul style="list-style-type: none"> <li>Vehicle maintenance when possible, will be performed within the construction staging area.</li> <li>Construction vehicles and equipment shall be checked regularly for leaks and repaired immediately.</li> </ul>
Accidental leaks or spills of oil, petroleum products, and substances listed under 40 CFR parts 110, 117, and 302 used or stored temporarily on site.	<ul style="list-style-type: none"> <li>Contractor to incorporate into regular safety meetings, a discussion of spill prevention and appropriate disposal procedures.</li> <li>Contractor's superintendent or representative overseer shall enforce proper spill prevention and control measures.</li> <li>Hazardous materials and wastes shall be stored in covered containers and protected from vandalism.</li> <li>A stockpile of spill cleanup materials shall be stored on site where it will be readily accessible.</li> </ul>
Miscellaneous trash and litter from construction workers and material wrappings.	<ul style="list-style-type: none"> <li>Trash containers will be placed throughout the site to encourage proper trash disposal.</li> </ul>
Construction debris.	<ul style="list-style-type: none"> <li>Construction debris will be monitored daily by contractor. Debris will be collected weekly and placed in disposal bins. Situations requiring immediate attention will be addressed on a case-by-case basis.</li> </ul>
Spills/Overflow of waste from portable toilets	<ul style="list-style-type: none"> <li>Portable toilets will be placed away from high-traffic vehicular areas and storm drain inlets.</li> <li>Portable toilets will be placed on a level ground surface.</li> <li>Portable toilets will be inspected regularly for leaks and will be serviced and sanitized at time intervals that will maintain sanitary conditions.</li> </ul>

**ATTACHMENT C**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment C – Sequence of Major Activities

The sequence of major activities which disturb soil during construction on this site will be divided into two stages. The first is site preparation that will include installation of TBMPs, clearing and grubbing of vegetation where applicable. This will disturb no more than 6.184 acres. The second is construction that will include construction of buildings with associated parking and drives, sidewalks, OSSF, the batch detention water quality and detention basin, construction of new pavement area, landscaping and site cleanup. This will disturb approximately 6.184 acres.

#### **Submit NOI to TCEQ**

**Installation of TBMPs – 6 acres**

**Clearing, grubbing and grading – 5 ac**

**Excavation for installation of utilities – 0.97 ac**

**Construction of new buildings and parking – 2.5 ac**

**Construction of batch detention water quality and detention basin – 0.17 ac**

**Grading, landscape revegetate, and site cleanup – 5 ac**

**Removal of TBMPs – 6 ac**

**ATTACHMENT D**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment D – Temporary Best Management Practices and Measures

- a. A description of how BMPs and measures will prevent pollution of surface water, groundwater or stormwater that originates upgradient from the site and flows across the site.

***Upgradient water will be intercepted by earthen channels and routed around the site development. All TBMPs are adequate for the drainage areas they serve.***

- b. A description of how BMPs and measures will prevent pollution of surface water or groundwater that originates on-site or flows off site, including pollution caused by contaminated stormwater runoff from the site.

***Site preparation, which is the initiation of all activity on the project, will disturb the largest amount of soil. Therefore, before any of this work can begin, the clearing and grading contractor will be responsible for the installation of all on-site control measures. The methodology for pollution prevention of on-site stormwater will include: (1) erection of silt fences along the downgradient boundary of construction activities for temporary erosion and sedimentation controls, (2) installation of rock berms with silt fencing downgradient from areas of concentrated stormwater flow for temporary erosion control, (3) Installation of gravel bags and drain inlet protection at inlets and downgradient areas of construction activities for sediment control (4) installation of stabilized construction entrance/exit(s) to reduce the dispersion of sediment from the site, and (5) installation of construction staging area(s).***

***Prior to the initiation of construction, all previously installed control measures will be repaired or reestablished for their designed or intended purpose. This work, which is the remainder of all activity on the project, may also disturb additional soil. The construction contractor will be responsible for the installation of all remaining on-site control measures that includes installation of the concrete truck washout pit(s), as construction phasing warrants.***

***Temporary measures are intended to provide a method of slowing the flow of runoff from the construction site in order to allow sediment and suspended solids to settle out of the runoff. By containing the sediment and solids within the site, they will not enter surface streams and/or sensitive features.***

- c. A description of how BMPs and measures will prevent pollutants from entering surface streams, sensitive features, or the aquifer.

***Temporary measures are intended to provide a method of slowing the flow of runoff from the construction site in order to allow sediment and suspended solids to settle out of the runoff. By containing the sediment and solids within the site, they will not enter surface streams and/or sensitive features.***

## JARRELL INDUSTRIAL PARK

### Water Pollution Abatement Plan

- d. A description of how, to the maximum extent practicable, BMPs and measures will maintain flow to naturally-occurring sensitive features identified in either the geologic assessment, TCEQ inspections, or during excavation, blasting, or construction.

***BMP measures utilized in this plan are intended to allow stormwater to continue downstream after passing through the BMPs. This will allow stormwater runoff to continue downgradient to streams or features that may exist downstream of the site.***

**ATTACHMENT F**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment F – Structural Practices

The following structural measures will be installed prior to the initiation of site preparation activities:

- Erection of silt fences along the downgradient boundary of construction activities and rock berms with silt fence for secondary protection, as located on Exhibit 1 and illustrated on Exhibit 2.
- Installation of gravel bags and drain inlet protection at inlets and downgradient areas of construction activities, as located on Exhibit 1 and illustrated on Exhibit 2.
- Installation of stabilized construction entrance/exit(s) and construction staging area(s), as located on Exhibit 1 and illustrated on Exhibit 2.

The following structural measures will be installed at the initiation of construction activities or as appropriate based on the construction sequencing:

- Installation of concrete truck washout pit(s), as required and located on Exhibit 1 and illustrated on Exhibit 2.

**ATTACHMENT G**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment G – Drainage Area Map

No more than ten (10) acres will be disturbed within a common drainage area at one time as proposed construction is less than 10 acres. All TBMPs utilized are adequate for the drainage areas served.

**ATTACHMENT I**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### INSPECTIONS

Designated and qualified person(s) shall inspect Pollution Control Measures weekly and within 24 hours after a storm event. An inspection report that summarizes the scope of the inspection, names and qualifications of personnel conducting the inspection, date of the inspection, major observations, and actions taken as a result of the inspection shall be recorded and maintained as part of Storm Water TPDES data for a period of three years after the Notice of Termination (NOT) has been filed. A copy of the Inspection Report Form is provided in this Storm Water Pollution Prevention Plan.

As a minimum, the inspector shall observe: (1) significant disturbed areas for evidence of erosion, (2) storage areas for evidence of leakage from the exposed stored materials, (3) structural controls (rock berm outlets, silt fences, drainage swales, etc.) for evidence of failure or excess siltation (over 6 inches deep), (4) vehicle exit point for evidence of off-site sediment tracking, (5) vehicle storage areas for signs of leaking equipment or spills, (6) concrete truck rinse-out pit for signs of potential failure, (7) embankment, spillways, and outlet of sediment basin (where applicable) for erosion damage, and (8) sediment basins (where applicable) for evidence that basin has accumulated 50% of its volume in silt. Deficiencies noted during the inspection will be corrected and documented within seven calendar days following the inspection or before the next anticipated storm event if practicable.

Contractor shall review Sections 1.3 and 1.4 of TCEQ's Technical Guidance Manual for additional BMP inspection and maintenance requirements.

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

Pollution Prevention Measure	Inspected in Compliance	Corrective Action Required	
		Description (use additional sheet if necessary)	Date Completed
Best Management Practices			
Natural vegetation buffer strips			
Temporary vegetation			
Permanent vegetation			
Sediment control basin			
Silt fences			
Rock berms			
Gravel filter bags			
Drain inlet protection			
Other structural controls			
Vehicle exits (off-site tracking)			
Material storage areas (leakage)			
Equipment areas (leaks, spills)			
Concrete washout pit (leaks, failure)			
General site cleanliness			
Trash receptacles			
Evidence of Erosion			
Site preparation			
Roadway or parking lot construction			
Utility construction			
Drainage construction			
Building construction			
Major Observations			
Sediment discharges from site			
BMPs requiring maintenance			
BMPs requiring modification			
Additional BMPs required			

\_\_\_\_\_ A brief statement describing the qualifications of the inspector is included in this SWP3.

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

"I further certify I am an authorized signatory in accordance with the provisions of 30 TAC §305.128."

\_\_\_\_\_  
Inspector's Name

\_\_\_\_\_  
Inspector's Signature

\_\_\_\_\_  
Date

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### PROJECT MILESTONE DATES

Date when major site grading activities begin:

<u>Construction Activity</u>	<u>Date</u>
Installation of BMPs	

Dates when construction activities temporarily or permanently cease on all or a portion of the project:

<u>Construction Activity</u>	<u>Date</u>

Dates when stabilization measures are initiated:

<u>Stabilization Activity</u>	<u>Date</u>
Removal of BMPs	

**ATTACHMENT J**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment J - Schedule of Interim and Permanent Soil Stabilization Practices

Interim on-site stabilization measures, which are continuous, will include minimizing soil disturbances by exposing the smallest practical area of land required for the shortest period of time and maximizing use of natural vegetation. As soon as practical, all disturbed soil will be stabilized as per project specifications in accordance with pages 1-35 to 1-60 of TCEQ's Technical Guidance Manual (TGM) RG-348 (2005). Mulching, netting, erosion blankets and seeding are acceptable.

Stabilization measures will be initiated as soon as practicable in portions of the site where construction activities have temporarily or permanently ceased, and except as provided below, will be initiated no more than fourteen (14) days after the construction activity in that portion of the site has temporarily or permanently ceased. Where construction activity on a portion of the site is temporarily ceased, and earth disturbing activities will be resumed within twenty-one (21) days, temporary stabilization measures do not have to be initiated on that portion of site. In areas experiencing droughts where the initiation of stabilization measures by the 14<sup>th</sup> day after construction activity has temporarily or permanently ceased is precluded by seasonably arid conditions, stabilization measures must be initiated as soon as practicable.

**PERMANENT STORMWATER  
SECTION (TCEQ-0600)**

# Permanent Stormwater Section

## Texas Commission on Environmental Quality

for Regulated Activities on the Edwards Aquifer Recharge Zone and Relating to 30 TAC §213.5(b)(4)(C), (D)(li), (E), and (5), Effective June 1, 1999

***To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.***

***Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.***

## Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Permanent Stormwater Section** is hereby submitted for TCEQ review and executive director approval. The application was prepared by:

Print Name of Customer/Agent: Taylor Dawson, P.E.

Date: 1 / 3 / 25

Signature of Customer/Agent



Regulated Entity Name: JARRELL INDUSTRIAL PARK

## Permanent Best Management Practices (BMPs)

***Permanent best management practices and measures that will be used during and after construction is completed.***

1. ☒ Permanent BMPs and measures must be implemented to control the discharge of pollution from regulated activities after the completion of construction.  
☐ N/A
2. ☒ These practices and measures have been designed, and will be constructed, operated, and maintained to insure that 80% of the incremental increase in the annual mass loading of total suspended solids (TSS) from the site caused by the regulated activity is removed. These quantities have been calculated in accordance with technical guidance prepared or accepted by the executive director.  
☒ The TCEQ Technical Guidance Manual (TGM) was used to design permanent BMPs and measures for this site.

- ☐ A technical guidance other than the TCEQ TGM was used to design permanent BMPs and measures for this site. The complete citation for the technical guidance that was used is: \_\_\_\_\_
- ☐ N/A
3. ☒ Owners must insure that permanent BMPs and measures are constructed and function as designed. A Texas Licensed Professional Engineer must certify in writing that the permanent BMPs or measures were constructed as designed. The certification letter must be submitted to the appropriate regional office within 30 days of site completion.
- ☐ N/A
4. Where a site is used for low density single-family residential development and has 20 % or less impervious cover, other permanent BMPs are not required. This exemption from permanent BMPs must be recorded in the county deed records, with a notice that if the percent impervious cover increases above 20% or land use changes, the exemption for the whole site as described in the property boundaries required by 30 TAC §213.4(g) (relating to Application Processing and Approval), may no longer apply and the property owner must notify the appropriate regional office of these changes.
- ☐ The site will be used for low density single-family residential development and has 20% or less impervious cover.
- ☐ The site will be used for low density single-family residential development but has more than 20% impervious cover.
- ☒ The site will not be used for low density single-family residential development.
5. The executive director may waive the requirement for other permanent BMPs for multi-family residential developments, schools, or small business sites where 20% or less impervious cover is used at the site. This exemption from permanent BMPs must be recorded in the county deed records, with a notice that if the percent impervious cover increases above 20% or land use changes, the exemption for the whole site as described in the property boundaries required by 30 TAC §213.4(g) (relating to Application Processing and Approval), may no longer apply and the property owner must notify the appropriate regional office of these changes.
- ☐ **Attachment A - 20% or Less Impervious Cover Waiver.** The site will be used for multi-family residential developments, schools, or small business sites and has 20% or less impervious cover. A request to waive the requirements for other permanent BMPs and measures is attached.
- ☐ The site will be used for multi-family residential developments, schools, or small business sites but has more than 20% impervious cover.
- ☒ The site will not be used for multi-family residential developments, schools, or small business sites.
6. ☒ **Attachment B - BMPs for Upgradient Stormwater.**

- ☐ A description of the BMPs and measures that will be used to prevent pollution of surface water, groundwater, or stormwater that originates upgradient from the site and flows across the site is attached.
- ☒ No surface water, groundwater or stormwater originates upgradient from the site and flows across the site, and an explanation is attached.
- ☐ Permanent BMPs or measures are not required to prevent pollution of surface water, groundwater, or stormwater that originates upgradient from the site and flows across the site, and an explanation is attached.
7. ☒ **Attachment C - BMPs for On-site Stormwater.**
- ☒ A description of the BMPs and measures that will be used to prevent pollution of surface water or groundwater that originates on-site or flows off the site, including pollution caused by contaminated stormwater runoff from the site is attached.
- ☐ Permanent BMPs or measures are not required to prevent pollution of surface water or groundwater that originates on-site or flows off the site, including pollution caused by contaminated stormwater runoff, and an explanation is attached.
8. ☒ **Attachment D - BMPs for Surface Streams.** A description of the BMPs and measures that prevent pollutants from entering surface streams, sensitive features, or the aquifer is attached. Each feature identified in the Geologic Assessment as sensitive has been addressed.
- ☐ N/A
9. ☒ The applicant understands that to the extent practicable, BMPs and measures must maintain flow to naturally occurring sensitive features identified in either the geologic assessment, executive director review, or during excavation, blasting, or construction.
- ☒ The permanent sealing of or diversion of flow from a naturally-occurring sensitive feature that accepts recharge to the Edwards Aquifer as a permanent pollution abatement measure has not been proposed.
- ☐ **Attachment E - Request to Seal Features.** A request to seal a naturally-occurring sensitive feature, that includes, for each feature, a justification as to why no reasonable and practicable alternative exists, is attached.
10. ☒ **Attachment F - Construction Plans.** All construction plans and design calculations for the proposed permanent BMP(s) and measures have been prepared by or under the direct supervision of a Texas Licensed Professional Engineer, and are signed, sealed, and dated. The plans are attached and, if applicable include:
- ☒ Design calculations (TSS removal calculations)
- ☒ TCEQ construction notes
- ☒ All geologic features
- ☒ All proposed structural BMP(s) plans and specifications
- ☐ N/A

11. ☒ **Attachment G - Inspection, Maintenance, Repair and Retrofit Plan.** A plan for the inspection, maintenance, repairs, and, if necessary, retrofit of the permanent BMPs and measures is attached. The plan includes all of the following:
- ☒ Prepared and certified by the engineer designing the permanent BMPs and measures
  - ☒ Signed by the owner or responsible party
  - ☒ Procedures for documenting inspections, maintenance, repairs, and, if necessary retrofit
  - ☒ A discussion of record keeping procedures
- ☐ N/A
12. ☐ **Attachment H - Pilot-Scale Field Testing Plan.** Pilot studies for BMPs that are not recognized by the Executive Director require prior approval from the TCEQ. A plan for pilot-scale field testing is attached.
- ☒ N/A
13. ☒ **Attachment I - Measures for Minimizing Surface Stream Contamination.** A description of the measures that will be used to avoid or minimize surface stream contamination and changes in the way in which water enters a stream as a result of the construction and development is attached. The measures address increased stream flashing, the creation of stronger flows and in-stream velocities, and other in-stream effects caused by the regulated activity, which increase erosion that results in water quality degradation.
- ☐ N/A

### ***Responsibility for Maintenance of Permanent BMP(s)***

***Responsibility for maintenance of best management practices and measures after construction is complete.***

14. ☒ The applicant is responsible for maintaining the permanent BMPs after construction until such time as the maintenance obligation is either assumed in writing by another entity having ownership or control of the property (such as without limitation, an owner's association, a new property owner or lessee, a district, or municipality) or the ownership of the property is transferred to the entity. Such entity shall then be responsible for maintenance until another entity assumes such obligations in writing or ownership is transferred.
- ☐ N/A
15. ☒ A copy of the transfer of responsibility must be filed with the executive director at the appropriate regional office within 30 days of the transfer if the site is for use as a multiple single-family residential development, a multi-family residential development, or a non-residential development such as commercial, industrial, institutional, schools, and other sites where regulated activities occur.
- ☐ N/A

**ATTACHMENT B**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment B – BMPs for Upgradient Stormwater

Upgradient stormwater will be intercepted by earthen channels and routed around the site.

The proposed Permanent Best Management Practices (PBMPs) for stormwater treatment is one (1) batch detention basin which is designed in accordance with the TCEQ's Technical Guidance Manual (TGM) RG-348 (2005) to remove 80% of the increase in Total Suspended Solids (TSS) from the site.

**ATTACHMENT C**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment C – BMPs for On-Site Stormwater

The proposed Permanent Best Management Practices (PBMPs) for stormwater treatment is one (1) batch detention basin which is designed in accordance with the TCEQ's Technical Guidance Manual (TGM) RG-348 (2005) to remove 80% of the increase in Total Suspended Solids (TSS) from the site.

**ATTACHMENT D**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment D – BMPs for Surface Streams

The proposed Permanent Best Management Practices (PBMPs) for stormwater treatment is one (1) batch detention basin which is designed in accordance with the TCEQ's Technical Guidance Manual (TGM) RG-348 (2005) to remove 80% of the increase in Total Suspended Solids (TSS) from the site.

**ATTACHMENT F**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment F – Construction Plans

Please refer to the Exhibits Section of this application for the Water Pollution Abatement Site Plans.

**ATTACHMENT G**

## JARRELL INDUSTRIAL PARK Water Pollution Abatement Plan

### PERMANENT POLLUTION ABATEMENT MEASURES MAINTENANCE SCHEDULE AND MAINTENANCE PROCEDURES

This document has been prepared to provide a description and schedule for the performance of maintenance on permanent pollution abatement measures. Maintenance measures to be performed will be dependent on what permanent pollution abatement measures are incorporated into the project. The project specific water pollution abatement plan should be reviewed to determine what permanent pollution abatement measures are incorporated into a project.

It should also be noted that the timing and procedures presented herein are general guidelines, adjustment to the timing and procedures may have to be made depending on project specific characteristics as well as weather related conditions but may not be altered without TCEQ approval.

Where a project is occupied by the owner, the owner may provide for maintenance with his own skilled forces or contract for recommended maintenance of Permanent Best Management Practices. Where a project is occupied or leased by a tenant, the owner shall require tenants to contract for such maintenance services either through a lease agreement, property owners association covenants, or other binding document.

I understand that I am responsible for maintenance of the Permanent Pollution Abatement Measures included in this project until such time as the maintenance obligation is either assumed in writing by another entity having ownership or control of the property or ownership is transferred.

I, the owner, have read and understand the requirements of the attached Maintenance Plan and Schedule.

  
\_\_\_\_\_  
Barry Cryer, Managing Member  
Jarrell Industrial Park LLC

  
\_\_\_\_\_  
Date

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### INSPECTION AND MAINTENANCE SCHEDULE FOR PERMANENT POLLUTION ABATEMENT MEASURES

Recommended Frequency	Task to be Performed												
	1	2	3	4	5	6	7	8	9	10	11	12	13
After Rainfall	√							√			√		√
Biannually*	√	√	√	√	√	√	√	√	√	√	√	√	√

***\*At least one biannual inspection must occur during or immediately after a rainfall event.***

***√Indicates maintenance procedure that applies to this specific site.***

See description of maintenance task to be performed on the following pages. Frequency of maintenance tasks may vary depending on amount of rainfall and other weather-related conditions but may not be altered without TCEQ approval.

*A written record should be kept of inspection results and maintenance performed.*

<b><i>Task No. &amp; Description</i></b>	<b><i>Included in this project</i></b>	
1. Mowing	Yes	No
2. Litter and Debris Removal	Yes	No
3. Erosion Control	Yes	No
4. Level Sensor	Yes	No
5. Nuisance Control	Yes	No
6. Structural Repairs and Replacement	Yes	No
7. Discharge Pipe	Yes	No
8. Detention and Drawdown Time	Yes	No
9. Sediment Removal	Yes	No
10. Logic Controller	Yes	No
11. Vegetated Filter Strips	Yes	No
12. Visually Inspect Security Fencing for Damage or Breach	Yes	No
13. Recordkeeping for Inspections, Maintenance, and Repairs	Yes	No

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### MAINTENANCE PROCEDURES FOR PERMANENT POLLUTION ABATEMENT MEASURES

**Note: Additional guidance can be obtained from TCEQ's Technical Guidance Manual (TGM) RG-348 (2005) Section 3.5.**

Inspections. Inspections should take place a minimum of twice a year. One inspection should take place during wet weather to determine if the basin is meeting the target detention time of 12 hours and a drawdown time of no more than 48 hours. The remaining inspections should occur between storm events so that manual operation of the valve and controller can be verified. The level sensor in the basin should be inspected and any debris or sediment in the area should be removed. The outlet structure and the trash screen should be inspected for signs of clogging. Debris and sediment should be removed from the orifice and outlet(s) as described in previous sections. Debris obstructing the valve should be removed. During each inspection, erosion areas inside and downstream of this BMP should be identified and repaired/revegetated immediately. *A written record should be kept of inspection results and corrective measures taken*

1. Mowing. The basin, basin side-slopes, and embankment of the basin must be mowed to prevent woody growth and control weeds. A mulching mower should be used, or the grass clippings should be caught and removed. Mowing should take place at least twice a year, or more frequently if vegetation exceeds 18 inches in height. More frequent mowing to maintain aesthetic appeal may be necessary in landscaped areas.
2. Litter and Debris Removal. Litter and debris removal should take place at least twice a year, as part of the periodic mowing operations and inspections. Debris and litter should be removed from the surface of the basin. Particular attention should be paid to floatable debris around the outlet structure. The outlet should be checked for possible clogging or obstructions and any debris removed.
3. Erosion control. The basin side slopes and embankment all may periodically suffer from slumping and erosion. To correct these problems, corrective action, such as regrading and revegetation, may be necessary. Correction of erosion control should take place whenever required based on the periodic inspections.
4. Level Sensor. The level sensor in the basin should be inspected and any debris or sediment in the area should be removed. Litter and debris removal should take place at least twice a year, as part of the periodic mowing operations and inspections. Debris and litter should be removed from the surface of the basin.
5. Nuisance Control. Standing water or soggy conditions may occur in the basin. Some standing water may occur after a storm event since the valve may close with 2 to 3 inches of water in the basin. Some flow into the basin may also occur between storms due to spring flow and residential water use that enters the storm sewer system. Twice a year, the facility should be evaluated in terms of nuisance control (insects, weeds, odors, algae, etc.).
6. Structural Repairs and Replacement. With each inspection, any damage to structural elements of the basin (pipes, concrete drainage structures, retaining walls, etc.) should be identified and

## JARRELL INDUSTRIAL PARK

### Water Pollution Abatement Plan

repaired immediately. An example of this type of repair can include patching of cracked concrete, sealing of voids, removal of vegetation from cracks and joints. The various inlet/outlet structures in a basin will eventually deteriorate and must be replaced. *A written record should be kept of inspection results and corrective measures taken*

7. Discharge Pipe. The basin discharge pipe shall be checked for accumulation of silt, debris or other obstructions which could block flow. Soil accumulations, vegetative overgrowth and other blockages should be cleared from the pipe discharge point. Erosion at the point of discharge shall be monitored. If erosion occurs, the addition of rock rubble to disperse the flow should be accomplished. *A written record should be kept of inspection results and corrective measures taken*
8. Detention and Drawdown Time. One inspection should take place during wet weather to determine if the basin is meeting the target detention time of 12 hours and a drawdown time of no more than 48 hours. This characteristic can be a sign of the need for maintenance. The minimum drawdown time is 24 hours. If drawdown time is less than 24 hours, the actuator valve shall be checked and partially closed to limit the drawdown time. Extensive drawdown time greater than 48 hours may indicate blockage of the discharge pipe. Corrective actions should be performed and completed within 15 working days. *A written record of the inspection findings and corrective actions performed should be made.*
9. Sediment Removal. A properly designed batch detention basin will accumulate quantities of sediment over time. The accumulated sediment can detract from the appearance of the facility and reduce the pollutant removal performance of the facility. The sediment also tends to accumulate near the outlet structure and can interfere with the level sensor operation. Sediment shall be removed from the basin at least every 5 years, when sediment depth exceeds 6 inches, when the sediment interferes with the level sensor or when the basin does not drain within 48 hours. Care should be taken not to compromise the basin lining during maintenance.
10. Logic Controller. The Logic Controller should be inspected as part of the twice-yearly investigations. Verify that the external indicators (active, cycle in progress) are operating properly by turning the controller off and on, and by initiating a cycle by triggering the level sensor in the basin. The valve should be manually opened and closed using the open/close switch to verify valve operation and to assist in inspecting the valve for debris. The solar panel should be inspected and any dust or debris on the panel should be carefully removed. The controller and all other circuitry and wiring should be inspected for signs of corrosion, damage from insects, water leaks, or other damage. At the end of the inspection, the controller should be reset.
11. Vegetated Filter Strips. Vegetation height for native grasses shall be limited to no more than 18-inches. When vegetation exceeds that height, the filter strip shall be cut to a height of approximately 4 inches. Turf grass shall be limited to a height of 4-inches with regular maintenance that utilizes a mulching mower. Trash and debris shall be removed from filter strip prior to cutting. Check filter strip for signs of concentrated flow and erosion. Areas of filter strip showing signs of erosion shall be repaired by scarifying the eroded area, reshaping, regrading,

## JARRELL INDUSTRIAL PARK

### Water Pollution Abatement Plan

and placement of solid block sod over the affected area. *A written record of the inspection findings and corrective actions performed should be made*

12. Visually Inspect Security Fencing for Damage or Breach. Check maintenance access gates for proper operation. Damage to fencing or gates shall be repaired within 5 working days. *A written record should be kept of inspection results and maintenance performed.*
13. Recordkeeping Procedures for Inspections, Maintenance, Repairs, and Retrofits.
  - Written records shall be kept by the party responsible for maintenance or a designated representative.
  - Written records shall be retained for a minimum of five years.

**ATTACHMENT I**

# JARRELL INDUSTRIAL PARK

## Water Pollution Abatement Plan

### Attachment I – Measures for Minimizing Surface Stream Contamination

Any points where discharge from the site is concentrated and erosive velocities exist will include appropriately sized energy dissipators to reduce velocities to non-erosive levels.

**AGENT AUTHORIZATION FORM**  
**(TCEQ-0599)**

**Agent Authorization Form**  
For Required Signature  
Edwards Aquifer Protection Program  
Relating to 30 TAC Chapter 213  
Effective June 1, 1999

I Barry Cryer,  
Print Name

Managing Member,  
Title - Owner/President/Other

of JARRELL INDUSTRIAL PARK, LLC,  
Corporation/Partnership/Entity Name

have authorized Pape-Dawson Consulting Engineers, LLC  
Print Name of Agent/Engineer

of Pape-Dawson Consulting Engineers, LLC.  
Print Name of Firm

to represent and act on the behalf of the above named Corporation, Partnership, or Entity for the purpose of preparing and submitting this plan application to the Texas Commission on Environmental Quality (TCEQ) for the review and approval consideration of regulated activities.

I also understand that:

1. The applicant is responsible for compliance with 30 Texas Administrative Code Chapter 213 and any condition of the TCEQ's approval letter. The TCEQ is authorized to assess administrative penalties of up to \$10,000 per day per violation.
2. For those submitting an application who are not the property owner, but who have the right to control and possess the property, additional authorization is required from the owner.
3. Application fees are due and payable at the time the application is submitted. The application fee must be sent to the TCEQ cashier or to the appropriate regional office. The application will not be considered until the correct fee is received by the commission.
4. A notarized copy of the Agent Authorization Form must be provided for the person preparing the application, and this form must accompany the completed application.
5. No person shall commence any regulated activity on the Edwards Aquifer Recharge Zone, Contributing Zone or Transition Zone until the appropriate application for the activity has been filed with and approved by the Executive Director.

SIGNATURE PAGE:

Applicant's Signature

Barry E  
12/23/2024 Date

THE STATE OF Texas §


County of Williamson §

BEFORE ME, the undersigned authority, on this day personally appeared Barry E Cryer known to me to be the person whose name is subscribed to the foregoing instrument, and acknowledged to me that (s)he executed same for the purpose and consideration therein expressed.

GIVEN under my hand and seal of office on this 23 day of Dec, 2024.

Sylvia Velez  
NOTARY PUBLIC  
Sylvia Velez  
Typed or Printed Name of Notary

MY COMMISSION EXPIRES: June 8, 2028



**APPLICATION FEE FORM**  
**(TCEQ-0574)**

# Application Fee Form

## Texas Commission on Environmental Quality

Name of Proposed Regulated Entity: JARRELL INDUSTRIAL PARK

Regulated Entity Location: 1000 CR308, Jarrell, TX 76537

Name of Customer: JARRELL INDUSTRIAL PARK, LLC

Contact Person: Barry Cryer

Phone: 512-971-2833

Customer Reference Number (if issued):CN 605899806

Regulated Entity Reference Number (if issued):RN 111277596

### Austin Regional Office (3373)

☐ Hays

☒ Williamson

☐ Travis

### San Antonio Regional Office (3362)

☐ Bexar

☐ Medina

☐ Uvalde

☐ Comal

☐ Kinney

Application fees must be paid by check, certified check, or money order, payable to the **Texas Commission on Environmental Quality**. Your canceled check will serve as your receipt. **This form must be submitted with your fee payment.** This payment is being submitted to:

☐ Austin Regional Office

☐ San Antonio Regional Office

☐ Mailed to: TCEQ - Cashier

Revenues Section

Mail Code 214

P.O. Box 13088

Austin, TX 78711-3088

☒ Overnight Delivery to: TCEQ - Cashier

12100 Park 35 Circle

Building A, 3rd Floor

Austin, TX 78753

(512)239-0357

### Site Location (Check All That Apply):

☒ Recharge Zone

☐ Contributing Zone

☐ Transition Zone

<i>Type of Plan</i>	<i>Size</i>	<i>Fee Due</i>
Water Pollution Abatement Plan, Contributing Zone Plan: One Single Family Residential Dwelling	Acres	\$
Water Pollution Abatement Plan, Contributing Zone Plan: Multiple Single Family Residential and Parks	Acres	\$
Water Pollution Abatement Plan, Contributing Zone Plan: Non-residential	10.78 legal limit Acres	\$ 6,500
Sewage Collection System	L.F.	\$
Lift Stations without sewer lines	Acres	\$
Underground or Aboveground Storage Tank Facility	Tanks	\$
Piping System(s)(only)	Each	\$
Exception	Each	\$

<i>Type of Plan</i>	<i>Size</i>	<i>Fee Due</i>
Extension of Time	Each	\$

Signature: 

Date: 1 / 3 / 25

## Application Fee Schedule

Texas Commission on Environmental Quality

Edwards Aquifer Protection Program 30 TAC Chapter 213 (effective 05/01/2008)

### **Water Pollution Abatement Plans and Modifications**

#### **Contributing Zone Plans and Modifications**

<i>Project</i>	<i>Project Area in Acres</i>	<i>Fee</i>
One Single Family Residential Dwelling	< 5	\$650
Multiple Single Family Residential and Parks	< 5	\$1,500
	5 < 10	\$3,000
	10 < 40	\$4,000
	40 < 100	\$6,500
	100 < 500	\$8,000
	≥ 500	\$10,000
Non-residential (Commercial, industrial, institutional, multi-family residential, schools, and other sites where regulated activities will occur)	< 1	\$3,000
	1 < 5	\$4,000
	5 < 10	\$5,000
	10 < 40	\$6,500
	40 < 100	\$8,000
	≥ 100	\$10,000

#### **Organized Sewage Collection Systems and Modifications**

<i>Project</i>	<i>Cost per Linear Foot</i>	<i>Minimum Fee- Maximum Fee</i>
Sewage Collection Systems	\$0.50	\$650 - \$6,500

#### **Underground and Aboveground Storage Tank System Facility Plans and Modifications**

<i>Project</i>	<i>Cost per Tank or Piping System</i>	<i>Minimum Fee- Maximum Fee</i>
Underground and Aboveground Storage Tank Facility	\$650	\$650 - \$6,500

#### **Exception Requests**

<i>Project</i>	<i>Fee</i>
Exception Request	\$500

***Extension of Time Requests***

<b><i>Project</i></b>	<b><i>Fee</i></b>
Extension of Time Request	\$150

**CORE DATA FORM**  
**(TCEQ-10400)**



TCEQ Use Only

# TCEQ Core Data Form

For detailed instructions regarding completion of this form, please read the Core Data Form Instructions or call 512-239-5175.

## SECTION I: General Information

<b>1. Reason for Submission</b> (If other is checked please describe in space provided.)		
<input checked="" type="checkbox"/> New Permit, Registration or Authorization (Core Data Form should be submitted with the program application.)		
<input type="checkbox"/> Renewal (Core Data Form should be submitted with the renewal form)	<input type="checkbox"/> Other	
<b>2. Customer Reference Number (if issued)</b>	<a href="#">Follow this link to search for CN or RN numbers in Central Registry**</a>	<b>3. Regulated Entity Reference Number (if issued)</b>
CN 605899806		RN 111277596

## SECTION II: Customer Information

<b>4. General Customer Information</b>		<b>5. Effective Date for Customer Information Updates</b> (mm/dd/yyyy)	
<input type="checkbox"/> New Customer		<input type="checkbox"/> Update to Customer Information	
<input type="checkbox"/> Change in Legal Name (Verifiable with the Texas Secretary of State or Texas Comptroller of Public Accounts)		<input type="checkbox"/> Change in Regulated Entity Ownership	
<b>The Customer Name submitted here may be updated automatically based on what is current and active with the Texas Secretary of State (SOS) or Texas Comptroller of Public Accounts (CPA).</b>			
<b>6. Customer Legal Name</b> (If an individual, print last name first: eg: Doe, John)		If new Customer, enter previous Customer below:	
JARRELL INDUSTRIAL PARK, LLC			
<b>7. TX SOS/CPA Filing Number</b>	<b>8. TX State Tax ID</b> (11 digits)	<b>9. Federal Tax ID</b> (9 digits)	<b>10. DUNS Number</b> (if applicable)
<b>11. Type of Customer:</b>	<input type="checkbox"/> Corporation	<input type="checkbox"/> Individual	Partnership: <input type="checkbox"/> General <input type="checkbox"/> Limited
Government: <input type="checkbox"/> City <input type="checkbox"/> County <input type="checkbox"/> Federal <input type="checkbox"/> State <input type="checkbox"/> Other	<input type="checkbox"/> Sole Proprietorship	<input type="checkbox"/> Other:	
<b>12. Number of Employees</b>		<b>13. Independently Owned and Operated?</b>	
<input type="checkbox"/> 0-20 <input type="checkbox"/> 21-100 <input type="checkbox"/> 101-250 <input type="checkbox"/> 251-500 <input type="checkbox"/> 501 and higher		<input type="checkbox"/> Yes <input type="checkbox"/> No	
<b>14. Customer Role</b> (Proposed or Actual) – as it relates to the Regulated Entity listed on this form. Please check one of the following			
<input type="checkbox"/> Owner <input type="checkbox"/> Operator <input type="checkbox"/> Owner & Operator			
<input type="checkbox"/> Occupational Licensee <input type="checkbox"/> Responsible Party <input type="checkbox"/> Voluntary Cleanup Applicant <input type="checkbox"/> Other:			
<b>15. Mailing Address:</b>			
	City	State	ZIP
<b>16. Country Mailing Information</b> (if outside USA)		<b>17. E-Mail Address</b> (if applicable)	
		jarrellbusinesspark@gmail.com	
<b>18. Telephone Number</b>	<b>19. Extension or Code</b>	<b>20. Fax Number</b> (if applicable)	
( ) -		( ) -	

## SECTION III: Regulated Entity Information

<b>21. General Regulated Entity Information</b> (If 'New Regulated Entity' is selected below this form should be accompanied by a permit application)	
<input type="checkbox"/> New Regulated Entity <input type="checkbox"/> Update to Regulated Entity Name <input type="checkbox"/> Update to Regulated Entity Information	
<b>The Regulated Entity Name submitted may be updated in order to meet TCEQ Agency Data Standards (removal of organizational endings such as Inc, LP, or LLC).</b>	
<b>22. Regulated Entity Name</b> (Enter name of the site where the regulated action is taking place.)	
JARRELL INDUSTRIAL PARK	

23. Street Address of the Regulated Entity: (No PO Boxes)	1000 CR308						
	City	Jarrell	State	TX	ZIP	76537	ZIP + 4
24. County	Williamson						

**Enter Physical Location Description if no street address is provided.**

25. Description to Physical Location:							
26. Nearest City					State	Nearest ZIP Code	
27. Latitude (N) In Decimal:	30.8548246			28. Longitude (W) In Decimal:	-97.615047		
Degrees	Minutes	Seconds	Degrees	Minutes	Seconds		
30	51	17.37	97	36	54.17		
29. Primary SIC Code (4 digits)	30. Secondary SIC Code (4 digits)		31. Primary NAICS Code (5 or 6 digits)		32. Secondary NAICS Code (5 or 6 digits)		
6512			531120				
33. What is the Primary Business of this entity? (Do not repeat the SIC or NAICS description.)							
light industrial							
34. Mailing Address:	7500 Chevy Chase Dr						
	City	Austin	State	TX	ZIP	78752	ZIP + 4
35. E-Mail Address:	jarrellbusinesspark@gmail.com						
36. Telephone Number	37. Extension or Code		38. Fax Number (if applicable)				
( 512 ) 971-2833			( ) -				

**39. TCEQ Programs and ID Numbers** Check all Programs and write in the permits/registration numbers that will be affected by the updates submitted on this form. See the Core Data Form instructions for additional guidance.


<input type="checkbox"/> Dam Safety	<input type="checkbox"/> Districts	<input checked="" type="checkbox"/> Edwards Aquifer	<input type="checkbox"/> Emissions Inventory Air	<input type="checkbox"/> Industrial Hazardous Waste
<input type="checkbox"/> Municipal Solid Waste	<input type="checkbox"/> New Source Review Air	<input type="checkbox"/> OSSF	<input type="checkbox"/> Petroleum Storage Tank	<input type="checkbox"/> PWS
<input type="checkbox"/> Sludge	<input type="checkbox"/> Storm Water	<input type="checkbox"/> Title V Air	<input type="checkbox"/> Tires	<input type="checkbox"/> Used Oil
<input type="checkbox"/> Voluntary Cleanup	<input type="checkbox"/> Waste Water	<input type="checkbox"/> Wastewater Agriculture	<input type="checkbox"/> Water Rights	<input type="checkbox"/> Other:

#### **SECTION IV: Preparer Information**

40. Name:	Jean Autrey, P.E, CESSWI	41. Title:	Program Manager
42. Telephone Number	43. Ext./Code	44. Fax Number	45. E-Mail Address
( 210 ) 375-9000		( ) -	jautrey@pape-dawson.com

#### **SECTION V: Authorized Signature**

**46.** By my signature below, I certify, to the best of my knowledge, that the information provided in this form is true and complete, and that I have signature authority to submit this form on behalf of the entity specified in Section II, Field 6 and/or as required for the updates to the ID numbers identified in field 39.

Company:	Pape-Dawson Consulting Engineers, LLC	Job Title:	Senior Vice President
Name (In Print):	Taylor Dawson, P.E.	Phone:	( 210 ) 375- 9000
Signature:		Date:	1 / 3 / 25

# **POLLUTANT LOAD AND REMOVAL CALCULATIONS**

# Texas Commission on Environmental Quality

## TSS Removal Calculations 04-20-2009

Project Name: **Jarrell Industri**

Date Prepared: **12/26/2024**

Additional information is provided for cells with a red triangle in the upper right corner. Place the cursor over the cell. Text shown in blue indicate location of instructions in the Technical Guidance Manual - RG-348.

Characters shown in red are data entry fields.

Characters shown in black (Bold) are calculated fields. Changes to these fields will remove the equations used in the

### 1. The Required Load Reduction for the total project:

Calculations from RG-348

Pages 3-27 to 3-3

Page 3-29 Equation 3.3:  $L_M = 27.2(A_N \times P)$

where:

$L_{M \text{ TOTAL PROJECT}}$  = Required TSS removal resulting from the proposed development = 80

$A_N$  = Net increase in impervious area for the project

P = Average annual precipitation, inches

Site Data: Determine Required Load Removal Based on the Entire Project

County = **Williamson**

Total project area included in plan \* = **10.78** acres

Predevelopment impervious area within the limits of the plan \* = **0.00** acres

Total post-development impervious area within the limits of the plan \* = **2.89** acres

Total post-development impervious cover fraction \* = **0.27**

P = **32** inches


$L_{M \text{ TOTAL PROJECT}}$  = **2515** lbs.

\* The values entered in these fields should be for the total project area.

Number of drainage basins / outfalls areas leaving the plan area = **1**

### 2. Drainage Basin Parameters (This information should be provided for each basin):

Drainage Basin/Outfall Area No. = **Basin**



Total drainage basin/outfall area =	<b>4.90</b>	acres
Predevelopment impervious area within drainage basin/outfall area =	<b>0.00</b>	acres
Post-development impervious area within drainage basin/outfall area =	<b>2.86</b>	acres
Post-development impervious fraction within drainage basin/outfall area =	<b>0.58</b>	
$L_{M \text{ THIS BASIN}}$ =	<b>2489</b>	lbs.

**3. Indicate the proposed BMP Code for this basin.**

Proposed BMP = **Extended Detention**  
Removal efficiency = **91** percent

**4. Calculate Maximum TSS Load Removed ( $L_R$ ) for this Drainage Basin by the selected BMP Type.**

RG-348 Page 3-33 Equation 3.7:  $L_R = (\text{BMP efficiency}) \times P \times (A_I \times 34.6 + A_P \times 0.54)$

where:

$A_C$  = Total On-Site drainage area in the BMP catchment area  
 $A_I$  = Impervious area proposed in the BMP catchment area  
 $A_P$  = Pervious area remaining in the BMP catchment area  
 $L_R$  = TSS Load removed from this catchment area by the proposed BMP

$A_C$ =	<b>4.90</b>	acres
$A_I$ =	<b>2.86</b>	acres
$A_P$ =	<b>2.04</b>	acres
$L_R$ =	<b>2914</b>	lbs

**5. Calculate Fraction of Annual Runoff to Treat the drainage basin / outfall area**

Desired $L_{M \text{ THIS BASIN}}$ =	<b>2515</b>	lbs.
F =	<b>0.86</b>	

**6. Calculate Capture Volume required by the BMP Type for this drainage basin / outfall area.**

Calculations from RG-348

Rainfall Depth =	<b>1.38</b>	inches
Post Development Runoff Coefficient =	<b>0.41</b>	
On-site Water Quality Volume =	<b>10034</b>	cubic feet

Calculations from RG-348 Pages 3-36 to 3-37

Off-site area draining to BMP = 0.00 acres  
Off-site Impervious cover draining to BMP = 0.00 acres  
Impervious fraction of off-site area = 0  
Off-site Runoff Coefficient = 0.00  
Off-site Water Quality Volume = 0 cubic feet

Storage for Sediment = 2007

Total Capture Volume (required water quality volume(s) x 1.20) = 12041 cubic feet

The following sections are used to calculate the required water quality volume(s) for the selected BMP.  
The values for BMP Types not selected in cell C45 will show NA.

#### 7. Retention/Irrigation System

Designed as Required in RG-348

Pages 3-42 to 3-4

Required Water Quality Volume for retention basin = NA cubic feet

Irrigation Area Calculations:

Soil infiltration/permeability rate = 0.1 in/hr Enter determined permeability rate or  
Irrigation area = NA square feet  
NA acres


#### 8. Extended Detention Basin System

Designed as Required in RG-348

Pages 3-46 to 3-5


Required Water Quality Volume for extended detention basin = 12041 cubic feet

# EXHIBITS

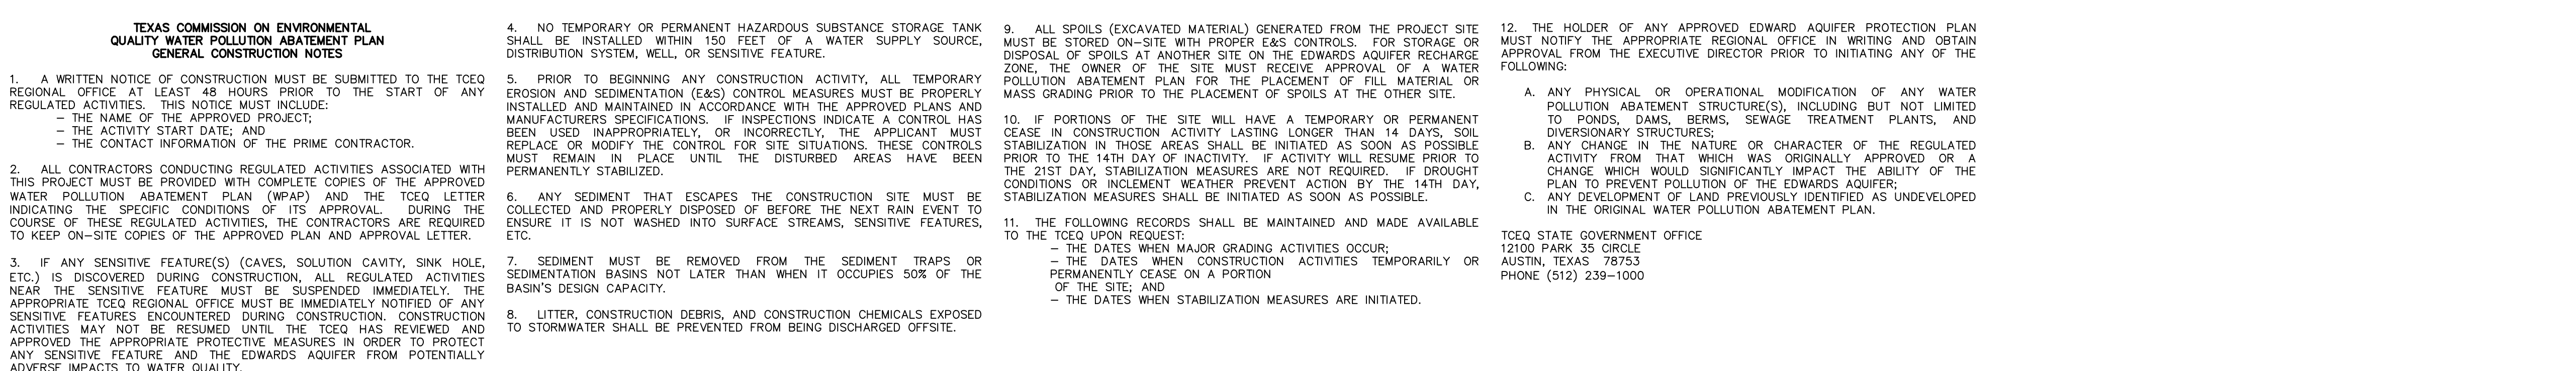

DATE	SIGNATURE	DESCRIPTION

DOCUMENT HAS BEEN PRODUCED FROM MATERIAL THAT WAS STORED AND/OR TRANSMITTED ELECTRONICALLY AND MAY HAVE BEEN INADVERTENTLY ALTERED. RELY ONLY ON FINAL HARDCOPY MATERIALS BEARING THE CONSULTANT'S ORIGINAL SIGNATURE AND SEAL.

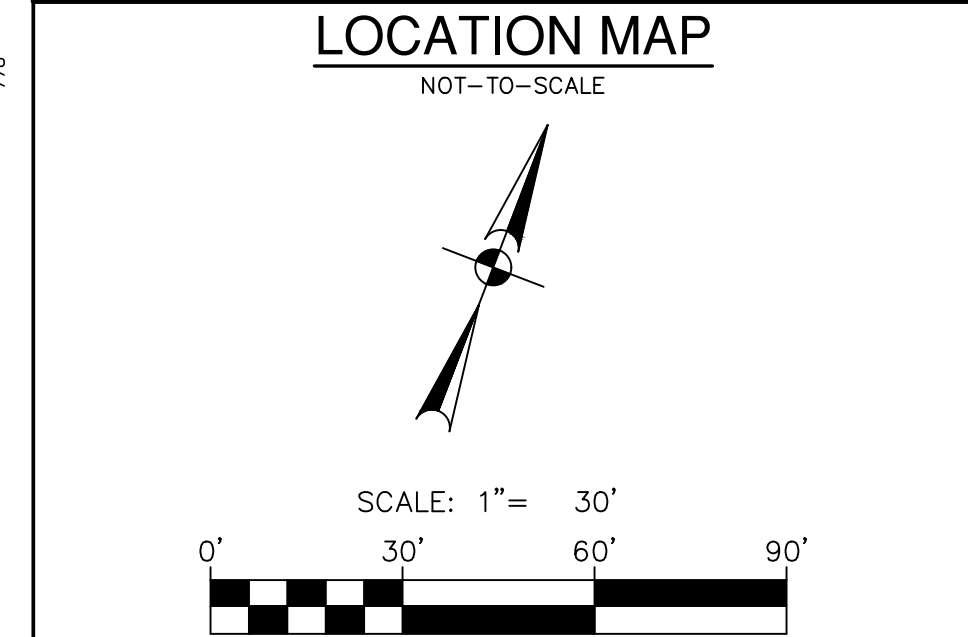

PROJECT LIMITS

DRAINAGE AREA BOUNDARY

EXISTING CONTOURS MAJOR

EXISTING CONTOURS MINOR

PROPOSED CONTOURS

FLOW ARROW (EXISTING)

FLOW ARROW (PROPOSED)

SILT FENCE

PROPOSED STORM DRAINAGE

WITH GRATE

JUNCTION BOX

CURB INLET

ROCK BERM

GRAVEL FILTER BAGS

STABILIZED CONSTRUCTION ENTRANCE/EXIT (FIELD LOCATE)

CONSTRUCTION EQUIPMENT, VEHICLE MATERIALS STORAGE AREA (FIELD LOCATE)

CONCRETE TRUCK WASH-OUT PIT (FIELD LOCATE)

1. DO NOT DISTURB VEGETATED AREAS (TREES, GRASS, WEEDS, BRUSH, ETC.) ANY MORE THAN NECESSARY FOR CONSTRUCTION.
2. CONSTRUCTION ENTRANCE/EXIT LOCATION, CONCRETE WASH-OUT PIT AND CONSTRUCTION EQUIPMENT AND MATERIAL STORAGE YARD TO BE DETERMINED IN THE FIELD.
3. STORM WATER POLLUTION PREVENTION CONTROLS MAY NEED TO BE MODIFIED IN THE FIELD TO ACCOMPLISH THE DESIRED EFFECT. ALL MODIFICATIONS ARE TO BE NOTED ON THIS EXHIBIT AND SIGNED AND DATED BY THE RESPONSIBLE PARTY.
4. RESTRICT ENTRY/EXIT TO THE PROJECT SITE TO DESIGNATED LOCATIONS BY USE OF ADEQUATE FENCING, IF NECESSARY.
5. ALL STORM WATER POLLUTION PREVENTION CONTROLS ARE TO BE MAINTAINED AND IN WORKING CONDITIONS AT ALL TIMES.
6. FOR A COMPLETE LISTING OF TEMPORARY STORM WATER POLLUTION PREVENTION CONTROLS REFER TO THE TPDES STORM WATER POLLUTION PREVENTION PLAN.
7. STORM WATER POLLUTION PREVENTION STRUCTURES SHOULD BE CONSTRUCTED WITHIN THE SITE BOUNDARIES. SOME OF THESE FEATURES MAY BE SHOWN OUTSIDE THE SITE BOUNDARIES ON THIS PLAN FOR VISUAL CLARITY.
8. AS SOON AS PRACTICAL, ALL DISTURBED SOIL THAT WILL NOT BE COVERED BY IMPEROVISED COVER SUCH AS PARKWAY AREAS, EASEMENTS AREAS, EMBANKMENT SLOPES, ETC. WILL BE STABILIZED PER APPLICABLE PROJECT SPECIFICATIONS.
9. BEST MANAGEMENT PRACTICES MAY BE INSTALLED IN STAGES TO CONCOIDE WITH THE DISTURBANCE OF UPGRADE AREAS.
10. BEST MANAGEMENT PRACTICES MAY BE REMOVED IN STAGES ONCE THE WATERSHED FOR THAT PORTION CONTROLLED BY THE BEST MANAGEMENT PRACTICES HAS BEEN STABILIZED IN ACCORDANCE WITH TPDES REQUIREMENTS.
11. UPON COMPLETION OF THE PROJECT, INCLUDING SITE STABILIZATION AND REDEMPTION, FINAL PAYMENT IS ISSUED. CONTRACTOR SHALL REMOVE ALL SEDIMENT AND EROSION CONTROL MEASURES, PAYING SPECIAL ATTENTION TO ROCK BERMS IN DRAINAGE FEEDERS.
12. WHERE VEGETATED FILTER STRIPS ARE INDICATED, CONTRACTOR SHALL VERIFY THAT SUFFICIENT VEGETATION EXISTS, OTHERWISE CONTRACTOR SHALL PLACE SILT FENCING IN LIEU OF VEGETATED FILTER STRIP.
13. SHADED AREA DENOTES LIMITS OF DISTURBED AREAS. OTHER AREAS WITHIN THE PROJECT LIMITS, WITH THE EXCEPTION OF A PART OF THE TEMPORARY EQUIPMENT AND MATERIAL STORAGE YARD, ARE NOT A PART OF THIS TPDES STORM WATER POLLUTION PREVENTION PLAN (SWP3) AND WILL NOT BE DISTURBED BY CIVIL CONSTRUCTION ACTIVITIES. HOUSEHOLD CONSTRUCTION ACTIVITIES WILL REQUIRE A SEPARATE STORM WATER POLLUTION PREVENTION PLAN.
14. PRIOR TO BEGINNING CONSTRUCTION, CONTRACTOR SHALL COORDINATE PLACEMENT OF TEMPORARY BEST MANAGEMENT PRACTICES WITHIN TxDOT RIGHT-OF-WAY WITH TxDOT.
15. CPS ENERGY MAY FUNCTION AS A SECONDARY OPERATOR ON THIS PROJECT AND MAY BE PROVIDING ELECTRIC UTILITIES FOR ON-SITE CONSTRUCTION AND OFF-SITE FEED TO THE PROJECT.


THIS SHEET HAS BEEN PREPARED FOR PURPOSES OF POLLUTION ABATEMENT ONLY. ALL OTHER CIVIL ENGINEERING RELATED INFORMATION SHOULD BE ACQUIRED FROM THE APPROPRIATE SHEET IN THE CIVIL IMPROVEMENT PLANS.

CITY NO. \_\_\_\_\_  
JOB NO. 51570-00  
DATE \_\_\_\_\_  
DESIGNER \_\_\_\_\_ DS  
CHECKED \_\_\_\_\_ DRAWN \_\_\_\_\_ VKE  
SHEET 11 OF 14

**PAPE-DAWSON  
ENGINEERS**

**JARRELL INDUSTRIAL PARK**  
JARRELL, TEXAS

# TEMPORARY WATER POLLUTION ABATEMENT PLAN

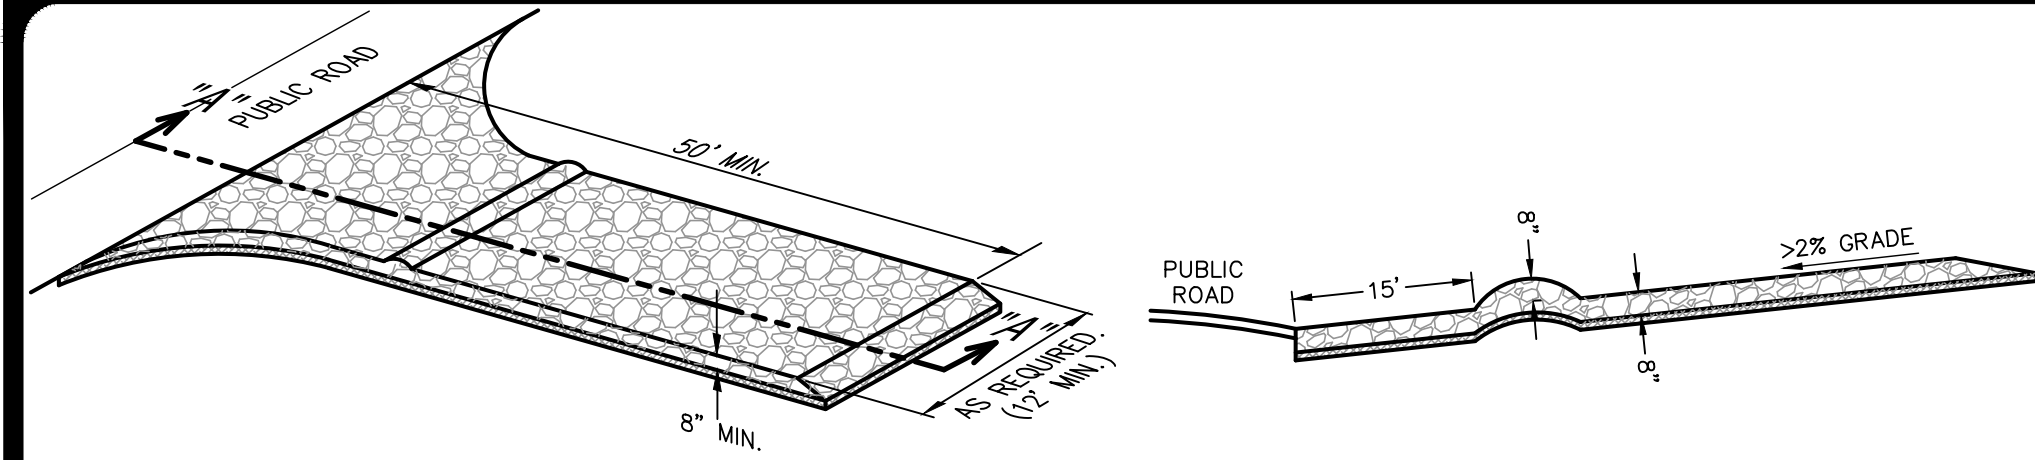

### SCHEMATIC OF TEMPORARY CONSTRUCTION ENTRANCE/EXIT

#### MATERIALS


1. THE AGGREGATE SHOULD CONSIST OF 4-INCH TO 8-INCH WASHED STONE OVER A STABLE FOUNDATION AS SPECIFIED IN THE PLAN.
2. THE AGGREGATE SHOULD BE PLACED WITH A MINIMUM THICKNESS OF 8-INCHES.
3. THE GEOTEXTILE FABRIC SHOULD BE DESIGNED SPECIFICALLY FOR USE AS A SOIL FILTRATION MEDIA WITH AN APPROXIMATE WEIGHT OF 6 OZ/YD<sup>2</sup>, A MULLEN BURST RATING OF 140 LB/IN<sup>2</sup>, AND AN EQUIVALENT OPENING SIZE GREATER THAN A NUMBER 50 SIEVE.
4. IF A WASHING FACILITY IS REQUIRED, A LEVEL AREA WITH A MINIMUM OF 4-INCH DIAMETER WASHED STONE OR COMMERCIAL ROCK SHOULD BE INCLUDED IN THE PLANS. DIVERT WASTEWATER TO A SEDIMENT TRAP OR BASIN.

#### INSTALLATION

1. AVOID CURVES ON PUBLIC ROADS AND STEEP SLOPES. REMOVE VEGETATION AND OTHER OBJECTIONABLE MATERIAL FROM THE FOUNDATION AREA. GRADE CROWN FOUNDATION FOR POSITIVE DRAINAGE.
2. THE MINIMUM WIDTH OF THE ENTRANCE/EXIT SHOULD BE 12 FEET OR THE FULL WIDTH OF EXIT ROADWAY, WHICHEVER IS GREATER.
3. THE CONSTRUCTION ENTRANCE SHOULD BE AT LEAST 50 FEET LONG.
4. IF THE SLOPE TOWARD THE ROAD EXCEEDS 2%, CONSTRUCT A RIDGE, 6-INCHES TO 8-INCHES HIGH WITH 3:1 (H:V) SIDE SLOPES, ACROSS THE FOUNDATION APPROXIMATELY 15 FEET FROM THE ENTRANCE TO DIVERT RUNOFF AWAY FROM THE PUBLIC ROAD.
5. PLACE GEOTEXTILE FABRIC AND GRADE FOUNDATION TO IMPROVE STABILITY, ESPECIALLY WHERE WET CONDITIONS ARE ANTICIPATED.
6. PLACE STONE TO DIMENSIONS AND GRADE SHOWN ON PLANS. LEAVE SURFACE SMOOTH AND SLOPE FOR DRAINAGE.
7. DIVERT ALL SURFACE RUNOFF AND DRAINAGE FROM THE STONE PAD TO A SEDIMENT TRAP OR BASIN.
8. INSTALL PIPE UNDER PAD AS NEEDED TO MAINTAIN PROPER PUBLIC ROAD DRAINAGE.

### STABILIZED CONSTRUCTION ENTRANCE/EXIT DETAIL

NOT-TO-SCALE

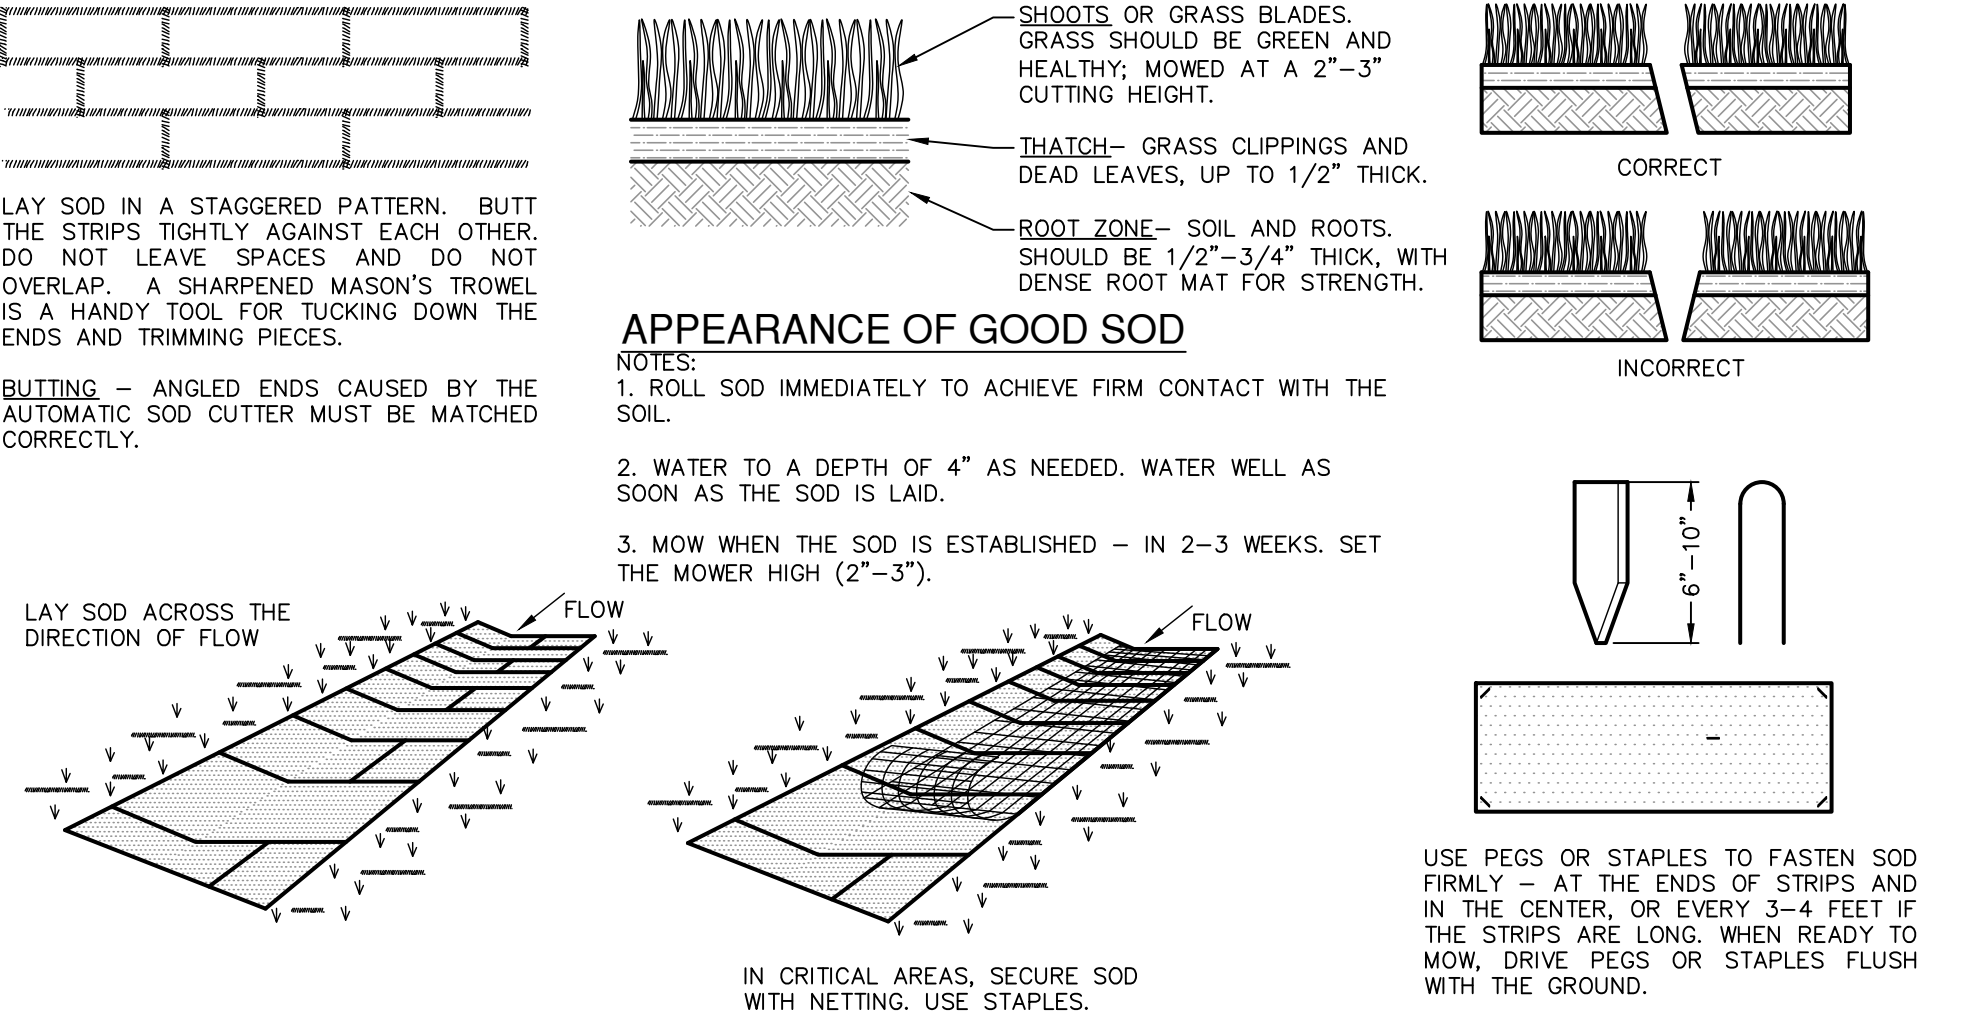

#### MATERIALS

1. SOD SHOULD BE MACHINE CUT AT A UNIFORM SOIL THICKNESS OF 3/4" INCH (± 1/4" INCH) AT THE TIME OF CUTTING. THIS THICKNESS SHOULD EXCLUDE SHOOT GROWTH AND THATCH.
2. PIECES OF SOD SHOULD BE CUT TO THE SUPPLIER'S STANDARD WIDTH AND LENGTH, WITH A MAXIMUM ALLOWABLE DEVIATION IN ANY DIMENSION OF 5%. TORN OR UNEVEN PADS SHOULD NOT BE ACCEPTABLE.
3. STANDARD SIZE SECTIONS OF SOD SHOULD BE STRONG ENOUGH TO SUPPORT THEIR OWN WEIGHT AND THEIR SIZE AND SHAPE WHEN SUSPENDED FROM A FIRM GRASP ON ONE END OF THE SECTION.
4. SOD SHOULD BE HARVESTED, DELIVERED, AND INSTALLED WITHIN A PERIOD OF 36 HOURS.

#### SITE PREPARATION

1. PRIOR TO SOD PREPARATION, AREAS TO BE SODDED SHOULD BE BROUGHT TO FINAL GRADE IN ACCORDANCE WITH THE APPROVED PLAN.
2. THE SURFACE SHOULD BE CLEARED OF ALL TRASH, DEBRIS AND OF ALL ROOTS, BRUSH, WIRE, GRADE STAKES AND OTHER OBJECTS THAT WOULD INTERFERE WITH PLANTING, FERTILIZING OR MAINTENANCE OPERATIONS.
3. FERTILIZE ACCORDING TO SOIL TESTS. FERTILIZER NEEDS CAN BE DETERMINED BY A SOIL TESTING LABORATORY OR REGIONAL RECOMMENDATIONS CAN BE MADE BY COUNTY AGRICULTURAL EXTENSION AGENTS. FERTILIZER SHOULD BE WORKED INTO THE SOIL TO A DEPTH OF 3 INCHES WITH A DISC, SPRINGTOOTH HARROW OR OTHER SUITABLE EQUIPMENT. ON SLOPING LAND, THE FINAL HARROWING OR DISCING OPERATION SHOULD BE ON THE CONTOUR.

#### INSTALLATION IN CHANNELS

1. SOD STRIPS IN WATERWAYS SHOULD BE LAID PERPENDICULAR TO THE DIRECTION OF FLOW. CARE SHOULD BE TAKEN TO BUTT ENDS OF STRIPS TIGHTLY (SEE FIGURE ABOVE).
2. AFTER ROLLING OR TAMPING, SOD SHOULD BE PEGGED OR STAPLED TO RESIST WASHOUT DURING THE ESTABLISHMENT PERIOD. MESH OR OTHER NETTING MAY BE PEGGED OVER THE SOD FOR EXTRA PROTECTION IN CRITICAL AREAS.

### SOD INSTALLATION DETAIL


NOT-TO-SCALE

#### COMMON TROUBLE POINTS

1. INADEQUATE RUNOFF CONTROL-SEDIMENT WASHES ONTO PUBLIC ROAD.
2. STONE TOO SMALL OR GEOTEXTILE FABRIC ABSENT, RESULTS IN MUDDY CONDITION AS STONE IS PRESSED INTO SOIL.
3. PAD TOO SHORT FOR HEAVY CONSTRUCTION TRAFFIC-EXTEND PAD BEYOND THE MINIMUM 50-FOOT LENGTH AS NECESSARY.
4. PAD NOT FLARED SUFFICIENTLY AT ROAD SURFACE, RESULTS IN MUD BEING TRACKED ON TO ROAD AND POSSIBLE DAMAGE TO ROAD.
5. UNSTABLE FOUNDATION - USE GEOTEXTILE FABRIC UNDER PAD AND/OR IMPROVE FOUNDATION DRAINAGE.

#### INSPECTION AND MAINTENANCE GUIDELINES

1. THE ENTRANCE SHOULD BE MAINTAINED IN A CONDITION, WHICH WILL PREVENT TRACKING OR FLOWING OF SEDIMENT ONTO PUBLIC RIGHTS-OF-WAY. THIS MAY REQUIRE PERIODIC TOP DRESSING WITH ADDITIONAL STONE AS CONDITIONS DEMAND AND REPAIR AND/OR CLEANOUT OF ANY MEASURES USED TO TRAP SEDIMENT.
2. ALL SEDIMENT SPILLED, DROPPED, WASHED OR TRACKED ONTO PUBLIC RIGHTS-OF-WAY SHOULD BE REMOVED IMMEDIATELY BY CONTRACTOR.
3. WHEN NECESSARY, WHEELS SHOULD BE CLEANED TO REMOVE SEDIMENT PRIOR TO ENTRANCE ONTO PUBLIC RIGHT-OF-WAY.
4. WHEN WASHING IS REQUIRED, IT SHOULD BE DONE ON AN AREA STABILIZED WITH CRUSHED STONE THAT DRAINS INTO AN APPROVED SEDIMENT TRAP OR SEDIMENT BASIN.
5. ALL SEDIMENT SHOULD BE PREVENTED FROM ENTERING ANY STORM DRAIN, DITCH OR WATER COURSE BY USING APPROVED METHODS.

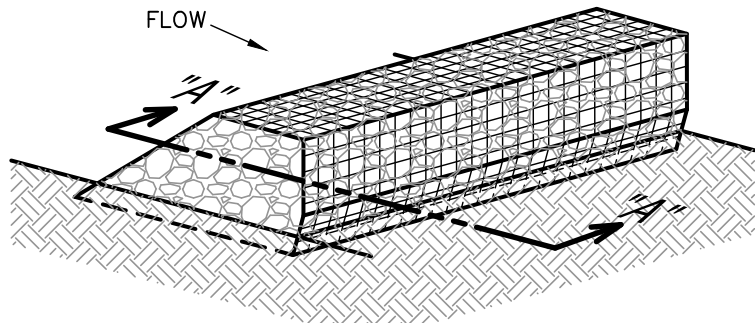

#### ROCK BERMS


THE PURPOSE OF A ROCK BERM IS TO SERVE AS A CHECK DAM IN AREAS OF CONCENTRATED FLOW, TO INTERCEPT SEDIMENT-LADEN RUNOFF, DETAIN THE SEDIMENT AND RELEASE THE WATER IN SHEET FLOW. THE ROCK BERM SHOULD BE USED WHEN THE CONTRIBUTING DRAINAGE AREA IS LESS THAN 5 ACRES. ROCK BERMS ARE USED IN AREAS WHERE THE VOLUME OF RUNOFF IS TOO GREAT FOR A SILT FENCE TO CONTAIN. THEY ARE LESS EFFECTIVE FOR SEDIMENT REMOVAL THAN SILT FENCES, PARTICULARLY FOR FINE PARTICLES, BUT ARE ABLE TO WITHSTAND HIGHER FLOWS THAN A SILT FENCE. AS SUCH, ROCK BERMS ARE OFTEN USED IN AREAS OF CHANNEL FLOWS (DITCHES, GULLIES, ETC.). ROCK BERMS ARE MOST EFFECTIVE AT REDUCING BED LOAD IN CHANNELS AND SHOULD NOT BE SUBSTITUTED FOR OTHER EROSION AND SEDIMENT CONTROL MEASURES FARTHER UP THE WATERSHED.

#### INSPECTION AND MAINTENANCE GUIDELINES

1. INSPECTION SHOULD BE MADE WEEKLY AND AFTER EACH RAINFALL BY THE RESPONSIBLE PARTY. FOR INSTALLATIONS IN STREAMBEDS, ADDITIONAL DAILY INSPECTIONS SHOULD BE MADE.
2. REMOVE SEDIMENT AND OTHER DEBRIS WHEN BUILDUP REACHES 6 INCHES AND DISPOSE OF THE ACCUMULATED SILT IN AN APPROVED MANNER THAT WILL NOT CAUSE ANY ADDITIONAL SILTATION.
3. REPAIR ANY LOOSE WIRE SHEATHING.
4. THE BERM SHOULD BE RESHAPED AS NEEDED DURING INSPECTION.
5. THE BERM SHOULD BE REPLACED WHEN THE STRUCTURE CEASES TO FUNCTION AS INTENDED DUE TO SILT ACCUMULATION AMONG THE ROCKS, WASHOUT, CONSTRUCTION TRAFFIC DAMAGE, ETC.
6. THE ROCK BERM SHOULD BE LEFT IN PLACE UNTIL ALL UPSTREAM AREAS ARE STABILIZED AND ACCUMULATED SILT REMOVED.

### ROCK BERM DETAIL

NOT-TO-SCALE

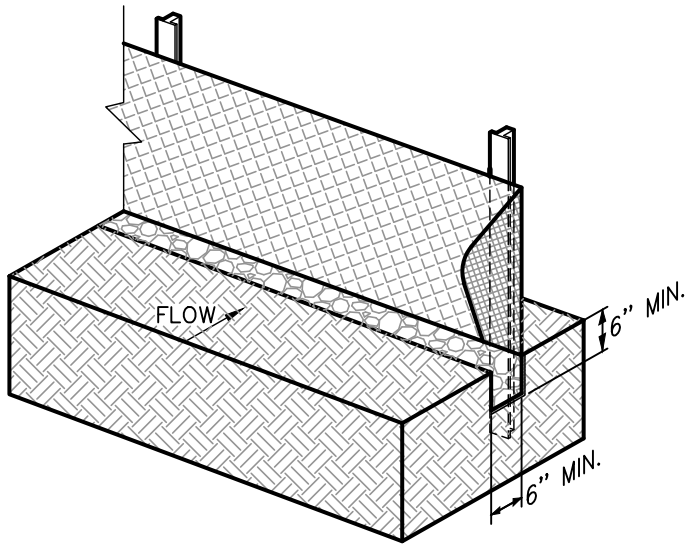

#### ISOMETRIC PLAN VIEW

#### SILT FENCE

A SILT FENCE IS A BARRIER CONSISTING OF GEOTEXTILE FABRIC SUPPORTED BY METAL POSTS TO PREVENT SOIL AND SEDIMENT LOSS FROM A SITE. WHEN PROPERLY USED, SILT FENCES CAN BE HIGHLY EFFECTIVE AT CONTROLLING SEDIMENT FROM DISTURBED AREAS. THEY CAUSE RUNOFF TO POND, ALLOWING HEAVIER SOLIDS TO SETTLE OUT. IF NOT PROPERLY INSTALLED, SILT FENCES ARE NOT LIKELY TO BE EFFECTIVE.

THE PURPOSE OF A SILT FENCE IS TO INTERCEPT AND DETAIN WATER-BORN SEDIMENT FROM UNPROTECTED AREAS OF A LIMITED EXTENT. SILT FENCE IS USED DURING THE PERIOD OF CONSTRUCTION NEAR THE PERIMETER OF A DISTURBED AREA TO INTERCEPT SEDIMENT WHILE ALLOWING WATER TO PERCOLATE THROUGH. THIS FENCE SHOULD REMAIN IN PLACE UNTIL THE DISTURBED AREA IS PERMANENTLY STABILIZED. SILT FENCE SHOULD NOT BE USED WHERE THERE IS A CONCENTRATION OF WATER IN A CHANNEL OR DRAINAGE WAY. IF CONCENTRATED FLOW OCCURS AFTER INSTALLATION, CORRECTIVE ACTION MUST BE TAKEN SUCH AS PLACING A ROCK BERM IN THE AREAS OF CONCENTRATED FLOW.

SILT FENCING WITHIN THE SITE MAY BE TEMPORARILY MOVED DURING THE DAY TO ALLOW CONSTRUCTION ACTIVITY PROVIDED IT IS REPLACED AND PROPERLY ANCHORED TO THE GROUND AT THE END OF THE DAY. SILT FENCES ON THE PERIMETER OF THE SITE OR AROUND DRAINAGE WAYS SHOULD NOT BE MOVED AT ANY TIME.

#### MATERIALS


1. SILT FENCE MATERIAL SHOULD BE POLYPROPYLENE, POLYETHYLENE, OR POLYAMIDE WOVEN OR NONWOVEN FABRIC. THE FABRIC SHOULD BE 36 INCHES, WITH A MINIMUM UNIT WEIGHT OF 4.5 OZ/YD, MULLEN BURST STRENGTH EXCEEDING 190 LB/IN<sup>2</sup>, ULTRAVIOLET STABILITY EXCEEDING 70%, AND MINIMUM APPARENT OPENING SIZE OF U.S. SIEVE NUMBER 30.
2. FENCE POSTS SHOULD BE MADE OF HOT ROLLED STEEL, AT LEAST 4 FEET LONG WITH TEE OR Y-BAR CROSS SECTION, SURFACE PAINTED OR GALVANIZED, MINIMUM WEIGHT 1.25 LB/FT, AND BRINELL HARDNESS EXCEEDING 140.
3. WOVEN WIRE BACKING TO SUPPORT THE FABRIC SHOULD BE GALVANIZED 2" X 4" WELDED WIRE, 12 GAUGE MINIMUM.

#### INSTALLATION

1. STEEL POSTS, WHICH SUPPORT THE SILT FENCE, SHOULD BE INSTALLED ON A SLIGHT ANGLE TOWARD THE ANTICIPATED RUNOFF SOURCE. POSTS MUST BE EMBEDDED A MINIMUM OF 1-FOOT DEEP AND SPACED NOT MORE THAN 8 FEET ON CENTER, WHERE WATER CONCENTRATES, THE MAXIMUM SPACING SHOULD BE 6 FEET.
2. LAY OUT FENCING DOWN-SLOPE OF DISTURBED AREA, FOLLOWING THE CONTOUR AS CLOSELY AS POSSIBLE. THE FENCE SHOULD BE SITED SO THAT THE MAXIMUM DRAINAGE AREA IS ¼ ACRE/100 FEET OF FENCE.

### SILT FENCE DETAIL

NOT-TO-SCALE

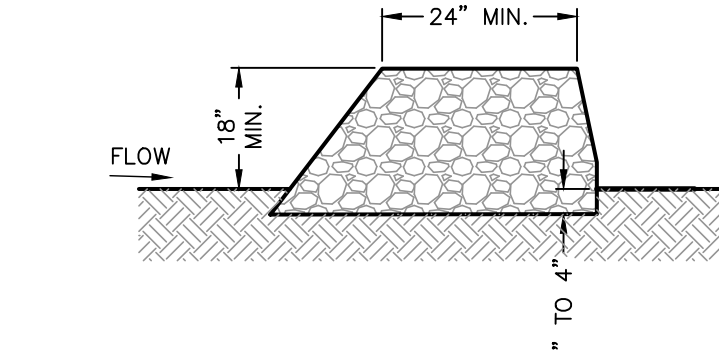

#### MATERIALS


1. THE BERM STRUCTURE SHOULD BE SECURED WITH A WOVEN WIRE SHEATHING HAVING MAXIMUM OPENING OF 1 INCH AND A MINIMUM WIRE DIAMETER OF 20 GAUGE GALVANIZED AND SHOULD BE SECURED WITH SHOAT RINGS.
2. CLEAN, OPEN GRADED 3-INCH TO 5-INCH DIAMETER ROCK SHOULD BE USED, EXCEPT IN AREAS WHERE HIGH VELOCITIES OR LARGE VOLUMES OF FLOW ARE EXPECTED, WHERE 5-INCH TO 8-INCH DIAMETER ROCKS MAY BE USED.

#### INSTALLATION

1. LAY OUT THE WOVEN WIRE SHEATHING PERPENDICULAR TO THE FLOW LINE. THE SHEATHING SHOULD BE 20 GAUGE WOVEN WIRE MESH WITH 1 INCH OPENINGS.
2. BERM SHOULD HAVE A TOP WIDTH OF 2 FEET MINIMUM WITH SIDE SLOPES BEING 2:1 (H:V) OR FLATTER.
3. PLACE THE ROCK ALONG THE SHEATHING AS SHOWN IN THE DIAGRAM TO A HEIGHT NOT LESS THAN 18".
4. WRAP THE WIRE SHEATHING AROUND THE ROCK AND SECURE WITH TIE WIRE SO THAT THE ENDS OF THE SHEATHING OVERLAP AT LEAST 2 INCHES, AND THE BERM RETAINS ITS SHAPE WHEN WALKED UPON.
5. BERM SHOULD BE BUILT ALONG THE CONTOUR AT ZERO PERCENT GRADE OR AS NEAR AS POSSIBLE.
6. THE ENDS OF THE BERM SHOULD BE TIED INTO EXISTING UPSLOPE GRADE AND THE BERM SHOULD BE BURIED IN A TRENCH APPROXIMATELY 3 TO 4 INCHES DEEP TO PREVENT FAILURE OF THE CONTROL.

#### COMMON TROUBLE POINTS

1. INSUFFICIENT BERM HEIGHT OR LENGTH (RUNOFF QUICKLY ESCAPES OVER THE TOP OR AROUND THE SIDES OF BERM).
2. BERM NOT INSTALLED PERPENDICULAR TO FLOW LINE (RUNOFF ESCAPING AROUND ONE SIDE).

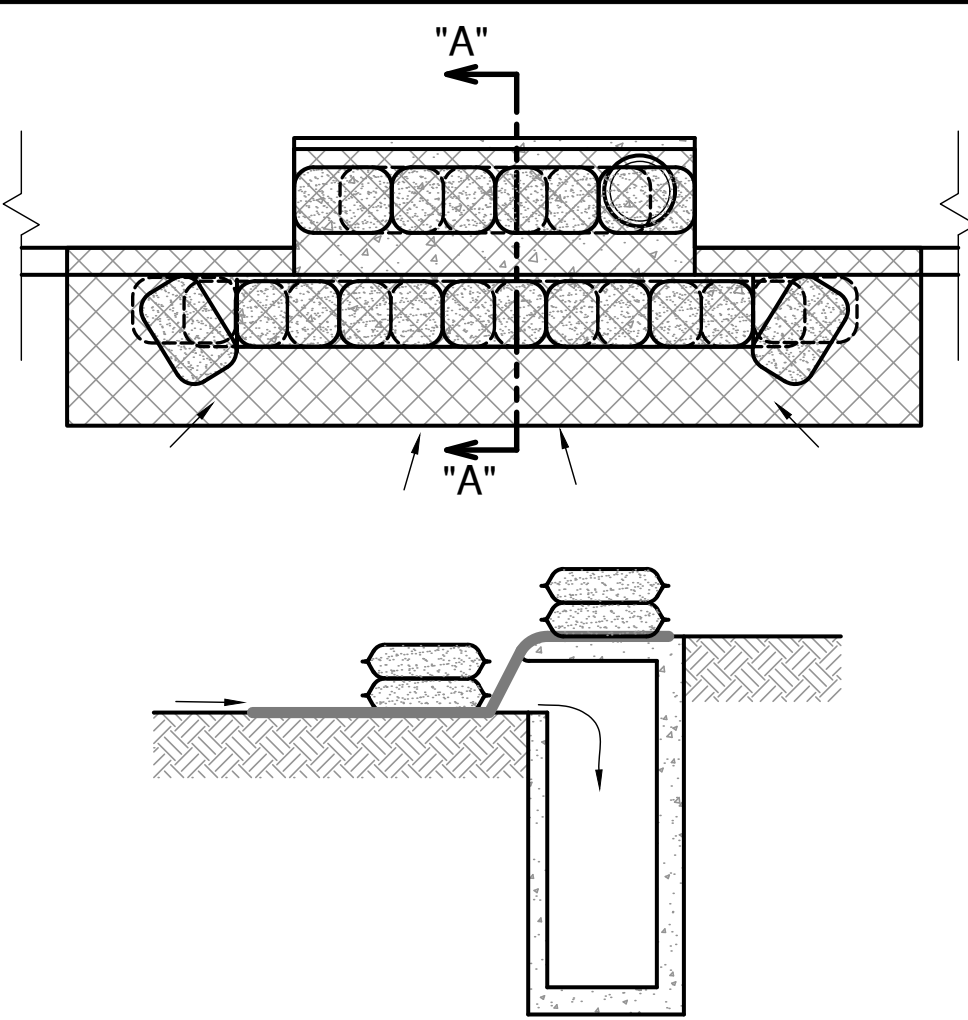


#### GENERAL NOTES

1. CONTRACTOR TO INSTALL 2"x4"-W1.4xW1.4 WIRE MESH SUPPORTING FILTER FABRIC OVER THE INLET OPENING. FABRIC MUST BE SECURED TO WIRE BACKING WITH CLIPS OR WIRE TIES AT THIS LOCATION. SAND BAGS FILLED WITH WASHED PEA GRAVEL SHOULD BE PLACED ON TOP OF WIRE MESH ON TOP OF THE INLET AS SHOWN ON THIS DETAIL TO HOLD WIRE MESH IN PLACE. SANDBAGS FILLED WITH WASHED PEA GRAVEL SHOULD ALSO BE PLACED ALONG THE GUTTER AS SHOWN ON THIS DETAIL TO HOLD WIRE MESH IN PLACE. SAND BAGS TO BE STACKED TO FORM A CONTINUOUS BARRIER AROUND INLETS.
2. THE BAGS SHOULD BE TIGHTLY ABUTTED AGAINST EACH OTHER TO PREVENT RUNOFF FROM FLOWING BETWEEN THE BAGS.
3. CHECK PLACEMENT OF DEVICE TO PREVENT GAPS BETWEEN DEVICE AND CURB.
4. INSPECT FILTER FABRIC AND PATCH OR REPLACE IF TORN OR MISSING.
5. STRUCTURES SHOULD BE REMOVED AND THE AREA STABILIZED ONLY AFTER THE REMAINING DRAINAGE AREA HAS BEEN PROPERLY STABILIZED.

### BAGGED GRAVEL CURB INLET PROTECTION DETAIL

NOT-TO-SCALE

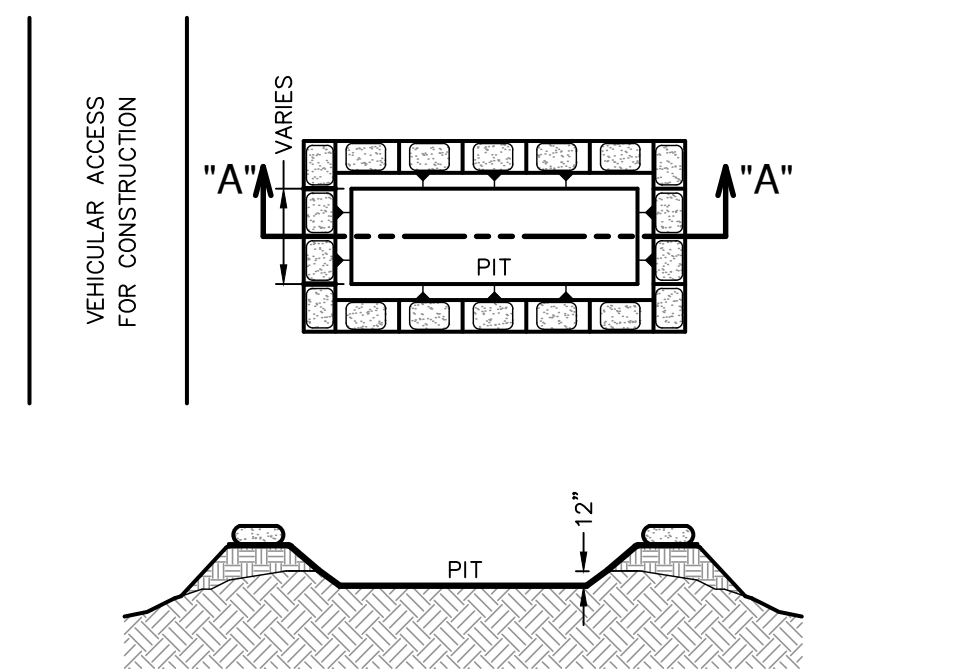

#### GENERAL NOTES

1. DETAIL ABOVE ILLUSTRATES MINIMUM DIMENSIONS. PIT CAN BE INCREASED IN SIZE DEPENDING ON EXPECTED FREQUENCY OF USE.
2. WASHOUT PIT SHALL BE LOCATED IN AN AREA EASILY ACCESSIBLE TO CONSTRUCTION TRAFFIC.
3. WASHOUT PIT SHALL NOT BE LOCATED IN AREAS SUBJECT TO INUNDATION FROM STORM WATER RUNOFF.
4. LOCATE WASHOUT AREA AT LEAST 50 FEET FROM SENSITIVE FEATURES, STORM DRAINS, OPEN DITCHES OR WATER BODIES.
5. TEMPORARY CONCRETE WASHOUT FACILITY SHOULD BE CONSTRUCTED WITH SUFFICIENT QUANTITY AND VOLUME TO CONTAIN ALL LIQUID AND CONCRETE WASTE GENERATED BY WASHOUT OPERATIONS.

#### MATERIALS


PLASTIC LINING MATERIAL SHOULD BE A MINIMUM OF 10 MIL IN POLYETHYLENE SHEETING AND SHOULD BE FREE OF HOLES, TEARS, OR OTHER DEFECTS THAT COMPROMISE THE IMPERMEABILITY OF THE MATERIAL.

#### MAINTENANCE

1. WHEN TEMPORARY CONCRETE WASHOUT FACILITIES ARE NO LONGER REQUIRED FOR THE WORK, THE HARDENED CONCRETE SHOULD BE REMOVED AND DISPOSED OF.
2. MATERIALS USED TO CONSTRUCT TEMPORARY CONCRETE WASHOUT FACILITIES SHOULD BE REMOVED FROM THE SITE OF THE WORK AND DISPOSED OF.
3. HOLES, DEPRESSIONS OR OTHER GROUND DISTURBANCES CAUSED BY THE REMOVAL OF THE TEMPORARY CONCRETE WASHOUT FACILITIES SHOULD BE BACKFILLED AND REPAIRED.

### CONCRETE TRUCK WASHOUT PIT DETAIL

NOT-TO-SCALE

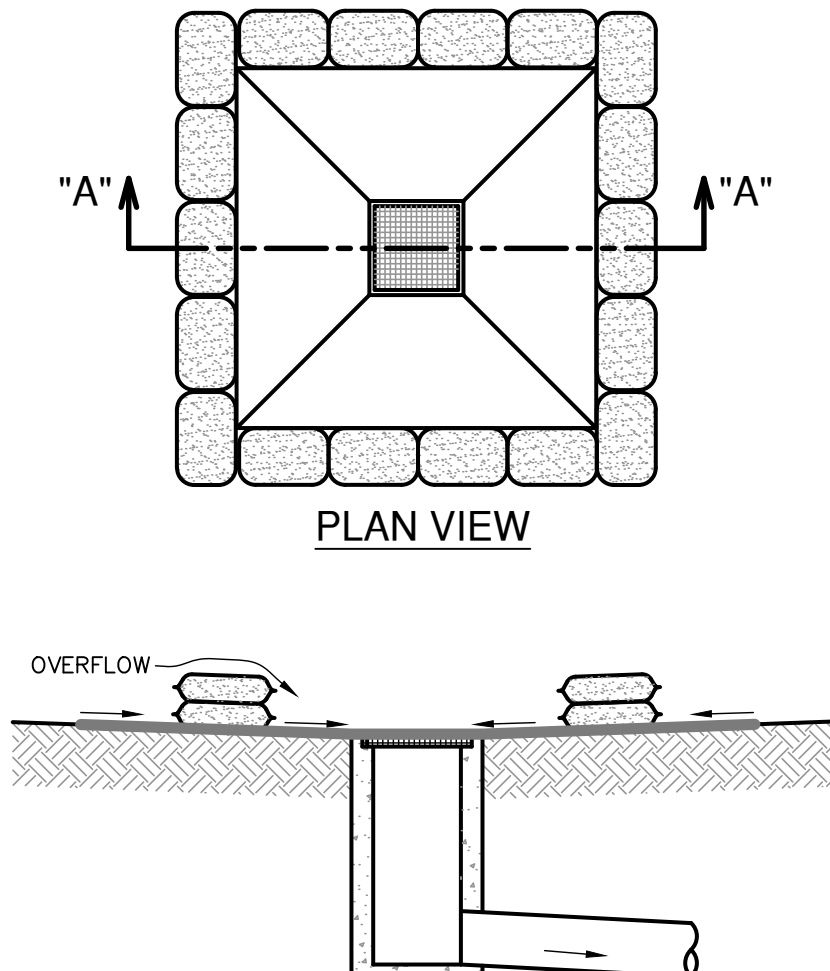


#### SECTION "A-A"

#### GENERAL NOTES


1. THE SANDBAGS SHOULD BE FILLED WITH WASHED PEA GRAVEL AND STACKED TO FORM A CONTINUOUS BARRIER ABOUT 1 FOOT HIGH AROUND INLETS.
2. THE BAGS SHOULD BE TIGHTLY ABUTTED AGAINST EACH OTHER TO PREVENT RUNOFF FROM FLOWING BETWEEN THE BAGS.
3. CHECK PLACEMENT OF DEVICE TO PREVENT GAPS BETWEEN DEVICE AND CURB.
4. INSPECT FILTER FABRIC AND PATCH OR REPLACE IF TORN OR MISSING.
5. STRUCTURES SHOULD BE REMOVED AND THE AREA STABILIZED ONLY AFTER THE REMAINING DRAINAGE AREA HAS BEEN PROPERLY STABILIZED.

### BAGGED GRAVEL GRATE INLET PROTECTION DETAIL

NOT-TO-SCALE



1. THE FILTER BAG MATERIAL SHALL BE MADE OF POLYPROPYLENE, POLYETHYLENE OR POLYAMIDE WOVEN FABRIC, MIN. UNIT WEIGHT OF 4 OUNCES/SY, HAVE A MULLEN BURST STRENGTH EXCEEDING 300 PSI AND ULTRAVIOLET STABILITY EXCEEDING 70%.
2. THE FILTER BAG SHALL BE FILLED WITH CLEAN, MEDIUM WASHED PEA GRAVEL TO COARSE GRAVEL (0.31 TO 0.75 INCH DIAMETER).
3. SAND SHALL NOT BE USED TO FILL THE FILTER BAGS.

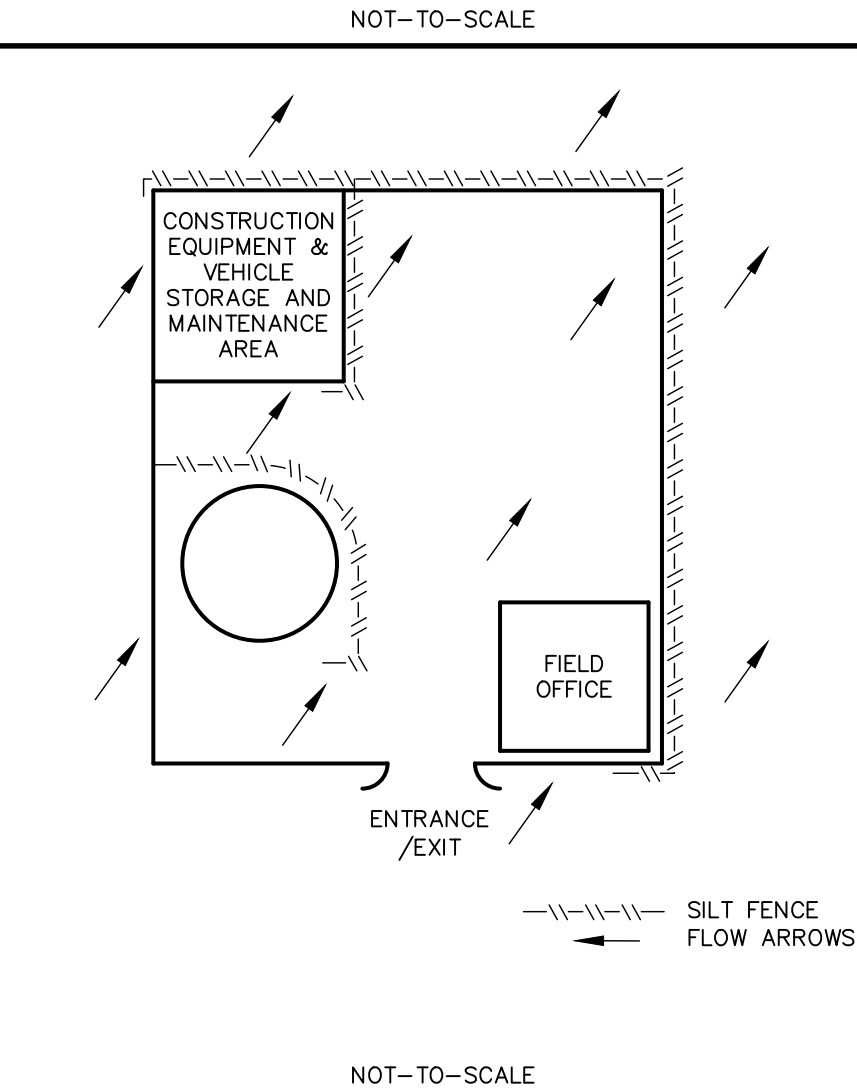

NOT-TO-SCALE

THE ENGINEERING SEAL HAS BEEN AFFIXED TO THIS SHEET ONLY FOR THE PURPOSE OF DEMONSTRATING COMPLIANCE WITH THE POLLUTION ABATEMENT SIZING AND TREATMENT REQUIREMENTS OF THE TEXAS COMMISSION ON ENVIRONMENTAL QUALITY'S EDWARDS AQUIFER TECHNICAL GUIDANCE MANUAL.

THIS SHEET HAS BEEN PREPARED FOR PURPOSES OF POLLUTION ABATEMENT ONLY. ALL OTHER CIVIL ENGINEERING RELATED INFORMATION SHOULD BE ACQUIRED FROM THE APPROPRIATE SHEET IN THE CIVIL IMPROVEMENT PLANS.

### WPAP EXHIBIT 2

NO.	REVISION	DATE



**PAPE-DAWSON ENGINEERS**

AUSTIN | SAN ANTONIO | HOUSTON | FORT WORTH | DALLAS  
10001 N. MOPAC EXPY., BLDG. 3, STE. 200 | AUSTIN, TX 78759 | 512-454-8711  
TYPE FIRM REGISTRATION #470 | TYPE FIRM REGISTRATION #10028801


**JARRELL INDUSTRIAL PARK**  
JARRELL, TEXAS

TEMPORARY WATER POLLUTION ABATEMENT PLAN DETAILS


CITY NO.	51570-00
JOB NO.	51570-00
DATE	
DESIGNER	DS
CHECKED	DRAWN VKB
SHEET	14 OF 14

Date: Feb 19, 2025 11:59am User ID: jveloz  
File: H:\Projects\515170\001 Construction Documents\Civil\WP-51570-00.dwg

THIS DOCUMENT HAS BEEN PRODUCED FROM MATERIAL THAT WAS STORED AND/OR TRANSMITTED ELECTRONICALLY AND MAY HAVE BEEN INADVERTENTLY ALTERED. RELY ONLY ON FINAL HARDCOPY MATERIALS BEARING THE CONSULTANT'S ORIGINAL SIGNATURE AND SEAL.


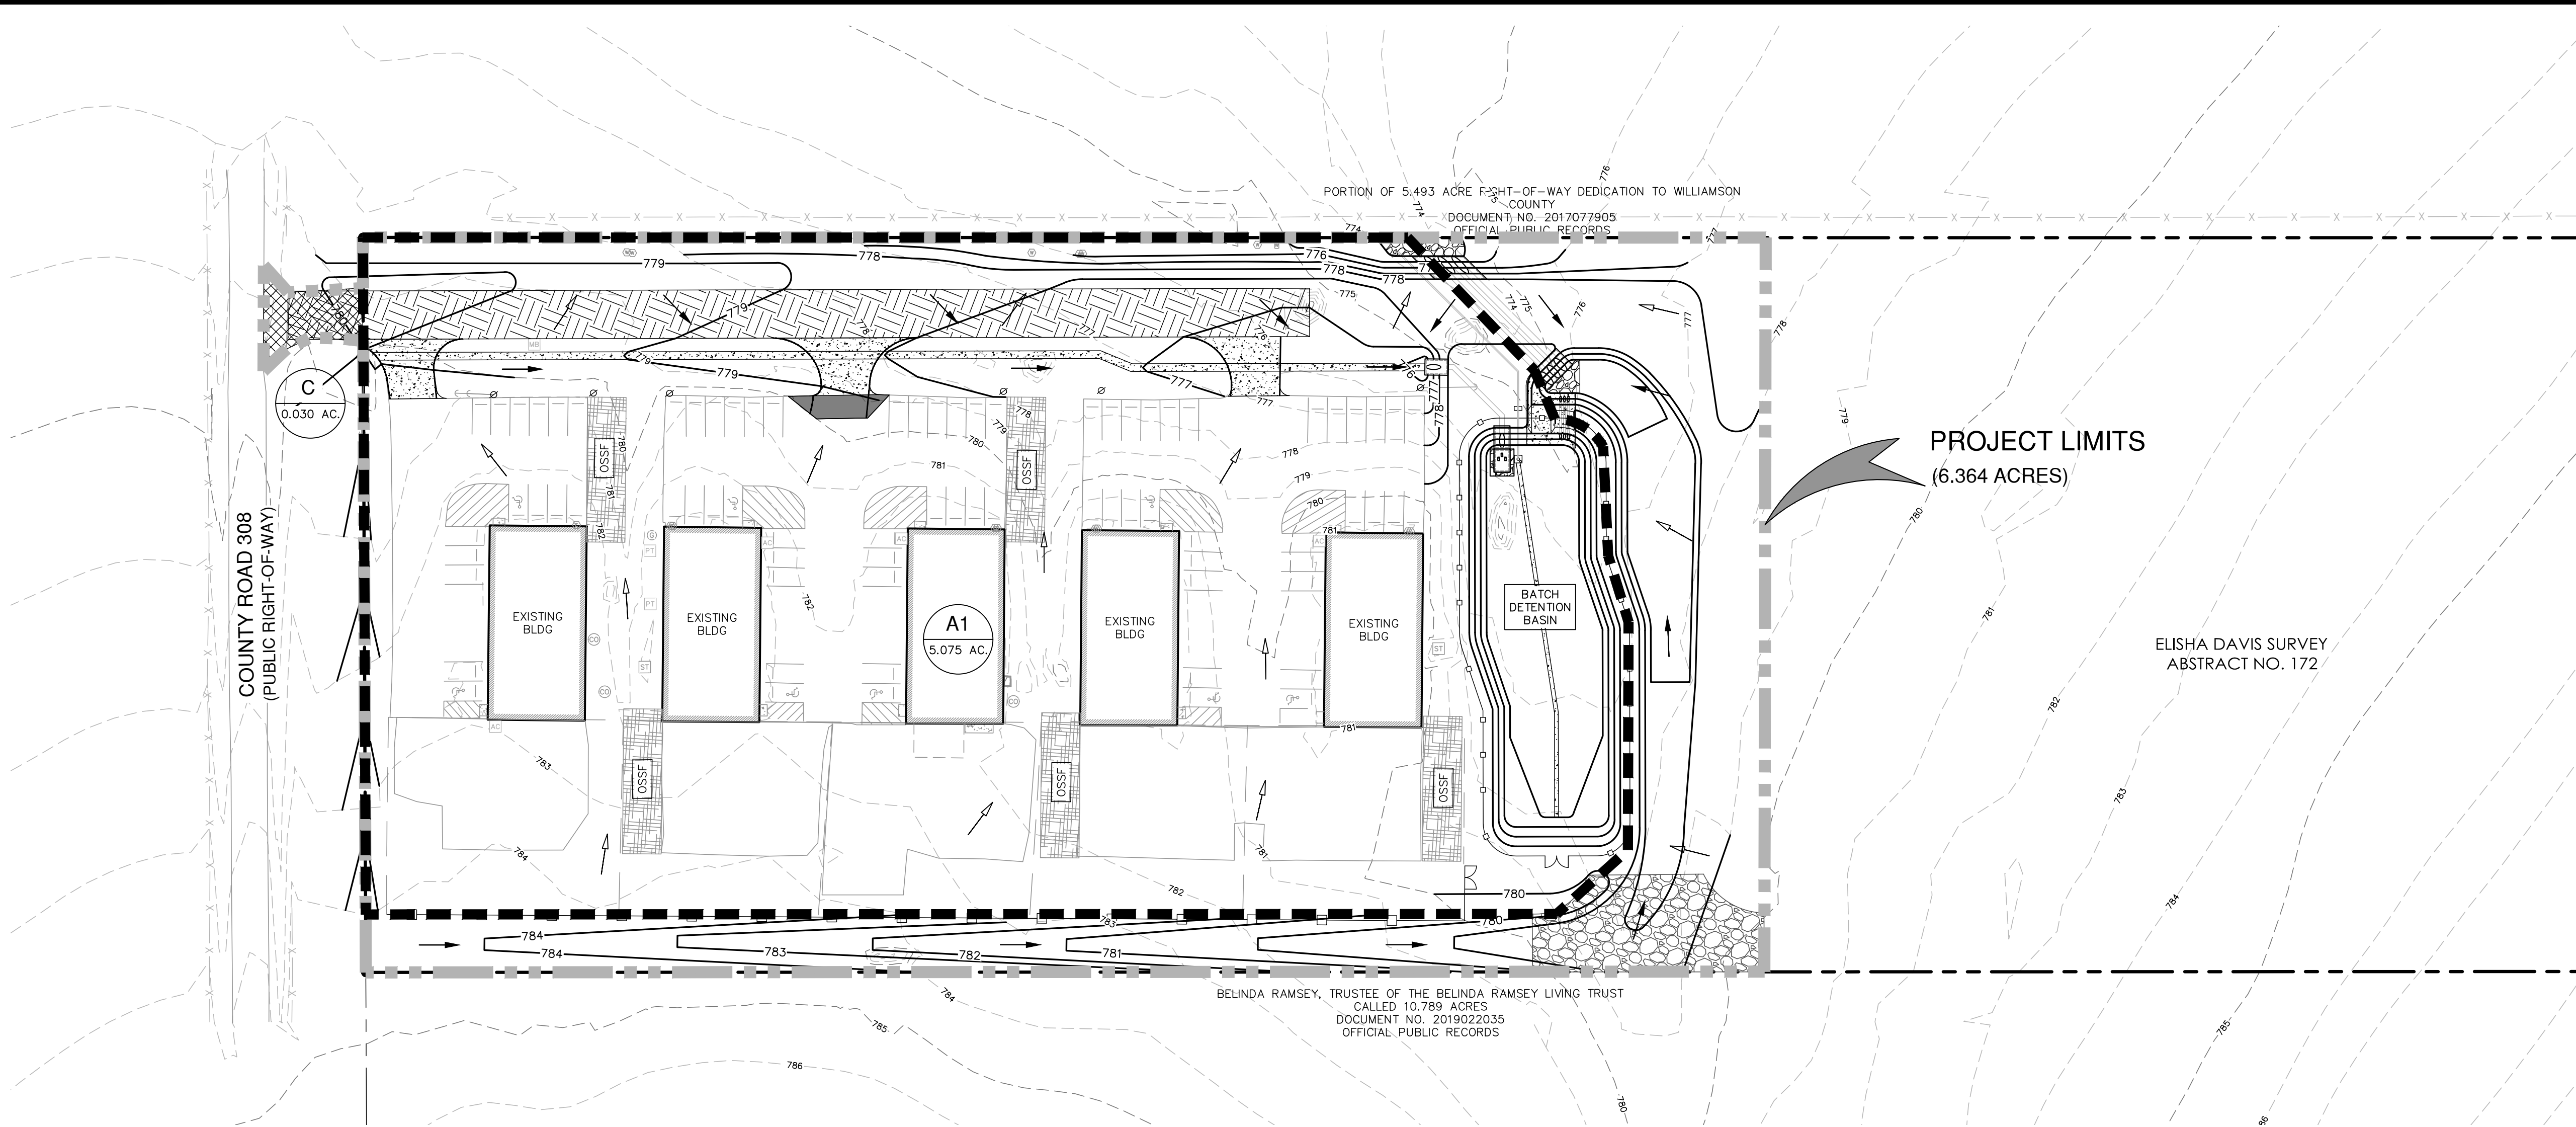


Watershed	Watershed Area (AC.)	Impervious Cover (AC.)	BMP Type	TSS Generated Annually (LBS.)	TSS Removed Annually (LBS.)
A1	4.90	2.86	Batch Detention	2489	2515
UNCAPTURED C	0.03	0.03	Overtreatment	26	0
TOTAL	4.930	2.89	---	2515	2515

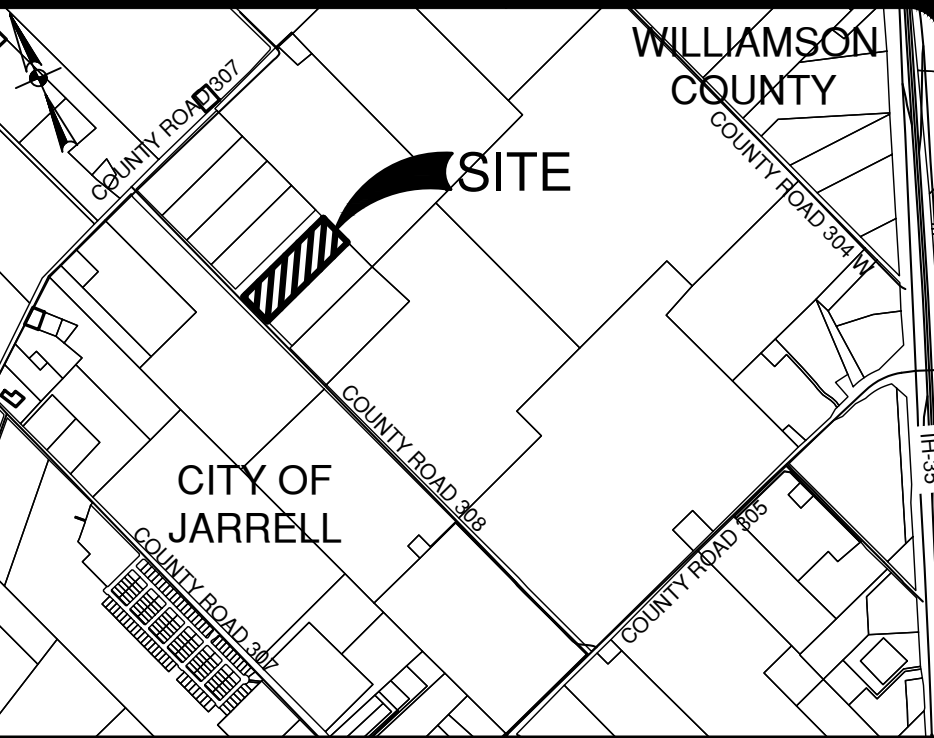


LOCATION MAP

NOT-TO-SCALE



LEGEND

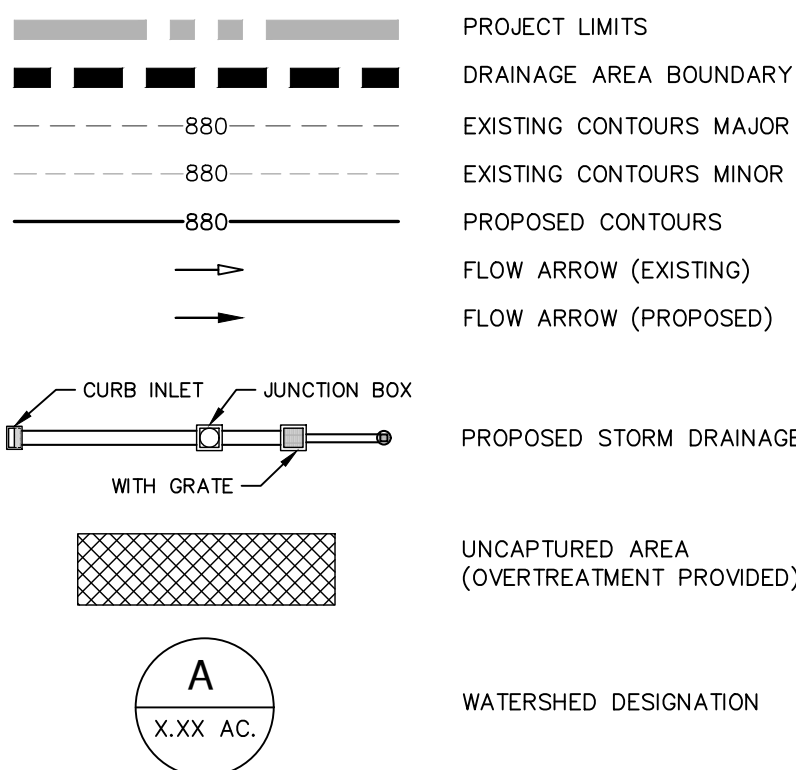

SUMMARY OF PERMANENT POLLUTION ABATEMENT MEASURES:

- TEMPORARY BMP'S WILL BE MAINTAINED UNTIL THE SITE IMPROVEMENTS ARE COMPLETED AND THE SITE HAS BEEN STABILIZED, INCLUDING SUFFICIENT VEGETATION BEING ESTABLISHED.
- DURING CONSTRUCTION, TO THE EXTENT PRACTICAL, CONTRACTOR SHALL MINIMIZE THE AREA OF SOIL DISTURBANCE. AREAS OF DISTURBED SOIL SHALL BE REVEGETATED TO STABILIZE SOIL USING SOLID SOD IN A STAGGERED PATTERN. SEE DETAIL ON TEMPORARY POLLUTION ABATEMENT DETAIL SHEET AND REFER TO SECTION 1.3.11 IN TCEQ'S TECHNICAL GUIDANCE MANUAL RG-348 (2005). SOD SHOULD BE USED IN CHANNELS AND ON SLOPES > 15%. THE CONTRACTOR MAY SUBSTITUTE THE USE OF SOD WITH THE PLACEMENT OF TOP SOIL AND A FRILABLE SEED BED WITH A PROTECTIVE MATTING OR HYDRAULIC MULCH ALONG WITH WATERING UNTIL VEGETATION IS ESTABLISHED. APPLICATIONS AND PRODUCTS SHALL BE THOSE APPROVED BY TXDOT AS OF FEBRUARY 2007 AND IN COMPLIANCE WITH THE TGM RG-348 (2005). SEED MIXTURE AND/OR GRASS TYPE TO BE DETERMINED BY OWNER AND SHOULD BE IN COMPLIANCE WITH TGM RG-348 (2005) GUIDELINES. IRRIGATION MAY BE REQUIRED IN ORDER TO ESTABLISH SUFFICIENT VEGETATION.
- FOR DISTURBED AREAS WHERE INSUFFICIENT SOIL EXISTS TO ESTABLISH VEGETATION, CONTRACTOR SHALL PLACE A MINIMUM OF 6" OF TOPSOIL PRIOR TO REVEGETATION.
- PERMANENT BMP'S FOR THIS SITE IS A BATCH DETENTION BASIN AND PERMANENT BMP'S HAVE BEEN DESIGNED TO REMOVE AT LEAST 80% OF THE INCREASED TOTAL SUSPENDED SOLIDS (TSS) FOR THE 6.364 ACRES IN ACCORDANCE WITH THE TCEQ'S TECHNICAL GUIDANCE MANUAL (TGM) RG-348 (2005).
- TYPICAL SLOPES ON THIS PROJECT RANGE FROM APPROXIMATELY 0.50% TO 5.00%.

PERMANENT POLLUTION ABATEMENT MEASURES:

- SILT FENCING AND ROCK BERMS, WHERE APPROPRIATE, WILL BE MAINTAINED UNTIL THE ROADWAY, UTILITY, DRAINAGE IMPROVEMENTS, AND BUILDING CONSTRUCTION ARE COMPLETED.
- A BATCH DETENTION BASIN WILL SERVE AS THE PERMANENT BEST MANAGEMENT PRACTICE (BMP) FOR DRAINAGE AREAS "A1" & "C".
- ENERGY DISSIPATORS (TO HELP REDUCE EROSION) WILL BE PROVIDED AT POINTS OF CONCENTRATED DISCHARGE WHERE EXCESSIVE VELOCITIES MAY BE ENCOUNTERED.

NOTES:

- CONTRACTOR SHALL INSTALL AND ESTABLISH VEGETATION FOR SOIL STABILIZATION PRIOR TO SITE CLOSEOUT.
- ALL PERMANENT BMP'S MUST BE CERTIFIED BY A REGISTERED PROFESSIONAL ENGINEER.

THE ENGINEERING SEAL HAS BEEN AFFIXED TO THIS SHEET ONLY FOR THE PURPOSE OF DEMONSTRATING COMPLIANCE WITH THE POLLUTION ABATEMENT SIZING AND TREATMENT REQUIREMENTS OF THE TEXAS COMMISSION ON ENVIRONMENTAL QUALITY'S EDWARDS AQUIFER TECHNICAL GUIDANCE MANUAL.

THIS SHEET HAS BEEN PREPARED FOR PURPOSES OF POLLUTION ABATEMENT ONLY. ALL OTHER CIVIL ENGINEERING RELATED INFORMATION SHOULD BE ACQUIRED FROM THE APPROPRIATE SHEET IN THE CIVIL IMPROVEMENT PLANS.

WPAP  
EXHIBIT 3

NO.	REVISION	DATE





**PAPE-DAWSON  
ENGINEERS**

AUSTIN | SAN ANTONIO | HOUSTON | FORT WORTH | DALLAS  
10801 N. MOPAC EXPY. BLDG. 3, STE 200 | AUSTIN, TX 78759 | 512.454.8711  
TXPE FIRM REGISTRATION #470 | TBPUS FIRM REGISTRATION #10028601

**JARRELL INDUSTRIAL PARK**  
JARRELL, TEXAS


PERMANENT WATER POLLUTION ABATEMENT PLAN

CITY NO.	51570-00
JOB NO.	51570-00
DATE	
DESIGNER	DS
CHECKED	DRAWN_VKB
SHEET	12 OF 14

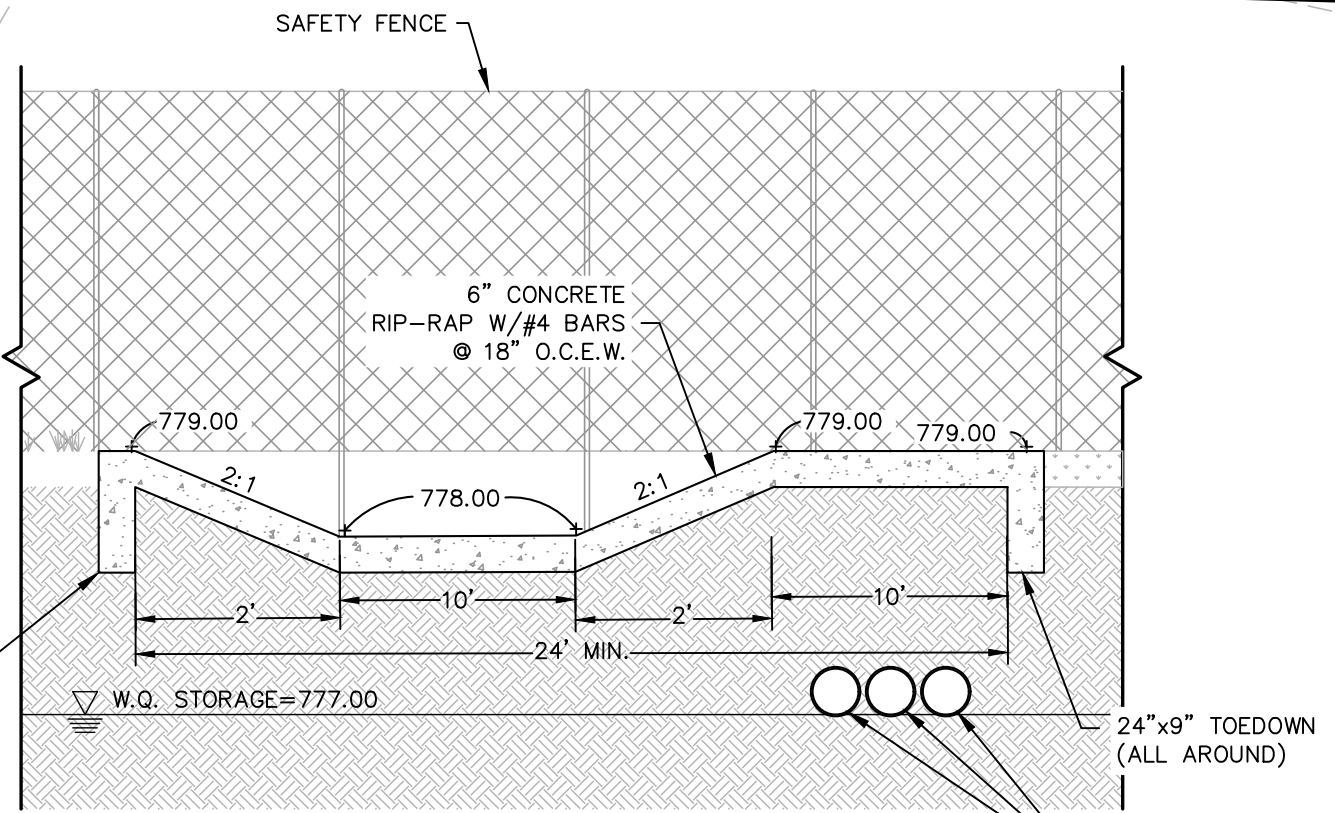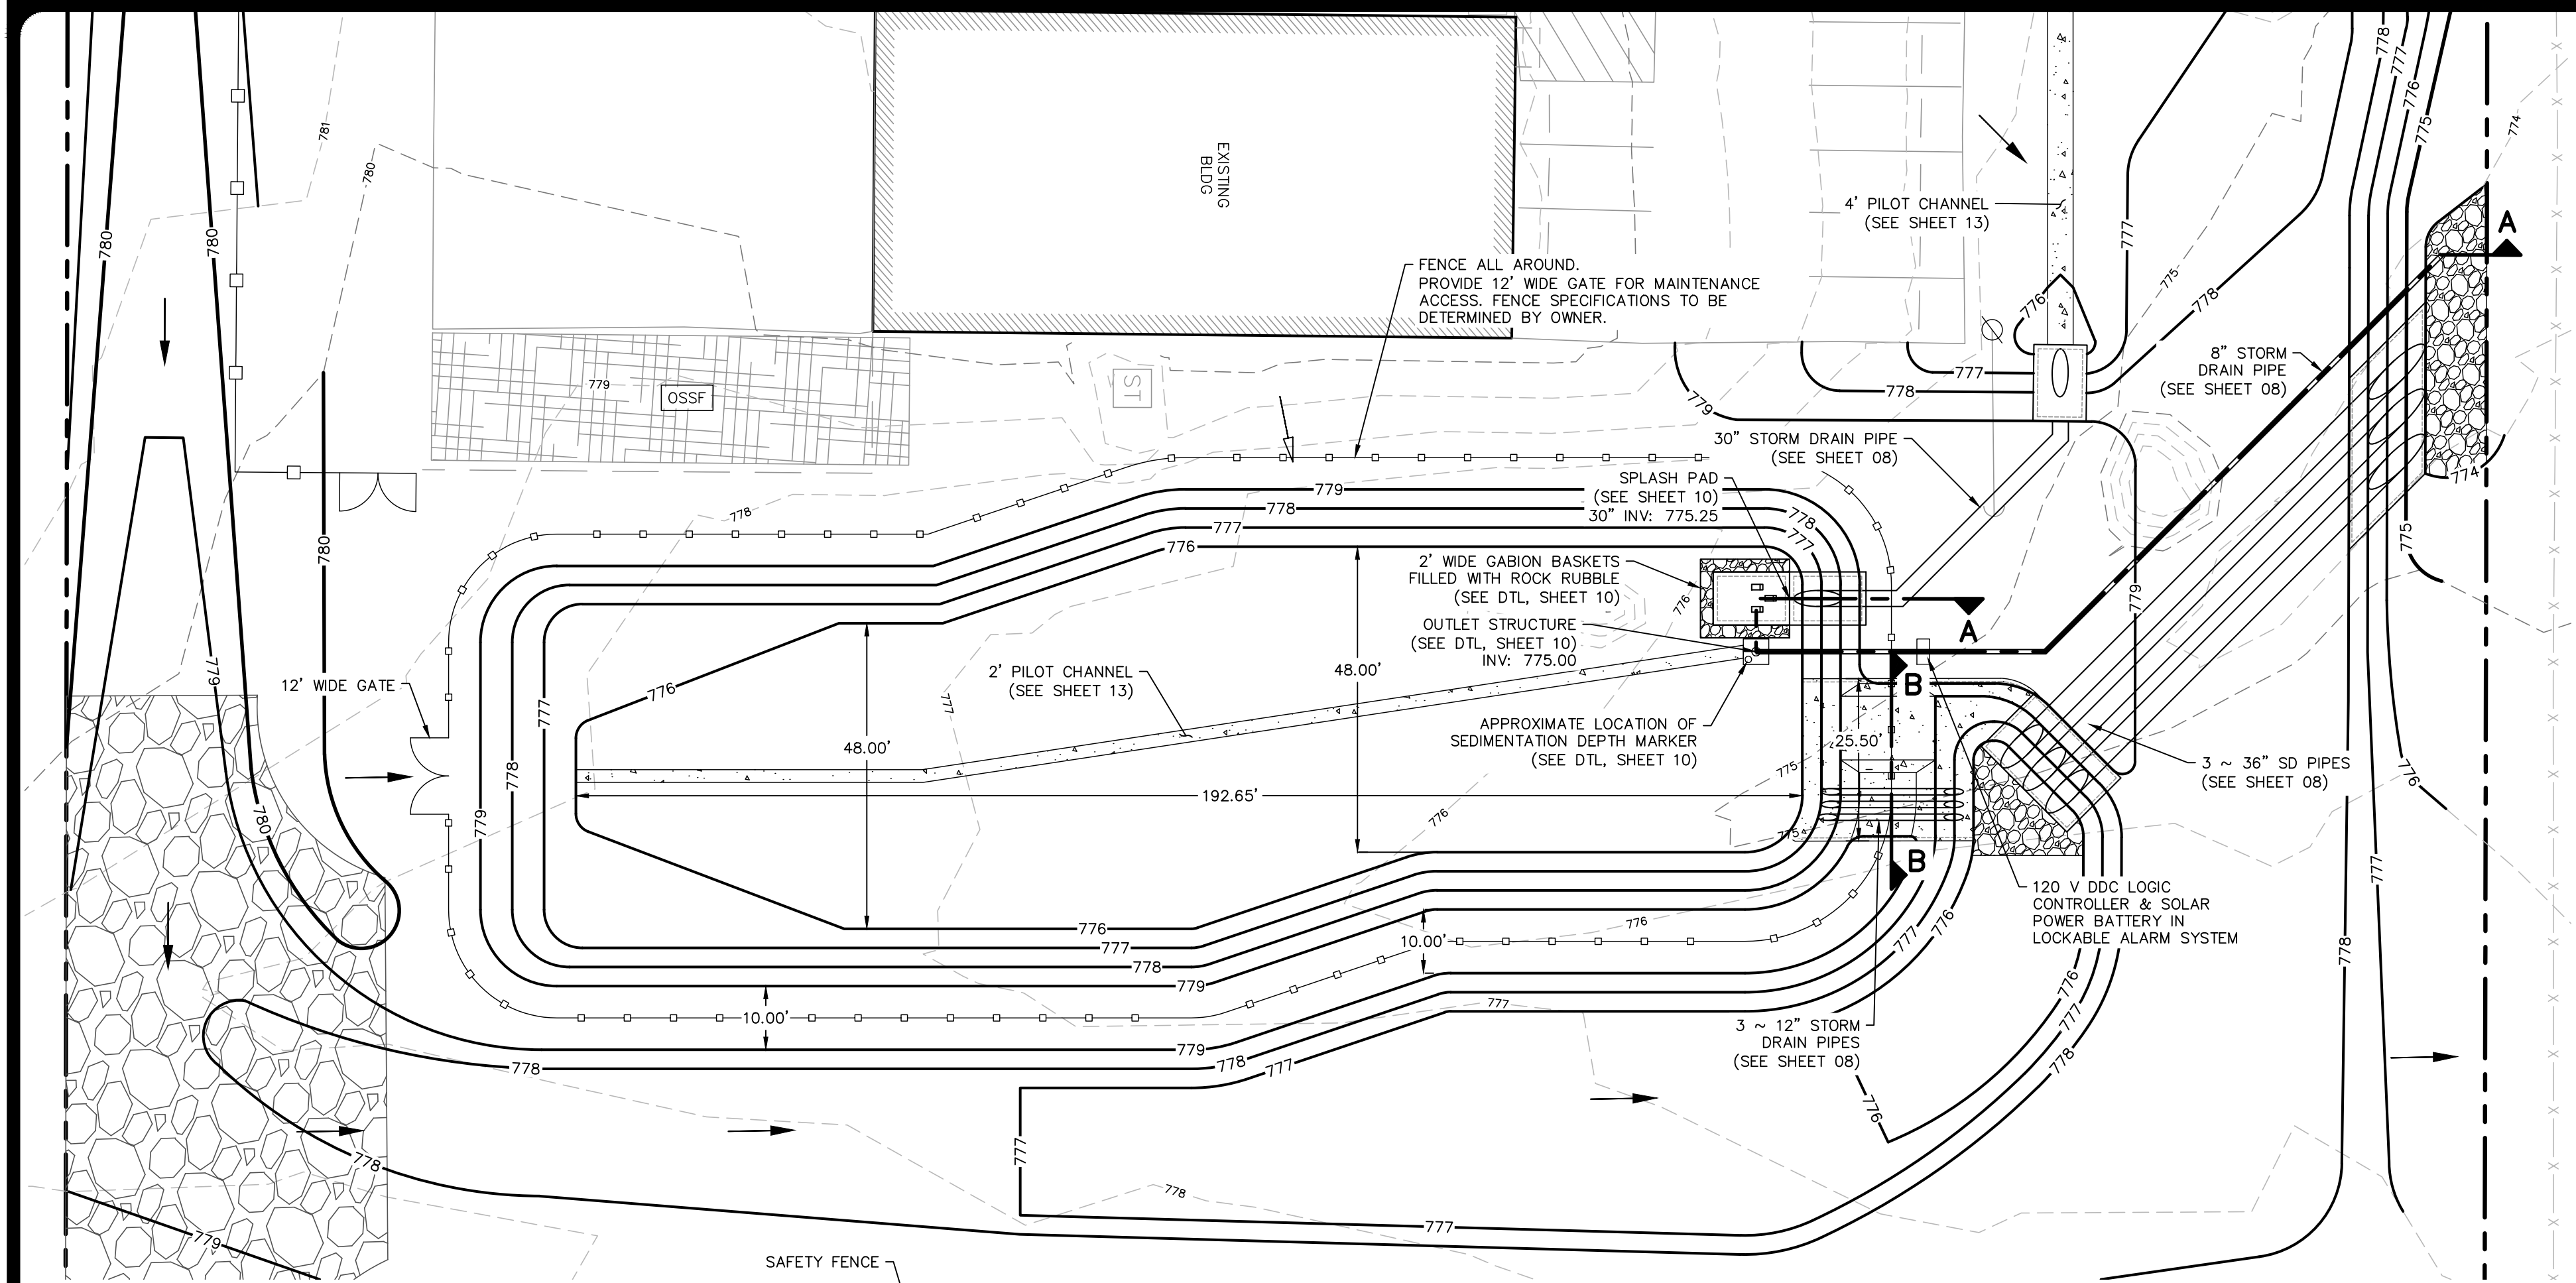

OVERFLOW WEIR CALCULATIONS	
$Q_{25}$	$= (C_w)(L)(h)^{3/2}$
$Q_{25}$	$= 16.79 \text{ cfs}$
$C$	$= 2.60$
$L$	$= 10 \text{ ft}$
$16.79$	$= (2.60)(10)(h)^{3/2}$
$h$	$= 0.75 \text{ ft}$

BASIN DESIGN DATA	
BASIN WATERSHED AREA	$= 213,411 \text{ SF (4.90 AC.)}$
RAINFALL DEPTH	$= 1.38 \text{ IN}$
REQUIRED CAPTURE VOLUME	$= 12,041 \text{ CF}$
BASIN STORM WATER DEPTH	$= 2.0 \text{ FT}$
BASIN CAPTURE VOLUME	$= 13,131 \text{ CF}$

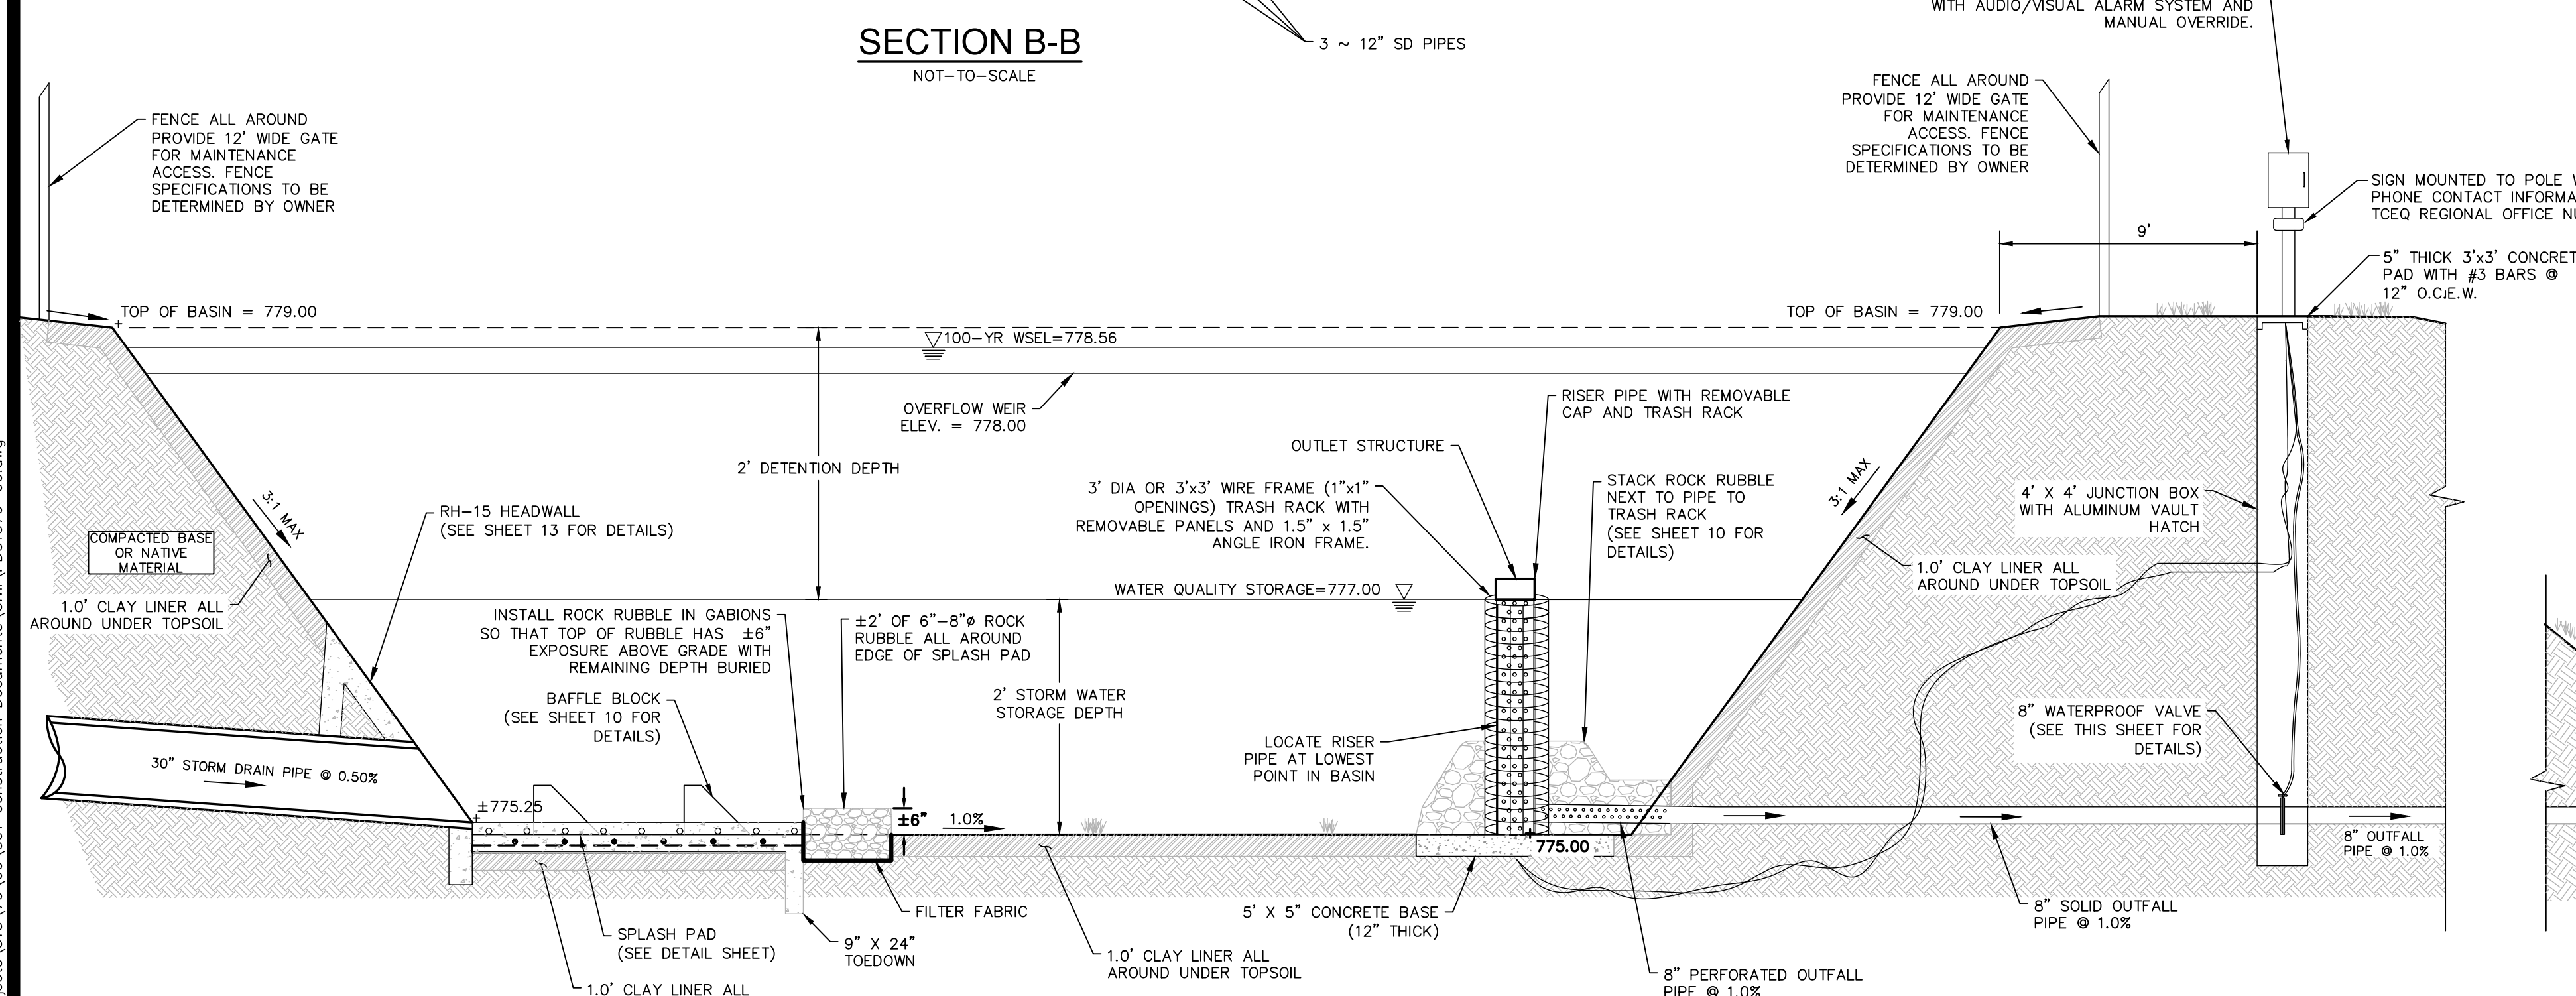

SECTION 'A-A'  
NOT-TO-SCALE

## SUMMARY OF PERMANENT POLLUTION ABATEMENT MEASURES

- SILT FENCING AND ROCK BERMS, WHERE APPROPRIATE, WILL BE MAINTAINED UNTIL ALL UTILITY AND DRAINAGE IMPROVEMENTS ARE COMPLETED.
- ENERGY DISSIPATERS (TO HELP REDUCE EROSION) WILL BE PROVIDED AT POINTS OF CONCENTRATED DISCHARGE WHERE EXCESSIVE VELOCITIES MAY BE ENCOUNTERED.
- THIS PROJECT DOES NOT INCLUDE THE INSTALLATION OF ABOVE GROUND STORAGE TANKS (AST) WITH VOLUME(S) GREATER THAN OR EQUAL TO 500 GALLONS.
- DRAINAGE PATTERNS ARE ILLUSTRATED BY FLOW ARROWS. SLOPES VARY THROUGHOUT THE SITE; TYPICAL SLOPES IN THIS PROJECT WILL RANGE FROM **0.5% TO 3%:1V**.
- PERMANENT BMP'S FOR THIS SITE INCLUDE ONE (1) PROPOSED BATCH DETENTION BASIN, HAS 80% OF THE INCREASED TOTAL SUSPENDED SOLIDS (TSS) FOR THE **6.364 ACRES** IN ACCORDANCE WITH THE TCEQ'S TECHNICAL GUIDANCE MANUAL (TGM) RG-348 (2005).
- FOR DISTURBED AREAS WHERE INSUFFICIENT SOIL EXISTS TO ESTABLISH VEGETATION, CONTRACTOR SHALL PLACE A MINIMUM OF 6" TOPSOIL PRIOR TO RE-VEGETATION.
- TEMPORARY BMP'S WILL BE MAINTAINED UNTIL THE SITE IMPROVEMENTS ARE COMPLETED AND THE SITE HAS BEEN STABILIZED, INCLUDING SUFFICIENT VEGETATION BEING ESTABLISHED IN ACCORDANCE WITH APPLICABLE PROJECT SPECIFICATIONS.
- DURING CONSTRUCTION, TO THE EXTENT PRACTICABLE, CONTRACTOR SHALL MINIMIZE THE AREA OF SOIL DISTURBANCE. AREAS OF DISTURBED SOIL SHALL BE RE-VEGETATED TO STABILIZE SOIL USING SOLID SOD IN A STAGGERED PATTERN. SEE DETAIL ON TEMPORARY POLLUTION ABATEMENT DETAIL SHEET AND REFER TO SECTION 1.3.11 IN TCEQ'S TECHNICAL GUIDANCE MANUAL (TGM) RG-348 (2005). SOD SHOULD BE USED IN CHANNELS AND ON SLOPES > 15%. THE CONTRACTOR MAY SUBSTITUTE THE USE OF SOD WITH THE PLACEMENT OF TOPSOIL AND A FRAGILE SEED BED WITH A PROTECTIVE MATTING OR HYDRAULIC MULCH ALONG WITH WATERING UNTIL VEGETATION IS ESTABLISHED. APPLICATIONS AND PRODUCTS SHALL BE THOSE APPROVED BY TxDOT AS OF FEBRUARY 2001 AND IN COMPLIANCE WITH THE TGM RG-348 (2005). SEED MIXTURE AND/OR GRASS TYPE TO BE DETERMINED BY OWNER AND SHOULD BE IN COMPLIANCE WITH TGM RG-348 (2005) GUIDELINES. IRRIGATION MAY BE REQUIRED IN ORDER TO ESTABLISH SUFFICIENT VEGETATION.
- ALL PERMANENT BMP'S MUST BE CERTIFIED BY A REGISTERED PROFESSIONAL ENGINEER.

## NOTES

- PROJECT RETAINING WALL DESIGNER (TEXAS LICENSED STRUCTURAL ENGINEER) TO PROVIDE A SIGNED AND SEALED SET OF STRUCTURAL RETAINING WALL PLANS, DETAILS AND SPECIFICATION. INSPECT RETAINING WALL CONSTRUCTION DURING BASIN CONSTRUCTION AND PROVIDE RETAINING WALL CONSTRUCTION CERTIFICATION UPON COMPLETION OF THE BASIN.
- UPON COMPLETION OF CONSTRUCTION, AND IN ACCORDANCE WITH TCEQ REGULATIONS, ALL PERMANENT BMP'S MUST BE CERTIFIED BY A REGISTERED PROFESSIONAL ENGINEER.
- ALL AREAS DISTURBED AS PART OF CONSTRUCTION OF BASIN SHALL BE REVEGETATED PRIOR TO COMPLETION.
- BASIN HAS BEEN DESIGNED USING TSS REMOVAL AND BMP SIZING CALCULATIONS AS PER THE TCEQ TGM RG-348 (2005).
- BASIN PLAN DEPICTS MINIMUM INTERIOR DIMENSIONS (LENGTH, WIDTH & HEIGHT FOR TCEQ REVIEW & APPROVAL. ACTUAL STRUCTURAL PLANS FOR CONSTRUCTION TO BE DESIGNED BY STRUCTURAL ENGINEER AT A LATER DATE.
- BASIN DRAWDOWN IS CONTROLLED BY THE 8" PVC PIPE. BASIN DRAWDOWN WILL OCCUR IN APPROXIMATELY 2 HOURS - VALVE THROTTLE FLOW REQUIRED.
- CONTRACTOR TO SET THE VALVE POSITION TO FULLY OPEN. AFTER INSTALLATION, OWNER/OPERATOR TO SET VALVE TO 25 DEGREES TO THROTTLE FLOW SO BASIN DRAINS WITHIN 24 HOURS.
- CONTRACTOR SHALL INSTALL AND ESTABLISH VEGETATION IN BASIN PER BASIN DETAIL SHEET PRIOR TO SITE CLOSEOUT.
- UPON COMPLETION OF CONSTRUCTION, AND IN ACCORDANCE WITH TCEQ REGULATIONS, ALL PERMANENT BMP'S MUST BE CERTIFIED BY A REGISTERED PROFESSIONAL ENGINEER.
- ALL AREAS DISTURBED AS PART OF CONSTRUCTION OF BASIN SHALL BE REVEGETATED PRIOR TO COMPLETION.

## SEQUENCE OF OPERATION

- UPON ACTIVATION OF FLOAT SWITCH, DDC CONTROLLER TO START DETENTION TIMER #1.
- DETENTION TIMER #1 TO BE MANUALLY SET TO 12 HOURS AND TO BE USER ADJUSTABLE.
- WHEN DETENTION TIMER #1 HAS ELAPSED, A 8" BUTTERFLY VALVE IS TO OPEN AND RELEASE DETAINED WATER BASIN.
- UPON DEACTIVATION OF FLOAT SWITCH, DDC CONTROLLER TO START DETENTION TIMER #2.
- DETENTION TIMER #2 TO BE MANUALLY SET TO 7 HOURS AND TO BE USER ADJUSTABLE.
- WHEN DETENTION TIMER #2 HAS ELAPSED, THE 8" BUTTERFLY VALVE IS TO CLOSE.
- VALVE TO BE ACTUATED PERIODICALLY TO SHOW ACTIVE REGARDLESS OF FLOAT SWITCH OPERATION.

## NOTES TO CONTRACTOR

### FOR EACH PHASE OF BATCH DETENTION BASIN CONSTRUCTION

- CONTRACTOR IS ADVISED THAT TCEQ DOES NOT ALLOW CHANGES TO PERMANENT POLLUTION ABATEMENT MEASURES WITHOUT THEIR PRIOR APPROVAL.
- CONTRACTOR SHALL NOTIFY CERTIFYING ENGINEER WHEN BASIN CONSTRUCTION HAS PROCEEDED TO THE FOLLOWING MILESTONES:
  - REINFORCING STEEL FOR BASIN OVERFLOW WALL OR RIP-RAP LINER HAS BEEN SET, CONCRETE HAS NOT BEEN PLACED AND DRAIN AND RISER PIPE IS IN PLACE. CONTRACTOR SHALL PROVIDE ENGINEER WITH SURVEY DATA WHICH DEMONSTRATES THE RISER PIPE HAS BEEN SET AT PROPER ELEVATION AND GRADE.
  - BASIN HAS BEEN COMPLETELY FINISHED INCLUDING SOD OR SEED PLACEMENT ON SIDE SLOPES (WHERE APPLICABLE).
- WORK SHALL NOT CONTINUE ON THE BASIN UNTIL THE ENGINEER HAS HAD AN OPPORTUNITY TO OBSERVE THE STATUS OF CONSTRUCTION AT EACH STAGE. CONTRACTOR SHALL PROVIDE ENGINEER A MINIMUM OF 24 HOURS ADVANCE NOTICE PRIOR TO TIME THE BASIN WILL BE AT THE REQUIRED STAGE.
- UPON SUBSTANTIAL COMPLETION, OR AS REQUESTED BY ENGINEER, CONTRACTOR TO PROVIDE CERTIFYING ENGINEER WITH FIELD SHOTS VERIFYING ELEVATIONS OF THE FOLLOWING:
  - TOP OF BANK/WALL AT EACH CORNER OF BASIN
  - TOE OF SLOPE AT EACH CORNER OF BASIN (INSIDE BASIN TOE)
  - SPLASH PAD/INLET PIPES
- BEFORE FINAL ACCEPTANCE OF CONSTRUCTION BY THE OWNER, THE CONTRACTOR WILL REMOVE ALL TRASH, DEBRIS, AND ACCUMULATED SILT FROM THE BASINS AND REESTABLISH THEM TO THE PROPER OPERATING CONDITION.


## LINER CONSTRUCTION REQUIREMENTS

ALL LINER CONSTRUCTION AND QA/QC ACTIVITIES MUST BE UNDER THE SUPERVISION OF AN INDEPENDENT LICENSED ENGINEER WITH EXPERIENCE IN GEOTECHNICAL ENGINEERING. THE ENGINEER OR DESIGNATED REPRESENTATIVE MUST BE ON SITE DURING ALL SIGNIFICANT LINER CONSTRUCTION ACTIVITIES, INCLUDING BUT NOT LIMITED TO:

- AT THE BEGINNING OF LINER CONSTRUCTION TO INSPECT SUBGRADE ACCEPTABILITY;
- DURING THE PROCESSING OF CLAY LINER MATERIAL FOR PLACEMENT TO ENSURE ADEQUATE MOISTURE CONDITIONING AND PARTICLE SIZE REDUCTION;
- DURING PLACEMENT OF CLAY LINER LIFTS TO ENSURE 6 INCH MAXIMUM LIFT DEPTH IS NOT EXCEEDED AND COMPACTION IS SUFFICIENT;
- DURING ALL GEOMEMBRANE INSTALLATION;
- DURING CLAY AND GEOMEMBRANE LINER TESTING;
- PRIOR TO PLACEMENT OF SUCCESSIVE CLAY LIFTS TO VERIFY ACCEPTABILITY OF PRIOR LIFT SURFACE;
- DURING CONSTRUCTION OF PENETRATIONS AND ANY OTHER CONSTRUCTION THAT WILL AFFECT THE INTEGRITY OF THE LINER (ACCESS RAMPS, PUMP PADS, ETC.);
- DURING PLACEMENT OF PROTECTIVE SOIL LAYER.
- FOLLOWING COMPLETION OF THE LINER CONSTRUCTION, SLR, GCLR, OR GLR (AS APPLICABLE FOR THE TYPE OF LINER INSTALLED) MUST BE PREPARED UNDER THE DIRECTION OF AND SEALED BY THE ENGINEER AND SUBMITTED TO THE CITY. THE REPORT IS INTENDED TO PROVIDE DOCUMENTATION OF ALL INSTALLATION METHODS AND TESTING PROCEDURES CONDUCTED DURING THE INSTALLATION OF THE LINER AND TO PROVIDE EVIDENCE THAT THE LINER WAS CONSTRUCTED IN ACCORDANCE WITH THE CONSTRUCTION PLANS, TECHNICAL SPECIFICATIONS AND QA/QC PLAN.


## GENERAL NOTES:

- THE LOCATIONS OF EXISTING UNDERGROUND UTILITIES ARE SHOWN IN AN APPROXIMATE MANNER ONLY AND HAVE NOT BEEN INDEPENDENTLY VERIFIED BY THE OWNER OR ITS REPRESENTATIVE. THE CONTRACTOR SHALL DETERMINE THE EXACT LOCATION OF ALL EXISTING UTILITIES BEFORE COMMENCING WORK, AND AGREES TO BE FULLY RESPONSIBLE FOR ANY AND ALL DAMAGES WHICH MIGHT BE ASSOCIATED BY THE CONTRACTOR'S FAILURE TO EXACTLY LOCATE AND PRESERVE ANY AND ALL UNDERGROUND UTILITIES.
- ALL RCP IS CLASS III UNLESS OTHERWISE NOTED.
- SEE NOTES SHEET 12 FOR CONTOUR AND SURVEY INFORMATION.

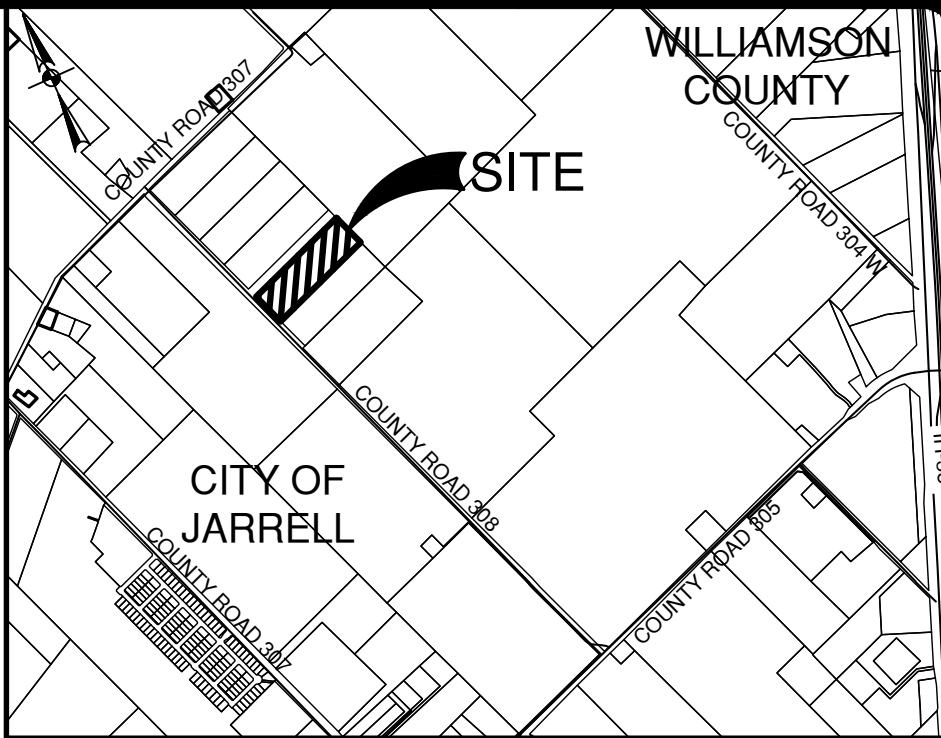

## LOCATION MAP

NOT-TO-SCALE

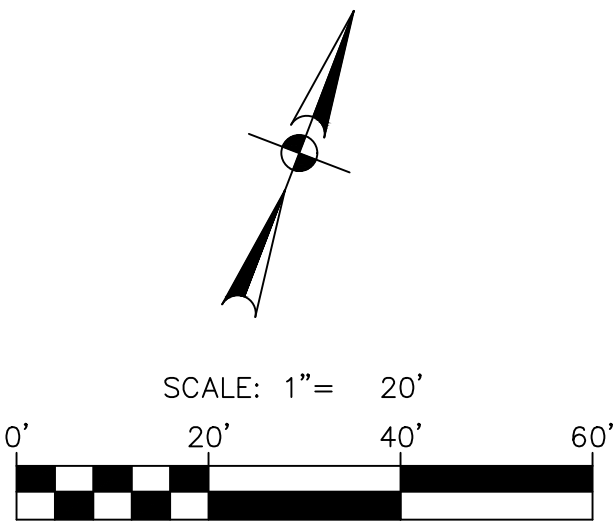

## LEGEND

---	PROPERTY LINE
- - - - -	EXISTING CONTOURS MAJOR
- - - - -	EXISTING CONTOURS MINOR
- - - - -	PROPOSED CONTOURS
+1000	PROPOSED SPOT ELEVATION
→	FLOW ARROW (EXISTING)
→	FLOW ARROW (PROPOSED)
—O—	EXISTING OVERHEAD ELECTRIC
—C—	CURB INLET
—J—	JUNCTION BOX
—G—	WITH GRATE
—S—	PROPOSED STORM DRAINAGE

**PAPE-DAWSON ENGINEERS**

AUSTIN | SAN ANTONIO | HOUSTON | FORT WORTH | DALLAS  
10801 N. MOPAC EXPY, BLDG. 3, STE. 200 | AUSTIN, TX 78759 | 512.454.8711  
TYPE FIRM REGISTRATION #470 | TBPUS FIRM REGISTRATION #1008801

**JARRELL INDUSTRIAL PARK**  
JARRELL, TEXAS

BATCH DETENTION BASIN PLAN

CITY NO. \_\_\_\_\_  
JOB NO. 51570-00  
DATE \_\_\_\_\_  
DESIGNER DS  
CHECKED DRAWN VKB  
SHEET 09 OF 14


THE ENGINEERING SEAL HAS BEEN AFFIXED TO THIS SHEET ONLY FOR THE PURPOSE OF DEMONSTRATING COMPLIANCE WITH THE POLLUTION ABATEMENT SIZING AND TREATMENT REQUIREMENTS OF THE TEXAS COMMISSION ON ENVIRONMENTAL QUALITY'S EDWARDS AQUIFER TECHNICAL GUIDANCE MANUAL.

THIS SHEET HAS BEEN PREPARED FOR PURPOSES OF POLLUTION ABATEMENT ONLY. ALL OTHER CIVIL ENGINEERING RELATED INFORMATION SHOULD BE ACQUIRED FROM THE APPROPRIATE SHEET IN THE CIVIL IMPROVEMENT PLANS.

**WPAP**  
**EXHIBIT 4**


Date: Feb 19, 2025 11:59am User ID: jveloz  
 File: H:\Projects\515170\001 Construction Documents\Civil\DT51570-00.dwg

THIS DOCUMENT HAS BEEN PRODUCED FROM MATERIAL THAT WAS STORED AND/OR TRANSMITTED ELECTRONICALLY AND MAY HAVE BEEN INADVERTENTLY ALTERED. RELY ONLY ON FINAL HARDCOPY MATERIALS BEARING THE CONSULTANT'S ORIGINAL SIGNATURE AND SEAL.




LAY SOD IN A STAGGERED PATTERN. BUTT THE STRIPS TIGHTLY AGAINST EACH OTHER. DO NOT LEAVE SPACES AND DO NOT OVERLAP. A SHARPENED MASON'S TROWEL IS A HANDY TOOL FOR TUCKING DOWN THE ENDS AND TRIMMING PIECES.

BUTTING - ANGLED ENDS CAUSED BY THE AUTOMATIC SOD CUTTER MUST BE MATCHED CORRECTLY.



CORRECT



INCORRECT

### SOD INSTALLATION

### MATERIALS


- SOD SHOULD BE MACHINE CUT AT A UNIFORM SOIL THICKNESS OF 3/4" INCH ( $\pm$  1/4" INCH) AT THE TIME OF CUTTING. THIS THICKNESS SHOULD EXCLUDE SHOOT GROWTH AND THATCH.
- PIECES OF SOD SHOULD BE CUT TO THE SUPPLIER'S STANDARD WIDTH AND LENGTH, WITH A MAXIMUM ALLOWABLE DEVIATION IN ANY DIMENSION OF 5% TORN OR UNEVEN PADS SHOULD NOT BE ACCEPTABLE.
- STANDARD SIZE SECTIONS OF SOD SHOULD BE STRONG ENOUGH TO SUPPORT THEIR OWN WEIGHT AND RETAIN THEIR SIZE AND SHAPE WHEN SUSPENDED FROM A FIRM GRASP ON ONE END OF THE SECTION.
- SOD SHOULD BE HARVESTED, DELIVERED, AND INSTALLED WITHIN A PERIOD OF 36 HOURS.

### SITE PREPARATION


- PRIOR TO SOIL PREPARATION, AREAS TO BE SODDED SHOULD BE BROUGHT TO FINAL GRADE IN ACCORDANCE WITH THE APPROVED PLAN.
- THE SURFACE SHOULD BE CLEARED OF ALL TRASH, DEBRIS AND OF ALL ROOTS, BRUSH, WIRE, GRADE STAKES AND OTHER OBJECTS THAT WOULD INTERFERE WITH PLANTING, FERTILIZING OR MAINTENANCE OPERATIONS.
- FERTILIZE ACCORDING TO SOIL TESTS. FERTILIZER NEEDS CAN BE DETERMINED BY A SOIL TESTING LABORATORY OR REGIONAL RECOMMENDATIONS CAN BE MADE BY COUNTY AGRICULTURAL EXTENSION AGENTS. FERTILIZER SHOULD BE WORKED INTO THE SOIL TO A DEPTH OF 3 INCHES WITH A DISC, SPRINGTOOTH HARROW OR OTHER SUITABLE EQUIPMENT. ON SLOPING LAND, THE FINAL HARROWING OR DISING OPERATION SHOULD BE ON THE CONTOUR.

### INSTALLATION IN CHANNELS

- SOD STRIPS IN WATERWAYS SHOULD BE LAID PERPENDICULAR TO THE DIRECTION OF FLOW. CARE SHOULD BE TAKEN TO BUTT ENDS OF STRIPS TIGHTLY (SEE FIGURE ABOVE).
- AFTER ROLLING OR TAMPING, SOD SHOULD BE PEGGED OR STAPLED TO RESIST WASHOUT DURING THE ESTABLISHMENT PERIOD. MESH OR OTHER NETTING MAY BE PEGGED OVER THE SOD FOR EXTRA PROTECTION IN CRITICAL AREAS.


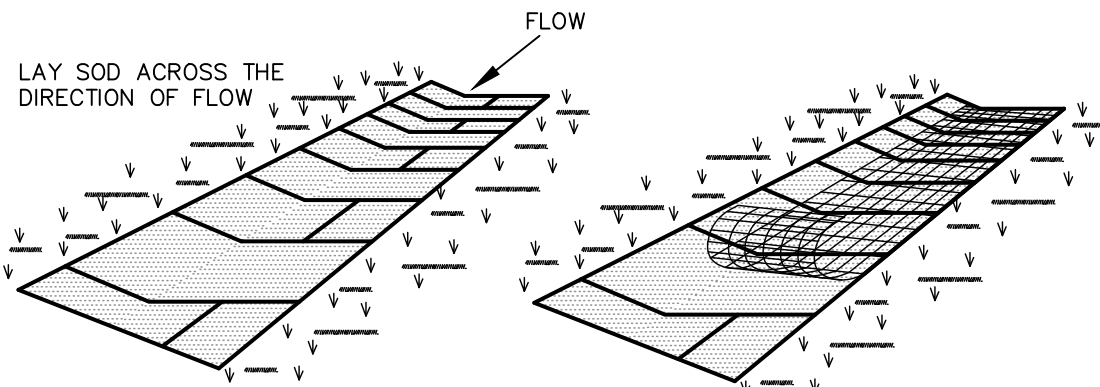


IN CRITICAL AREAS, SECURE SOD WITH NETTING. USE STAPLES.

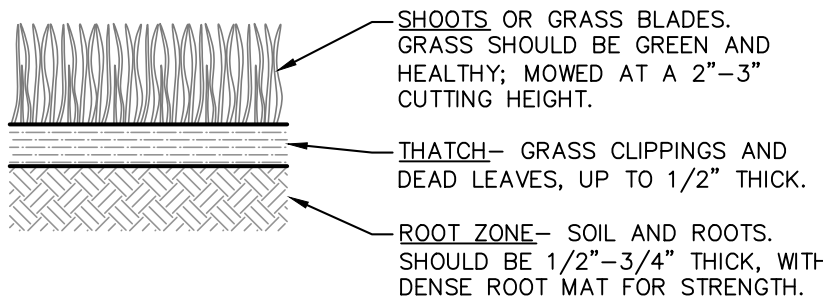

### APPEARANCE OF GOOD SOD

- NOTES:
- ROLL SOD IMMEDIATELY TO ACHIEVE FIRM CONTACT WITH THE SOIL.
  - WATER TO A DEPTH OF 4" AS NEEDED. WATER WELL AS SOON AS THE SOD IS LAID.
  - MOW WHEN THE SOD IS ESTABLISHED - IN 2-3 WEEKS. SET THE MOWER HIGH (2"-3").



USE PEGS OR STAPLES TO FASTEN SOD FIRMLY - AT THE ENDS OF STRIPS AND IN THE CENTER, OR EVERY 3-4 FEET IF THE STRIPS ARE LONG. WHEN READY TO MOW, DRIVE PEGS OR STAPLES FLUSH WITH THE GROUND.

### GENERAL INSTALLATION (VA. DEPT. OF CONSERVATION, 1992)


- SOD SHOULD NOT BE CUT OR LAID IN EXCESSIVELY WET OR DRY WEATHER. SOD ALSO SHOULD NOT BE LAID ON SOIL SURFACES THAT ARE FROZEN.
- DURING PERIODS OF HIGH TEMPERATURE, THE SOIL SHOULD BE LIGHTLY IRRIGATED IMMEDIATELY PRIOR TO LAYING THE SOD, TO COOL THE SOIL AND REDUCE ROOT BURNING AND DIEBACK.
- THE FIRST ROW OF SOD SHOULD BE LAID IN A STRAIGHT LINE WITH SUBSEQUENT ROWS PLACED PARALLEL TO AND BUTTING TIGHTLY AGAINST EACH OTHER. LATERAL JOINTS SHOULD BE STAGGERED TO PROMOTE MORE UNIFORM GROWTH AND STRENGTH. CARE SHOULD BE EXERCISED TO ENSURE THAT SOD IS NOT STRETCHED OR OVERLAPPED AND THAT ALL JOINTS ARE BUTTED TIGHT IN ORDER TO PREVENT VOIDS WHICH WOULD CAUSE DRYING OF THE ROOTS (SEE FIGURE ABOVE).
- ON SLOPES 3:1 OR GREATER, OR WHEREVER EROSION MAY BE A PROBLEM, SOD SHOULD BE LAID WITH STAGGERED JOINTS AND SECURED BY STAPLING OR OTHER APPROVED METHODS. SOD SHOULD BE INSTALLED WITH THE LENGTH PERPENDICULAR TO THE SLOPE (ON CONTOUR).
- AS SODDING OF CLEARLY DEFINED AREAS IS COMPLETED, SOD SHOULD BE ROLLED OR TAMPED TO PROVIDE FIRM CONTACT BETWEEN ROOTS AND SOIL.
- AFTER ROLLING, SOD SHOULD BE IRRIGATED TO A DEPTH SUFFICIENT THAT THE UNDERSIDE OF THE SOD PAD AND THE SOIL 4 INCHES BELOW THE SOD IS THOROUGHLY WET.
- UNTIL SUCH TIME A GOOD ROOT SYSTEM BECOMES DEVELOPED, IN THE ABSENCE OF ADEQUATE RAINFALL, WATERING SHOULD BE PERFORMED AS OFTEN AS NECESSARY TO MAINTAIN MOIST SOIL TO A DEPTH OF AT LEAST 4 INCHES.
- THE FIRST MOWING SHOULD NOT BE ATTEMPTED UNTIL THE SOD IS FIRMLY ROOTED, USUALLY 2-3 WEEKS. NOT MORE THAN ONE THIRD OF THE GRASS LEAF SHOULD BE REMOVED AT ANY ONE CUTTING.

### INSPECTION AND MAINTENANCE GUIDELINES

- SOD SHOULD BE INSPECTED WEEKLY AND AFTER EACH RAIN EVENT TO LOCATE AND REPAIR ANY DAMAGE.
- DAMAGE FROM STORMS OR NORMAL CONSTRUCTION ACTIVITIES SUCH AS TIRE RUTS OR DISTURBANCE OF SWALE STABILIZATION SHOULD BE REPAIRED AS SOON AS PRACTICAL.

### SOD INSTALLATION DETAIL


NOT-TO-SCALE

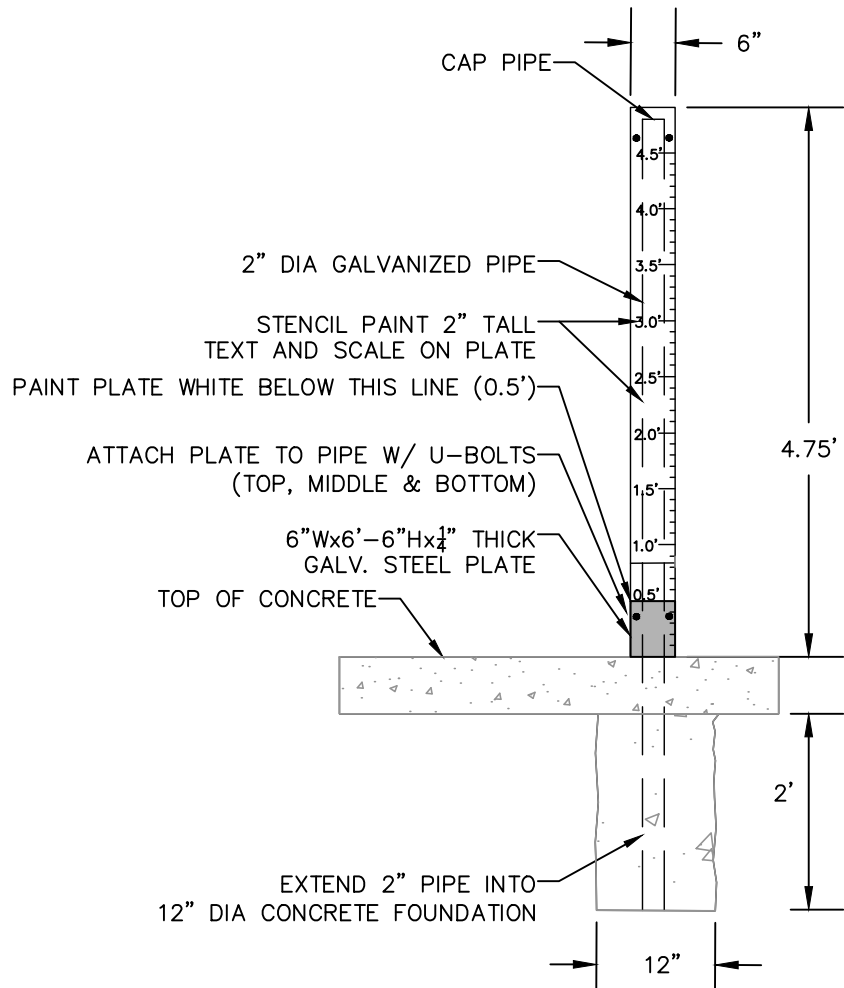

### SEDIMENT DEPTH MARKER


NOT-TO-SCALE

NOTE: ONCE SEDIMENT IS ABOVE THE 6" DESIGNATION, THE BASIN MUST BE CLEANED OUT TO DESIGN ELEVATIONS AND VOLUMES PER PLAN.

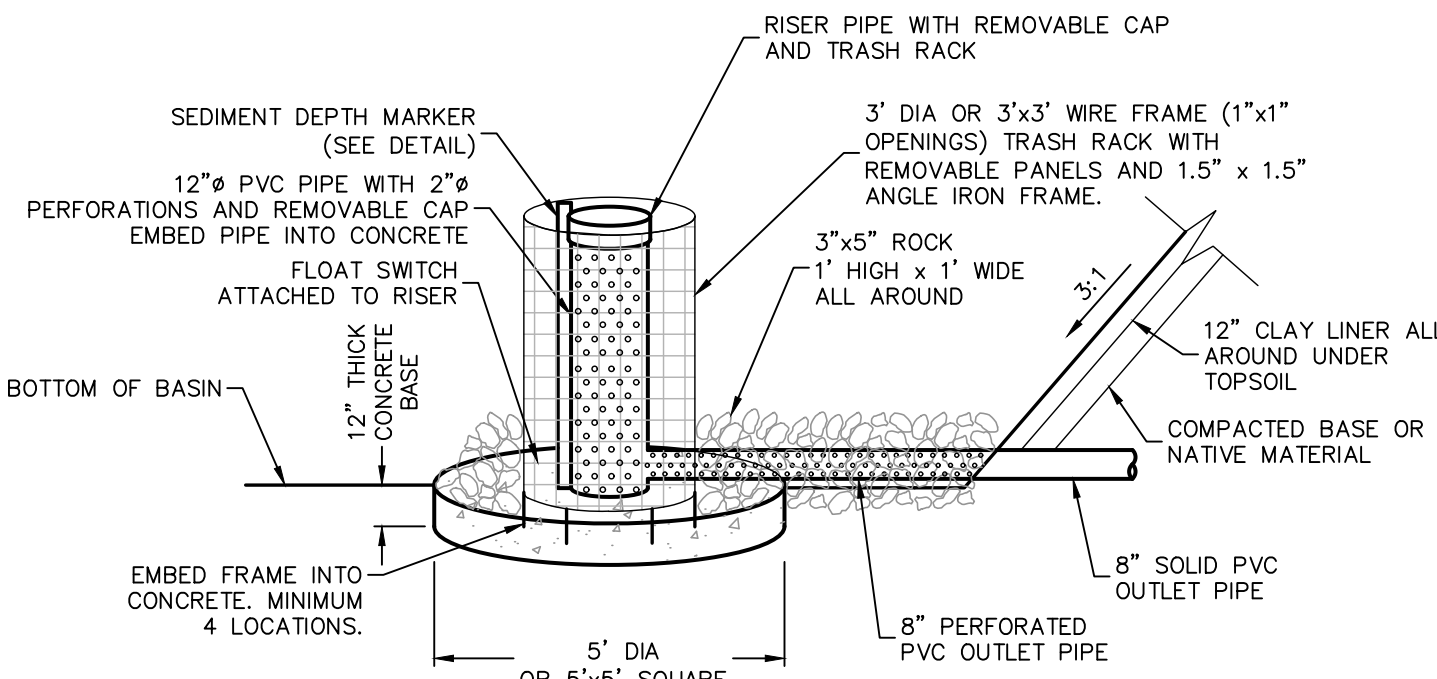


### OUTLET STRUCTURE DETAIL WITH OUTFALL PIPE

NOT-TO-SCALE

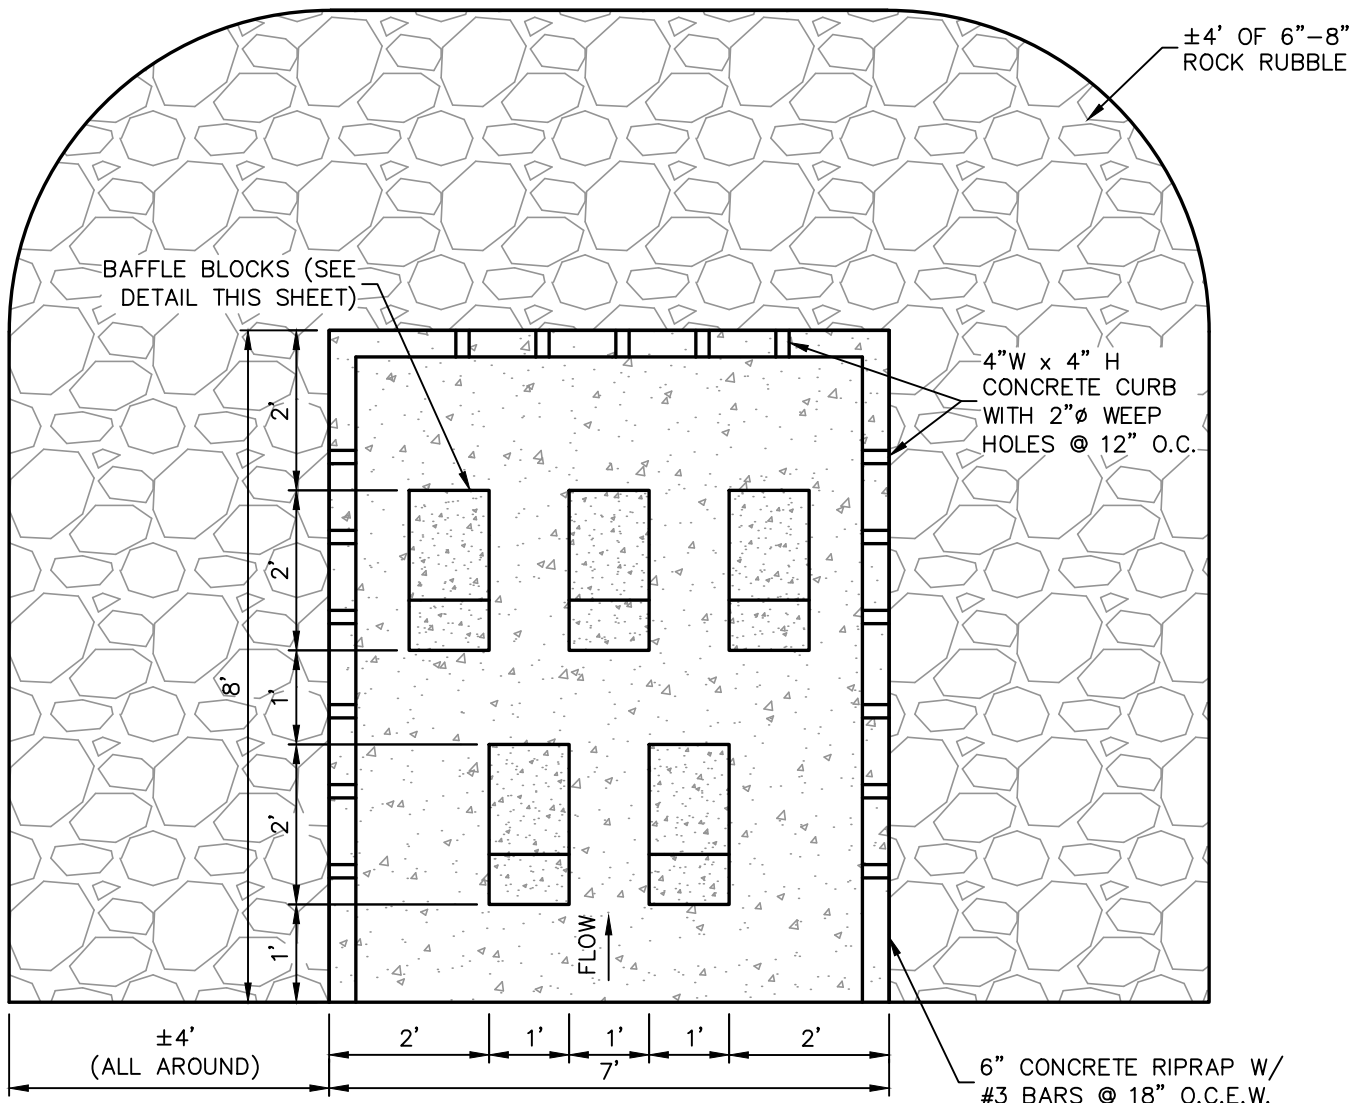


### SPLASH PAD DETAIL

NOT-TO-SCALE

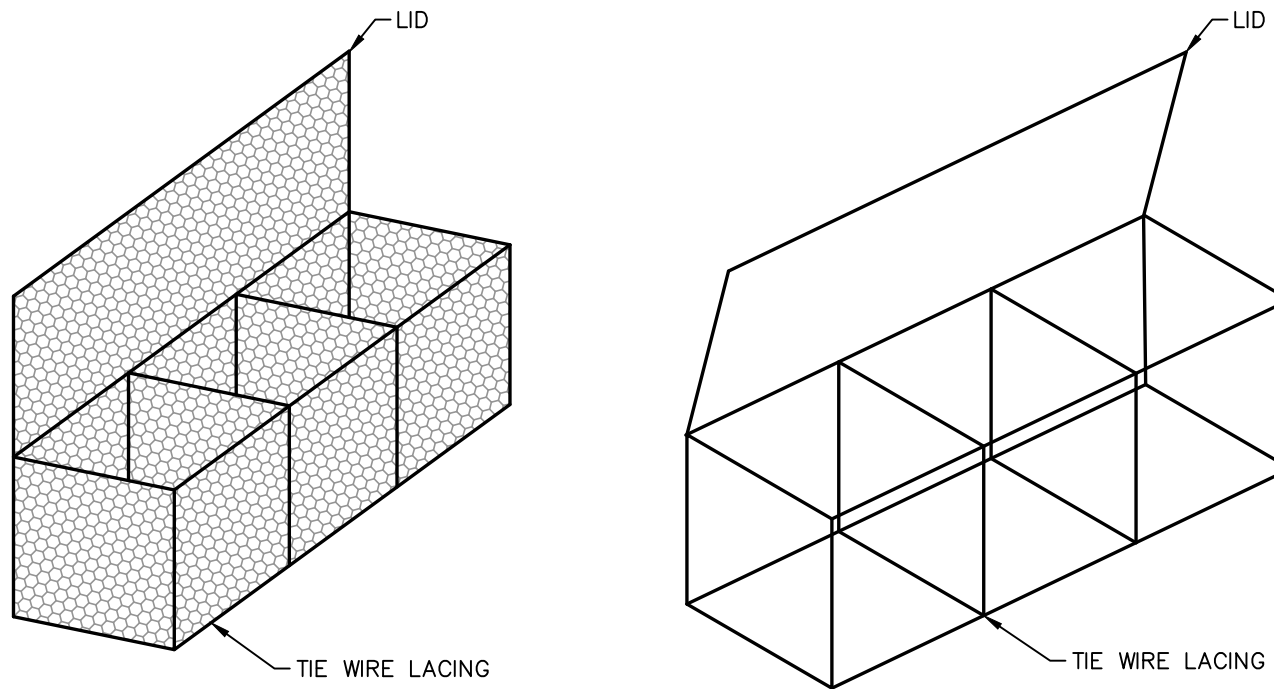

### TYPICAL ASSEMBLED GABION BASKET DETAIL

NOT-TO-SCALE

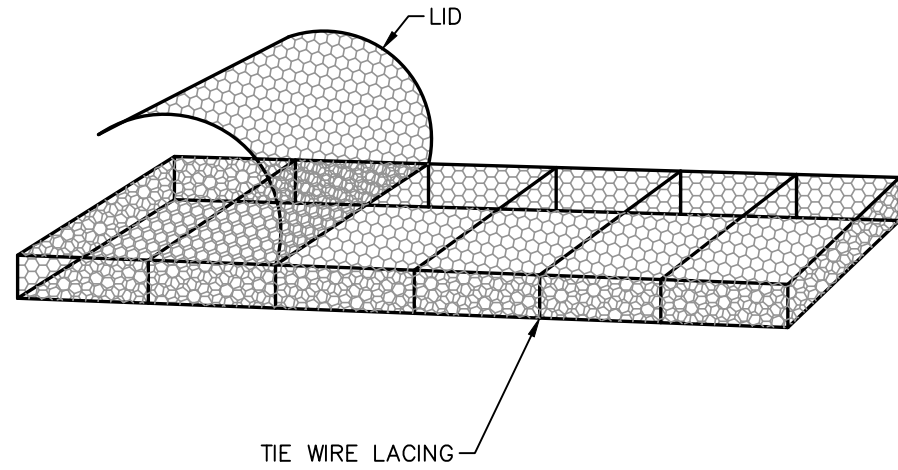

### TYPICAL ASSEMBLED GABION MATTRESS DETAIL

NOT-TO-SCALE

### FILTER FABRIC SPECIFICATIONS

THE SEPARATION LAYER BETWEEN THE SAND FILTER AND GRAVEL LAYERS SHALL BE A DRAINAGE MATTING CONSISTING OF NON-WOVEN FILTER FABRIC MEETING THE FOLLOWING SPECIFICATIONS:

PROPERTY	TEST METHOD	SPECIFICATION
WEIGHT (OZ/SY)	ASTM D 5261	$\geq 4.0$
GRAB STRENGTH (LBS.)	ASTM D 4632	$\geq 90$
ELONGATIONS (%)	ASTM D 4632	$\leq 55$
TRAPEZOID TEAR (LBS)	ASTM D 4533	$\geq 50$
CBR PUNCTURE STRENGTH (LBS)	ASTM D 6241	$\geq 300$
UV RESISTANCE AFTER 500 HRS. (%)	ASTM D 4355	$\geq 70$
	ASTM D 4751	70-80
FLOW RATE (GPM/SF)	ASTM D 4491	$\geq 90$

FABRIC OVERLAP SHALL BE A MINIMUM OF 24". ALL OVERLAPS SHALL BE WIRE TIED AT A MAXIMUM OF 36" INTERVALS

### CLAY LINER SPECIFICATIONS

PROPERTY	TEST METHOD	SPECIFICATION
PERMEABILITY (CM/SEC)	ASTM D 2434	$1 \times 10^{-6}$
PLASTICITY INDEX OF CLAY (%)	ASTM D 423/D 424	NOT LESS THAN 15
LIQUID LIMIT OF CLAY (%)	ASTM D 2216	NOT LESS THAN 30
CLAY PARTICLES PASSING (%)	ASTM D 422	NOT LESS THAN 30
CLAY COMPACTION (%)	ASTM D 2216	95% OF STANDARD PROCTOR DENSITY

NOTES:  
1. THE CLAY LINER SHALL HAVE A MINIMUM THICKNESS OF TWELVE (12) INCHES.

### GRADING AND DRAINAGE GENERAL NOTES:

- ALL GRADES AND CONTOURS SHOWN ARE FINAL, TOP OF FINISHED SURFACE ELEVATIONS.
- POSITIVE DRAINAGE SHALL BE MAINTAINED ON ALL SURFACE AREAS WITHIN THE SCOPE OF THIS PROJECT. CONTRACTOR SHOULD TAKE PRECAUTIONS NOT TO ALLOW PONDING OF WATER.
- NO ABRUPT CHANGE OF GRADE SHALL OCCUR.
- ALL DISTURBED AREAS SHALL BE REVEGETATED, BY THE CONTRACTOR, IN ACCORDANCE WITH PROJECT SPECIFICATIONS AND LANDSCAPING PLANS.
- THE CONTRACTOR WILL BE RESPONSIBLE FOR DETERMINING EXACT LOCATION OF ALL UTILITIES AND DRAINAGE STRUCTURES WHETHER SHOWN ON THE PLANS OR NOT. THE CONTRACTOR SHALL UNCOVER EXISTING UTILITIES PRIOR TO CONSTRUCTION TO VERIFY SIZE, GRADE, AND LOCATION. THE CONTRACTOR SHALL NOTIFY THE ENGINEER IMMEDIATELY OF ANY DEVIATIONS FROM PLANS PRIOR TO BEGINNING CONSTRUCTION. ANY DAMAGE TO EXISTING UTILITIES, WHETHER SHOWN ON THE PLANS OR NOT, SHALL BE THE CONTRACTOR'S RESPONSIBILITY TO REPAIR, AT HIS EXPENSE.
- ALL MATERIALS AND CONSTRUCTION PROCEDURES WITHIN THE SCOPE OF THIS CONTRACT WHERE NOT SPECIFICALLY COVERED IN THE PROJECT SPECIFICATIONS SHALL CONFORM TO ALL APPLICABLE CITY OF BULVERDE SPECIFICATIONS FOR PUBLIC WORKS CONSTRUCTION.
- CONTRACTOR SHALL BE RESPONSIBLE FOR RESTORING TO ORIGINAL, OR BETTER CONDITION, TO ANY DAMAGES DONE TO EXISTING BUILDINGS, UTILITIES, PAVEMENT, CURBS, SIDEWALKS OR DRIVEWAYS.
- THE CONTRACTOR SHALL BE RESPONSIBLE FOR COORDINATING WITH ALL NECESSARY UTILITY COMPANIES FOR PROVIDING TEMPORARY UTILITY SERVICES DURING CONSTRUCTION.
- THE CONTRACTOR SHALL SAW CUT EXISTING PAVEMENT AT NEW PAVEMENT AND CURB JUNCTURES. NO JAGGED OR IRREGULAR CUTS IN PAVEMENT WILL BE ALLOWED OR ACCEPTED.
- THE CONTRACTOR SHALL BE RESPONSIBLE FOR ACQUIRING ALL PERMITS, TESTS, APPROVALS, AND ACCEPTANCES REQUIRED TO COMPLETE CONSTRUCTION OF THIS PROJECT.
- ALL EXCAVATION IS UNCLASSIFIED.
- SEE CIVIL DETAIL SHEETS FOR APPLICABLE DETAILS.
- REFER TO PROJECT SPECIFICATIONS FOR ADDITIONAL SPECIFICATIONS AND CONTRACT INFORMATION.
- REFER TO GEOTECHNICAL REPORT FOR SUBSURFACE INFORMATION AND CONSTRUCTION INFORMATION.
- ALL PROPOSED SPOT ELEVATIONS HAVE BEEN TRUNCATED TO SAVE SPACE ON THIS PLAN.

### NOTES:

- CONTRACTOR SHALL INSTALL AND ESTABLISH VEGETATION IN BASINS PER BASIN DETAIL SHEET PRIOR TO SITE CLOSEOUT.
- UPON COMPLETION OF CONSTRUCTION, AND IN ACCORDANCE WITH TCEQ REGULATIONS, ALL PERMANENT BMP'S (FILTERSTRIPS AND BASINS) MUST BE CERTIFIED BY A REGISTERED PROFESSIONAL ENGINEER.
- ALL AREAS DISTURBED AS PART OF CONSTRUCTION OF BASINS SHALL BE REVEGETATED PRIOR TO COMPLETION.

### NOTES

- CONTRACTOR SHALL ENGAGE A TEXAS LICENSED STRUCTURAL ENGINEER TO PROVIDE A SIGNED AND SEALED SET OF STRUCTURAL PLANS, DETAILS AND SPECIFICATION FOR THE STRUCTURAL COMPONENTS OF THE POLLUTION ABATEMENT BASIN INCLUDING INLET DISCHARGE AND BYPASS COMPONENTS. CONTRACTOR SHALL ALSO PROVIDE FOR STRUCTURAL ENGINEER'S INSPECTION DURING BASIN CONSTRUCTION AND STRUCTURAL ENGINEER'S CONSTRUCTION CERTIFICATION UPON COMPLETION OF BASIN.
- UPON COMPLETION OF CONSTRUCTION, AND IN ACCORDANCE WITH TCEQ REGULATIONS, ALL PERMANENT BMP'S MUST BE CERTIFIED BY A REGISTERED PROFESSIONAL ENGINEER.
- ALL AREAS DISTURBED AS PART OF CONSTRUCTION OF BASIN SHALL BE REVEGETATED PRIOR TO COMPLETION.
- BASIN HAS BEEN DESIGNED USING TSS REMOVAL AND BMP SIZING CALCULATIONS AS PER THE TCEQ TGM RG-348 (2005).
- BASIN PLAN DEPICTS MINIMUM INTERIOR DIMENSIONS (LENGTH, WIDTH & HEIGHT FOR TCEQ REVIEW & APPROVAL. ACTUAL STRUCTURAL PLANS FOR CONSTRUCTION TO BE DESIGNED BY STRUCTURAL ENGINEER AT A LATER DATE.
- CONTRACTOR TO SET THE VALVE POSITION TO FULLY OPEN.

THE ENGINEERING SEAL HAS BEEN AFFIXED TO THIS SHEET ONLY FOR THE PURPOSE OF DEMONSTRATING COMPLIANCE WITH THE POLLUTION ABATEMENT SIZING AND TREATMENT REQUIREMENTS OF THE TEXAS COMMISSION ON ENVIRONMENTAL QUALITY'S EDWARDS AQUIFER TECHNICAL GUIDANCE MANUAL.

THIS SHEET HAS BEEN PREPARED FOR PURPOSES OF POLLUTION ABATEMENT ONLY. ALL OTHER CIVIL ENGINEERING RELATED INFORMATION SHOULD BE ACQUIRED FROM THE APPROPRIATE SHEET IN THE CIVIL IMPROVEMENT PLANS.

WPAP  
EXHIBIT 5

DATE	
NO.	
REVISION	



**PAPE-DAWSON**  
**ENGINEERS**  
JARRELL INDUSTRIAL PARK  
JARRELL, TEXAS  
BATCH DETENTION BASIN DETAILS

JARRELL INDUSTRIAL PARK  
JARRELL, TEXAS  
BATCH DETENTION BASIN DETAILS

CITY NO. \_\_\_\_\_  
JOB NO. 51570-00  
DATE \_\_\_\_\_  
DESIGNER DS  
CHECKED DRAWN VKB  
SHEET 10 OF 14
