



**GALLEGOS ENGINEERING, INC.**

Firm No. F-003084

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

## **CONTRIBUTING ZONE PLAN (CZP)**

PROJECT NAME:

**SERENITY OAKS, UNIT 5  
Comal County, TX**

FOR:

**REGULATED ACTIVITIES  
ON THE CONTRIBUTING ZONE  
TO THE EDWARDS AQUIFER  
30 TAC §213.24(1)**

PREPARED BY:

**Richard M. Gallegos, P.E.**

**GALLEGOS ENGINEERING, INC.**

**FIRM REGISTRATION # F-003084**

**P.O. Box 690067**

**San Antonio, TX 78269**

**[rg@gallegoseng.com](mailto:rg@gallegoseng.com)**

**DATE: JANUARY 6, 2025**

## Table of Contents

### Serenity Oaks Subdivision, Unit 5 – Contributing Zone Plan

<b>Edwards Aquifer Application Cover Page (TCEQ-20705).....</b>	<b>Tab 1</b>
<b>Contributing Zone Plan Application (TCEQ-10257).....</b>	<b>Tab 2</b>
Attachment A - Road Map, <b>Tab A</b>	
Attachment B - USGS Quadrangle Map, <b>Tab B</b>	
Attachment C - Project Narrative, <b>Tab C</b>	
Attachment D - Factors Affecting Surface Water Quality, <b>Tab D</b>	
Attachment E - Volume and Character of Stormwater, <b>Tab E</b>	
Attachment F - Suitability Letter from Authorized Agent (if OSSF is proposed), <b>Tab F</b>	
Attachment G - Alternative Secondary Containment Methods (if AST with an alternative method of secondary containment is proposed), <b>NA to this plan, Tab G</b>	
Attachment H - AST Containment Structure Drawings (if AST is prop.), <b>NA to this plan, Tab H</b>	
Attachment I - 20% or Less Impervious Cover Declaration (if project is multi-family residential, a school, or a small business and 20% or less impervious cover is proposed for the site), <b>Tab I</b>	
Attachment J - BMPs for Upgradient Stormwater, <b>Tab J</b>	
Attachment K - BMPs for On-site Stormwater, <b>Tab K</b>	
Attachment L - BMPs for Surface Streams, <b>Tab L</b>	
Attachment M - Construction Plans, <b>Tab M</b>	
Attachment N - Inspection, Maintenance, Repair and Retrofit Plan, <b>Tab N</b>	
Attachment O - Pilot-Scale Field Testing Plan, if BMPs not based on Complying with the Edwards Aquifer Rules: Technical Guidance for BMPs, <b>NA to this plan, Tab O</b>	
Attachment P - Measures for Minimizing Surface Stream Contamination, <b>Tab P</b>	
<b>Storm Water Pollution Prevention Plan (SWPPP) .....</b>	<b>Tab 3</b>
<b>Copy of Notice of Intent (NOI).....</b>	<b>Tab 4</b>
<b>Agent Authorization Form (TCEQ-0599), if application submitted by agent .....</b>	<b>Tab 5</b>
<b>Application Fee Form (TCEQ-0574).....</b>	<b>Tab 6</b>
<b>Check Payable to the “Texas Commission on Environmental Quality” .....</b>	<b>Tab 7</b>
<b>Core Data Form (TCEQ-10400).....</b>	<b>Tab 8</b>



# Texas Commission on Environmental Quality

## Edwards Aquifer Application Cover Page

---

### Our Review of Your Application

The Edwards Aquifer Program staff conducts an administrative and technical review of all applications. The turnaround time for administrative review can be up to 30 days as outlined in 30 TAC 213.4(e). Generally administrative completeness is determined during the intake meeting or within a few days of receipt. The turnaround time for technical review of an administratively complete Edwards Aquifer application is 90 days as outlined in 30 TAC 213.4(e). Please know that the review and approval time is directly impacted by the quality and completeness of the initial application that is received. In order to conduct a timely review, it is imperative that the information provided in an Edwards Aquifer application include final plans, be accurate, complete, and in compliance with [30 TAC 213](#).

### Administrative Review

1. [Edwards Aquifer applications](#) must be deemed administratively complete before a technical review can begin. To be considered administratively complete, the application must contain completed forms and attachments, provide the requested information, and meet all the site plan requirements. The submitted application and plan sheets should be final plans. Please submit one full-size set of plan sheets with the original application, and half-size sets with the additional copies.

To ensure that all applicable documents are included in the application, the program has developed tools to guide you and web pages to provide all forms, checklists, and guidance. Please visit the below website for assistance: <http://www.tceq.texas.gov/field/eapp>.

2. This Edwards Aquifer Application Cover Page form (certified by the applicant or agent) must be included in the application and brought to the administrative review meeting.
3. Administrative reviews are scheduled with program staff who will conduct the review. Applicants or their authorized agent should call the appropriate regional office, according to the county in which the project is located, to schedule a review. The average meeting time is one hour.
4. In the meeting, the application is examined for administrative completeness. Deficiencies will be noted by staff and emailed or faxed to the applicant and authorized agent at the end of the meeting, or shortly after. Administrative deficiencies will cause the application to be deemed incomplete and returned.

An appointment should be made to resubmit the application. The application is re-examined to ensure all deficiencies are resolved. The application will only be deemed administratively complete when all administrative deficiencies are addressed.

5. If an application is received by mail, courier service, or otherwise submitted without a review meeting, the administrative review will be conducted within 30 days. The applicant and agent will be contacted with the results of the administrative review. If the application is found to be administratively incomplete, it can be retrieved from the regional office or returned by regular mail. If returned by mail, the regional office may require arrangements for return shipping.
6. If the geologic assessment was completed before October 1, 2004 and the site contains “possibly sensitive” features, the assessment must be updated in accordance with the *Instructions to Geologists* (TCEQ-0585 Instructions).

### Technical Review

1. When an application is deemed administratively complete, the technical review period begins. The regional office will distribute copies of the application to the identified affected city, county, and groundwater conservation district whose jurisdiction includes the subject site. These entities and the public have 30 days to provide comments on the application to the regional office. All comments received are reviewed by TCEQ.
2. A site assessment is usually conducted as part of the technical review, to evaluate the geologic assessment and observe existing site conditions. The site must be accessible to our staff. The site boundaries should be

clearly marked, features identified in the geologic assessment should be flagged, roadways marked and the alignment of the Sewage Collection System and manholes should be staked at the time the application is submitted. If the site is not marked the application may be returned.

3. We evaluate the application for technical completeness and contact the applicant and agent via Notice of Deficiency (NOD) to request additional information and identify technical deficiencies. There are two deficiency response periods available to the applicant. There are 14 days to resolve deficiencies noted in the first NOD. If a second NOD is issued, there is an additional 14 days to resolve deficiencies. If the response to the second notice is not received, is incomplete or inadequate, or provides new information that is incomplete or inadequate, the application must be withdrawn or will be denied. Please note that because the technical review is underway, whether the application is withdrawn or denied **the application fee will be forfeited**.
4. The program has 90 calendar days to complete the technical review of the application. If the application is technically adequate, such that it complies with the Edwards Aquifer rules, and is protective of the Edwards Aquifer during and after construction, an approval letter will be issued. Construction or other regulated activity may not begin until an approval is issued.

### Mid-Review Modifications

It is important to have final site plans prior to beginning the permitting process with TCEQ to avoid delays.

Occasionally, circumstances arise where you may have significant design and/or site plan changes after your Edwards Aquifer application has been deemed administratively complete by TCEQ. This is considered a “Mid-Review Modification”. Mid-Review Modifications may require redistribution of an application that includes the proposed modifications for public comment.

If you are proposing a Mid-Review Modification, two options are available:

- If the technical review has begun your application can be denied/withdrawn, your fees will be forfeited, and the plan will have to be resubmitted.
- TCEQ can continue the technical review of the application as it was submitted, and a modification application can be submitted at a later time.

If the application is denied/withdrawn, the resubmitted application will be subject to the administrative and technical review processes and will be treated as a new application. The application will be redistributed to the affected jurisdictions.

Please contact the regional office if you have questions. If your project is located in Williamson, Travis, or Hays County, contact TCEQ’s Austin Regional Office at 512-339-2929. If your project is in Comal, Bexar, Medina, Uvalde, or Kinney County, contact TCEQ’s San Antonio Regional Office at 210-490-3096

Please fill out all required fields below and submit with your application.

<b>1. Regulated Entity Name: Serenity Oaks, Unit 5</b>					<b>2. Regulated Entity No.: 1064755122</b>				
<b>3. Customer Name: Gale Estates, LLC</b>					<b>4. Customer No.: 603643685</b>				
<b>5. Project Type:</b> (Please circle/check one)	New		Modification			Extension		Exception <input checked="" type="checkbox"/>	
<b>6. Plan Type:</b> (Please circle/check one)	WPAP	CZP <input checked="" type="checkbox"/>	SCS	UST	AST	EXP	EXT	Technical Clarification	Optional Enhanced Measures
<b>7. Land Use:</b> (Please circle/check one)	Residential <input checked="" type="checkbox"/>		Non-residential			<b>8. Site (acres):</b>			65.15
<b>9. Application Fee:</b>	\$6,500		<b>10. Permanent BMP(s):</b>				NA		
<b>11. SCS (Linear Ft.):</b>	NA		<b>12. AST/UST (No. Tanks):</b>				NA		
<b>13. County:</b>	Comal		<b>14. Watershed:</b>				Guadalupe River		

# Application Distribution

Instructions: Use the table below to determine the number of applications required. One original and one copy of the application, plus additional copies (as needed) for each affected incorporated city, county, and groundwater conservation district are required. Linear projects or large projects, which cross into multiple jurisdictions, can require additional copies. Refer to the “Texas Groundwater Conservation Districts within the EAPP Boundaries” map found at:

[http://www.tceq.texas.gov/assets/public/compliance/field\\_ops/eapp/EAPP%20GWCD%20map.pdf](http://www.tceq.texas.gov/assets/public/compliance/field_ops/eapp/EAPP%20GWCD%20map.pdf)

For more detailed boundaries, please contact the conservation district directly.

Austin Region			
County:	Hays	Travis	Williamson
Original (1 req.)	—	—	—
Region (1 req.)	—	—	—
County(ies)	—	—	—
Groundwater Conservation District(s)	<input type="checkbox"/> Edwards Aquifer Authority <input type="checkbox"/> Barton Springs/ Edwards Aquifer <input type="checkbox"/> Hays Trinity <input type="checkbox"/> Plum Creek	<input type="checkbox"/> Barton Springs/ Edwards Aquifer	NA
City(ies) Jurisdiction	<input type="checkbox"/> Austin <input type="checkbox"/> Buda <input type="checkbox"/> Dripping Springs <input type="checkbox"/> Kyle <input type="checkbox"/> Mountain City <input type="checkbox"/> San Marcos <input type="checkbox"/> Wimberley <input type="checkbox"/> Woodcreek	<input type="checkbox"/> Austin <input type="checkbox"/> Bee Cave <input type="checkbox"/> Pflugerville <input type="checkbox"/> Rollingwood <input type="checkbox"/> Round Rock <input type="checkbox"/> Sunset Valley <input type="checkbox"/> West Lake Hills	<input type="checkbox"/> Austin <input type="checkbox"/> Cedar Park <input type="checkbox"/> Florence <input type="checkbox"/> Georgetown <input type="checkbox"/> Jerrell <input type="checkbox"/> Leander <input type="checkbox"/> Liberty Hill <input type="checkbox"/> Pflugerville <input type="checkbox"/> Round Rock

San Antonio Region					
County:	Bexar	Comal	Kinney	Medina	Uvalde
Original (1 req.)	—	_1_	—	—	—
Region (1 req.)	—	_1_	—	—	—
County(ies)	—	_1_	—	—	—
Groundwater Conservation District(s)	<input type="checkbox"/> Edwards Aquifer Authority <input type="checkbox"/> Trinity-Glen Rose	<input type="checkbox"/> Edwards Aquifer Authority	<input type="checkbox"/> Kinney	<input type="checkbox"/> EAA <input type="checkbox"/> Medina	<input type="checkbox"/> EAA <input type="checkbox"/> Uvalde
City(ies) Jurisdiction	<input type="checkbox"/> Castle Hills <input type="checkbox"/> Fair Oaks Ranch <input type="checkbox"/> Helotes <input type="checkbox"/> Hill Country Village <input type="checkbox"/> Hollywood Park <input type="checkbox"/> San Antonio (SAWS) <input type="checkbox"/> Shavano Park	<input type="checkbox"/> Bulverde <input type="checkbox"/> Fair Oaks Ranch <input type="checkbox"/> Garden Ridge <input type="checkbox"/> New Braunfels <input type="checkbox"/> Schertz	NA	<input type="checkbox"/> San Antonio ETJ (SAWS)	NA

I certify that to the best of my knowledge, that the application is complete and accurate. This application is hereby submitted to TCEQ for administrative review and technical review.	
Richard M. Gallegos, P.E	
Print Name of Customer/Authorized Agent	January 20, 2025
Signature of Customer/Authorized Agent	Date

<b>**FOR TCEQ INTERNAL USE ONLY**</b>			
Date(s) Reviewed:		Date Administratively Complete:	
Received From:		Correct Number of Copies:	
Received By:		Distribution Date:	
EAPP File Number:		Complex:	
Admin. Review(s) (No.):		No. AR Rounds:	
Delinquent Fees (Y/N):		Review Time Spent:	
Lat./Long. Verified:		SOS Customer Verification:	
Agent Authorization Complete/Notarized (Y/N):		Fee Check:	Payable to TCEQ (Y/N):
Core Data Form Complete (Y/N):			Signed (Y/N):
Core Data Form Incomplete Nos.:			Less than 90 days old (Y/N):

# Contributing Zone Plan Application

## Texas Commission on Environmental Quality

for Regulated Activities on the Contributing Zone to the Edwards Aquifer and Relating to 30 TAC §213.24(1), Effective June 1, 1999

*To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.*

*Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.*

## Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Contributing Zone Plan Application** is hereby submitted for TCEQ review and Executive Director approval. The application was prepared by:

Print Name of Customer/Agent: Richard M. Gallegos

Date: December 27, 2024

Signature of Customer/Agent:



Regulated Entity Name: Serenity Oaks Subdivision, Unit 5

## Project Information

1. County: Comal
2. Stream Basin: Guadalupe
3. Groundwater Conservation District (if applicable): NA
4. Customer (Applicant):

Contact Person: Jason Gale

Entity: Gale Estates, LLC

Mailing Address: 15315 San Pedro

City, State: San Antonio, Texas

Telephone: 210-4905237

Email Address: acs1@satx.rr.com

Zip: 78232

Fax: 210-490-0913

5. Agent/Representative (If any):

Contact Person: Richard M. Gallegos, P.E.

Entity: Gallegos Engineering, Inc.

Mailing Address: PO Boc 690067

City, State: San Antonio, Texas

Zip: 78269

Telephone: 210-641-0812

Fax: NA

Email Address: rg@gallegoseng.com

6. Project Location:

- ☐ The project site is located inside the city limits of \_\_\_\_\_.
- ☐ The project site is located outside the city limits but inside the ETJ (extra-territorial jurisdiction) of \_\_\_\_\_.
- ☐ The project site is not located within any city's limits or ETJ.

7. ☒ The location of the project site is described below. Sufficient detail and clarity has been provided so that the TCEQ's Regional staff can easily locate the project and site boundaries for a field investigation.

Located 2.4 miles east on Rebecca Ck. Rd. from intersection of Hwy 281 North of Spring Branch, TX, Rt. 1.4 miles south-southeast on Rayner Ranch Blvd.

8. ☒ **Attachment A - Road Map.** A road map showing directions to and the location of the project site is attached. The map clearly shows the boundary of the project site.

9. ☐ **Attachment B - USGS Quadrangle Map.** A copy of the official 7 ½ minute USGS Quadrangle Map (Scale: 1" = 2000') is attached. The map(s) clearly show:

- ☐ Project site boundaries.
- ☐ USGS Quadrangle Name(s).

10. ☐ **Attachment C - Project Narrative.** A detailed narrative description of the proposed project is attached. The project description is consistent throughout the application and contains, at a minimum, the following details:

- ☐ Area of the site
- ☐ Offsite areas
- ☐ Impervious cover
- ☐ Permanent BMP(s)
- ☐ Proposed site use
- ☐ Site history
- ☐ Previous development
- ☐ Area(s) to be demolished

11. Existing project site conditions are noted below:

- ☐ Existing commercial site
- ☐ Existing industrial site

- ☐ Existing residential site
- ☒ Existing paved and/or unpaved roads
- ☐ Undeveloped (Cleared)
- ☐ Undeveloped (Undisturbed/Not cleared)
- ☐ Other: \_\_\_\_\_

12. The type of project is:

- ☒ Residential: # of Lots: 44
- ☐ Residential: # of Living Unit Equivalents: \_\_\_\_\_
- ☐ Commercial
- ☐ Industrial
- ☐ Other: \_\_\_\_\_

13. Total project area (size of site): 65.15 Acres

Total disturbed area: 8.32 Acres

14. Estimated projected population: 110

15. The amount and type of impervious cover expected after construction is complete is shown below:

**Table 1 - Impervious Cover**

<i><b>Impervious Cover of Proposed Project</b></i>	<i><b>Sq. Ft.</b></i>	<i><b>Sq. Ft./Acre</b></i>	<i><b>Acres</b></i>
Structures/Rooftops	132,000	÷ 43,560 =	3.03
Parking	66,000	÷ 43,560 =	1.51
Other paved surfaces	177,240	÷ 43,560 =	4.07
Total Impervious Cover	375,240	÷ 43,560 =	8.61

**Total Impervious Cover 8.61 ÷ Total Acreage 65.15 X 100 = 13.2% Impervious Cover**

16. ☒ **Attachment D - Factors Affecting Surface Water Quality.** A detailed description of all factors that could affect surface water quality is attached. If applicable, this includes the location and description of any discharge associated with industrial activity other than construction.

17. ☒ Only inert materials as defined by 30 TAC 330.2 will be used as fill material.

### ***For Road Projects Only***

***Complete questions 18 - 23 if this application is exclusively for a road project.***

☒ N/A

18. Type of project:

- ☐ TXDOT road project.
- ☐ County road or roads built to county specifications.
- ☐ City thoroughfare or roads to be dedicated to a municipality.
- ☐ Street or road providing access to private driveways.

19. Type of pavement or road surface to be used:

- ☐ Concrete
- ☐ Asphaltic concrete pavement
- ☐ Other: \_\_\_\_\_

20. Right of Way (R.O.W.):

Length of R.O.W.: \_\_\_\_\_ feet.

Width of R.O.W.: \_\_\_\_\_ feet.

$L \times W = \text{_____ Ft}^2 \div 43,560 \text{ Ft}^2/\text{Acre} = \text{_____ acres.}$

21. Pavement Area:

Length of pavement area: \_\_\_\_\_ feet.

Width of pavement area: \_\_\_\_\_ feet.

$L \times W = \text{_____ Ft}^2 \div 43,560 \text{ Ft}^2/\text{Acre} = \text{_____ acres.}$

Pavement area \_\_\_\_\_ acres  $\div$  R.O.W. area \_\_\_\_\_ acres  $\times 100 = \text{_____ \%}$  impervious cover.

22. ☐ A rest stop will be included in this project.

☐ A rest stop will not be included in this project.

23. ☐ Maintenance and repair of existing roadways that do not require approval from the TCEQ Executive Director. Modifications to existing roadways such as widening roads/adding shoulders totaling more than one-half (1/2) the width of one (1) existing lane require prior approval from the TCEQ.

***Stormwater to be generated by the Proposed Project***

24. ☒ **Attachment E - Volume and Character of Stormwater.** A detailed description of the volume (quantity) and character (quality) of the stormwater runoff which is expected to occur from the proposed project is attached. The estimates of stormwater runoff quality and quantity are based on area and type of impervious cover. Include the runoff coefficient of the site for both pre-construction and post-construction conditions.

***Wastewater to be generated by the Proposed Project***

25. ☒ Wastewater is to be discharged in the contributing zone. Requirements under 30 TAC §213.6(c) relating to Wastewater Treatment and Disposal Systems have been satisfied.

☐ N/A



26. Wastewater will be disposed of by:

☒ On-Site Sewage Facility (OSSF/Septic Tank):

☐ **Attachment F - Suitability Letter from Authorized Agent.** An on-site sewage facility will be used to treat and dispose of the wastewater from this site. The appropriate licensing authority's (authorized agent) written approval is attached. It states that the land is suitable for the use of private sewage facilities and will meet or exceed the requirements for on-site sewage facilities as specified under 30 TAC Chapter 285 relating to On-site Sewage Facilities.

☒ Each lot in this project/development is at least one (1) acre (43,560 square feet) in size. The system will be designed by a licensed professional engineer or registered sanitarian and installed by a licensed installer in compliance with 30 TAC Chapter 285.

☐ Sewage Collection System (Sewer Lines):

The sewage collection system will convey the wastewater to the \_\_\_\_\_ (name) Treatment Plant. The treatment facility is:

☐ Existing.

☐ Proposed.

☐ N/A

### ***Permanent Aboveground Storage Tanks(ASTs) ≥ 500 Gallons***

***Complete questions 27 - 33 if this project includes the installation of AST(s) with volume(s) greater than or equal to 500 gallons.***

☒ N/A

27. Tanks and substance stored:

**Table 2 - Tanks and Substance Storage**

<b><i>AST Number</i></b>	<b><i>Size (Gallons)</i></b>	<b><i>Substance to be Stored</i></b>	<b><i>Tank Material</i></b>
1			
2			
3			
4			
5			

**Total x 1.5 = \_\_\_\_\_ Gallons**

28. ☐ The AST will be placed within a containment structure that is sized to capture one and one-half (1 1/2) times the storage capacity of the system. For facilities with more than

5 of 11

one tank system, the containment structure is sized to capture one and one-half (1 1/2) times the cumulative storage capacity of all systems.

- ☐ **Attachment G - Alternative Secondary Containment Methods.** Alternative methods for providing secondary containment are proposed. Specifications showing equivalent protection for the Edwards Aquifer are attached.

29. Inside dimensions and capacity of containment structure(s):

**Table 3 - Secondary Containment**

<i>Length (L)(Ft.)</i>	<i>Width(W)(Ft.)</i>	<i>Height (H)(Ft.)</i>	<i>L x W x H = (Ft3)</i>	<i>Gallons</i>

**Total: \_\_\_\_\_ Gallons**

30. Piping:

- ☐ All piping, hoses, and dispensers will be located inside the containment structure.
- ☐ Some of the piping to dispensers or equipment will extend outside the containment structure.
- ☐ The piping will be aboveground
- ☐ The piping will be underground

31. ☐ The containment area must be constructed of and in a material impervious to the substance(s) being stored. The proposed containment structure will be constructed of: \_\_\_\_\_.

32. ☐ **Attachment H - AST Containment Structure Drawings.** A scaled drawing of the containment structure is attached that shows the following:

- ☐ Interior dimensions (length, width, depth and wall and floor thickness).
- ☐ Internal drainage to a point convenient for the collection of any spillage.
- ☐ Tanks clearly labeled
- ☐ Piping clearly labeled
- ☐ Dispenser clearly labeled

33. ☐ Any spills must be directed to a point convenient for collection and recovery. Spills from storage tank facilities must be removed from the controlled drainage area for disposal within 24 hours of the spill.

- ☐ In the event of a spill, any spillage will be removed from the containment structure within 24 hours of the spill and disposed of properly.

- ☐ In the event of a spill, any spillage will be drained from the containment structure through a drain and valve within 24 hours of the spill and disposed of properly. The drain and valve system are shown in detail on the scaled drawing.

## **Site Plan Requirements**

**Items 34 - 46 must be included on the Site Plan.**

34. ☒ The Site Plan must have a minimum scale of 1" = 400'.  
Site Plan Scale: 1" = 400'.
35. 100-year floodplain boundaries:
- ☐ Some part(s) of the project site is located within the 100-year floodplain. The floodplain is shown and labeled.
- ☒ No part of the project site is located within the 100-year floodplain.  
The 100-year floodplain boundaries are based on the following specific (including date of material) sources(s): \_\_\_\_\_.
36. ☐ The layout of the development is shown with existing and finished contours at appropriate, but not greater than ten-foot contour intervals. Lots, recreation centers, buildings, roads, etc. are shown on the site plan.
- ☒ The layout of the development is shown with existing contours at appropriate, but not greater than ten-foot contour intervals. Finished topographic contours will not differ from the existing topographic configuration and are not shown. Lots, recreation centers, buildings, roads, etc. are shown on the site plan.
37. ☒ A drainage plan showing all paths of drainage from the site to surface streams.
38. ☒ The drainage patterns and approximate slopes anticipated after major grading activities.
39. ☒ Areas of soil disturbance and areas which will not be disturbed.
40. ☒ Locations of major structural and nonstructural controls. These are the temporary and permanent best management practices.
41. ☒ Locations where soil stabilization practices are expected to occur.
42. ☐ Surface waters (including wetlands).  
☒ N/A
43. ☐ Locations where stormwater discharges to surface water.  
☒ There will be no discharges to surface water.
44. ☐ Temporary aboveground storage tank facilities.  
☒ Temporary aboveground storage tank facilities will not be located on this site.

45. ☐ Permanent aboveground storage tank facilities.  
☒ Permanent aboveground storage tank facilities will not be located on this site.
46. ☒ Legal boundaries of the site are shown.

### ***Permanent Best Management Practices (BMPs)***

***Practices and measures that will be used during and after construction is completed.***

47. ☐ Permanent BMPs and measures must be implemented to control the discharge of pollution from regulated activities after the completion of construction.  
☒ N/A
48. ☐ These practices and measures have been designed, and will be constructed, operated, and maintained to insure that 80% of the incremental increase in the annual mass loading of total suspended solids (TSS) from the site caused by the regulated activity is removed. These quantities have been calculated in accordance with technical guidance prepared or accepted by the executive director.  
☐ The TCEQ Technical Guidance Manual (TGM) was used to design permanent BMPs and measures for this site.  
☐ A technical guidance other than the TCEQ TGM was used to design permanent BMPs and measures for this site. The complete citation for the technical guidance that was used is: \_\_\_\_\_.  
☒ N/A
49. ☐ Owners must insure that permanent BMPs and measures are constructed and function as designed. A Texas Licensed Professional Engineer must certify in writing that the permanent BMPs or measures were constructed as designed. The certification letter must be submitted to the appropriate regional office within 30 days of site completion.  
☒ N/A
50. Where a site is used for low density single-family residential development and has 20 % or less impervious cover, other permanent BMPs are not required. This exemption from permanent BMPs must be recorded in the county deed records, with a notice that if the percent impervious cover increases above 20% or land use changes, the exemption for the whole site as described in the property boundaries required by 30 TAC §213.4(g) (relating to Application Processing and Approval), may no longer apply and the property owner must notify the appropriate regional office of these changes.  
☒ The site will be used for low density single-family residential development and has 20% or less impervious cover.  
☐ The site will be used for low density single-family residential development but has more than 20% impervious cover.  
☐ The site will not be used for low density single-family residential development.

51. The executive director may waive the requirement for other permanent BMPs for multi-family residential developments, schools, or small business sites where 20% or less impervious cover is used at the site. This exemption from permanent BMPs must be recorded in the county deed records, with a notice that if the percent impervious cover increases above 20% or land use changes, the exemption for the whole site as described in the property boundaries required by 30 TAC §213.4(g) (relating to Application Processing and Approval), may no longer apply and the property owner must notify the appropriate regional office of these changes.

- ☐ **Attachment I - 20% or Less Impervious Cover Waiver.** The site will be used for multi-family residential developments, schools, or small business sites and has 20% or less impervious cover. A request to waive the requirements for other permanent BMPs and measures is attached.
- ☐ The site will be used for multi-family residential developments, schools, or small business sites but has more than 20% impervious cover.
- ☒ The site will not be used for multi-family residential developments, schools, or small business sites.

52. ☒ **Attachment J - BMPs for Upgradient Stormwater.**

- ☐ A description of the BMPs and measures that will be used to prevent pollution of surface water, groundwater, or stormwater that originates upgradient from the site and flows across the site is attached.
- ☐ No surface water, groundwater or stormwater originates upgradient from the site and flows across the site, and an explanation is attached.
- ☒ Permanent BMPs or measures are not required to prevent pollution of surface water, groundwater, or stormwater that originates upgradient from the site and flows across the site, and an explanation is attached.

53. ☐ **Attachment K - BMPs for On-site Stormwater.**

- ☐ A description of the BMPs and measures that will be used to prevent pollution of surface water or groundwater that originates on-site or flows off the site, including pollution caused by contaminated stormwater runoff from the site is attached.
- ☒ Permanent BMPs or measures are not required to prevent pollution of surface water or groundwater that originates on-site or flows off the site, including pollution caused by contaminated stormwater runoff, and an explanation is attached.

54. ☐ **Attachment L - BMPs for Surface Streams.** A description of the BMPs and measures that prevent pollutants from entering surface streams is attached.

☒ N/A

55. ☐ **Attachment M - Construction Plans.** Construction plans and design calculations for the proposed permanent BMPs and measures have been prepared by or under the direct supervision of a Texas Licensed Professional Engineer, and are signed, sealed, and dated. Construction plans for the proposed permanent BMPs and measures are

attached and include: Design calculations, TCEQ Construction Notes, all proposed structural plans and specifications, and appropriate details.

☒ N/A

56. ☐ **Attachment N - Inspection, Maintenance, Repair and Retrofit Plan.** A site and BMP specific plan for the inspection, maintenance, repair, and, if necessary, retrofit of the permanent BMPs and measures is attached. The plan fulfills all of the following:

- ☐ Prepared and certified by the engineer designing the permanent BMPs and measures
- ☐ Signed by the owner or responsible party
- ☐ Outlines specific procedures for documenting inspections, maintenance, repairs, and, if necessary, retrofit.
- ☐ Contains a discussion of record keeping procedures

☒ N/A

57. ☐ **Attachment O - Pilot-Scale Field Testing Plan.** Pilot studies for BMPs that are not recognized by the Executive Director require prior approval from the TCEQ. A plan for pilot-scale field testing is attached.

☒ N/A

58. ☒ **Attachment P - Measures for Minimizing Surface Stream Contamination.** A description of the measures that will be used to avoid or minimize surface stream contamination and changes in the way in which water enters a stream as a result of the construction and development is attached. The measures address increased stream flashing, the creation of stronger flows and in-stream velocities, and other in-stream effects caused by the regulated activity, which increase erosion that result in water quality degradation.

☐ N/A

***Responsibility for Maintenance of Permanent BMPs and Measures after Construction is Complete.***

59. ☒ The applicant is responsible for maintaining the permanent BMPs after construction until such time as the maintenance obligation is either assumed in writing by another entity having ownership or control of the property (such as without limitation, an owner's association, a new property owner or lessee, a district, or municipality) or the ownership of the property is transferred to the entity. Such entity shall then be responsible for maintenance until another entity assumes such obligations in writing or ownership is transferred.
60. ☒ A copy of the transfer of responsibility must be filed with the executive director at the appropriate regional office within 30 days of the transfer if the site is for use as a multiple single-family residential development, a multi-family residential development,

or a non-residential development such as commercial, industrial, institutional, schools, and other sites where regulated activities occur.

### ***Administrative Information***

- 61. ☒ Submit one (1) original and one (1) copy of the application, plus additional copies as needed for each affected incorporated city, groundwater conservation district, and county in which the project will be located. The TCEQ will distribute the additional copies to these jurisdictions.
- 62. ☒ Any modification of this Contributing Zone Plan may require TCEQ review and Executive Director approval prior to construction, and may require submission of a revised application, with appropriate fees.
- 63. ☒ The site description, controls, maintenance, and inspection requirements for the storm water pollution prevention plan (SWPPP) developed under the EPA NPDES general permits for stormwater discharges have been submitted to fulfill paragraphs 30 TAC §213.24(1-5) of the technical report. All requirements of 30 TAC §213.24(1-5) have been met by the SWPPP document.
- ☐ The Temporary Stormwater Section (TCEQ-0602) is included with the application.






BLANCO

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
GEOLOGICAL SURVEY


Edwards Aquifer Recharge Zone and Contributing Zone Map  
Edwards Aquifer Authority Rule Chapter 713  
STATE OF TEXAS  
TEXAS WATER DEVELOPMENT BOARD  
PAYTON

FISCHER  
QUADRANGLE  
TEXAS  
7.5 MINUTE SERIES (TOPOGRAPHIC)

ROUGH HOLLOW

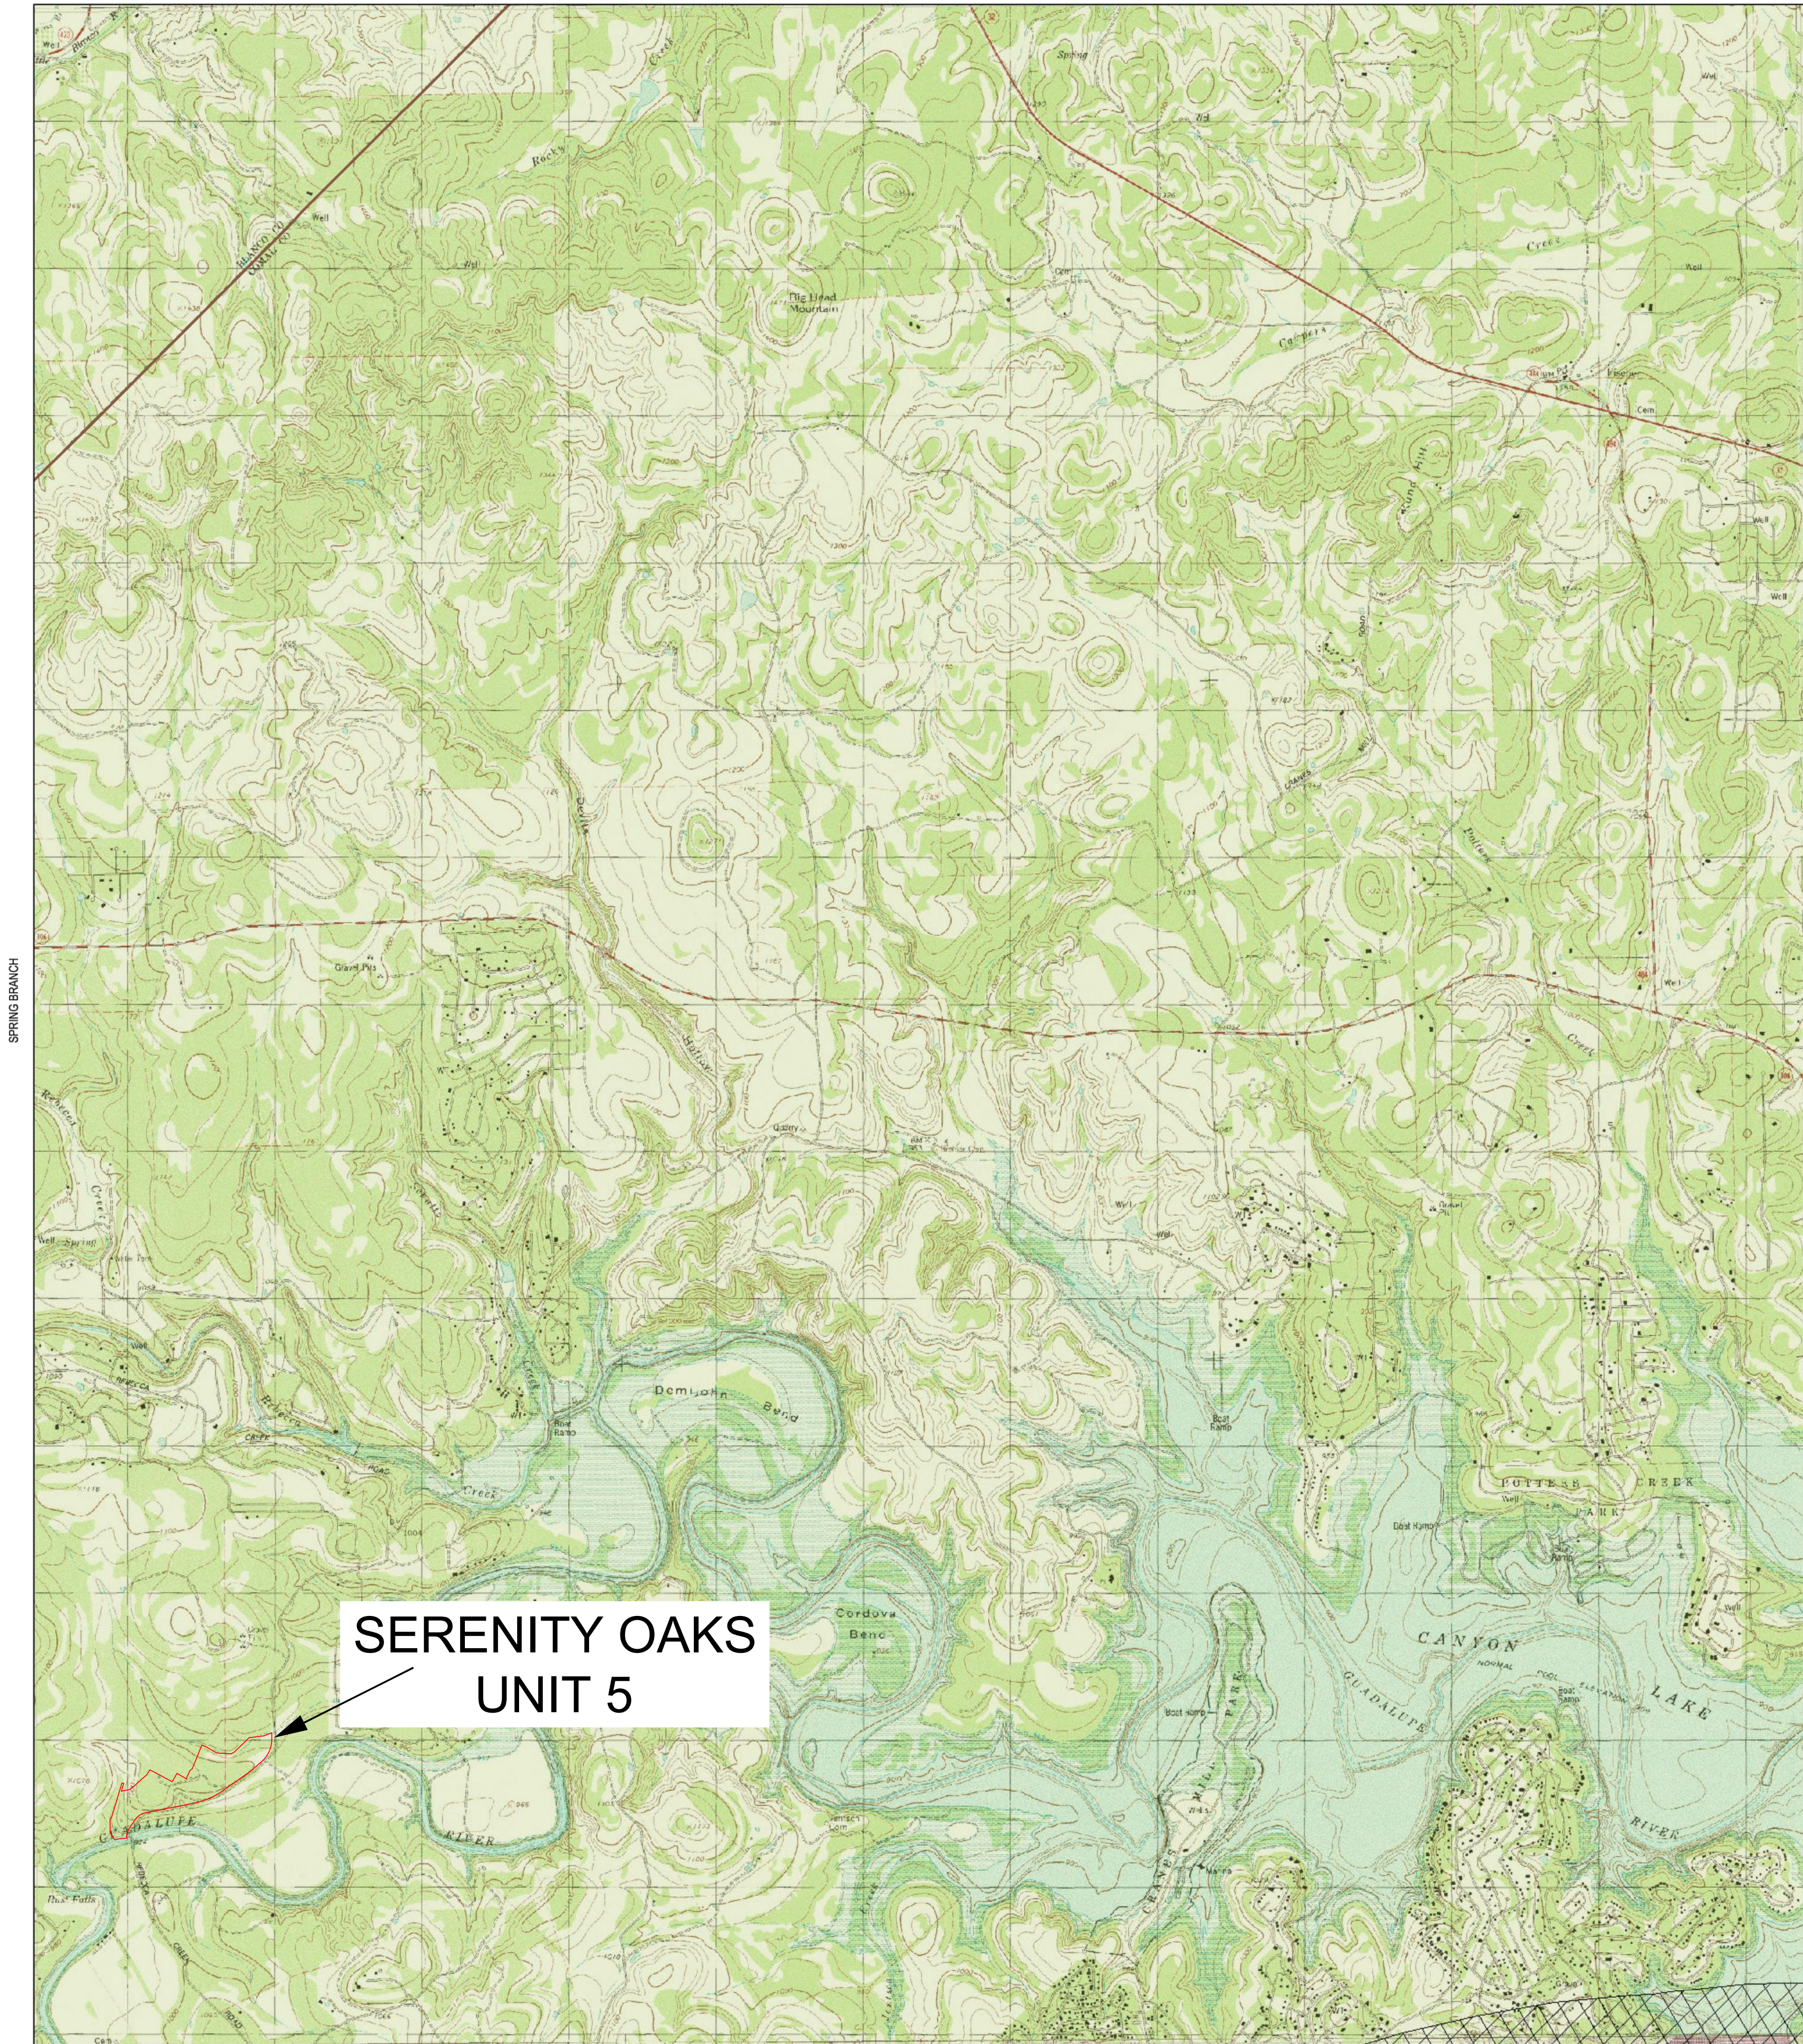

Digital Raster Graphic Enhanced (DRGE) produced through an Innovative partnership agreement between The Land Information Technology Company, Ltd., of Aurora, CO and the USGS. DRGE is a scanned image of a USGS standard series 7.5 minute topographic map. Mapped, edited and published by the Geological Survey. Control by USGS and NCS/NCAA. Topography by photogrammetric methods from aerial photographs taken and field checked between 1950 and 1990. Polyconic projection. 1927 North American datum. 10,000-foot grid based on Texas coordinate system, south central zone (Lambert conformal conic). 1000-meter Universal Transverse Mercator grid ticks, zone 14.



ROAD CLASSIFICATION

Primary highway, hard surface ——— Light-duty road, hard or improved surface ———

Secondary highway, hard surface ——— Unimproved road ———

○ Interstate Route ○ U. S. Route ○ State Route

Drainage Area  
Recharge Zone  
Contributing Zone within the Transition Zone  
Artesian Zone

This area regulated by EDWARDS AQUIFER AUTHORITY RULES, ch. 713, (Water Quality), subchs. E (Spill Reporting) and F (Regulated Materials Registration, Storage, and Planning).

This area in Hays and Comal Counties regulated by EDWARDS AQUIFER AUTHORITY RULES, ch. 713, (Water Quality), subch. H (Prohibitions).

Author: Sarah Eason

Date Saved: 11/10/2014 1:43:21 PM

Document Path: S:\Regulatory\Regulatory.mxd

QUADRANGLE:  
FISCHER

SMITH





## **GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024

### **PROJECT NARRATIVE SERENITY OAKS, UNIT 5**

The subject 65.15 acres is presently raw hill country land which is to be developed into 44 Single-Family Residential Lots. Canyon Lake Water Supply will own and maintain the community water system supplying potable water to said lots.

The initial construction will consist of 2,954 l.f. of street constructed to Comal County specifications (22' of pavement width over a 60' ROW) and related drainage structural concrete. This amounts to 177,240 s.f. of street pavement or 4.07 acres of impervious cover. Driveways and/or sidewalks account for another 66,000 s.f. or 1.51 acres.

The ultimate construction will be that of 44 Single Family Homes Averaging approximately 3,000 s.f. each. These structural rooftops will be approximately equal to 132,000 s.f. or 3.03 acres of impervious cover.

The grand total impervious cover is, therefore, 375,240 s.f. (8.61 acres) or 13.2% of the 65.15 acre subdivision. Consequently, as per TCEQ rule 30 TAC §213.4(g), there will be no permanent BMPs since this is to be a Single-family Residential Subdivision with less than 20% impervious cover. **Based on this low impervious cover we request an exception to any Permanent BMPs.**

**ATTACHMENT C**



## **GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024

### **FACTORS AFFECTING SURFACE WATER QUALITY SERENITY OAKS, UNIT 5**

The following are factors that could affect surface groundwater quality both during and after construction.

1. During construction contamination could come from oil, grease, diesel or gasoline drippings from construction equipment and also from the process of excavation materials and grading. If fuel or a hazardous substance spill occurs, the contaminated soil will be removed and placed in an impervious container to be disposed offsite at an approved disposal location.
2. The placement of excavated materials will have appropriately sized erosion and sedimentation controls placed downgradient.
3. After construction is complete, the potential sources of contamination would be from sediments brought onsite by vehicles, fuel, oil and grease from vehicles, fertilizers used for lawn care and pesticides used by the individual homeowners.

**ATTACHMENT D**



## **GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024

### **VOLUME AND CHARACTER OF STORMWATER SERENITY OAKS, UNIT 5**

The stormwater runoff for the preconstruction conditions of these 65.15 acres would be across rocky soil, with native vegetation consisting of grasses, brush and trees. These precondition flows, proceed south and southeasterly along existing swales. A completed earthen detention pond and existing swales transfer the runoff to the Rebecca Creek and ultimately the Guadalupe River.

The proposed Single-Family Residential subdivision will generate an insignificant increase in stormwater runoff, which after exiting each residential lot; will be carried by roadside ditches, drainage pipe, improved earthen channels to the south of this development to existing swales on developer owned property, eventually to the Guadalupe River.

After construction there will be inconsequential amount of sediment and chemicals carried from this project.

See Attachment "X", Page CZP 1 and 2, Drainage Area Map with Runoff Calculations for Post Developed Stormwater flows. Pre Developed flows were used to design an existing (and Comal County approved) detention basin upstream from this unit. These Pre Condition flows were computed using large drainage areas encompassing the total watershed for the pond and are irrelevant to flows needed for designing the channels and pipe crossings for this unit and are, therefore, individually calculated or shown.

**ATTACHMENT E**



## **GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024


### **OSSF SUITABILITY LETTER FROM AUTHORIZED AGENT SERENITY OAKS, UNIT 5**

An on-site sewage facility (OSSF) will be provided for each residential lot in this subdivision as a means of sewage disposal. A permit for each individual OSSF will be issued after approval by Comal County engineer's Office, the licensing authority.

The "OSSF Suitability Letter" from Comal County for the Subdivision follows this page.

Each lot must obtain a permit from the Comal County Assistant County Engineer, to construct an OSSF. This requires that each system is designed by either a licensed professional engineer or a registered sanitarian and installed by a licensed installer. The design and installation shall be in compliance with 30 TAC §285.

Signed: \_\_\_\_\_

  
Richard M. Gallegos, P.E.  
Authorized Agent

12/28/24

**ATTACHMENT F**

**COMAL COUNTY**  
ENGINEER'S OFFICE



November 8, 2022

Scott Armstrong  
15315 San Pedro  
San Antonio, TX 78280  
e-mail: ACS1@SATX.RR.COM

Re: Serenity Oaks Unit 5 within Comal County Texas

Dear Mr. Armstrong:

We are in receipt of your August 23, 2022 application for the referenced proposed subdivision. We approved your application (see attached).

If you have any questions or need additional information, please contact our office.

Sincerely,

Robert Boyd, P.E.  
Comal County Assistant Engineer

cc: Jen Crowmover, Comal County Commissioner, Precinct No. 4

Application for Licensing Authority Recommendation  
for Private Sewerage Facilities for a Proposed Subdivision

2022-  
100016

Fee Schedule:

5 or less tracts: \$20/tract

6 or more tracts: \$100 base fee + \$5/tract

Total Fee: \$ 325.00

Received by: Kg

Make Check Payable to Comal County

Date: August 23, 2022

Subdivision Name: SECRECY OAKS, UNIT FIVE

Owner's Name: GALE ESTATES, L.L.C.

Address: 15315 SAW REDD, SAN ANTONIO, TX 78232

Phone #: 710-994-5237

According to TAC §285.4(c), persons proposing residential subdivisions, manufactured housing communities, multi-unit residential developments, business parks, or other similar structures that use OSSFs for sewage disposal shall submit planning materials, prepared by a professional engineer or professional sanitarian, for these developments to the permitting authority and receive approval prior to submitting an OSSF application:

- An overall site plan
- Topographic map
- 100-year floodplain map
- Soil survey
- Location of water wells
- Locations of easements as identified in TAC §285.91(10) (relating to Tables)
- A complete report detailing the types of OSSFs to be considered and their compatibility with area-wide drainage and groundwater
- A comprehensive drainage plan
- Edwards Aquifer requirements that are pertinent to the proposed OSSF
- If the proposed development includes restaurants or buildings with food service establishments, the planning materials must show adequate land area for doubling the land needed for the treatment units

Comal County also asks for an existing improvements sketch and gate combination(s) in order to adequately inspect the site for use of OSSFs for sewage disposal.

Applicant/Agent Signature

Date of Review (must be within 45 days of receipt): 11/8/22

☒ Approved

☐ Denied

Reason(s) for Denial: \_\_\_\_\_

Reviewer: \_\_\_\_\_

J.D.R.

\* Note: This sheet shall be first with all planning materials listed above following behind.



**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024

**ALTERNATIVE SECONDARY CONTAINMENT METHODS  
SERENITY OAKS, UNIT 5**

NOT APPLICABLE TO THIS PLAN.

**ATTACHMENT G**





**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024

**A.S.T. CONTAINMENT STRUCTURE DRAWINGS  
SERENITY OAKS, UNIT 5**

NOT APPLICABLE TO THIS PLAN.

**ATTACHMENT H**



## **GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024

### **20% OR LESS IMPERVIOUS COVER WAIVER SERENITY OAKS, UNIT 5**

I hereby certify that Serenity Oaks Subdivision, Unit 5 is being developed as Single-Family Residential with a total purposed impervious cover of less than 20%.

Signed: \_\_\_\_\_

Richard M. Gallegos, P.E.  
Authorized Agent

12/28/24

**ATTACHMENT I**



## **GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 28, 2024

### **EXEMPTION FROM PERMANENT BMPs SERENITY OAKS, UNIT 5 For Upgradient Stormwater**

Serenity Oaks Subdivision, Unit 5 is by TCEQ rule, exempt from providing permanent BMPs for stormwater control. This exemption is allowed since it is to be a Single-Family Residential Development and the total impervious cover, including housing, streets, drives, sidewalks and all other impervious structures, cover less than 20% of the total 65.15 acres.

The total proposed impervious cover of 13.2% is calculated on page 2, Section A. of the Contributing Zone Plan Application for Regulated Activities.

Storm waters generated upgradient and flowing across this site are from large Single Family Residential tracts and present no negative contaminants. These flows will be opposed by silt fencing and/or rock berms in conjunction with those generated onsite. Although clean storm water has a potential to become contaminated as it flows downstream over soil.

**ATTACHMENT J**



**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 29, 2024

**EXEMPTION FROM PERMANENT BMPs  
SERENITY OAKS, UNIT 5  
For On-Site Stormwater**

Serenity Oaks Subdivision, Unit 5 is by TCEQ rule, exempt from providing permanent BMPs for stormwater control. This exemption is allowed since it is to be a Single-Family Residential Development and the total impervious cover, including housing, streets, drives, sidewalks and all other impervious structures, cover less than 20% of the total 65.15 acres.

The total proposed impervious cover of 13.2% is calculated on page 2, Section A. of the Contributing Zone Plan Application for Regulated Activities. Drawings supporting calculation of this percentage may be seen on Sheet CZP 2, as part of Attachment "X".

**ATTACHMENT K**



**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 29, 2024

**EXEMPTION FROM PERMANENT BMPs  
SERENITY OAKS, UNIT 5  
For Surface Streams**

Serenity Oaks Subdivision, Unit 5 is by TCEQ rule, exempt from providing permanent BMPs for stormwater control. This exemption is allowed since it is to be a Single-Family Residential Development and the total impervious cover, including housing, streets, drives, sidewalks and all other impervious structures, cover less than 20% of the total 65.15 acres.

The total proposed impervious cover of 13.2% is calculated on page 2, Section A. of the Contributing Zone Plan Application for Regulated Activities. Drawings supporting calculation of this percentage may be seen on Sheet CZP 2, as part of Attachment "X".

**ATTACHMENT L**



**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 29, 2024


**CONSTRUCTION PLANS  
SERENITY OAKS, UNIT 5  
For Permanent BMPs**

Serenity Oaks Subdivision, Unit 5 is by TCEQ rule, exempt from providing permanent BMPs for stormwater control. Therefore, no BMP construction plans are provided.

However, installation instructions are provided in Attachment "X", Page CZP 2.

**ATTACHMENT M**

# STREET & DRAIN CIVIL CONSTRUCTION PLANS FOR SERENITY OAKS SUBDIVISION UNIT 5

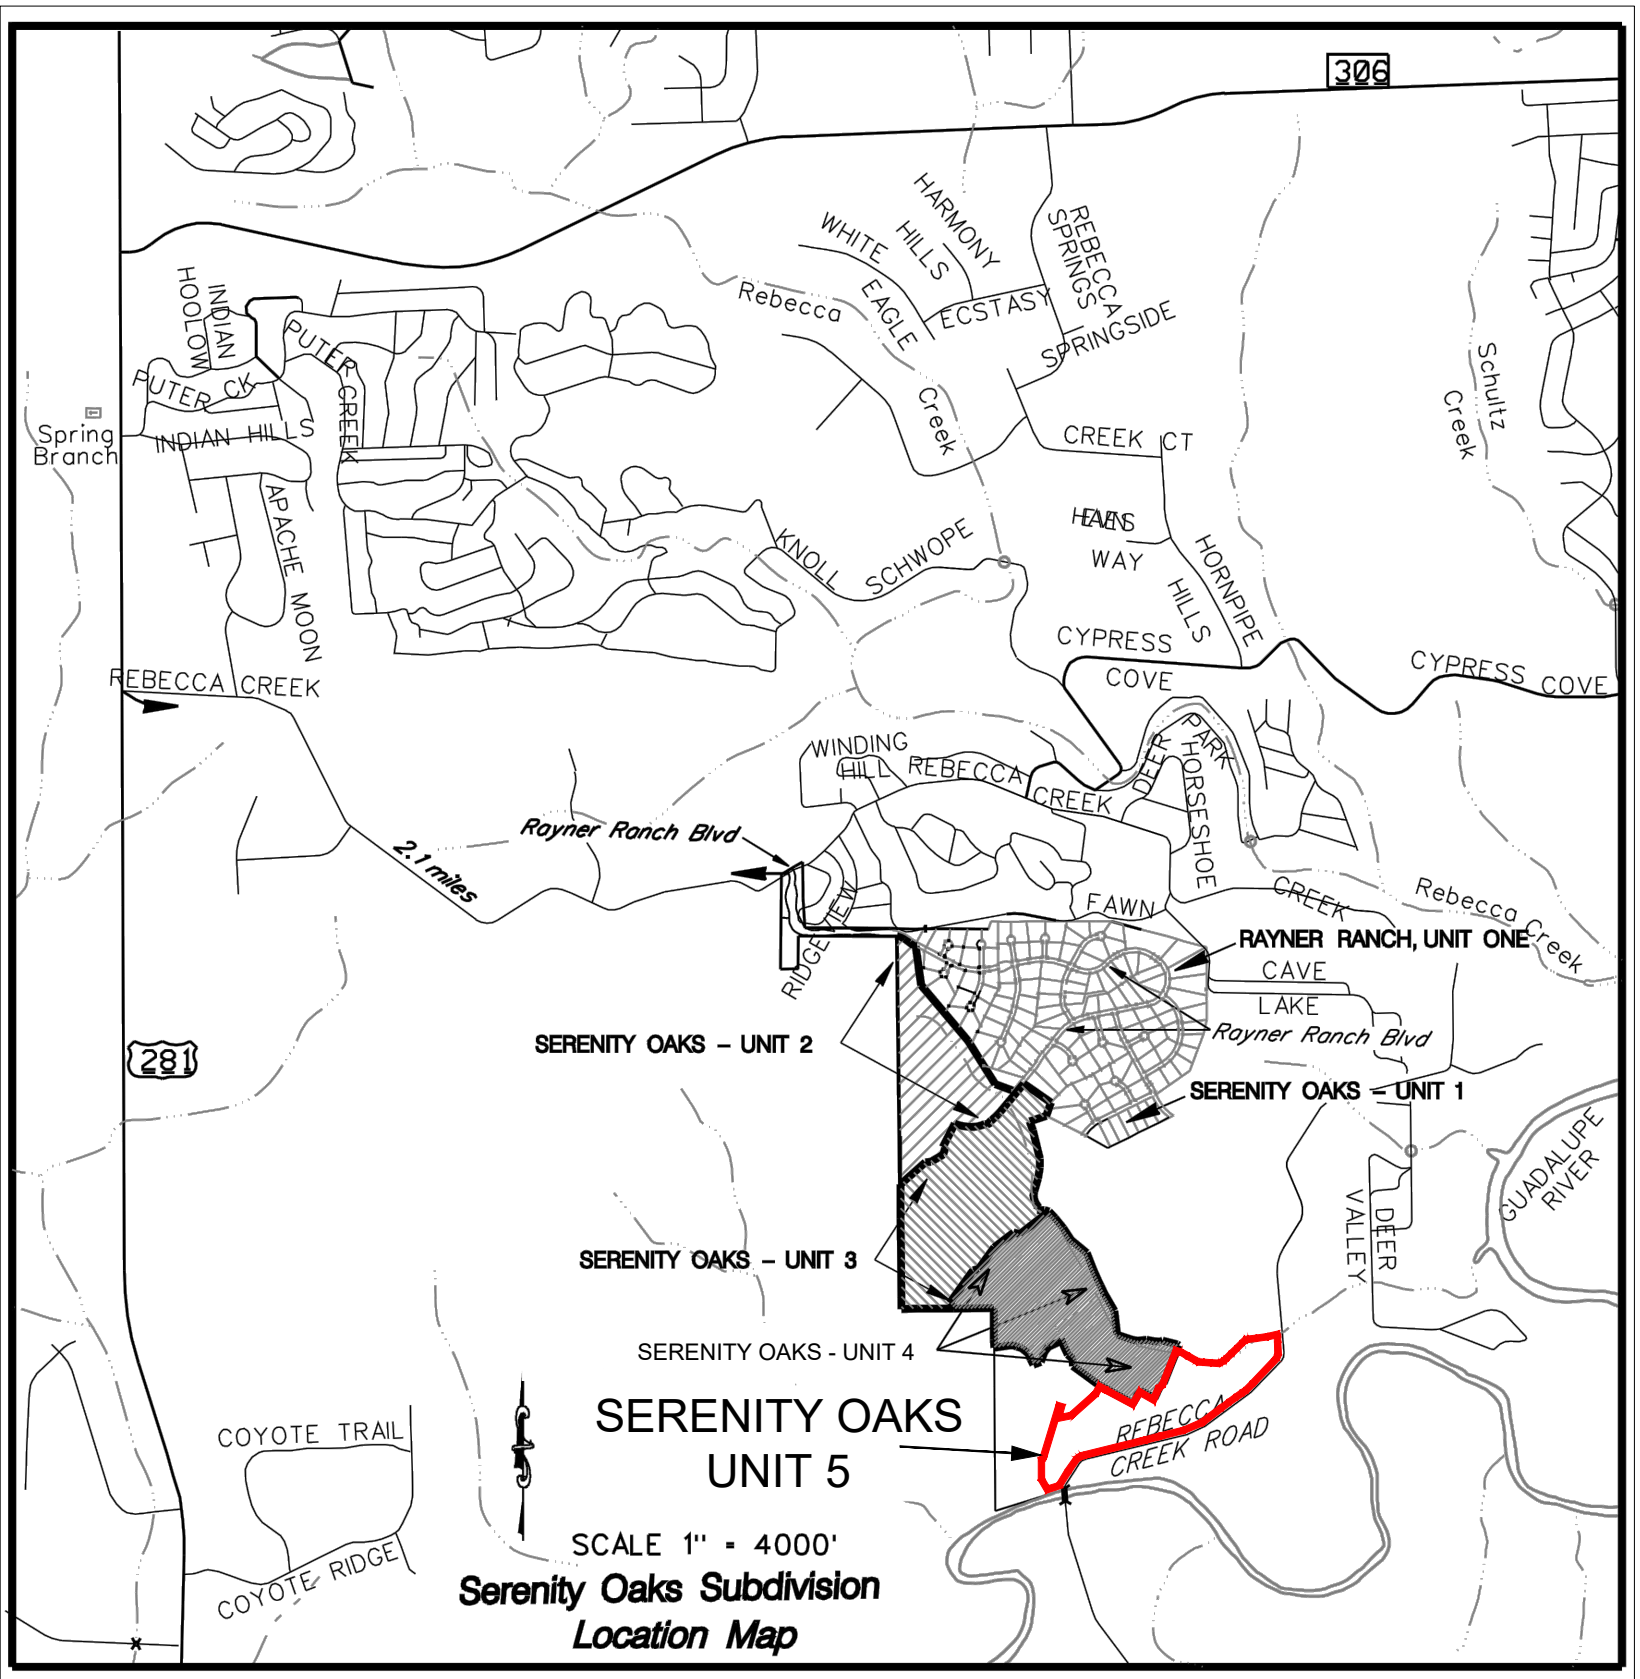

NOT-TO-SCALE

PREPARED FOR:

**GALE ESTATES, LLC**  
15315 SAN PEDRO  
SAN ANTONIO, TEXAS 78232  
(210) 494-5237

PREPARED BY:



SAN ANTONIO, TEXAS    [www.gallegoseng.com](http://www.gallegoseng.com)    PH: 210.641.0812  
FIRM REGISTRATION # F-003084

## SHEET INDEX

- 1 COVER
- 2 GENERAL NOTES
- 3 SWPPP
- 4 SWPPP NARRATIVE
- 5 SWPPP DETAILS
- 6 OVERALL PROJECT LAYOUT
- 7 STREET PLAN & PROFILE – SERENITY PASS 0+00 – 12+00
- 8 STREET PLAN & PROFILE – SERENE PARK 10+50 – 20+50
- 9 STREET PLAN & PROFILE – SERENE PARK 0+00 – 10+50
- 10 CHANNEL A PLAN & PROFILE – CHANNEL A 0+00 – 10+00
- 11 CHANNEL A PLAN & PROFILE – CHANNEL A 10+00 – 16+20.44
- 12 CHANNEL B PLAN & PROFILE – CHANNEL B 0+00 – 2+78
- 13 CHANNEL C PLAN & PROFILE – CHANNEL C 0+00 – 1+33
- 14 CHANNEL F PLAN & PROFILE – CHANNEL F 0+00 – 3+55
- 15 ENTRANCE TO REBECCA CREEK – DRIVEWAY DETAILS
- 16 DETAILS – RIPRAP DETAILS
- 17 DETAILS – 4-WAY INLET
- 18 GENERAL DETAILS
- 19 TRAFFIC SIGNAGE PLAN
- 20 TXDOT SIGN MOUNTING DETAIL SMD (GEN)-08
- 21 TXDOT SIGN MOUNTING DETAIL SMD (SLIP-1)-08
- 22 TXDOT SIGN MOUNTING DETAIL SMD (SLIP-2)-08
- 23 DETENTION POND LAYOUT AND DETAILS
- 24 CULVERT CROSSING DETAILS – CULVERTS B, F1, AND F2



THE SEAL APPEARING ON  
THIS DOCUMENT WAS  
AUTHORIZED BY  
RICHARD M. GALLEGOS, P.E. 86916  
APRIL 8, 2023  
ALTERATION OF A SEALED DOCUMENT  
WITHOUT PROPER NOTIFICATION  
TO THE RESPONSIBLE ENGINEER  
IS AN OFFENSE UNDER THE  
TEXAS ENGINEERING PRACTICE ACT



GENERAL NOTES

1. THE CONTRACTOR SHALL INFORM AND COORDINATE HIS EFFORT WITH CANYON LAKE WATER SERVICE COMPANY FOR CONNECTING TO EXISTING WATER MAINS. CONTRACTOR SHALL VERIFY EXISTING PIPE MATERIALS AND CLASSES PRIOR TO PURCHASING CONNECTION FITTINGS. CONTRACTOR SHALL OBTAIN A WATER CONNECTION PERMIT TO TIE INTO THE EXISTING WATER MAIN BEFORE THE START OF CONSTRUCTION.
2. ALL EXCESS TRENCH EXCAVATION MATERIAL SHALL BE DISPOSED OF ON SITE IN A TIMELY MANNER. THE CONTRACTOR SHALL PROPERLY SCHEDULE OPERATIONS EACH DAY SO AS TO ACCOMPLISH BACKFILL (COMPACTION) AND REMOVAL OF EXCESS MATERIALS AND PLACE BASE MATERIAL AT THE END OF EACH DAYS WORK AT LEAST ONE (1) HOUR BEFORE SUNDOWN, NO OPEN HOLES OR TRENCHES WILL BE ALLOWED OVERNIGHT WITHIN A PUBLIC RIGHT-OF-WAY. CONTRACTOR SHALL COMPLY WITH ALL CITY REQUIREMENTS FOR WORK WITHIN PUBLIC STREET RIGHTS-OF-WAY.
3. OWNER OCCUPANCY OF THE WATER SYSTEMS SHALL BE GOVERNED BY THE RULES FOR OWNER'S RIGHT TO OCCUPANCY IN ACCORDANCE WITH ANY APPLICABLE REQUIREMENTS OF THE CITY. REQUIRED INSPECTIONS AND TESTS SHALL HAVE BEEN SUCCESSFULLY COMPLETED AND RECORDED PRIOR TO OCCUPANCY. PRIOR TO OCCUPANCY BY THE OWNER, THE CONTRACTOR SHALL PROVIDE OPERATION AND MAINTENANCE OF THE SYSTEM INSTALLED WITHIN THE RIGHTS-OF-WAY AND EASEMENTS OF THIS PROJECT.
4. THE CONTRACTOR SHALL REFERENCE AND COORDINATE WITH MECHANICAL, ELECTRICAL, LANDSCAPE, IRRIGATION AND PLUMBING (MEP) PLANS FOR PRECISE UTILITY SERVICE LOCATIONS. INSTALLATION SHALL MEET ALL CITY CODE AND UTILITY COMPANY REQUIREMENTS.
5. CONTRACTOR AND/OR CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR STRUCTURAL DESIGN/GEOTECHNICAL/SAFETY/EQUIPMENT CONSULTANT, IF ANY, SHALL REVIEW THESE PLANS AND AVAILABLE GEOTECHNICAL INFORMATION AND THE ANTICIPATED INSTALLATION SITE(S) WITHIN THE PROJECT WORK AREA IN ORDER TO IMPLEMENT CONTRACTOR'S TRENCH EXCAVATION SAFETY PROTECTION SYSTEMS, PROGRAMS AND/OR PROCEDURES. THE CONTRACTOR'S IMPLEMENTATION OF THE SYSTEMS, PROGRAMS AND/OR PROCEDURES SHALL PROVIDE FOR ADEQUATE TRENCH EXCAVATION SAFETY PROTECTION THAT COMPLIES WITH AS A MINIMUM, OSHA STANDARDS FOR TRENCH EXCAVATIONS. SPECIFICALLY, CONTRACTOR AND/OR CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR SAFETY CONSULTANT SHALL IMPLEMENT A TRENCH SAFETY PROGRAM IN ACCORDANCE WITH OSHA STANDARDS GOVERNING THE PRESENCE AND ACTIVITIES OF INDIVIDUALS WORKING IN AND AROUND TRENCH EXCAVATION.
6. CONTRACTOR SHALL BE RESPONSIBLE FOR THE SAFE AND PROPER REMOVAL AND LAWFUL DISPOSAL OF ALL TRASH AND DEBRIS IN ACCORDANCE WITH APPLICABLE CODES AND CITY REGULATIONS.
7. CONTRACTOR IS RESPONSIBLE FOR REMOVAL OF ALL WASTE MATERIALS UPON PROJECT COMPLETION.
8. THE CONTRACTOR SHALL FURNISH AND MAINTAIN ALL TRAFFIC CONTROL DEVICES, LIGHTING, OR WARNING CONTROL DEVICES USED OR REQUIRED TO COMPLETE WORK.
9. ALL SPOIL AND OTHER UNSUITABLE MATERIAL FROM THIS PROJECT SHALL BE DISPOSED ON SITE BY THE CONTRACTOR AT THEIR EXPENSE IN ACCORDANCE WITH LOCAL, STATE, & FEDERAL REGULATIONS. NO WORK OR MATERIALS SHALL BE STARTED OR PLACED WITHIN THE 100-YEAR FLOODPLAIN WITH PRIOR APPROVAL.
10. THE CONTRACTOR SHALL IMMEDIATELY NOTIFY THE ARCHITECT/ENGINEER OF ANY AND ALL CONFLICTS OR DISCREPANCIES OF THESE PLANS.
11. CONTRACTOR AGREES THAT HE SHALL ASSUME SOLE AND COMPLETE RESPONSIBILITY FOR JOB SITE CONDITIONS DURING THE CONSTRUCTION OF THE PROJECT, INCLUDING SAFETY OF ALL PERSONS AND PROPERTY; THAT THIS REQUIREMENT SHALL APPLY CONTINUOUSLY AND NOT BE LIMITED TO NORMAL WORKING HOURS AND THAT THE CONTRACTOR SHALL DEFEND, INDEMNIFY AND HOLD THE OWNERS, THE ARCHITECT AND THE ENGINEER HARMLESS FROM ANY AND ALL LIABILITY, REAL OR ALLEGED, IN CONNECTION WITH THE PERFORMANCE OF THE WORK ON THIS PROJECT, EXCEPTING FROM LIABILITY ARISING FROM SOLE NEGLIGENCE OF THE OWNER, ARCHITECT OR ENGINEER.
12. BARRICADES AND WARNING SIGNS SHALL CONFORM TO THE TEXAS MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (TMUTCD) AND GENERALLY BE LOCATED TO AFFORD MAXIMUM PROTECTION TO THE PUBLIC AS WELL AS CONSTRUCTION PERSONNEL AND EQUIPMENT AND TO ASSURE AN EXPEDITIOUS TRAFFIC FLOW AT ALL TIMES DURING CONSTRUCTION. THE SIGNS SHALL BE COORDINATED WITH SEQUENCE OF CONSTRUCTION.
13. THE CONTRACTOR SHALL BE RESPONSIBLE FOR ALL TRAFFIC CONTROL IN ACCORDANCE WITH TEXAS MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (TMUTCD) STANDARDS. THE CONTRACTOR SHALL ESTABLISH A TRAFFIC ROUTING PLAN FOR CONSTRUCTION MATERIALS EQUIPMENT AND ALL OTHER SHIPMENTS INTO AND AWAY FROM THE SITE WHICH IS ACCEPTABLE TO THE CITY OFFICIALS. ONCE THIS PLAN IS ESTABLISHED, THE CONTRACTOR SHALL IMPLEMENT THE CONTROLS DICTATED THEREIN.
14. THE CONTRACTOR SHALL SAWCUT ANY EXISTING CURB & GUTTER, ASPHALT, CONCRETE, ETC. TO RECEIVE ALL NEW WORK AND TO FACILITATE ALL DEMOLITIONS.
15. THE CONTRACTOR SHALL REPAIR ANY AND ALL DAMAGED PAVING OR OTHER SURFACE FEATURES DUE TO THE CONTRACTOR'S CONSTRUCTION ACTIVITIES. REPAIR OR REPLACEMENT SHALL BE AT THE CONTRACTORS EXPENSE.
16. CONTRACTOR SHALL BE RESPONSIBLE FOR PROVIDING REQUIRED SECURITY TO PROTECT HIS OWN PROPERTY, MATERIALS, EQUIPMENT AND WORK IN PROGRESS.
17. THE CONTRACTOR SHALL VERIFY ALL CONDITIONS WITHIN THE WORK SITE, INCLUDING SOIL CONDITIONS, IN THE FIELD BEFORE COMMENCING WORK. IT IS THE CONTRACTOR'S RESPONSIBILITY TO REPORT ANY DISCREPANCIES TO THE ARCHITECT/ENGINEER BEFORE PROCEEDING WITH THE WORK.

18. COMAL COUNTY SHALL HAVE ACCESS TO PARTS OF THE PROJECT DURING ALL PHASES OF CONSTRUCTION ACTIVITY. CONTRACTOR SHALL CONTINUOUSLY MONITOR CONSTRUCTION OPERATIONS AND COOPERATE WITH THE COUNTY TO MINIMIZE INCONVENIENCES TO THE PUBLIC USE OF THE ADJACENT BUSINESSES. THE CONTRACTOR SHALL CONFINE OPERATIONS TO SUCH AN AREA AS TO PREVENT WORKERS, MATERIALS OR EQUIPMENT INTO AREAS OCCUPIED OR USED BY THE ADJACENT BUSINESSES OR THE PUBLIC.
19. CONTRACTOR SHALL COMPLY WITH ALL APPLICABLE BUILDING CODES AND REGULATIONS FOR CONSTRUCTION AS WELL AS SAFETY CODES AND INSPECTION PROVISIONS APPLICABLE TO THIS PROJECT.
20. CONTRACTOR SHALL BE RESPONSIBLE FOR THE PROPER AND ADEQUATE PROTECTION OF ALL LANDSCAPING AND TREES WHERE DEMOLITION WILL OCCUR. THE CONTRACTOR SHALL BE RESPONSIBLE FOR REPLACEMENT IF DAMAGE IS CAUSED DURING DEMOLITION OR CONSTRUCTION AT NO ADDITIONAL COST TO THE OWNER.
21. CONTACT COUNTY PUBLIC WORKS DEPT. 48 HOURS PRIOR TO ANY CONCRETE PLACEMENT WITHIN CITY RIGHT-OF-WAY TO MAKE ARRANGEMENTS FOR INSPECTION.
22. ALL TEMPORARY EROSION AND SEDIMENTATION CONTROLS WILL BE INSTALLED BY THE CONTRACTOR PRIOR TO CONSTRUCTION, MAINTAINED DURING CONSTRUCTION AND REMOVED BY THE CONTRACTOR IMMEDIATELY FOLLOWING THE FINAL PROJECT ACCEPTANCE.
23. THE PLACEMENT OF EROSION AND SEDIMENTATION CONTROLS SHALL BE IN ACCORDANCE WITH T.C.E.Q. GUIDELINES. A COPY OF THE APPROVED SWPPP SHALL BE PROVIDED TO THE CITY PRIOR TO CONSTRUCTION.
24. THE CONTRACTOR SHALL BE RESPONSIBLE FOR DEVELOPING ALL DIMENSION/CONSTRUCTION CONTROL THROUGHOUT THE DURATION OF THE PROJECT WORK. THE CONTRACTOR SHALL AT HIS OWN COST VERIFY ALL DIMENSIONS, ELEVATIONS AND CONTROL USED FOR THE PROJECT WHICH MAY IMPACT THE CONTRACTOR'S PERFORMANCE ON THE WORK. ALL COST OF REPLACEMENT OF EXISTING SURVEY OR PROPERTY CONTROL DUE TO THE CONTRACTOR'S WORK SHALL BE BORNE BY THE CONTRACTOR.
25. THE CONTRACTOR IS REQUIRED TO VERIFY PROJECT ELEVATIONS.
26. CONTRACTOR SHALL MAINTAIN ADEQUATE DRAINAGE THROUGHOUT THE DURATION OF THE PROJECT WORK. THE CONTRACTOR SHALL RESHAPE, REGRADE AND RESTORE ANY DRAINAGE ROUTES THAT WERE DISTURBED DURING CONSTRUCTION SO AS NOT TO IMPEDE DRAINAGE.
27. PRIOR TO FINAL ACCEPTANCE, THE SITE SHALL BE CHECKED FOR CONFORMANCE TO FINAL GRADES BY THE CONTRACTOR.
28. ALL CONSTRUCTION DEBRIS, TRASH AND UNSUITABLE MATERIAL SHALL BE DISPOSED OF IN APPROVED CONTAINERS AND REMOVED TO AN APPROVED SPOIL DISPOSAL SITE BY THE CONTRACTOR.
29. THE PROJECT HAS NO TEMPORARY OR PERMANENT SPOIL OR TRASH DISPOSAL AREAS. ALL SPOILS AND TRASH ARE CONSIDERED PROPERTY OF THE CONTRACTOR AND SHALL BE REMOVED FROM THE SITE ON A DAILY BASIS. THE CONTRACTOR SHALL DISPOSE OF ALL WASTES TO A LICENSED LANDFILL AS REGULATED AND PERMITTED BY CURRENT LAW AND REGULATIONS.
30. ALL EXISTING GRADES INSIDE THE CONSTRUCTION LIMITS LINE NOT AFFECTED BY CONSTRUCTION SHALL REMAIN EXCEPT AS REQUIRED FOR POSITIVE DRAINAGE FROM SITE.
31. CONTRACTOR SHALL PROVIDE MINIMAL GRADING FOR POSITIVE DRAINAGE OF WATER AWAY FROM BUILDINGS AND FOR ADEQUATE DRAINAGE OF WATER FROM SITE AS REQUIRED.
32. CONTRACTOR SHALL BE RESPONSIBLE FOR ACQUIRING ALL PERMITS, TESTS, APPROVALS, AND ACCEPTANCES REQUIRED TO COMPLETE CONSTRUCTION OF THE PROJECT.
33. DUE TO FEDERAL REGULATION TITLE 49, PART 192.181, GAS UTILITY MUST MAINTAIN ACCESS TO GAS VALVES AT ALL TIMES. THE CONTRACTOR MUST PROTECT AND WORK AROUND ANY GAS VALVES THAT ARE IN THE PROJECT AREA.
34. THE CONTRACTOR SHALL VERIFY THE EXACT LOCATION OF UNDERGROUND UTILITIES AND DRAINAGE STRUCTURES WHETHER SHOWN ON PLANS OR NOT.
35. ALL CONSTRUCTION, UNLESS OTHERWISE NOTED SHALL CONFORM TO THE COMAL COUNTY PUBLIC WORKS STANDARD SPECIFICATIONS FOR CONSTRUCTION AND IS SUBJECT TO INSPECTIONS AND APPROVAL BY THE COUNTY.
36. BIDDERS ARE NOTIFIED TO MAKE SUBSURFACE INVESTIGATIONS WHERE THE AREA IS KNOWN TO CONTAIN POOR SOILS. ALL EXCAVATION SHALL BE UNCLASSIFIED REGARDLESS OF MATERIAL ENCOUNTERED. NO ADDITIONAL PAYMENT WILL BE MADE FOR WATER, SAND, GRAVEL, OR OTHER UNSTABLE CONDITIONS ENCOUNTERED IN THE EXCAVATION.
37. CONTRACTOR SHALL IMMEDIATELY NOTIFY THE ENGINEER OF ANY QUESTIONS THAT MAY ARISE CONCERNING THE INTENT, PLACEMENT, OR LIMITS OF DIMENSIONS ON GRADES NECESSARY FOR CONSTRUCTION OF THIS PROJECT.
38. REFER TO GEOTECHNICAL REPORT FOR SUBSURFACE INFORMATION AND CONSTRUCTION GUIDELINES.
39. CONTRACTOR MUST CALL THE TEXAS ONE CALL SYSTEM BEFORE DIGGING, DRILLING, OR BLASTING, 48 HOURS PRIOR TO SUCH ACTIVITIES. (DIAL 811)
40. ALL HANDICAP RAMPS, SIGNS, SYMBOLS, AND PAINTED SURFACES MUST CONFORM TO THE LATEST A.D.A. REQUIREMENTS. ALL RAMPS AND SLOPES SHALL ALSO CONFORM TO THE LATEST A.D.A. REQUIREMENTS.
41. BARRICADES AND TRAFFIC CONTROL ARE SUBSIDIARY ITEMS. INCLUDE IN BASE BID PHASE.

GRADING NOTES

1. BOUNDARY AND TOPOGRAPHIC INFORMATION WITHIN PROPOSED RIGHT-OF-WAYS WAS TAKEN FROM A SURVEY BY ACS INC. LAND SURVEYING.
2. NEW FINISHED CONTOURS SHOWN ARE TOP OF PAVING IN AREAS TO RECEIVE PAVEMENT AND TOP OF TOPSOIL IN AREAS TO BE SEEDED.
3. TOPSOIL AND SEEDING OF ALL DISTURBED AREA IS THE SITE CONTRACTOR'S RESPONSIBILITY. SITE GRADING CONTRACTOR SHALL PLACE ALL TOPSOIL REQUIRED IN CURBED ISLANDS AND IN LANDSCAPED AREAS.
  - a. ROUGH GRADE ELEVATIONS SHALL BE AS FOLLOWS:
    - I. 4" BELOW FINISHED CONTOURS IN SEEDED AREAS.
    - II. 18" BELOW FINISHED CONTOURS IN CONCRETE PAVED AREAS.
    - III. 8" BELOW THE SIDEWALK AREAS.
4. DIMENSIONS ON BUILDINGS ARE FOR GRADING PURPOSES ONLY AND ARE NOT TO BE USED TO LAYOUT FOOTINGS.
5. REFER TO STRUCTURAL DRAWINGS FOR FOUNDATION INFORMATION.
6. GRADING CONTRACTOR SHALL NOTIFY AND COOPERATE WITH ALL UTILITY COMPANIES OR FIRMS HAVING FACILITIES ON OR ADJACENT TO THE SITE BEFORE DISTURBING, ALTERING, REMOVING, RELOCATING, ADJUSTING OR CONNECTING TO SAID FACILITIES. CONTRACTOR SHALL PAY ALL COSTS IN CONNECTION WITH THE ALTERATION OR RELOCATION OF THE FACILITIES. CONTRACTOR TO RAISE OR LOWER TOPS OF EXISTING MANHOLES AS REQUIRED TO MATCH FINISHED GRADES.
7. GRADING CONTRACTOR SHALL COOPERATE AND WORK WITH ALL OTHER CONTRACTORS PERFORMING WORK ON THIS PROJECT TO INSURE PROPER AND TIMELY COMPLETION OF THIS PROJECT.
8. THE GRADING CONTRACTOR SHALL USE WHATEVER MEASURES ARE REQUIRED TO PREVENT SILT AND CONSTRUCTION DEBRIS FROM FLOWING ONTO ADJACENT PROPERTIES. CONTRACTOR SHALL COMPLY WITH ALL LOCAL EROSION AND SILTATION ORDINANCES. CONTRACTOR TO REMOVE ALL TEMPORARY EROSION CONTROL STRUCTURES UPON COMPLETION OF PERMANENT DRAINAGE FACILITIES AND NOT BEFORE ALL AREAS DRAINING INTO THESE STRUCTURES ARE SUFFICIENTLY STABILIZED.
9. FOR ANY WORK ON THE COUNTY RIGHT-OF-WAY, THE GRADING CONTRACTOR SHALL NOT STORE MATERIAL, EXCESS DIRT OR EQUIPMENT IN THE RIGHT-OF-WAY. THE PAVEMENT SHALL BE KEPT FREE FROM ANY MUD OR EXCAVATION WASTE FROM TRUCKS OR OTHER EQUIPMENT. ON COMPLETION OF WORK ALL EXCESS
10. MATERIAL SHALL BE REMOVED FROM THE RIGHT-OF-WAY. A QUALIFIED SOILS LABORATORY SHALL BE ON-SITE DURING EXCAVATION TO DETERMINE THE SUITABILITY OF THE EXISTING SUB-GRADE AND EXISTING ON-SITE MATERIAL PRIOR TO BEGINNING MAY FILLING OPERATIONS.
11. GRADING CONTRACTOR SHALL TAKE ALL AVAILABLE PRECAUTIONS TO CONTROL DUST. CONTRACTOR TO CONTROL DUST BY SPRINKLING, OR BY OTHER METHODS AS DIRECTED BY ENGINEER AND/OR OWNER'S REPRESENTATIVE AT NOT ADDITIONAL COST TO OWNER.
12. GRADING CONTRACTOR TO COMPLY WITH ALL STATE AND LOCAL SEDIMENT CONTROL AND AIR POLLUTION ORDINANCES OR RULES. BEFORE ANY MACHINE WORK IS DONE, CONTRACTOR SHALL STAKE OUT AND MARK THE ITEMS ESTABLISHED BY THE SITE PLAN. CONTROL POINTS SHALL BE PRESERVED AT ALL TIMES DURING THE COURSE OF THE PROJECT. ARCHITECT MUST APPROVE STAKED ITEMS PRIOR TO CONSTRUCTION.
13. CONTRACTOR TO COORDINATE ALL WORK WITH OTHER UTILITY INSTALLATIONS NOT COVERED IN PLANS (ELECTRIC, TELEPHONE, GAS, CABLE, ETC.) AND ALLOW FOR THEIR OPERATIONS AND CONSTRUCTION TO BE PERFORMED.
14. EXISTING UTILITIES ARE APPROXIMATE AND MUST BE FIELD VERIFIED PRIOR TO CONSTRUCTION.

UTILITY LOCATION

THE EXISTING UTILITIES AS SHOWN ARE FROM INFORMATION PROVIDED BY THE UTILITY COMPANIES AND FIELD OBSERVATIONS. HOWEVER, NOT ALL EXISTING UTILITY LINES HAVE NOT BEEN FIELD LOCATED, AND ARE SHOWN IN THE APPROXIMATE LOCATION FOR THE CONVENIENCE OF THE CONTRACTOR. IT SHALL BE THE RESPONSIBILITY OF THE CONTRACTOR TO FIELD VERIFY THE EXACT LOCATION AND DEPTH OF ALL UTILITIES PRIOR TO COMMENCING EXCAVATION, AND TO NOTIFY THE OWNERS OF THOSE UTILITIES AT LEAST FORTY-EIGHT HOURS IN ADVANCE OF CONSTRUCTION. THE CONTRACTOR SHALL MAKE PROVISIONS TO PROTECT OR SUPPORT ALL EXISTING UTILITIES DURING CONSTRUCTION. ANY DAMAGE TO EXISTING UTILITIES DURING CONSTRUCTION SHALL BE REPAIRED TO THE CURRENT STANDARDS OF THE OWNER OF THE UTILITY AT THE EXPENSE OF THE CONTRACTOR.

TRENCH EXCAVATION PROTECTION

CONTRACTOR AND/OR CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR STRUCTURAL DESIGN/GEOTECHNICAL//SAFETY/EQUIPMENT CONSULTANT, IF ANY SHALL REVIEW THESE PLANS AND ANY AVAILABLE GEOTECHNICAL INFORMATION AND THE ANTICIPATED INSTALLATION SITE(S) WITHIN THE PROJECT WORK AREA IN ORDER TO DEVELOP THE CONTRACTOR'S PLANS TO IMPLEMENT THE PROJECT DESCRIBED IN THE CONTRACT DOCUMENTS. THE CONTRACTOR'S PLAN SHALL PROVIDE FOR ADEQUATE TRENCH SAFETY SYSTEMS THAT COMPLY WITH AS MINIMUM, OSHA STANDARDS FOR TRENCH EXCAVATIONS. SPECIFICALLY, CONTRACTOR OF CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR SAFETY CONSULTANT SHALL DEVELOP AND IMPLEMENT A TRENCH SAFETY PROGRAM IN ACCORDANCE WITH OSHA STANDARDS GOVERNING THE PRESENCE AND ACTIVITIES OF INDIVIDUALS WORKING IN AND AROUND TRENCH EXCAVATION.

NOTE:  
CONTRACTOR TO FIELD VERIFY  
LOCATIONS OF ALL EXISTING  
UTILITY LINES, VALVES, AND  
APPURTENANCES.  
(NO SEPARATE PAY ITEM)

REVISIONS				
NO.	DATE	DESCRIPTION	BY	
PROJ. #:	DATE:	DRAWN BY:	CHECKED BY:	R.M.G.
US-SER	09/30/22	S.G.	S.G.	

PRIN REGISTRATION # F43084

**GALLEGOS  
ENGINEERING,  
INC.**

SAN ANTONIO, TEXAS    www.gallegoseng.com    PH: 210.641.0812

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLEGOS, P.E. 88916 NOVEMBER 2, 2022 ALTERATION OF A SEALED DOCUMENT WITHOUT THE SIGNATURE OF THE REGISTERED PROFESSIONAL ENGINEER IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT






SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

STREET AND DRAINAGE PLANS  
GENERAL NOTES  
GALE ESTATES, L.L.C.






ESTIMATED STORM WATER POLLUTION PREVENTION PLAN & TEMPORARY SEDIMENTATION AND EROSION CONTROL PLAN QUANTITIES		
SERENITY OAKS, UNIT 5		
ITEM	UNIT	QUANTITY
STABILIZED CONSTRUCTION ENTRANCE	EACH	2
SILT FENCE	L.F.	5,880
CONCRETE TRUCK WASHOUT	EACH	1

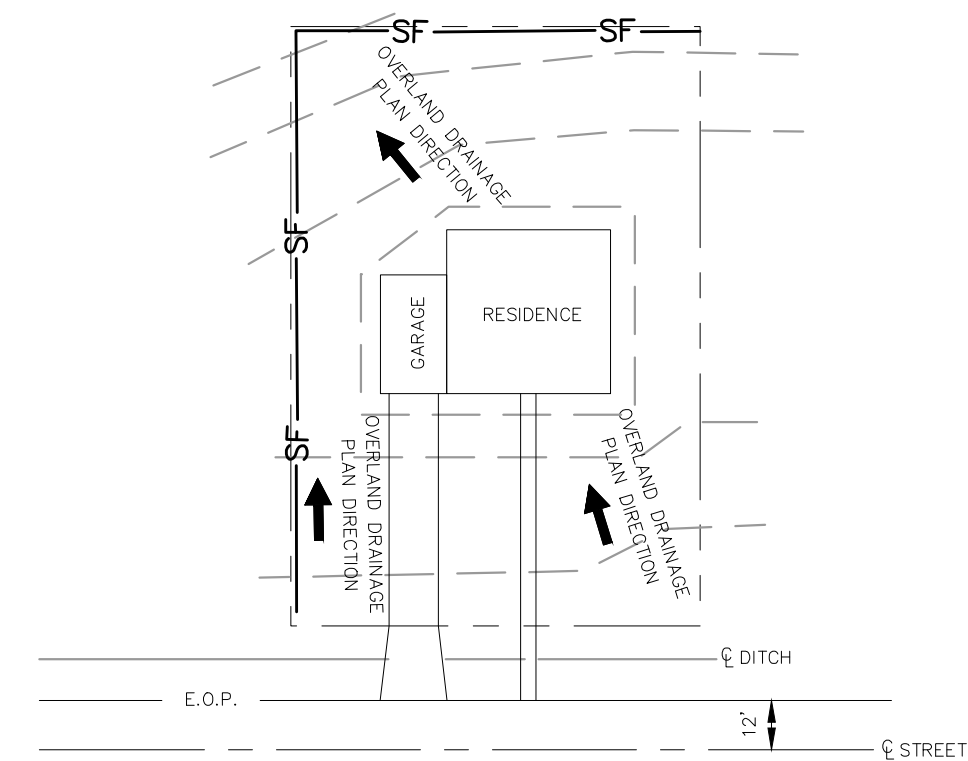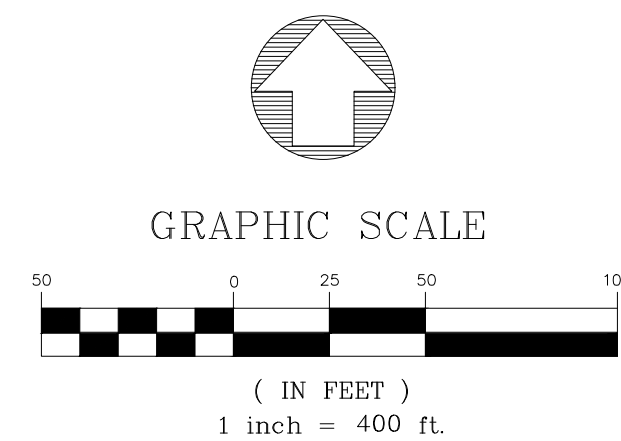

TYPICAL LOT  
EROSION/SEDIMENT  
CONTROL DETAIL  
NOT TO SCALE

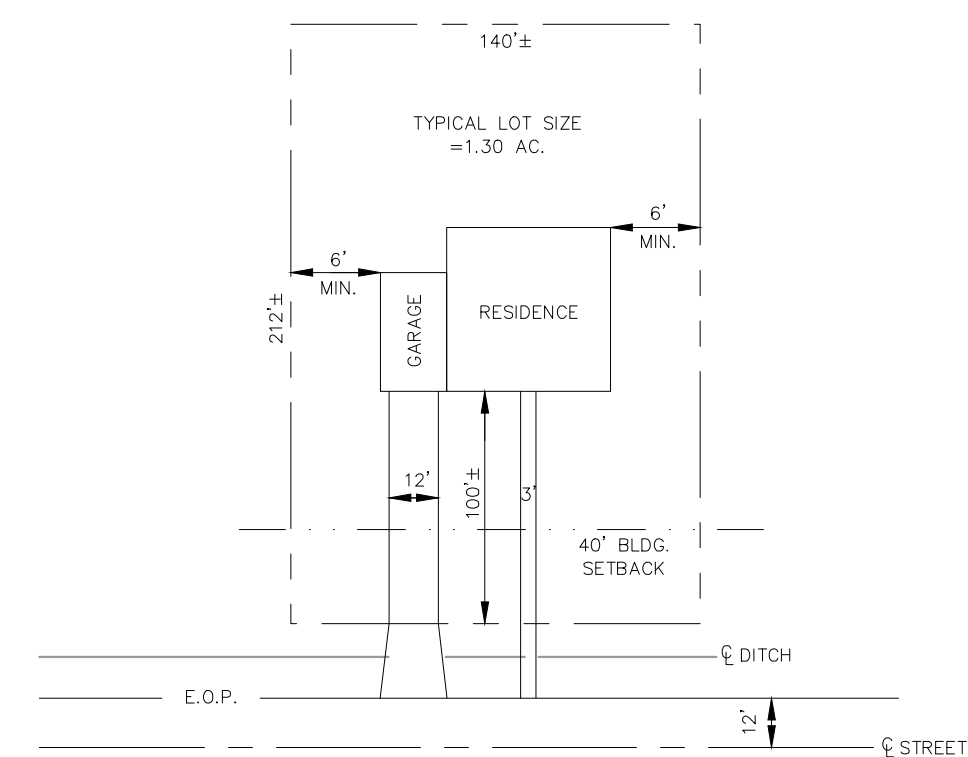

TYPICAL LOT DETAIL

NOT TO SCALE

<u>IMPERVIOUS COVER CALC.</u>	
RESIDENCE	±,--- S.F.
GARAGE	±--- S.F.
DRIVEWAY	±,--- S.F.
WALK	±--- S.F.
<u>TOTAL</u>	<u>±,--- S.F.</u>

SUBDIVISION TOTAL: 45 LOTS X --- S.F.  
= --- S.F.

STREET PAVEMENT TOTAL: --- S.F.

SUB-TOTAL IMPERVIOUS COVER: --- S.F. = --- ACRES

TOTAL ACREAGE FOR UNIT 5: 89.96 ACRES

TOTAL IMPERVIOUS COVER FOR UNIT 5: ---%

REVISIONS					
NO.	DATE	DESCRIPTION	BY		

FIRM REGISTRATION # F-003084



**GALLEGOS  
ENGINEERING,  
INC.**

FIRM REGISTRATION

**SAN ANTONIO, TEXAS    www.gallegoseng.com    PH: 210.641.0812**

THE SEAL APPEARING ON  
THIS DOCUMENT WAS  
AUTHORIZED BY  
RICHARD M. GALLEGOS, P.E. 86916  
NOVEMBER 2, 2022  
ALTERATION OF A SEALED DOCUMENT  
WITHOUT PROPER NOTIFICATION  
TO THE RESPONSIBLE ENGINEER  
IS AN OFFENSE UNDER THE  
TEXAS ENGINEERING PRACTICE ACT



SERENITY OAKS SUBDIVISION, UNIT 5  
 COMAL COUNTY, TEXAS

STORM WATER POLLUTION  
PREVENTION PLAN  
GALE ESTATES, L.L.C.

REVENTIUN FLAK  
GALE ESTATES, L.L.C.

SHEET 3  
OF 24



S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEET\504-U5-SWPPP NAR.dwg

SITE DESCRIPTION

PROJECT: SERENITY OAKS SUBDIVISION UNIT 5  
A PROPOSED SINGLE FAMILY RESIDENTIAL DEVELOPMENT LOCATED IN THE COUNTY OF COMAL, LOCATED OFF RAYNER RANCH ROAD.

PROJECT DESCRIPTION:  
THE CONSTRUCTION OF STREETS, DRAINAGE, WATER, AND UTILITY FACILITIES NECESSARY FOR THE DEVELOPMENT OF A SINGLE-FAMILY RESIDENTIAL SUBDIVISION.

MAJOR SOIL DISTURBING ACTIVITIES:  
ACTIVITIES ASSOCIATED WITH STREET, DRAIN, & UTILITY CONSTRUCTION--TRENCHING, STOCKPILING SPOILS AND EXCAVATION.

TOTAL PROJECT AREA: ± 89.96 ACRES  
TOTAL AREA TO BE DISTURBED: ± 89.96 ACRES

WEIGHTED RUNOFF COEFFICIENT (AFTER CONSTRUCTION): 0.62

EXISTING CONDITION OF SOIL & VEGETATIVE COVER AND % OF EXISTING VEGETATIVE COVER:

THE SOIL TYPE(S) ON SITE ARE AS FOLLOWS:  
1. ROCK WITH SOME TOP SOIL.

NAME OF RECEIVING WATERS: TRIBUTARY OF GUADALUPE RIVER

SOIL STABILIZATION PRACTICES:

- TEMPORARY SEEDING
- PERMANENT PLANTING, SODDING, OR SEEDING
- MULCHING
- SOIL RETENTION BLANKET
- BUFFER ZONES
- ☒ PRESERVATIVE OF NATURAL RESOURCES

OTHER:

STRUCTURAL PRACTICES:

- ☒ SILT FENCES
- HAY BALES
- ☒ ROCK BERMS
- DIVERSION, INTERCEPTOR, OR PERIMETER DIKES
- DIVERSION, INTERCEPTOR, OR PERIMETER SWALES
- DIVERSION, DIKE AND SWALE COMBINATIONS
- PIPE SLOPE DRAINS
- PAVED FLUMES
- ☒ ROCK BEDDING AT CONSTRUCTION EXIT
- TIMBER MATTING AT CONSTRUCTION EXIT
- CHANNEL LINERS
- SEDIMENT TRAPS
- SEDIMENT BASINS
- CURB INLET GRAVEL FILTER
- STONE OUTLET STRUCTURES
- CURBS AND GUTTERS
- STORM SEWERS
- VELOCITY CONTROL DEVICES

OTHER:

NARRATIVE – SEQUENCE OF CONSTRUCTION (STORM WATER MANAGEMENT) ACTIVITIES:

STRUCTURAL PRACTICES, AS APPLICABLE, WILL BE INSTALLED PRIOR TO EACH PHASE OF THE PROJECT AND MAINTAINED DURING THE CONSTRUCTION OF THAT PHASE. SOIL STABILIZATION PRACTICES WILL CLOSELY FOLLOW COMPLETION AND ACCEPTANCE OF CONSTRUCTION FOR EACH PROJECT PHASE.

STORM WATER MANAGEMENT:

THE CONTRACTOR WILL INSTALL AND MAINTAIN SEDIMENTATION AND EROSION CONTROL MEASURES AS SPECIFIED IN THE STORM WATER POLLUTION PREVENTION PLAN, TEMPORARY SEDIMENTATION & EROSION CONTROL PLAN, AND AS DIRECTED BY AUTHORIZED OFFICIALS.

CONTRACTOR TO PLACE EXCAVATED MATERIAL ON THE HIGH SIDE OF THE TRENCH.

SITE DESCRIPTION

OTHER EROSION AND SEDIMENT CONTROLS:

MAINTENANCE:  
ALL EROSION AND SEDIMENT CONTROLS WILL BE MAINTAINED IN GOOD WORKING ORDER. IF A REPAIR IS NECESSARY, IT WILL BE DONE AT THE EARLIEST DATE POSSIBLE, BUT NO LATER THAN 7 CALENDAR DAYS AFTER THE SURROUNDING EXPOSED GROUND HAS DRIED SUFFICIENTLY TO PREVENT FURTHER DAMAGE FROM HEAVY EQUIPMENT.

INSPECTION:  
AN INSPECTION WILL BE PERFORMED BY THE CONTRACTOR EVERY 2 WEEKS AS WELL AS AFTER EVERY HALF INCH OR MORE OF RAIN (AS RECORDED ON A NON-FREEZING RAIN GAUGE TO BE LOCATED AT THE PROJECT SITE). THE CONTROLS WILL BE REVISED AS NECESSARY.

WASTE MATERIALS:  
ALL WASTE MATERIAL WILL BE COLLECTED AND STORED IN A METAL DUMPSTER. THE DUMPSTER WILL MEET ALL STATE AND LOCAL CITY SOLID WASTE MANAGEMENT REGULATIONS. ALL TRASH AND CONSTRUCTION DEBRIS FROM THE SITE WILL BE DEPOSITED IN THE DUMPSTER. THE DUMPSTER WILL BE EMPTIED AS NECESSARY OR AS REQUIRED BY LOCAL REGULATION, AND THE TRASH WILL BE HUALED TO A LOCAL DUMP. NO CONSTRUCTION WASTE MATERIAL WILL BE BURIED ON SITE.

HAZARDOUS WASTE (INCLUDING SPILL REPORTING):  
AT A MINIMUM, ANY PRODUCTS IN THE FOLLOWING CATEGORIES ARE CONSIDERED TO BE HAZARDOUS:  
  
PAINTS, ACIDS FOR CLEANING MASONARY SURFACES, CLEANING SOLVENTS ASPHALT PRODUCTS, CHEMICAL ADDITIVES FOR SOIL STABILIZATION, OR CONCRETE CURING COMPOUNDS AND ADDITIVES. IN THE EVENT OF A SPILL WHICH MAY BE HAZARDOUS, THE SPILL COORDINATOR SHOULD BE CONTACTED IMMEDIATELY.

SANITARY WASTE:  
ALL SANITARY WASTE WILL BE COLLECTED FROM THE PORTABLE UNITS AS NECESSARY OR AS REQUIRED BY LOCAL REGULATION BY A LICENSED SANITARY WASTE MANAGEMENT CONTRACTOR.

OFFSITE VEHICLE TRACKING:

- HAUL ROADS DAMPENED FOR DUST CONTROL
- LOADED HAUL TRUCKS TO BE COVERED WITH TARPULIN
- EXCESS DIRT ON ROAD REMOVED DAILY
- ☒ STABILIZED CONSTRUCTION ENTRANCE

OTHER:

REMARKS:

OWNER’S CERTIFICATION

I CERTIFY UNDER PENALTY OF LAW THAT THIS DOCUMENT AND ALL ATTACHMENTS WERE PREPARED UNDER MY SUPERVISION IN ACCORDANCE WITH SYSTEM DESIGNED TO ASSURE THAT QUALIFIED PERSONAL PROPERLY GATHER AND EVALUATE THE INFORMATION SUBMITTED. BASED ON MY INQUIRY OF THE PERSON OR PERSONS WHO MANAGE THE SYSTEM, OR THOSE PERSONS DIRECTLY RESPONSIBLE FOR GATHERING THE INFORMATION SUBMITTED IS, TO THE BEST OF MY KNOWLEDGE AND BELIEF, TRUE, ACCURATE, AND COMPLETE. I AM AWARE THAT THERE ARE SIGNIFICANT PENALTIES FOR SUBMITTING FALSE INFORMATION, INCLUDING THE POSSIBILITY OF FINE AND IMPRISONMENT FOR KNOWING VIOLATIONS.

OWNER DATE

CONTRACTOR’S CERTIFICATION

I CERTIFY UNDER PENALTY OF LAW THAT I UNDERSTAND THE TERMS AND CONDITIONS OF THE GENERAL TEXAS POLLUTANT DISCHARGE ELIMINATION SYSTEM (TPDES) PERMIT THAT AUTHORIZES THE STORM WATER DISCHARGES ASSOCIATED WITH INDUSTRIAL ACTIVITY FROM THE CONSTRUCTION SITE IDENTIFIED AS PART OF THIS CERTIFICATION PLAN.

SIGNATURE (CONTRACTOR) DATE

REVISIONS			
NO.	DATE	DESCRIPTION	BY
PROJ. #:	DATE:	DRAWN BY:	CHECKED BY:
U5-SER	09/30/22	S.G.	R.M.G.

FIRM REGISTRATION # F-40804




GALLEGOS

ENGINEERING,

INC.

SAN ANTONIO, TEXAS    www.gallegoseng.com    PH: 210.641.0812

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLEGOS, P.E. 86916 NOVEMBER 2, 2022 ALTERATION OF A SEALED DOCUMENT WITHOUT THE SIGNATURE OF THE LICENSED ENGINEER IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT






SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

STORM WATER POLLUTION  
PREVENTION PLAN

GALE ESTATES, L.L.C.

SHEET 4  
OF 24



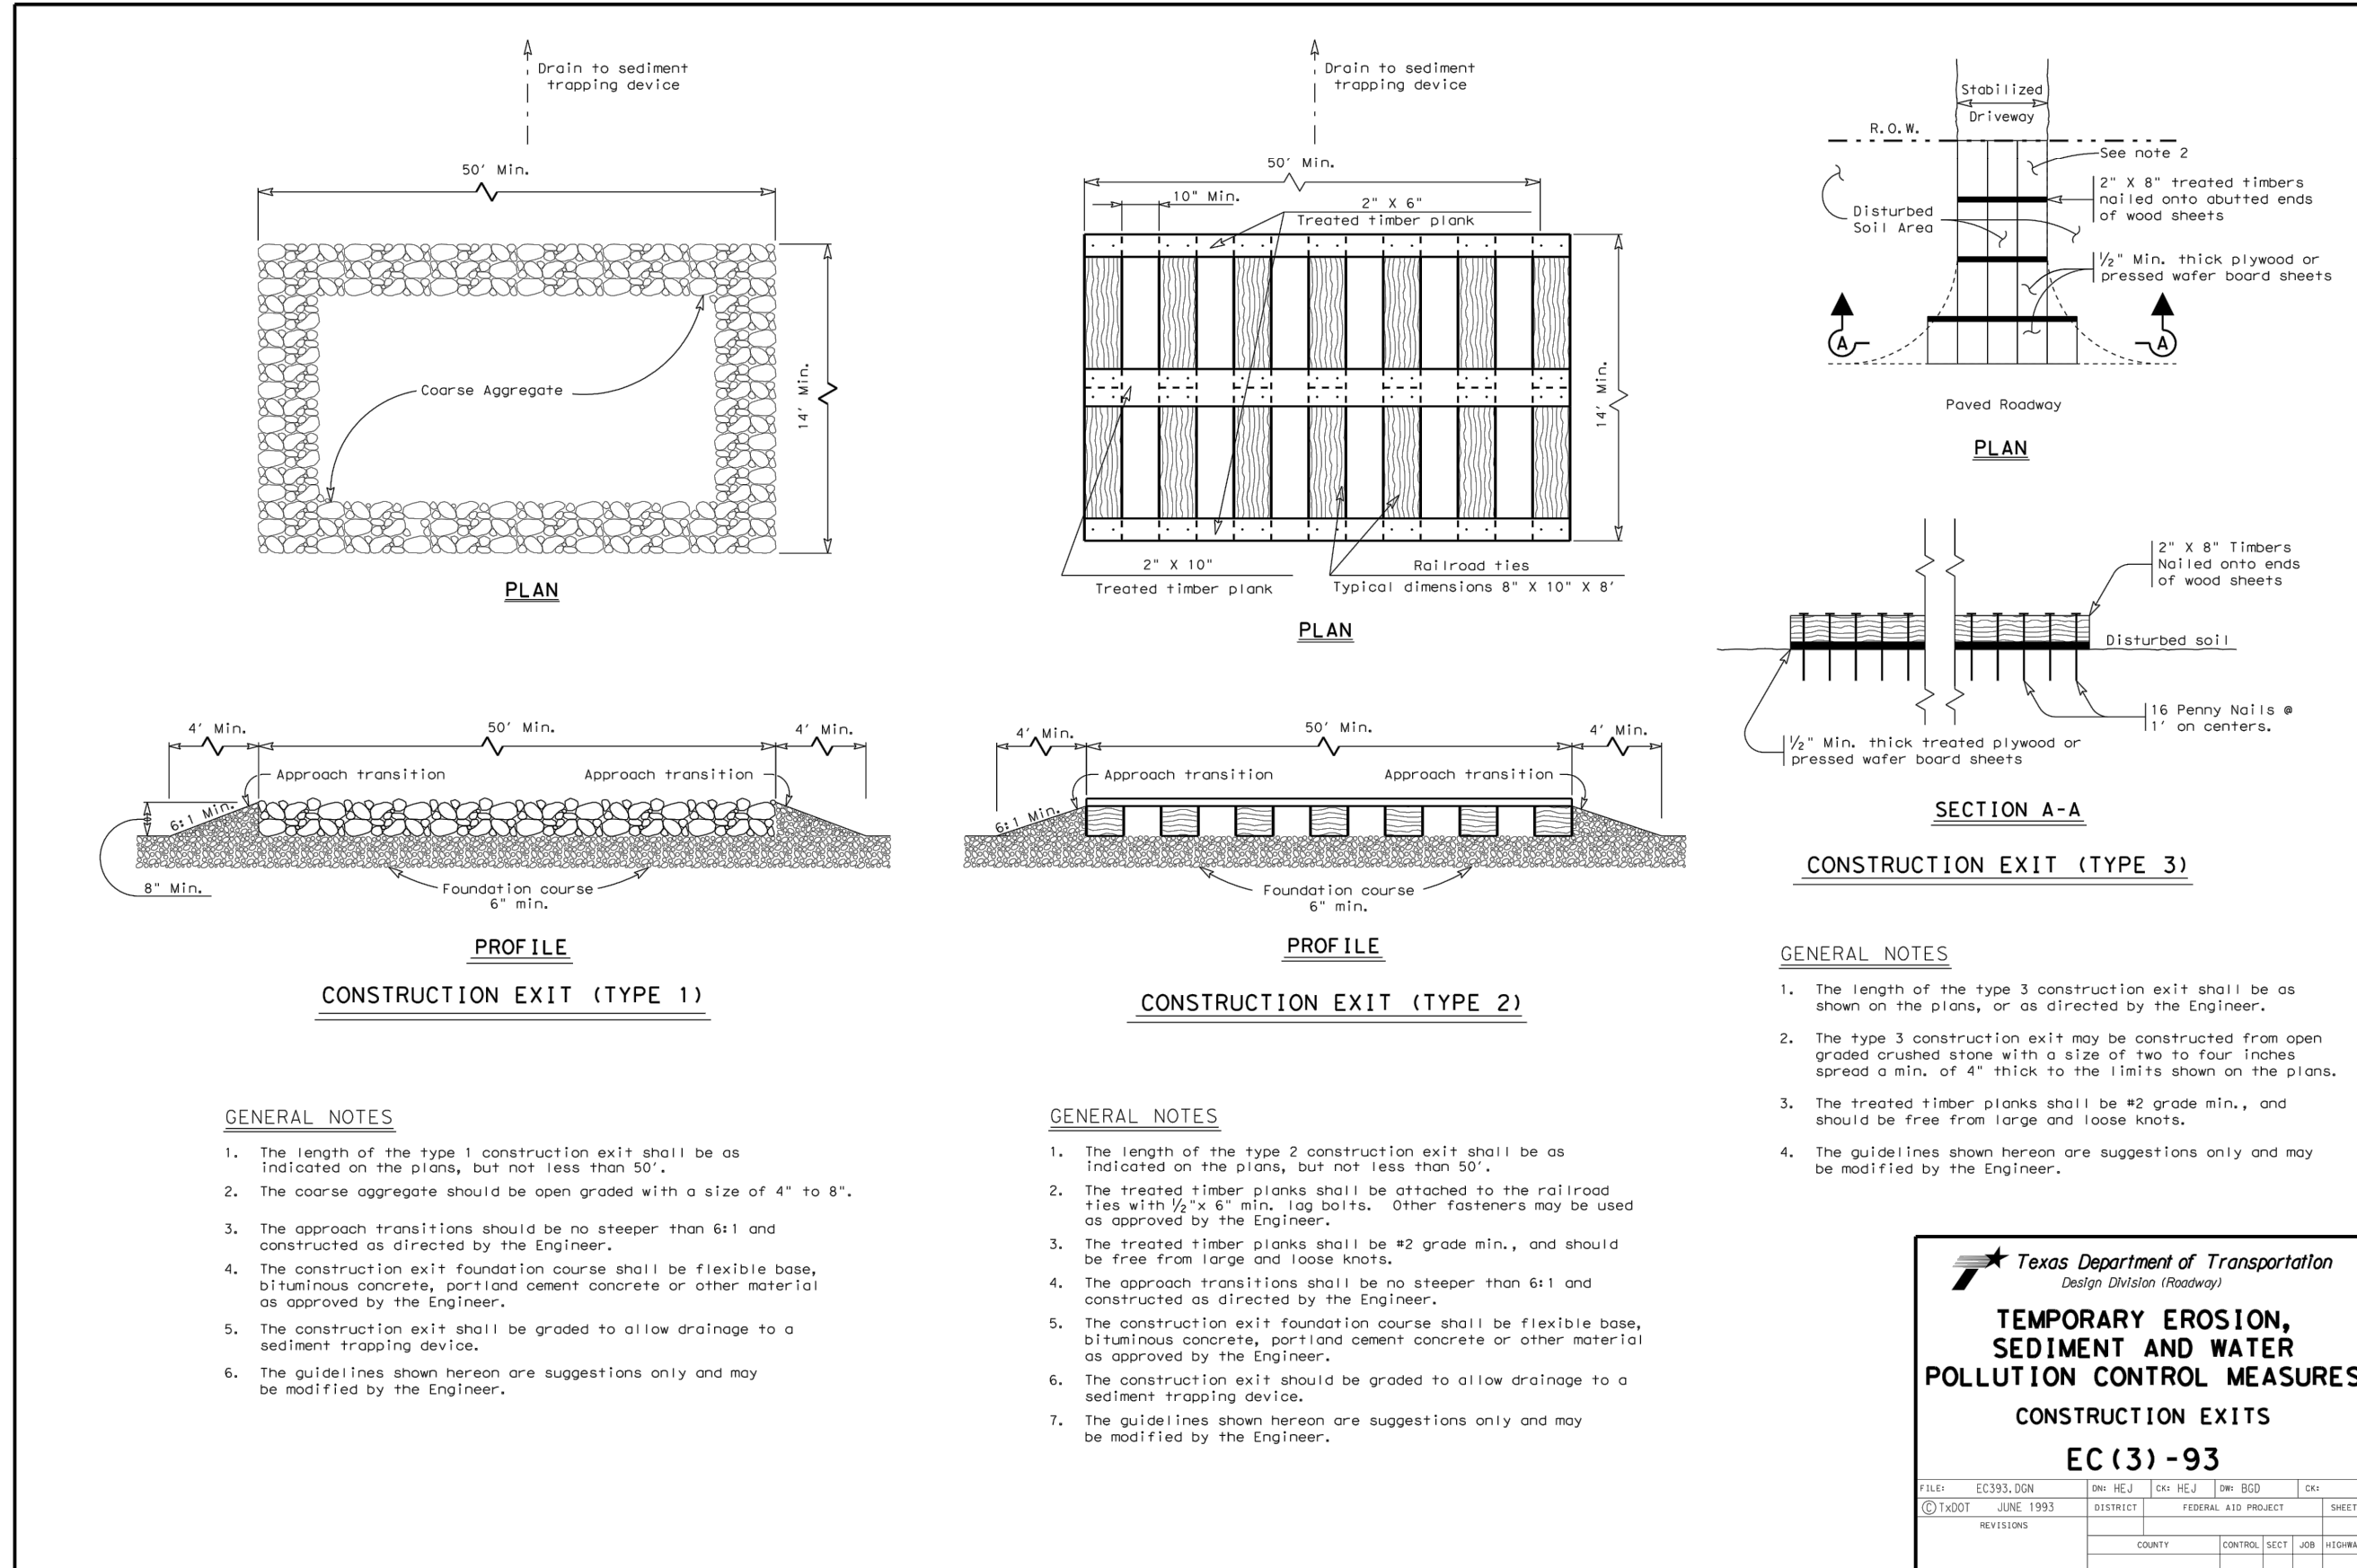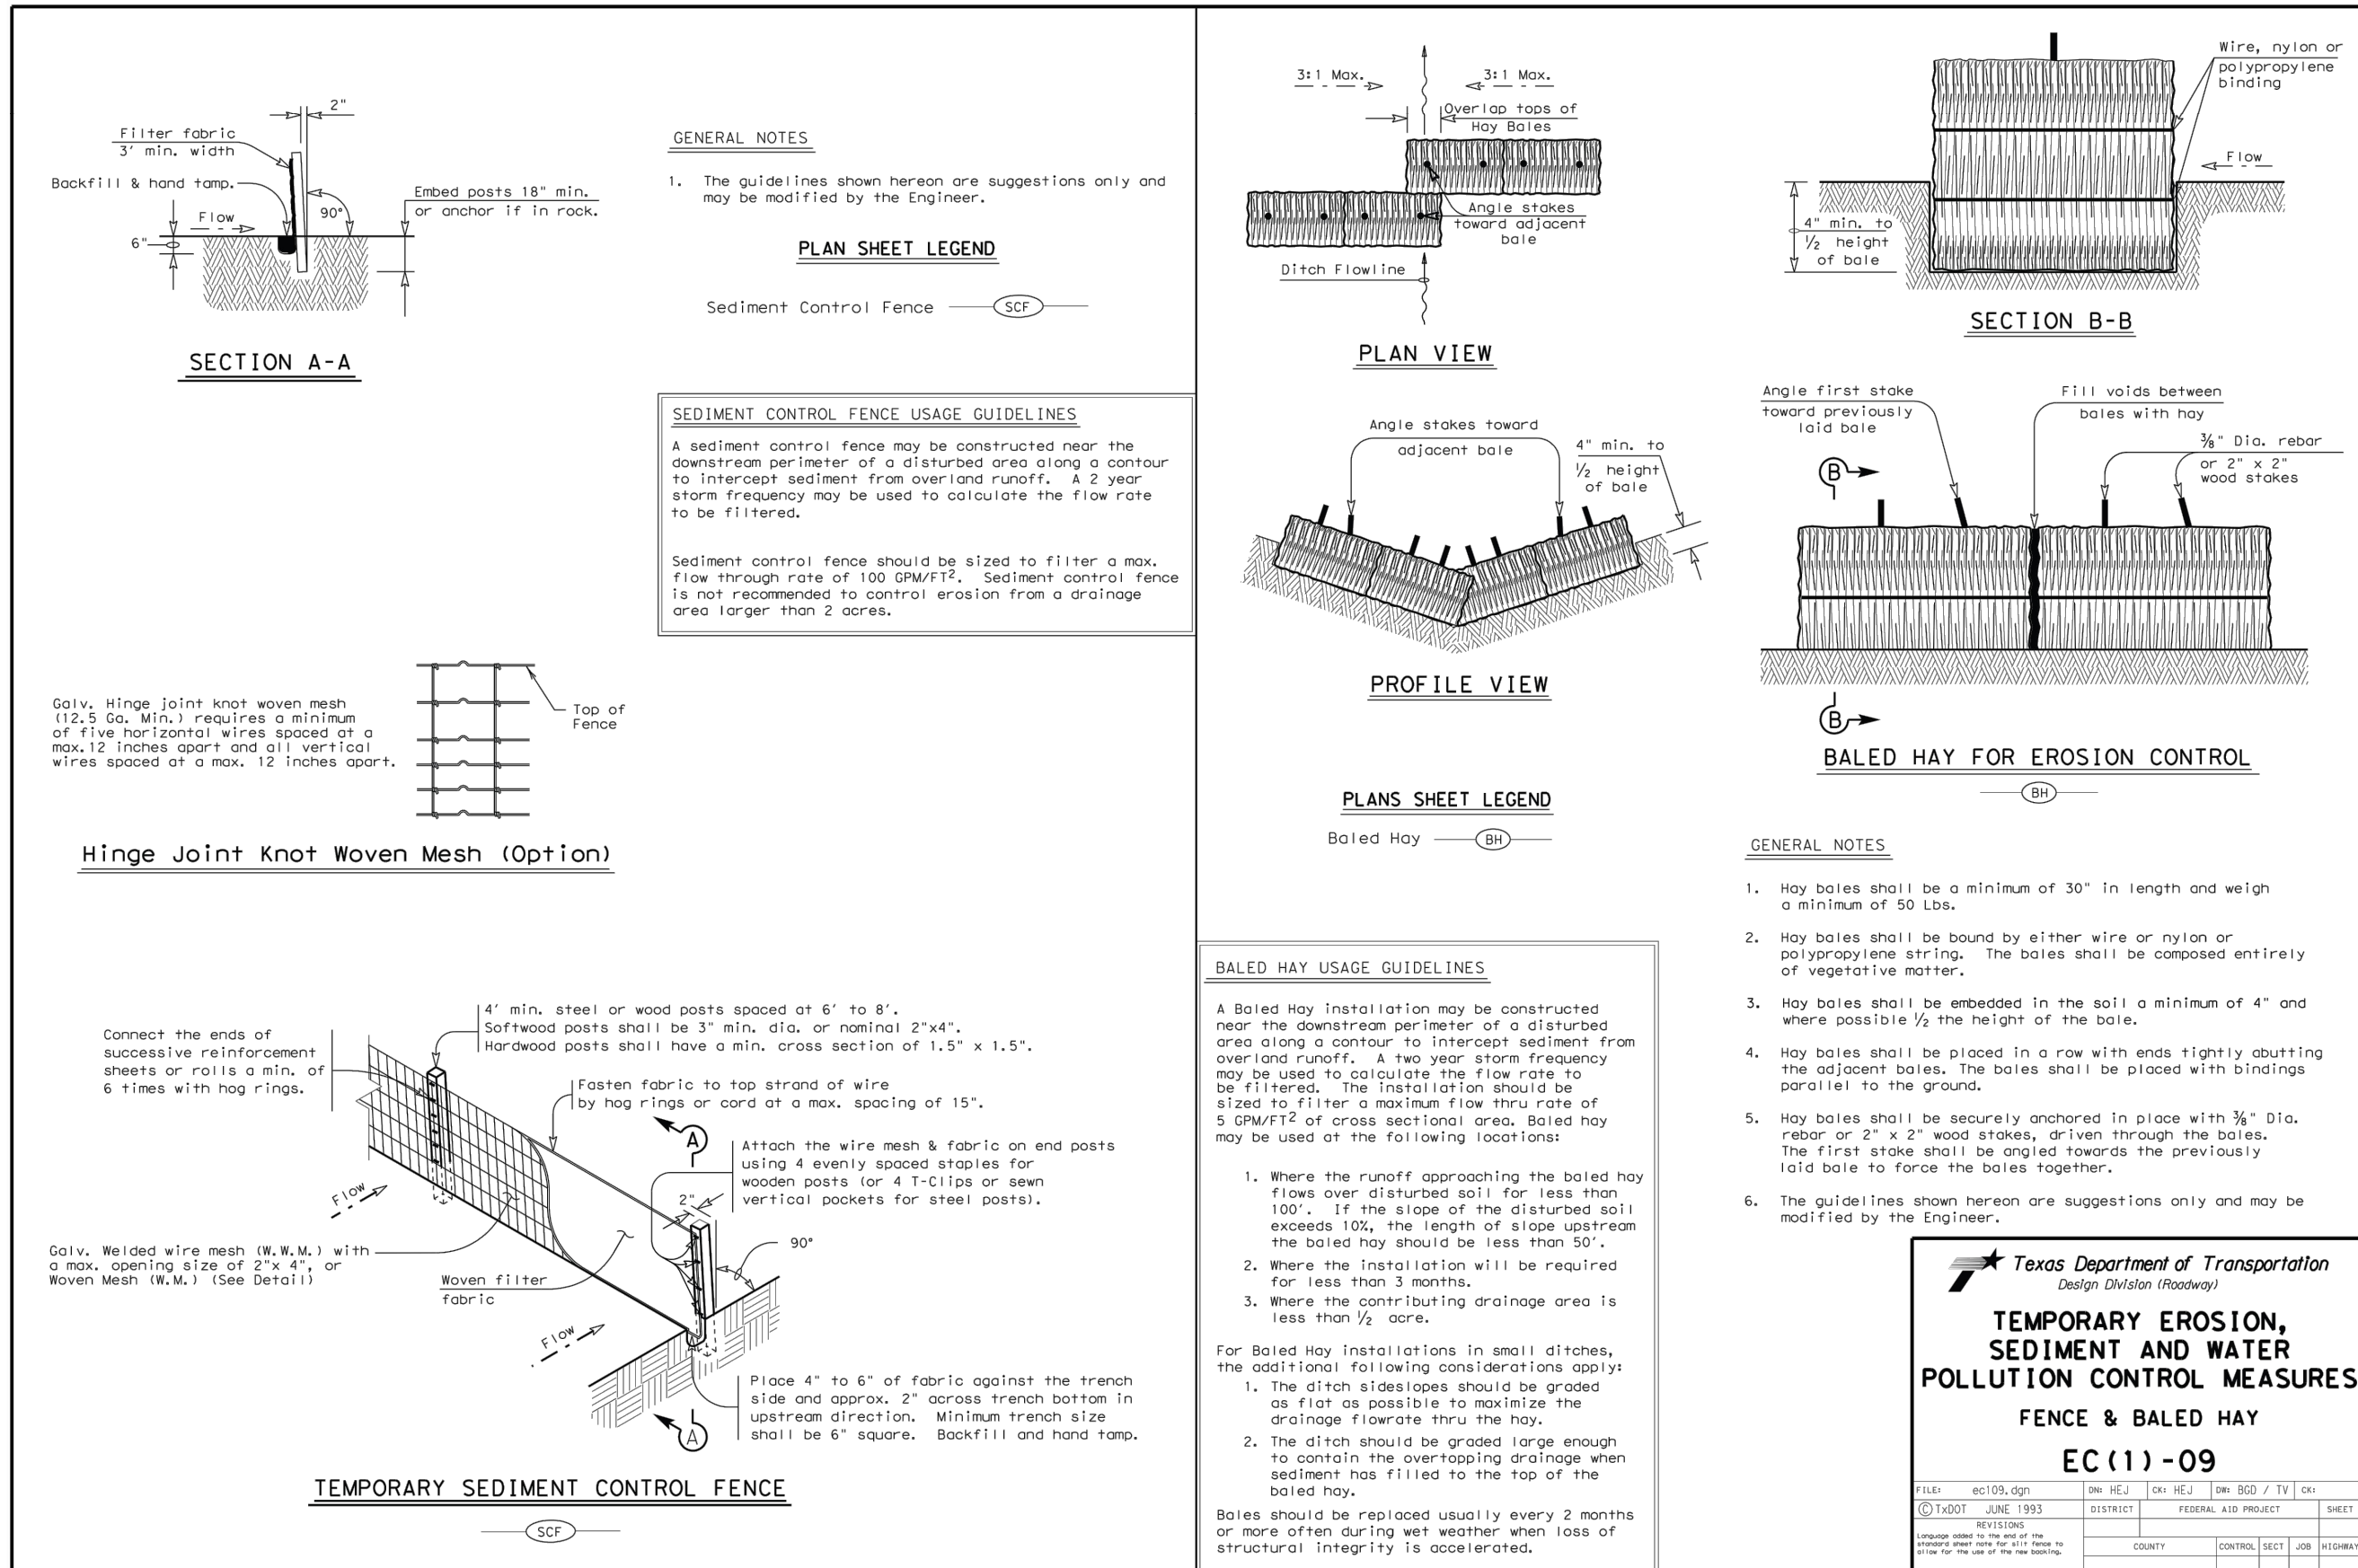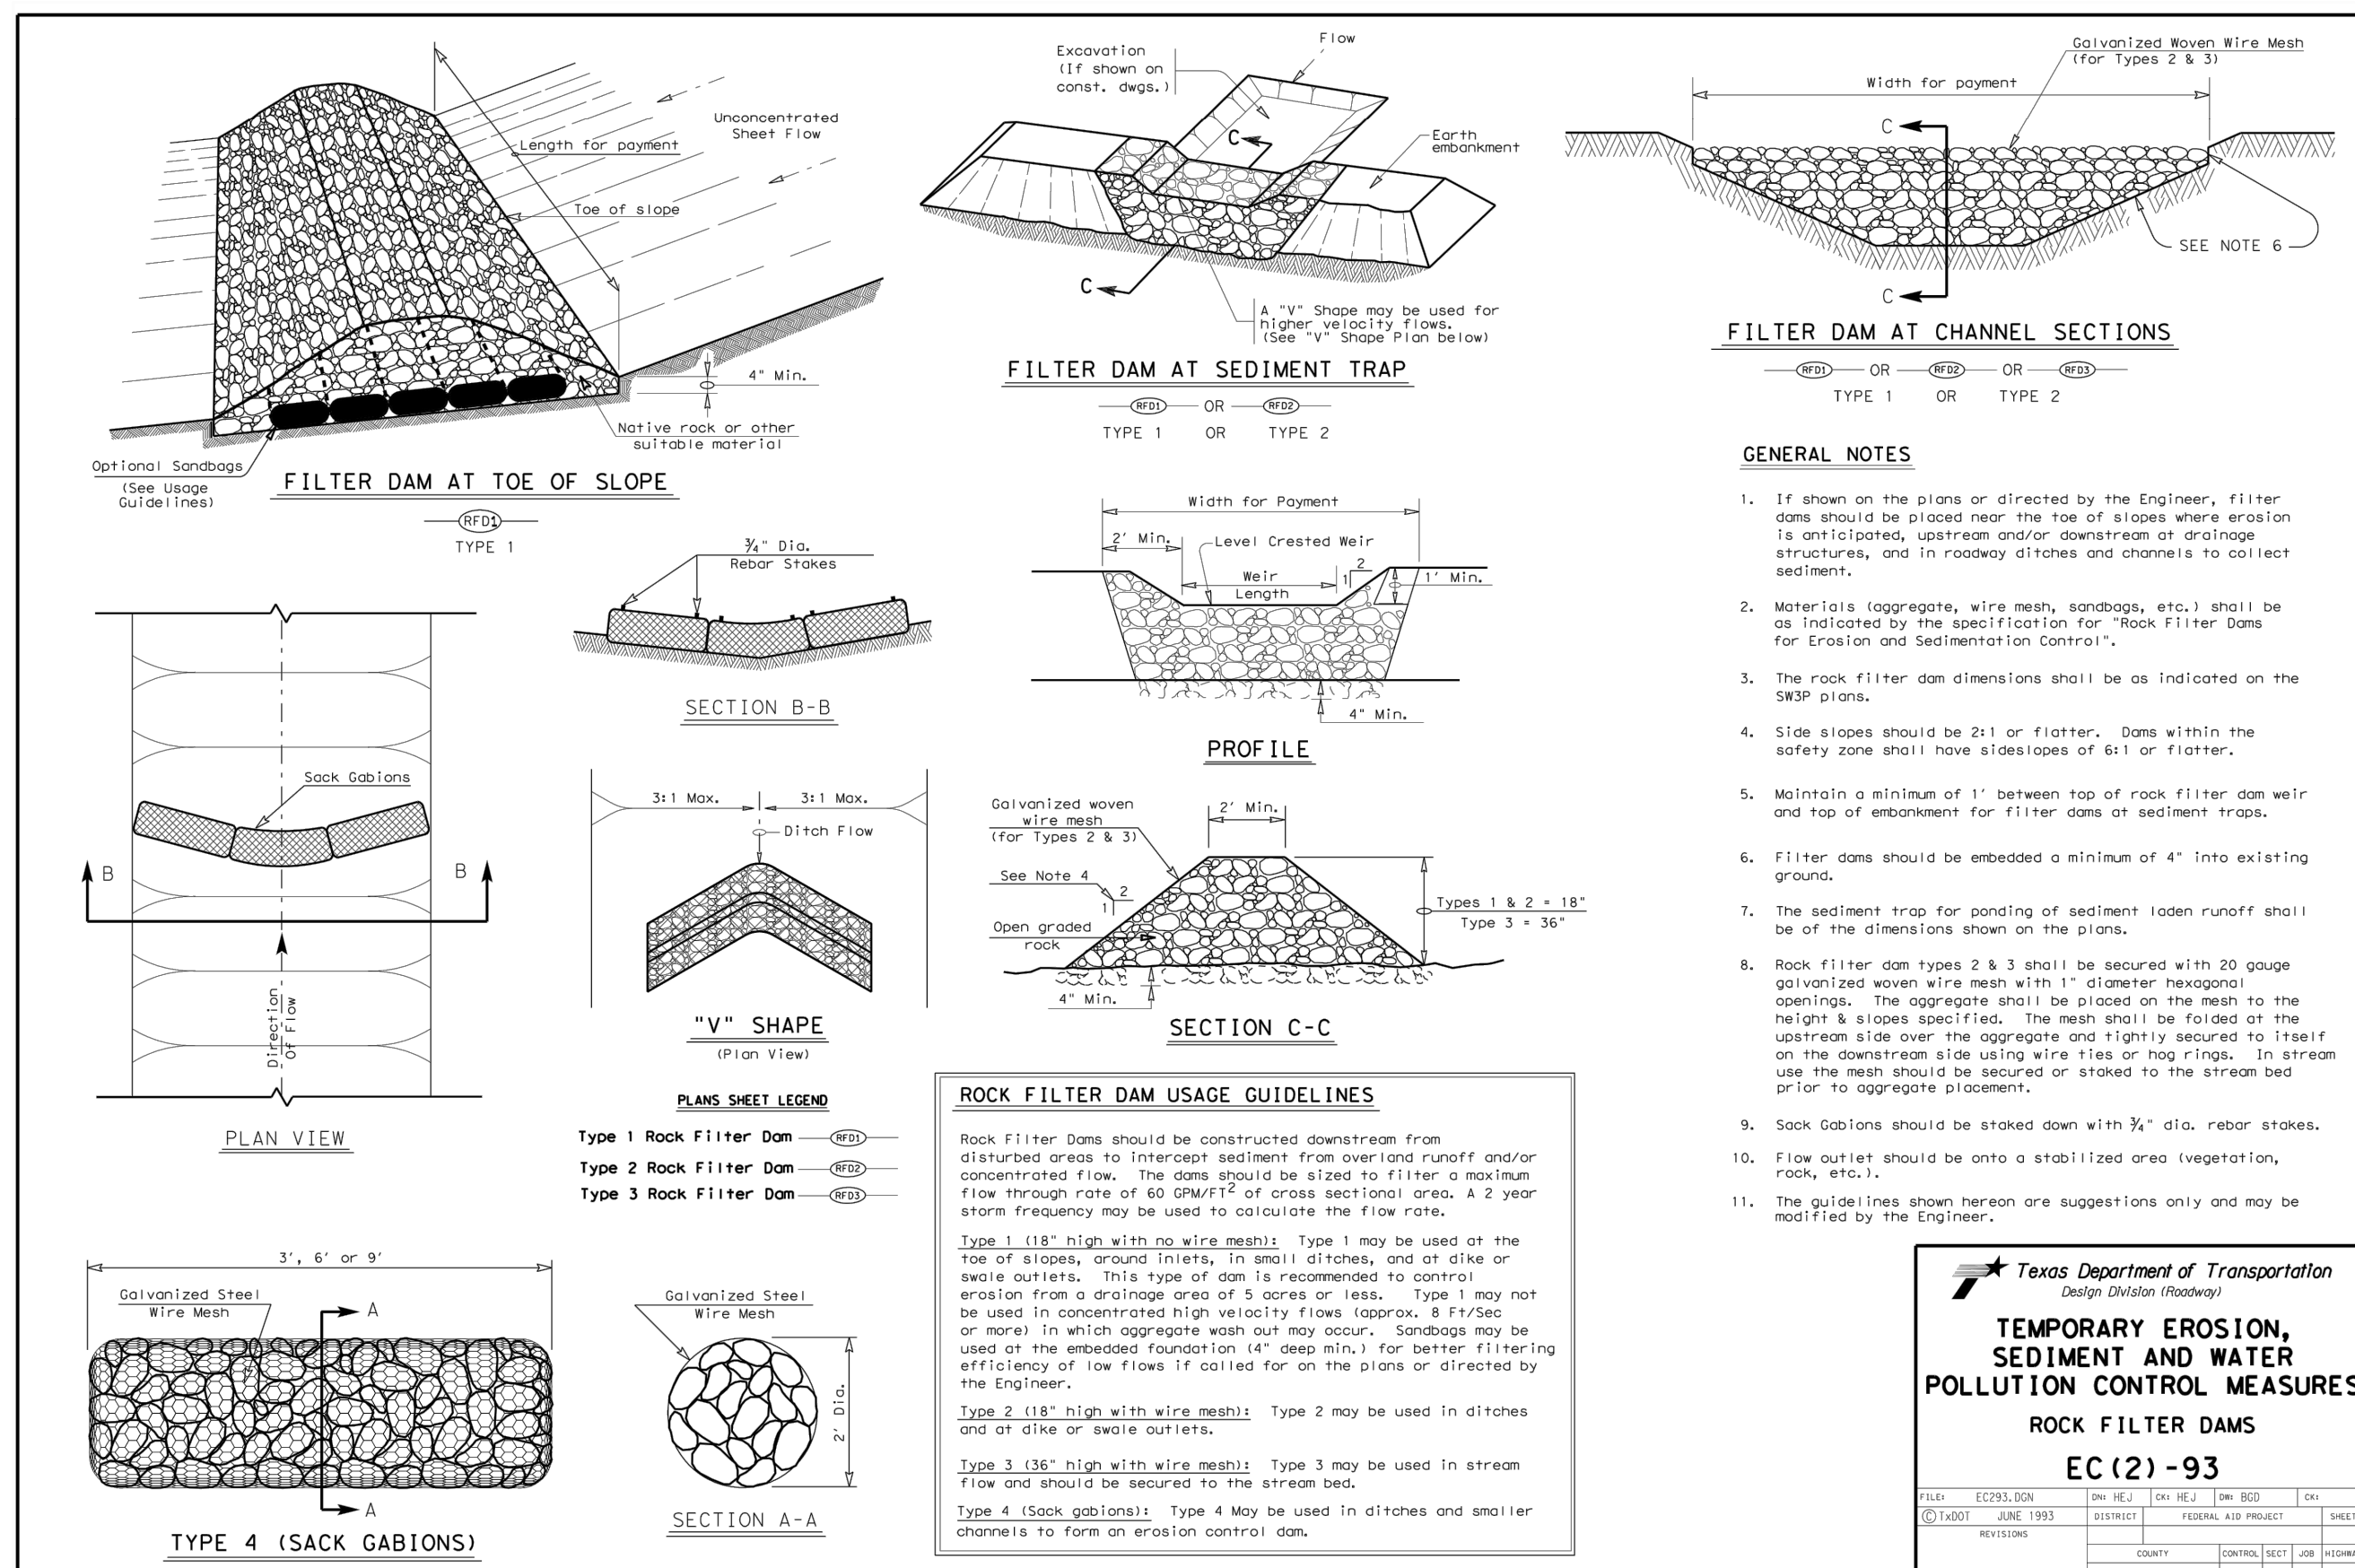





















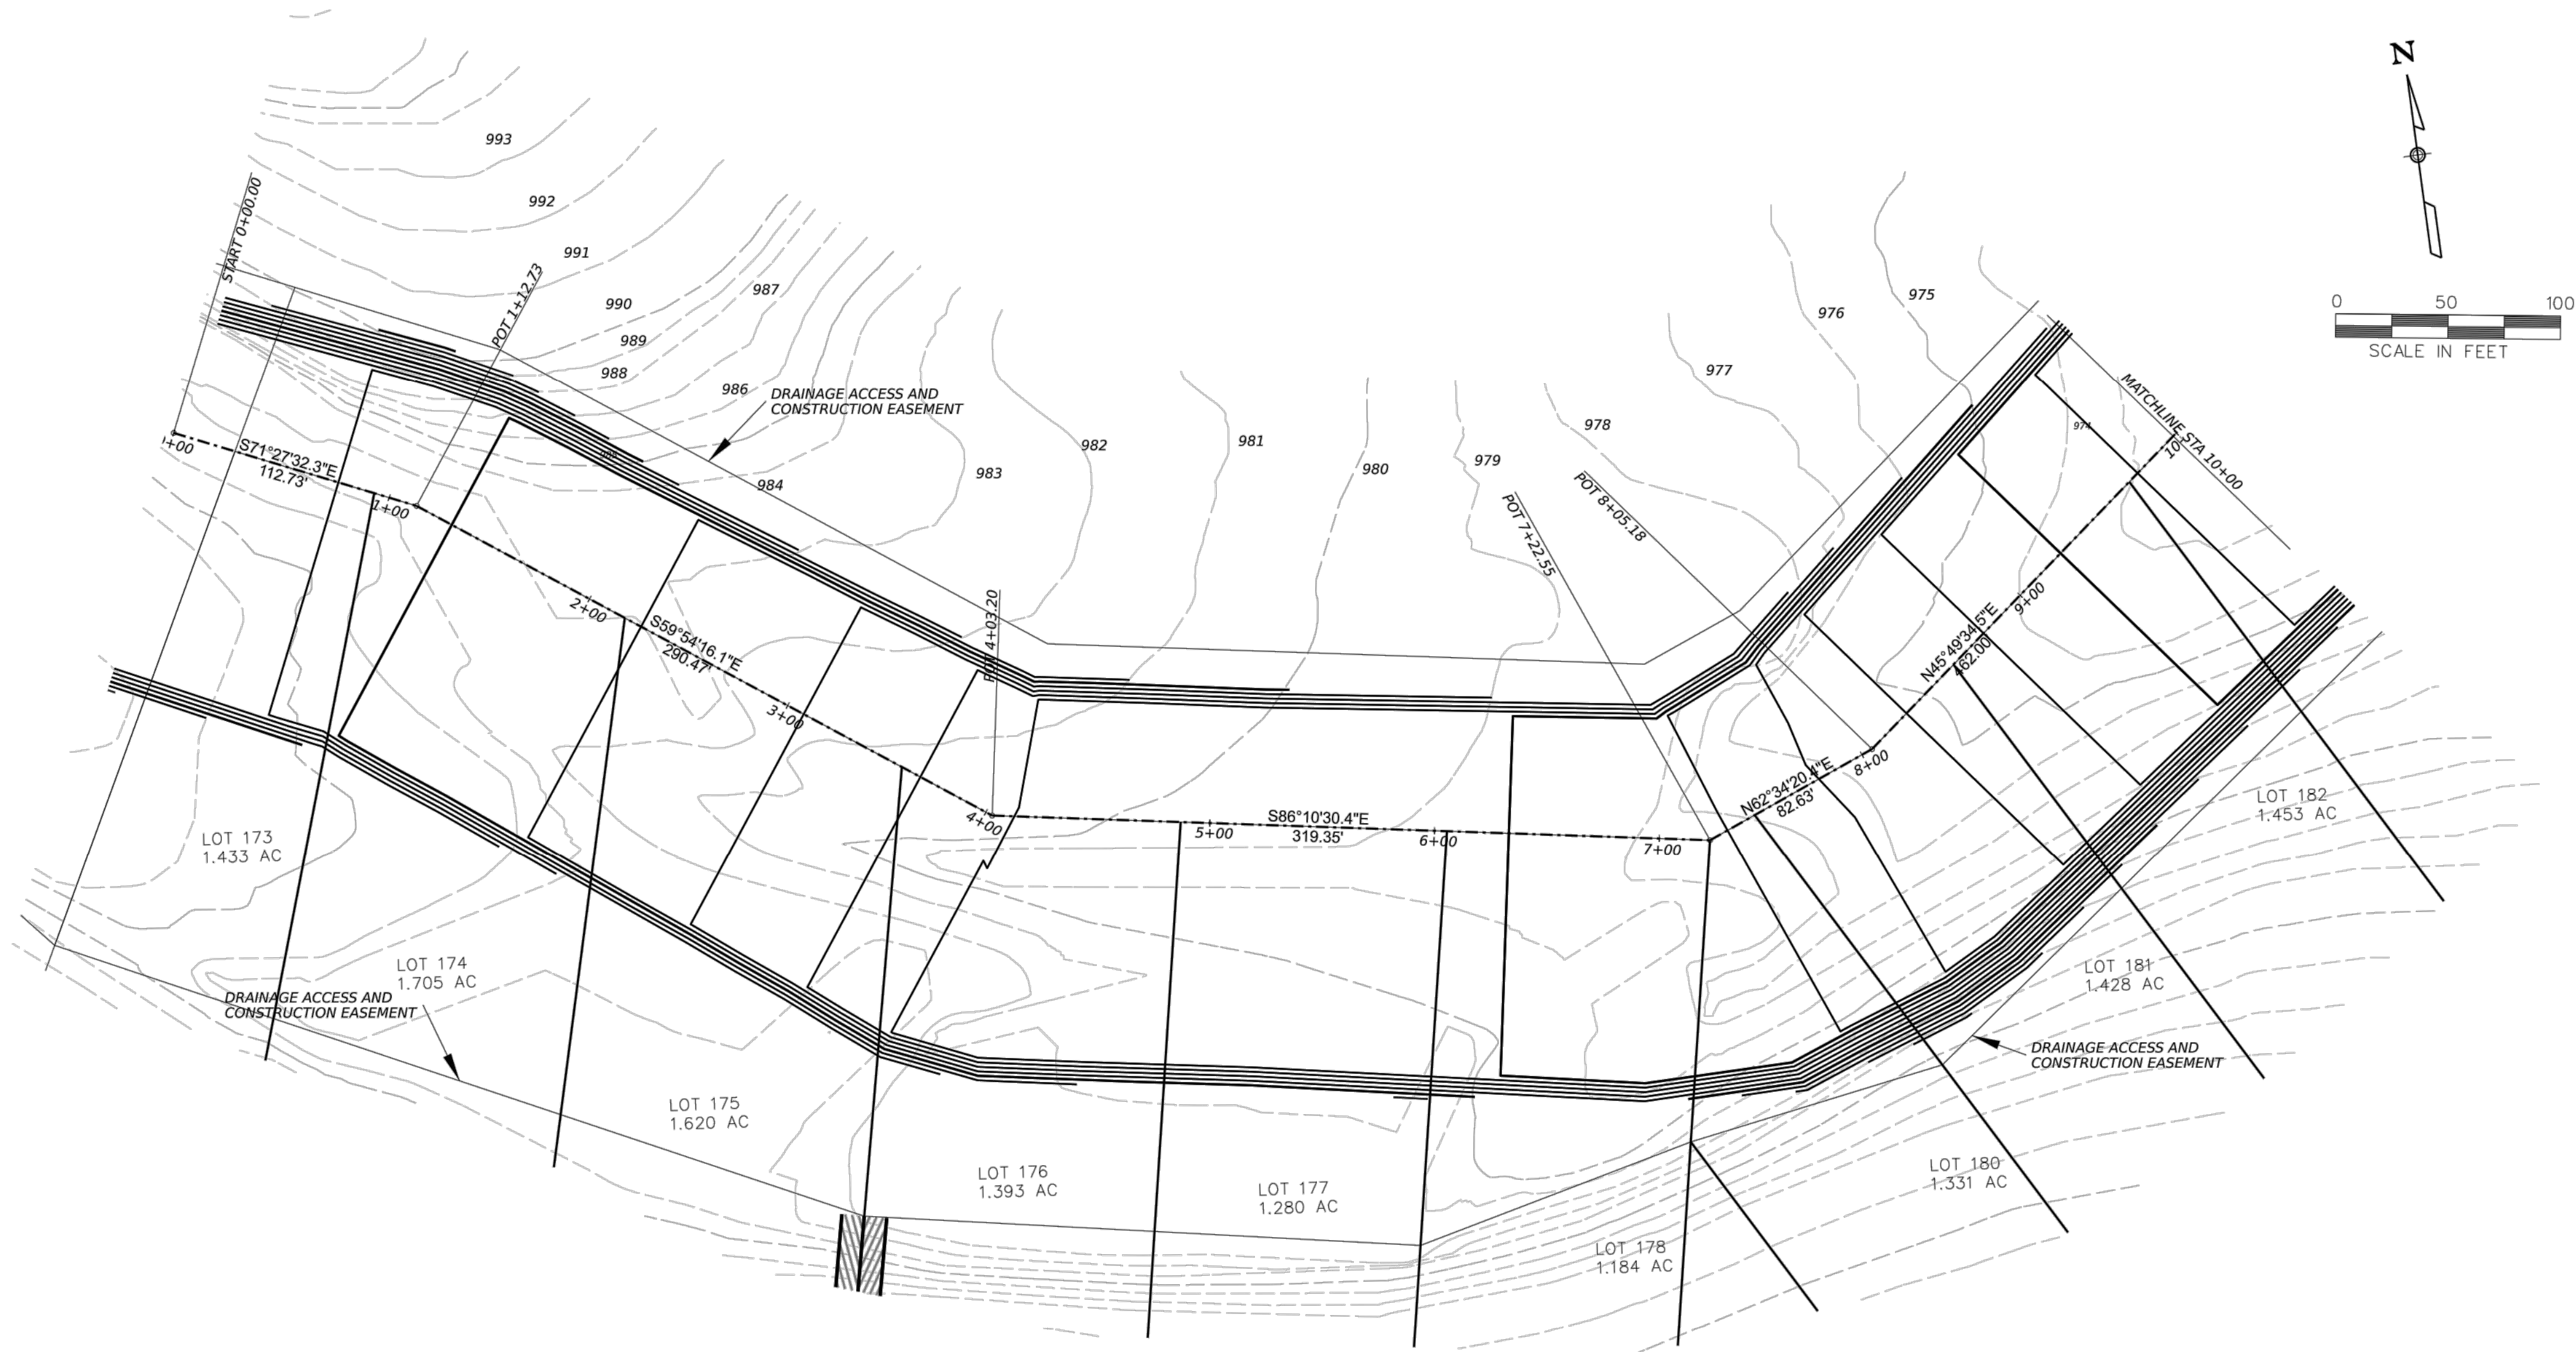

CHANNEL A PLAN  
SCALE: 1" = 50'


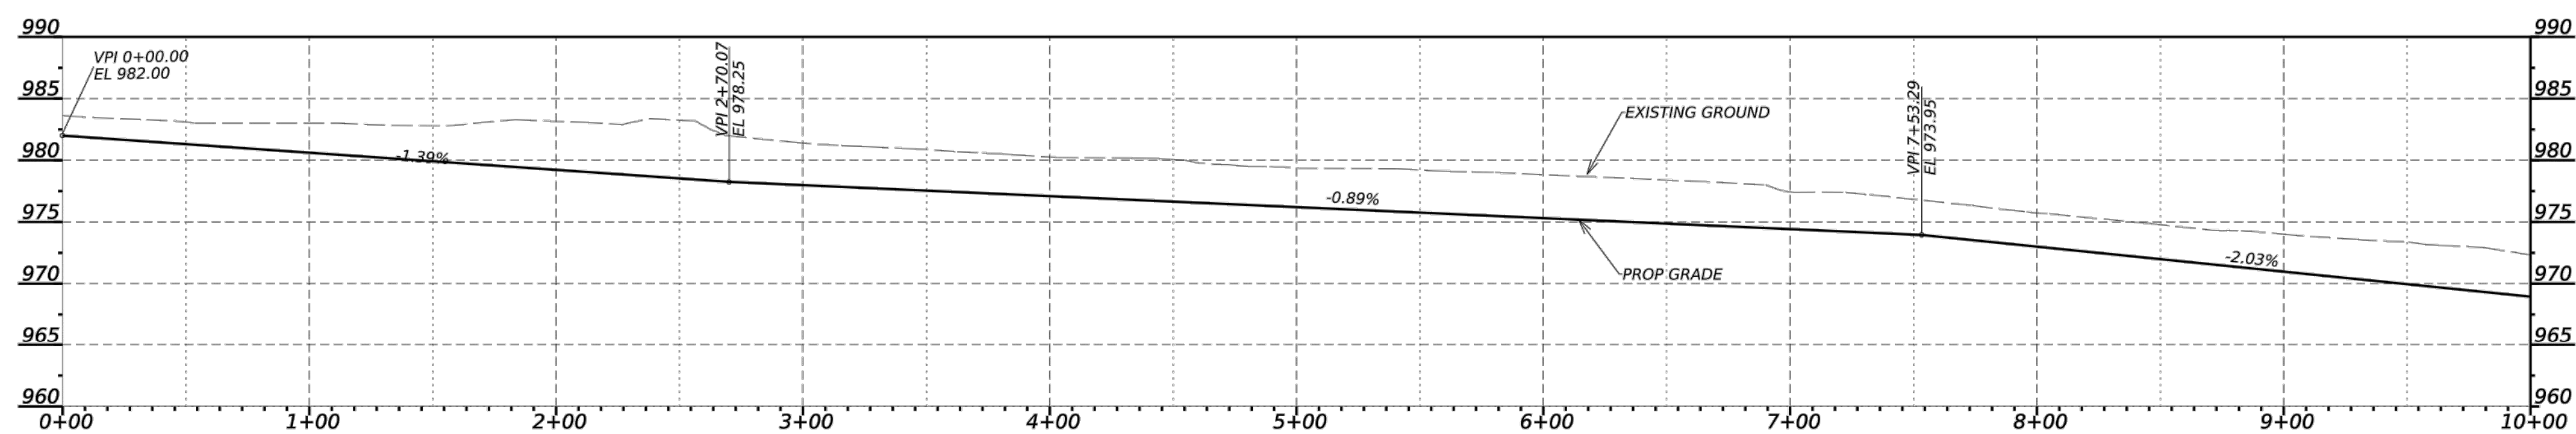


Proposed Elevation	982.00	981.31	980.61	979.92	979.22	978.52	977.98	977.63	977.09	976.64	976.20	975.75	975.31	974.86	974.42	973.97	973.00	971.98	970.97	969.95	968.94
Existing Elevation	983.63	983.08	983.00	982.79	983.15	983.25	981.40	980.86	980.26	980.05	979.37	979.21	978.84	978.40	977.42	976.83	975.73	974.77	973.99	973.37	972.33

CHANNEL A PROFILE  
SCALE: 1" = 50'H  
1" = 5'V



S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEETS\ST1-05-GRD-CHAN-A 10-00-16+20.44.dwg

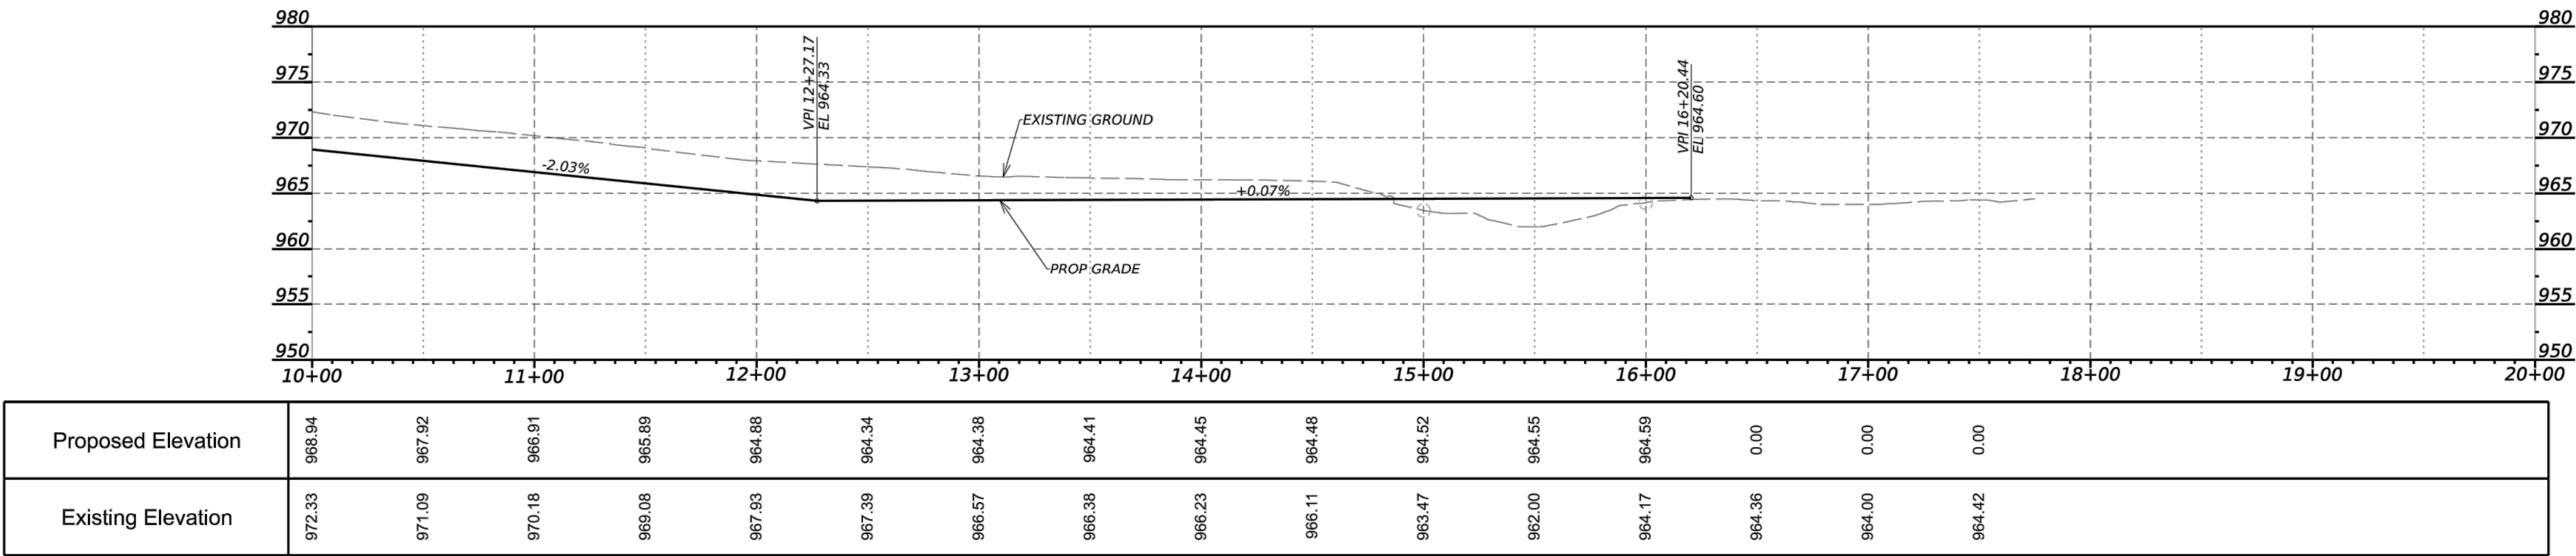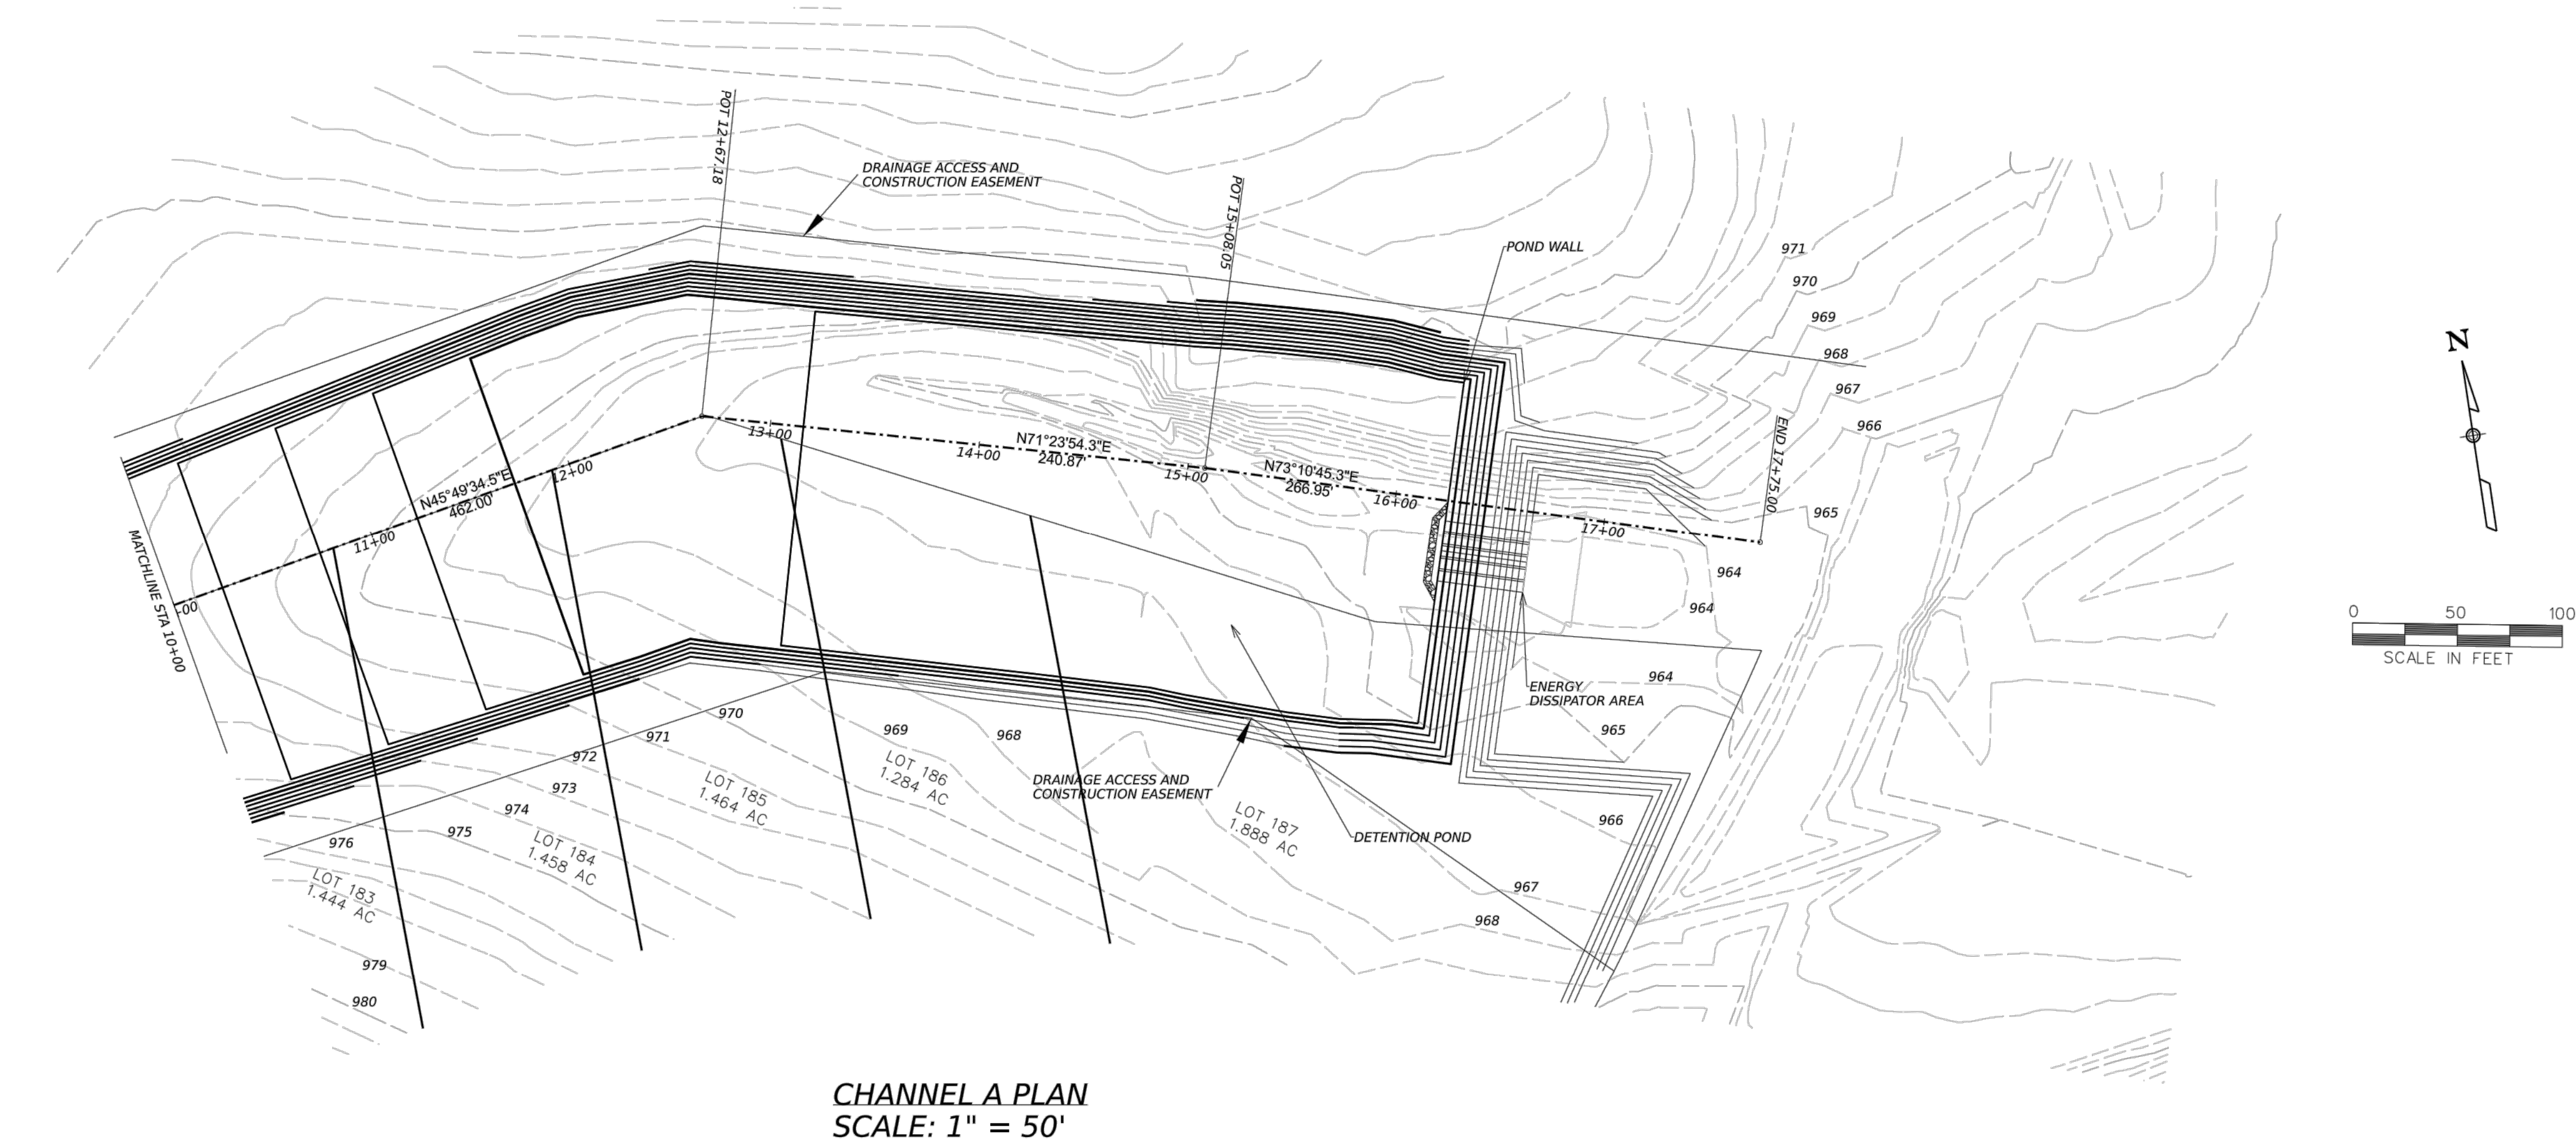

REVISIONS

NO.	DATE	DESCRIPTION	BY

PROJ. #:

U5-SER

DATE:

03/06/23

DGN. BY:

S.G.

CHKD. BY:

S.G.

R.M.G.

FIRM REGISTRATION # F40304

GALLECOS  
ENGINEERING,  
INC.

SAN ANTONIO, TEXAS    www.gallecoseng.com    PH: 210.641.0812

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLECOS, P.E. 86916 APRIL 6, 2023 ALTERATION OF A SEALED DOCUMENT WITHOUT REISSUING THE SEAL OR SIGNATURE IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT

STATE OF TEXAS

RICHARD M. GALLECOS

86916

EXPIRATION DATE 04/06/2026





SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

CHANNEL A PLAN & PROFILE  
STA 10+00 – STA 16+20.44  
GALE ESTATES, L.L.C.

SHEET 11  
OF 24



S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEETS\12-US-GRD-CHAN-B 01-00-2+78.dwg

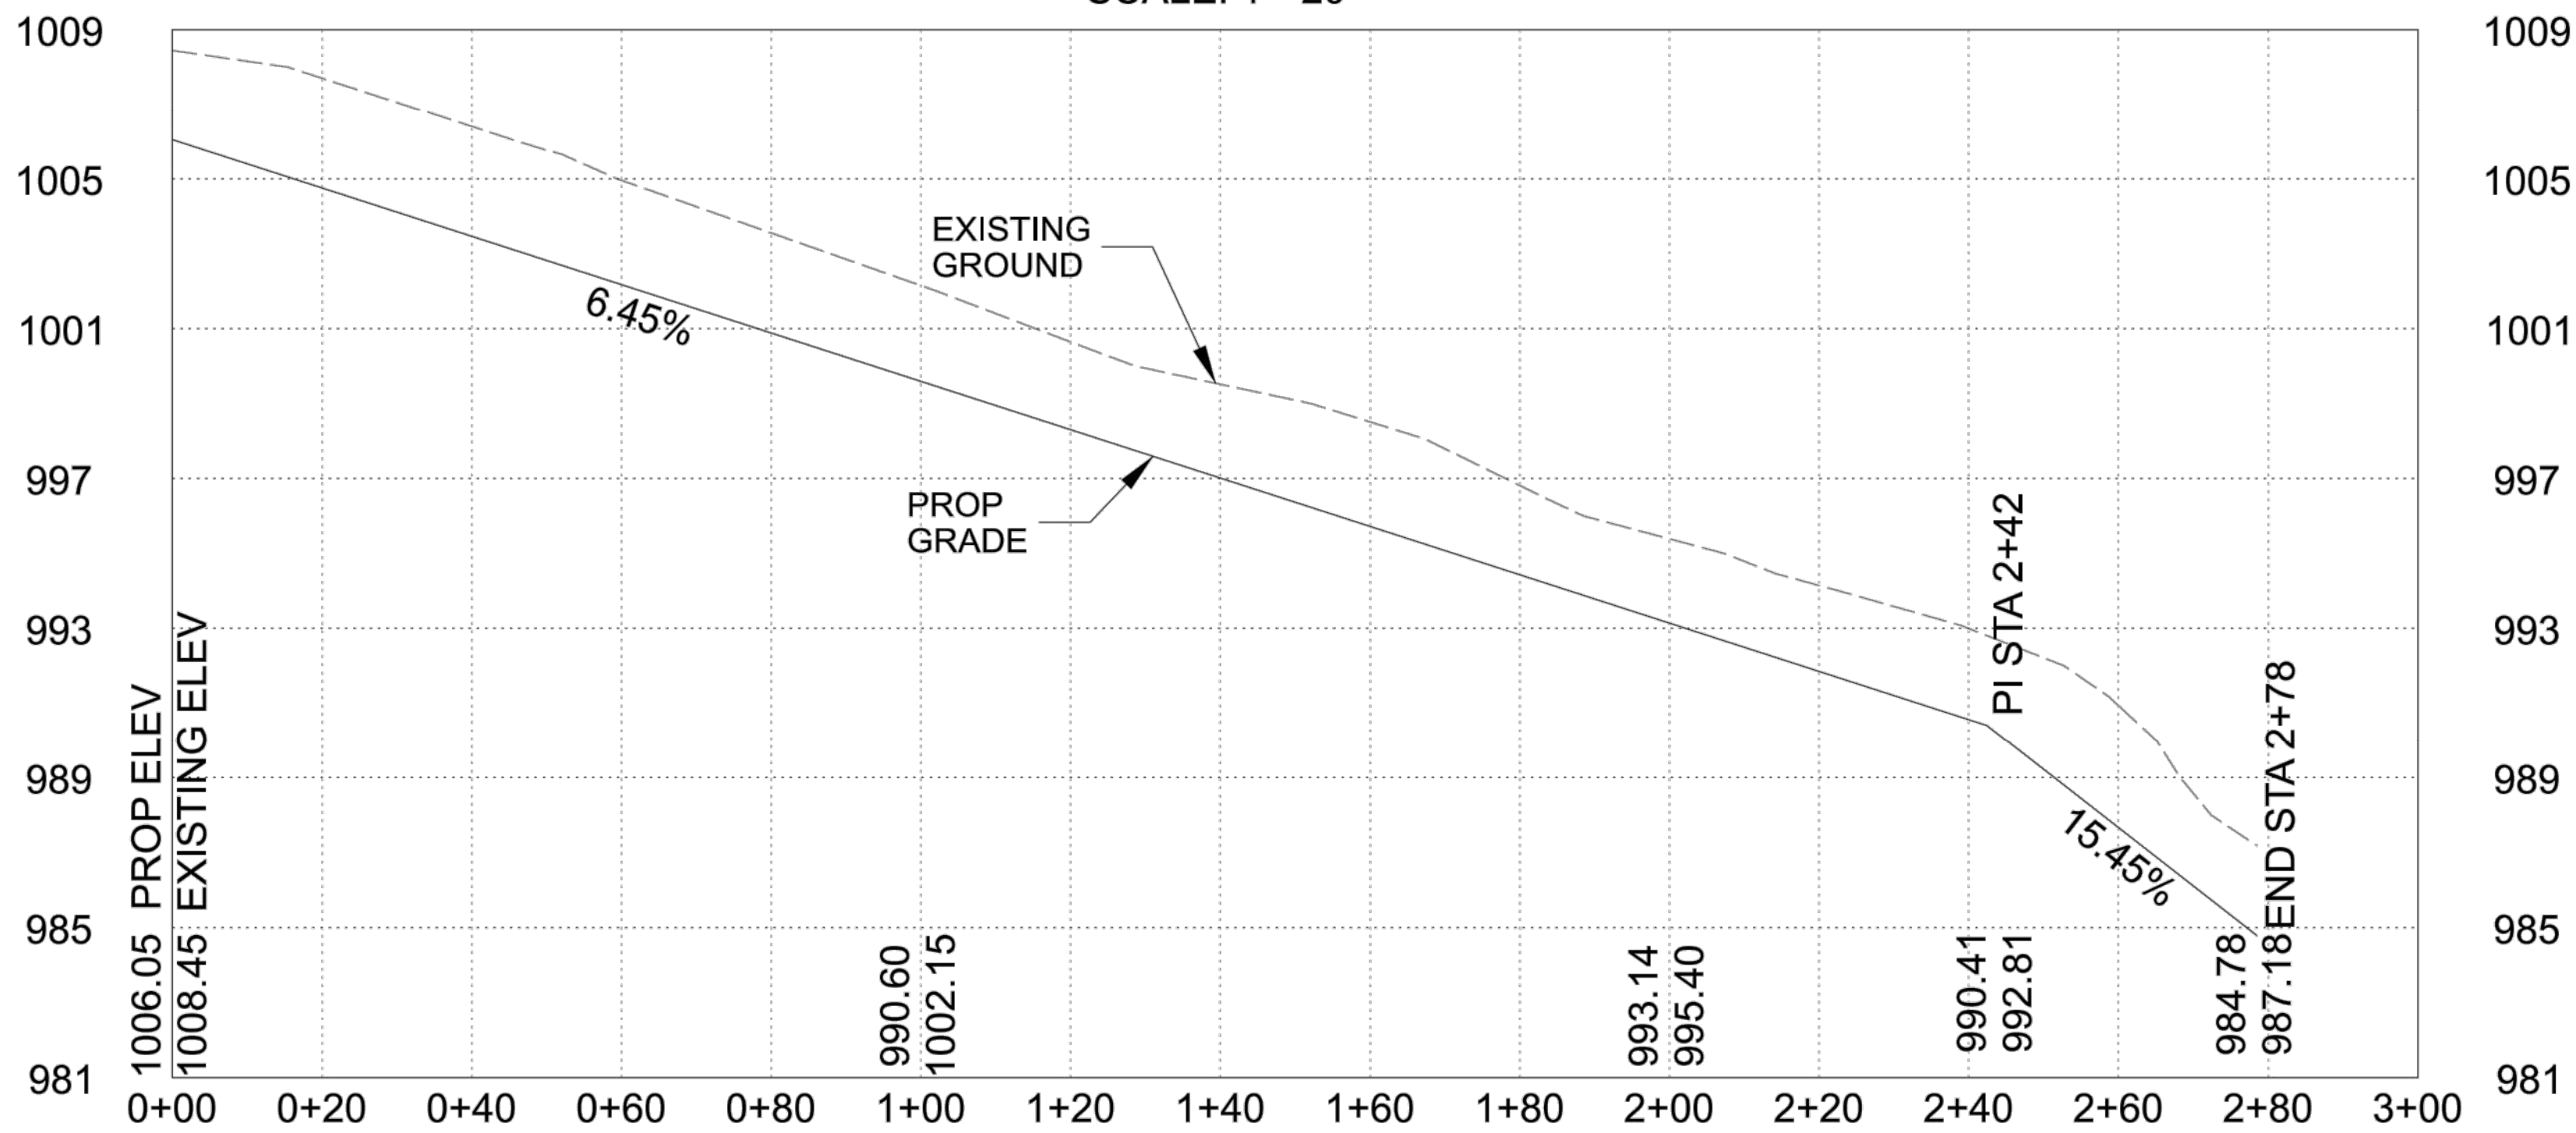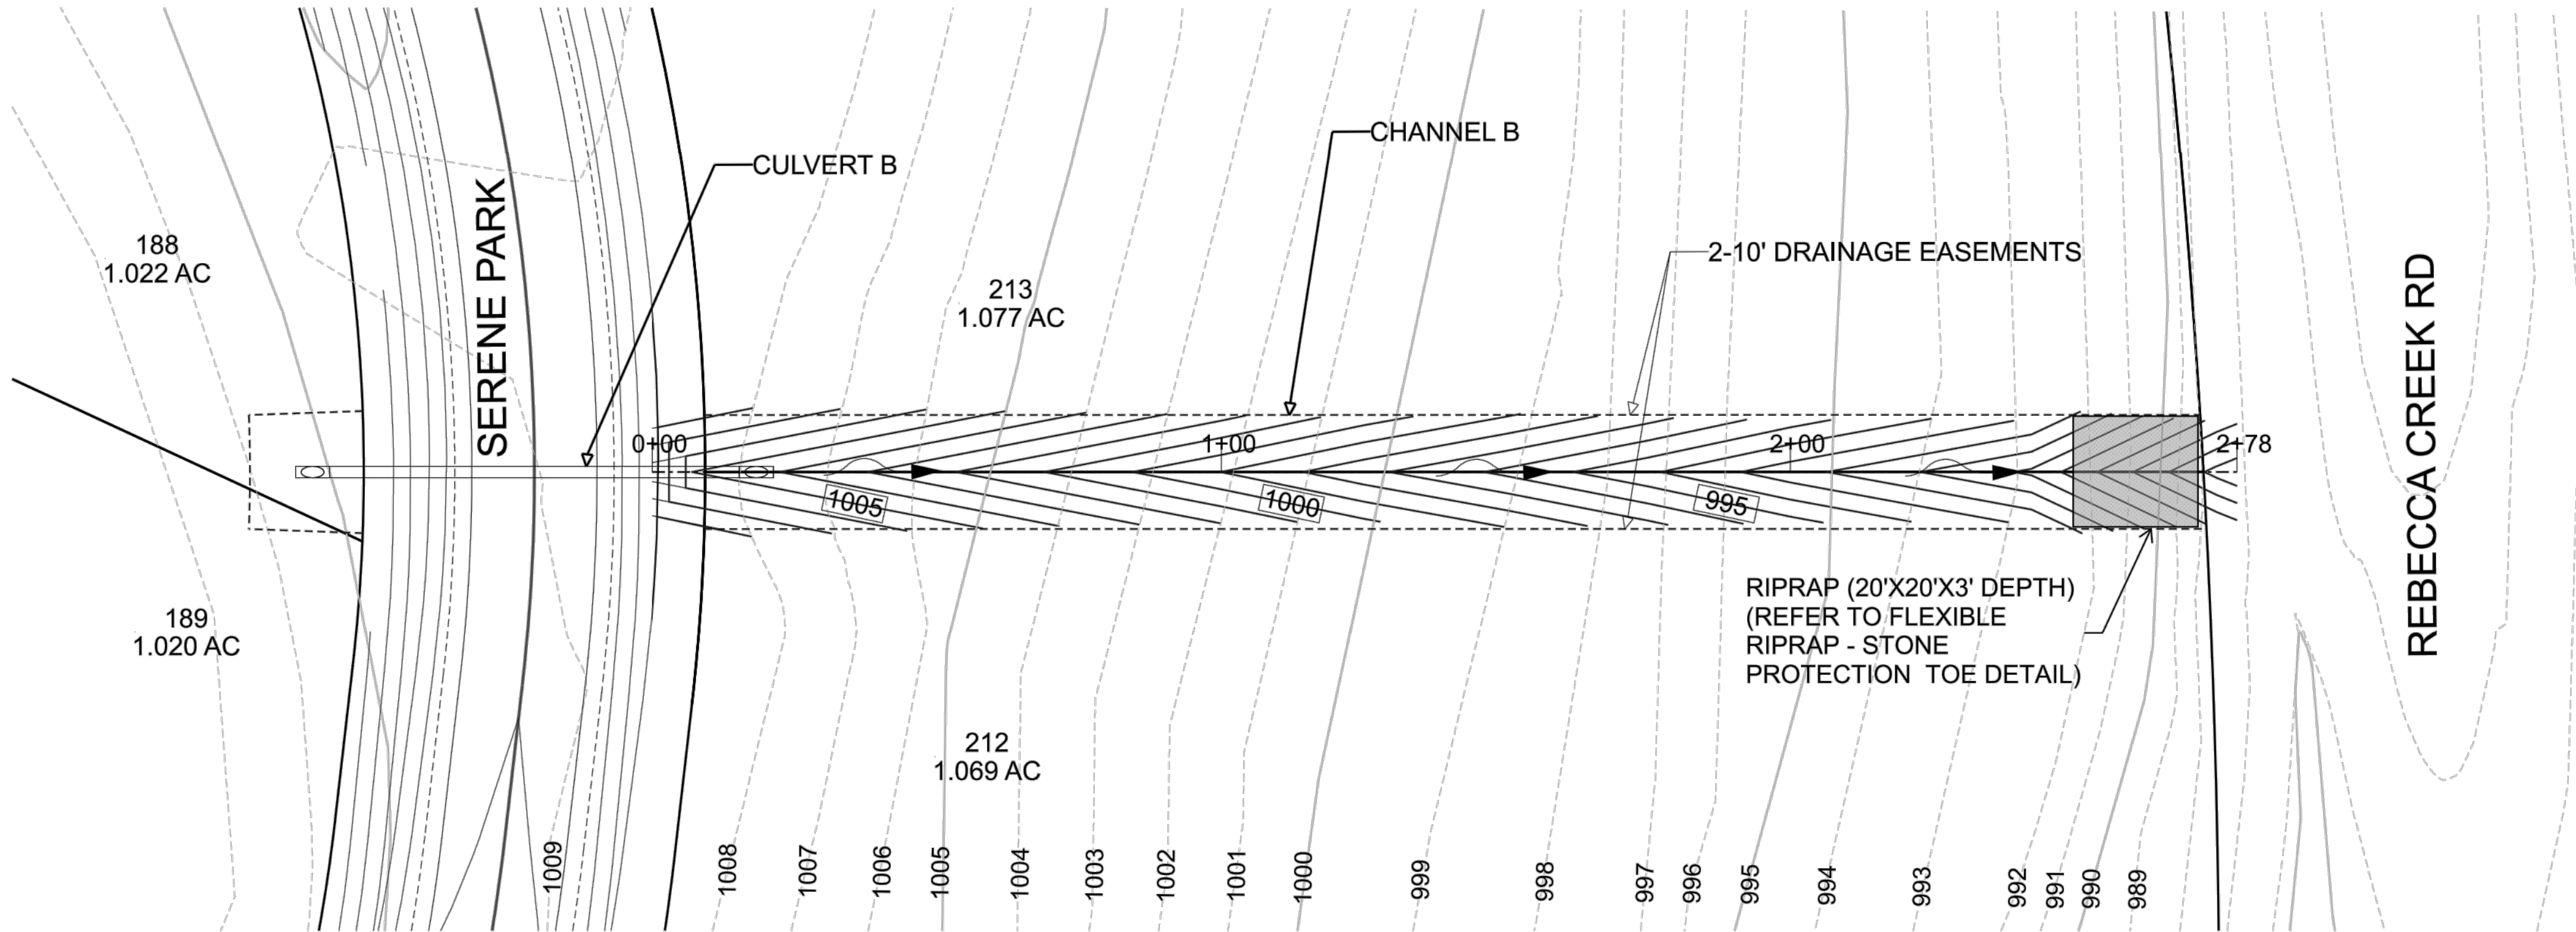

LEGEND

- #### PROP. CONTOUR
- #### EXIST. CONTOUR

REVISIONS				
NO.	DATE	DESCRIPTION	BY	
PROJ. #	DATE	DGN. BY	DWN. BY	CHKD. BY
U5-SER	03/06/23	S.G.	S.G.	R.M.G.

FIRM REGISTRATION # F40804

**GALLECOS ENGINEERING, INC.**

SAN ANTONIO, TEXAS www.gallecoseng.com PH: 210.641.0812

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLECOS, P.E. 86916 APRIL 6, 2023 ALTERATION OF A SEALED DOCUMENT WITHOUT THE SIGNATURE OF THE REGISTERED PROFESSIONAL ENGINEER IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT

STATE OF TEXAS  
RICHARD M. GALLECOS  
86916  
MECHANICAL ENGINEERING

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS



**CHANNEL B PLAN & PROFILE**

STA 0+00 - STA 2+78

GALE ESTATES, L.L.C.



S:\Projects\00-GENERAL\00-ACS Serenity Unit\5\Drawings\Sheet\513-US-GRD-CHAN-C 0+00-1+33.dwg

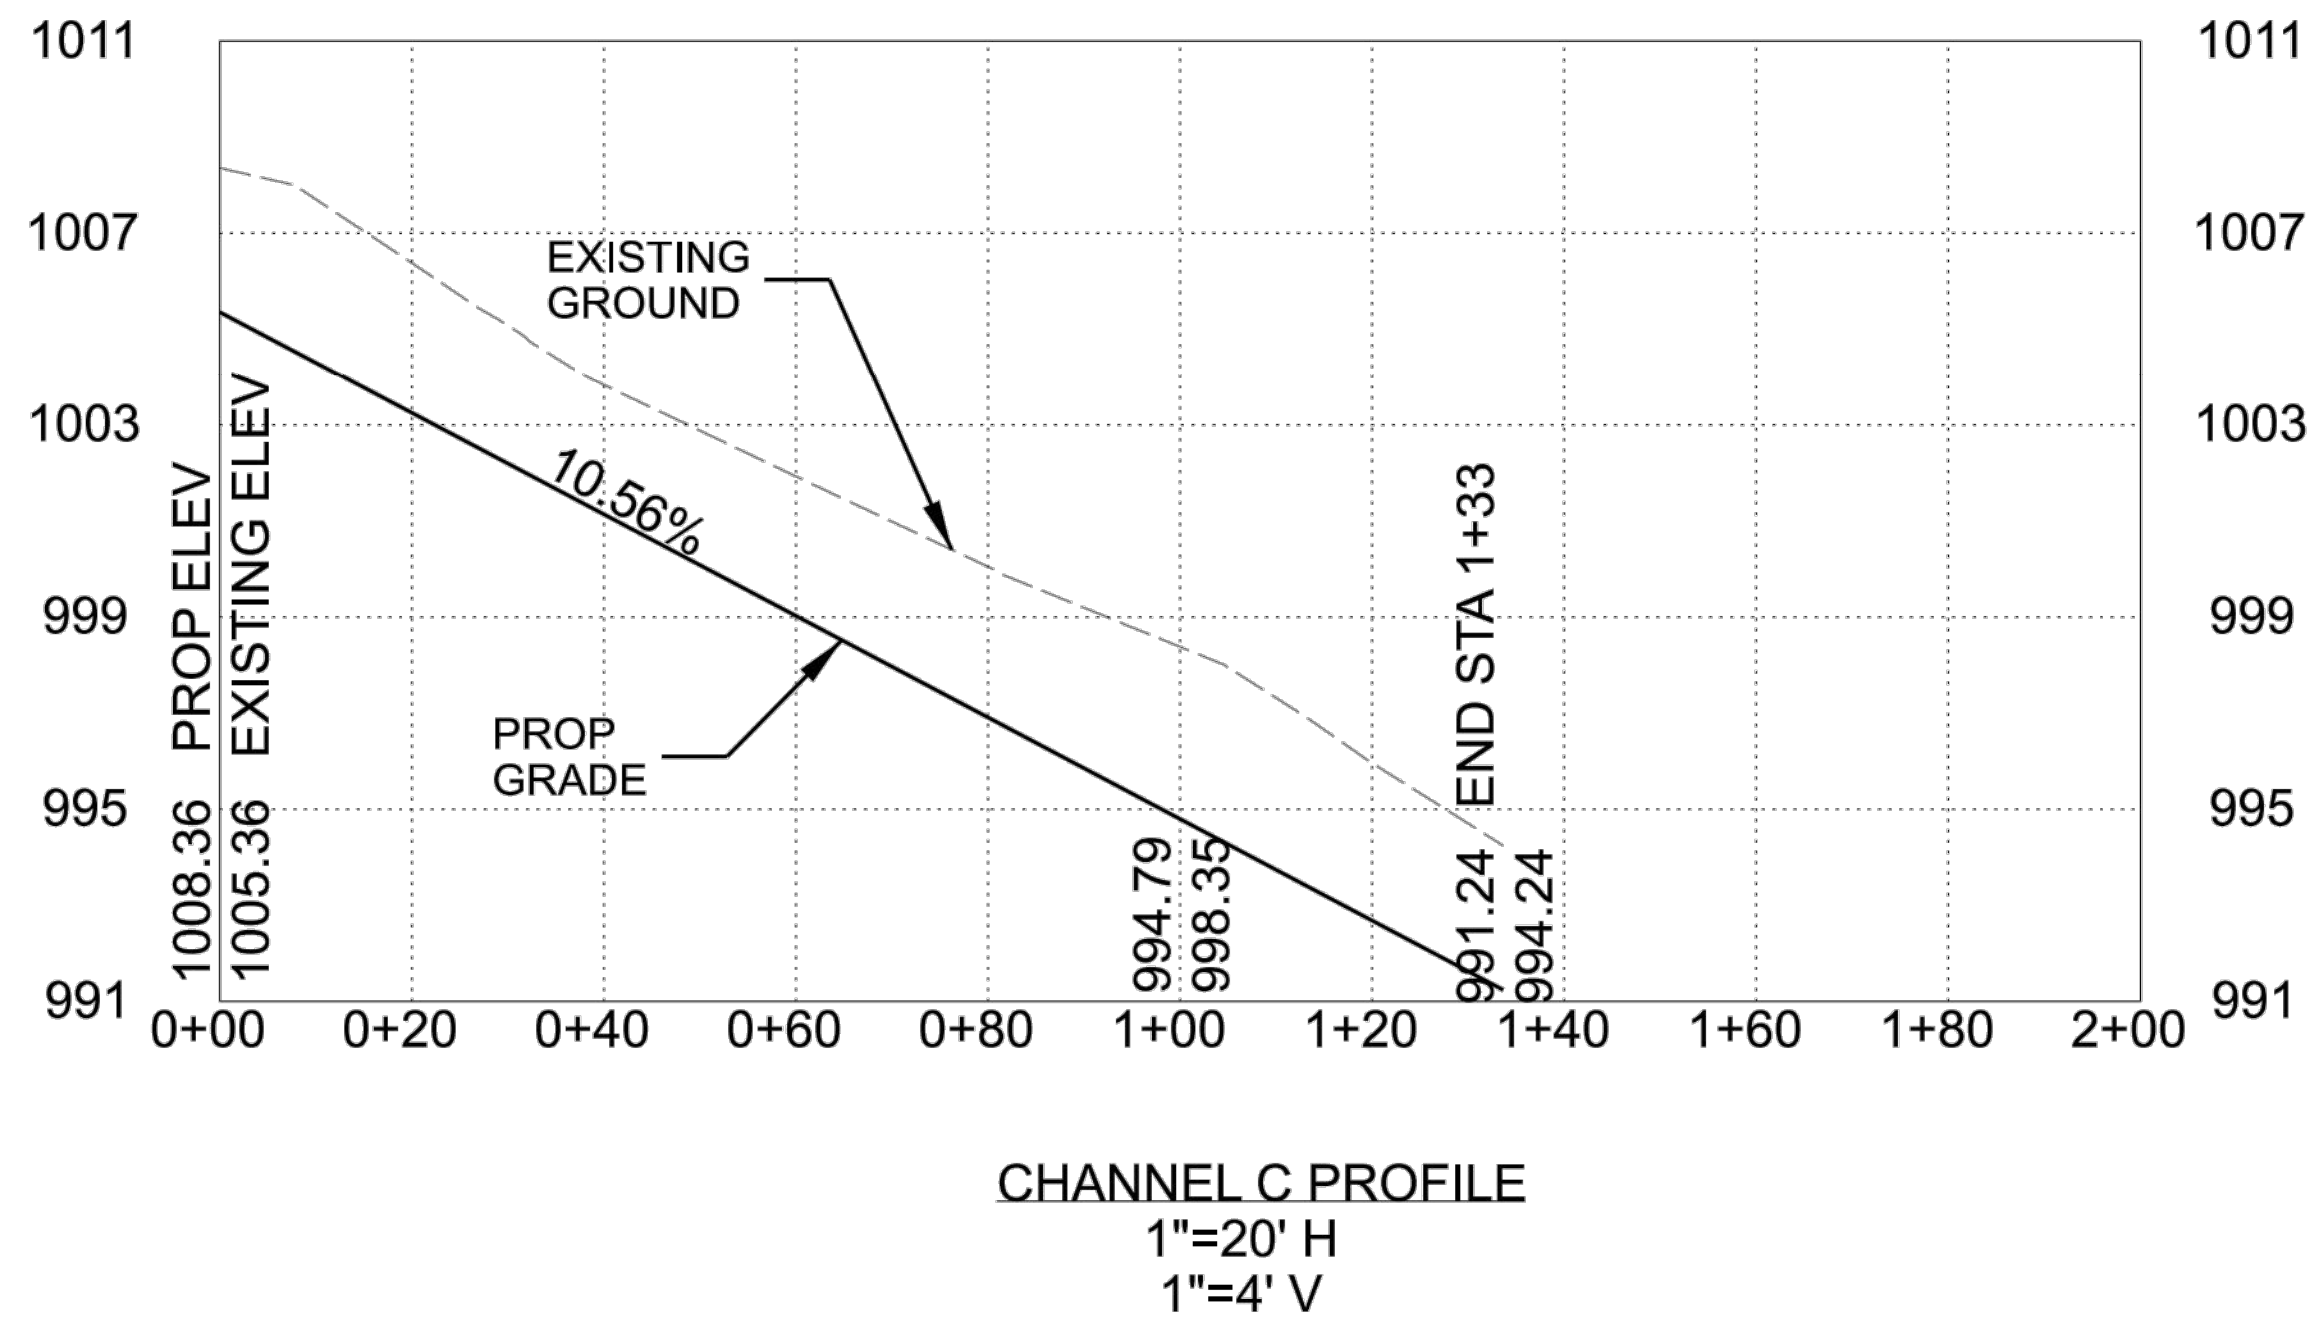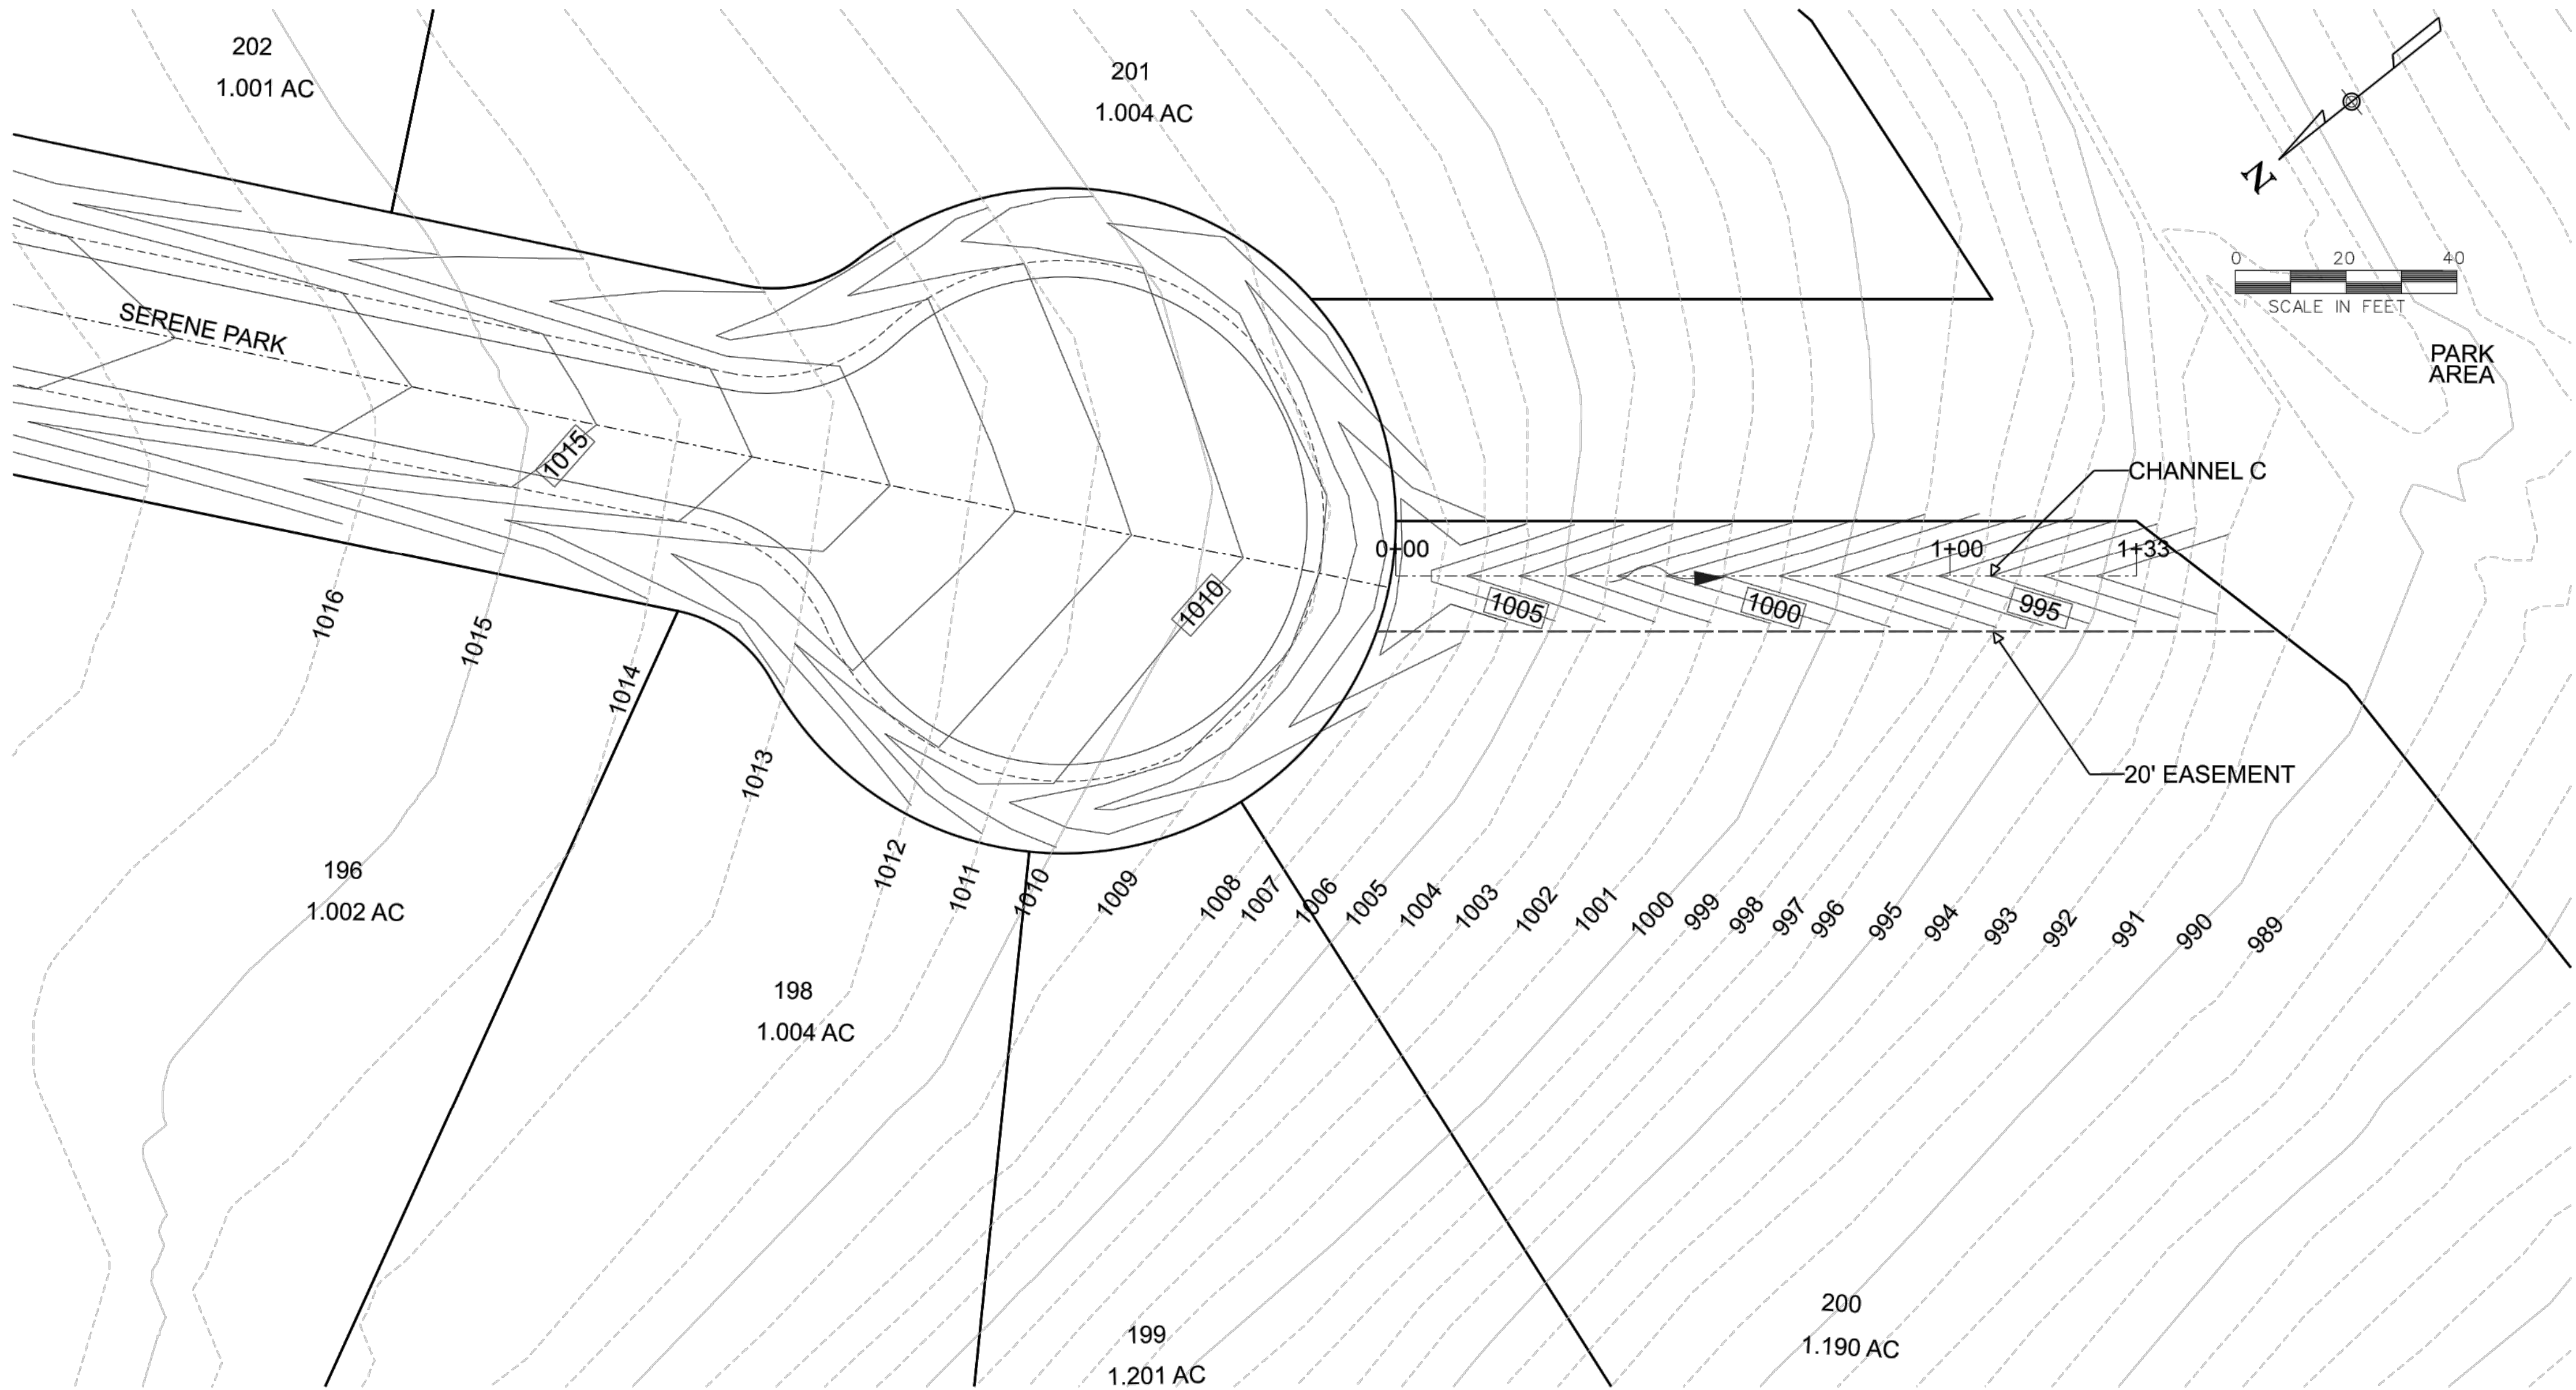

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

CHANNEL C PLAN & PROFILE  
STA 0+00 - STA 1+33  
GALE ESTATES, L.L.C.

SHEET 13  
OF 24

THE SEAL APPEARING ON  
THIS DOCUMENT WAS  
AUTHORIZED BY  
RICHARD M. GALLECOS, P.E. 86916  
NOVEMBER 2, 2022  
ALTERATION OF A SEALED DOCUMENT  
WITHOUT THE SIGNATURE OF THE  
REGISTERED PROFESSIONAL ENGINEER  
IS AN OFFENSE UNDER THE  
TEXAS ENGINEERING PRACTICE ACT





GALLECOS  
ENGINEERING,  
INC.  
SAN ANTONIO, TEXAS www.gallecoseng.com PH: 210.641.0812

FIRM REGISTRATION # F408084

REVISIONS				
NO.	DATE	DESCRIPTION	BY	
PROJ. #:	DATE:	DGN. BY:	CHKD. BY:	R.M.G.
US-SER	09/30/22	S.G.	S.G.	



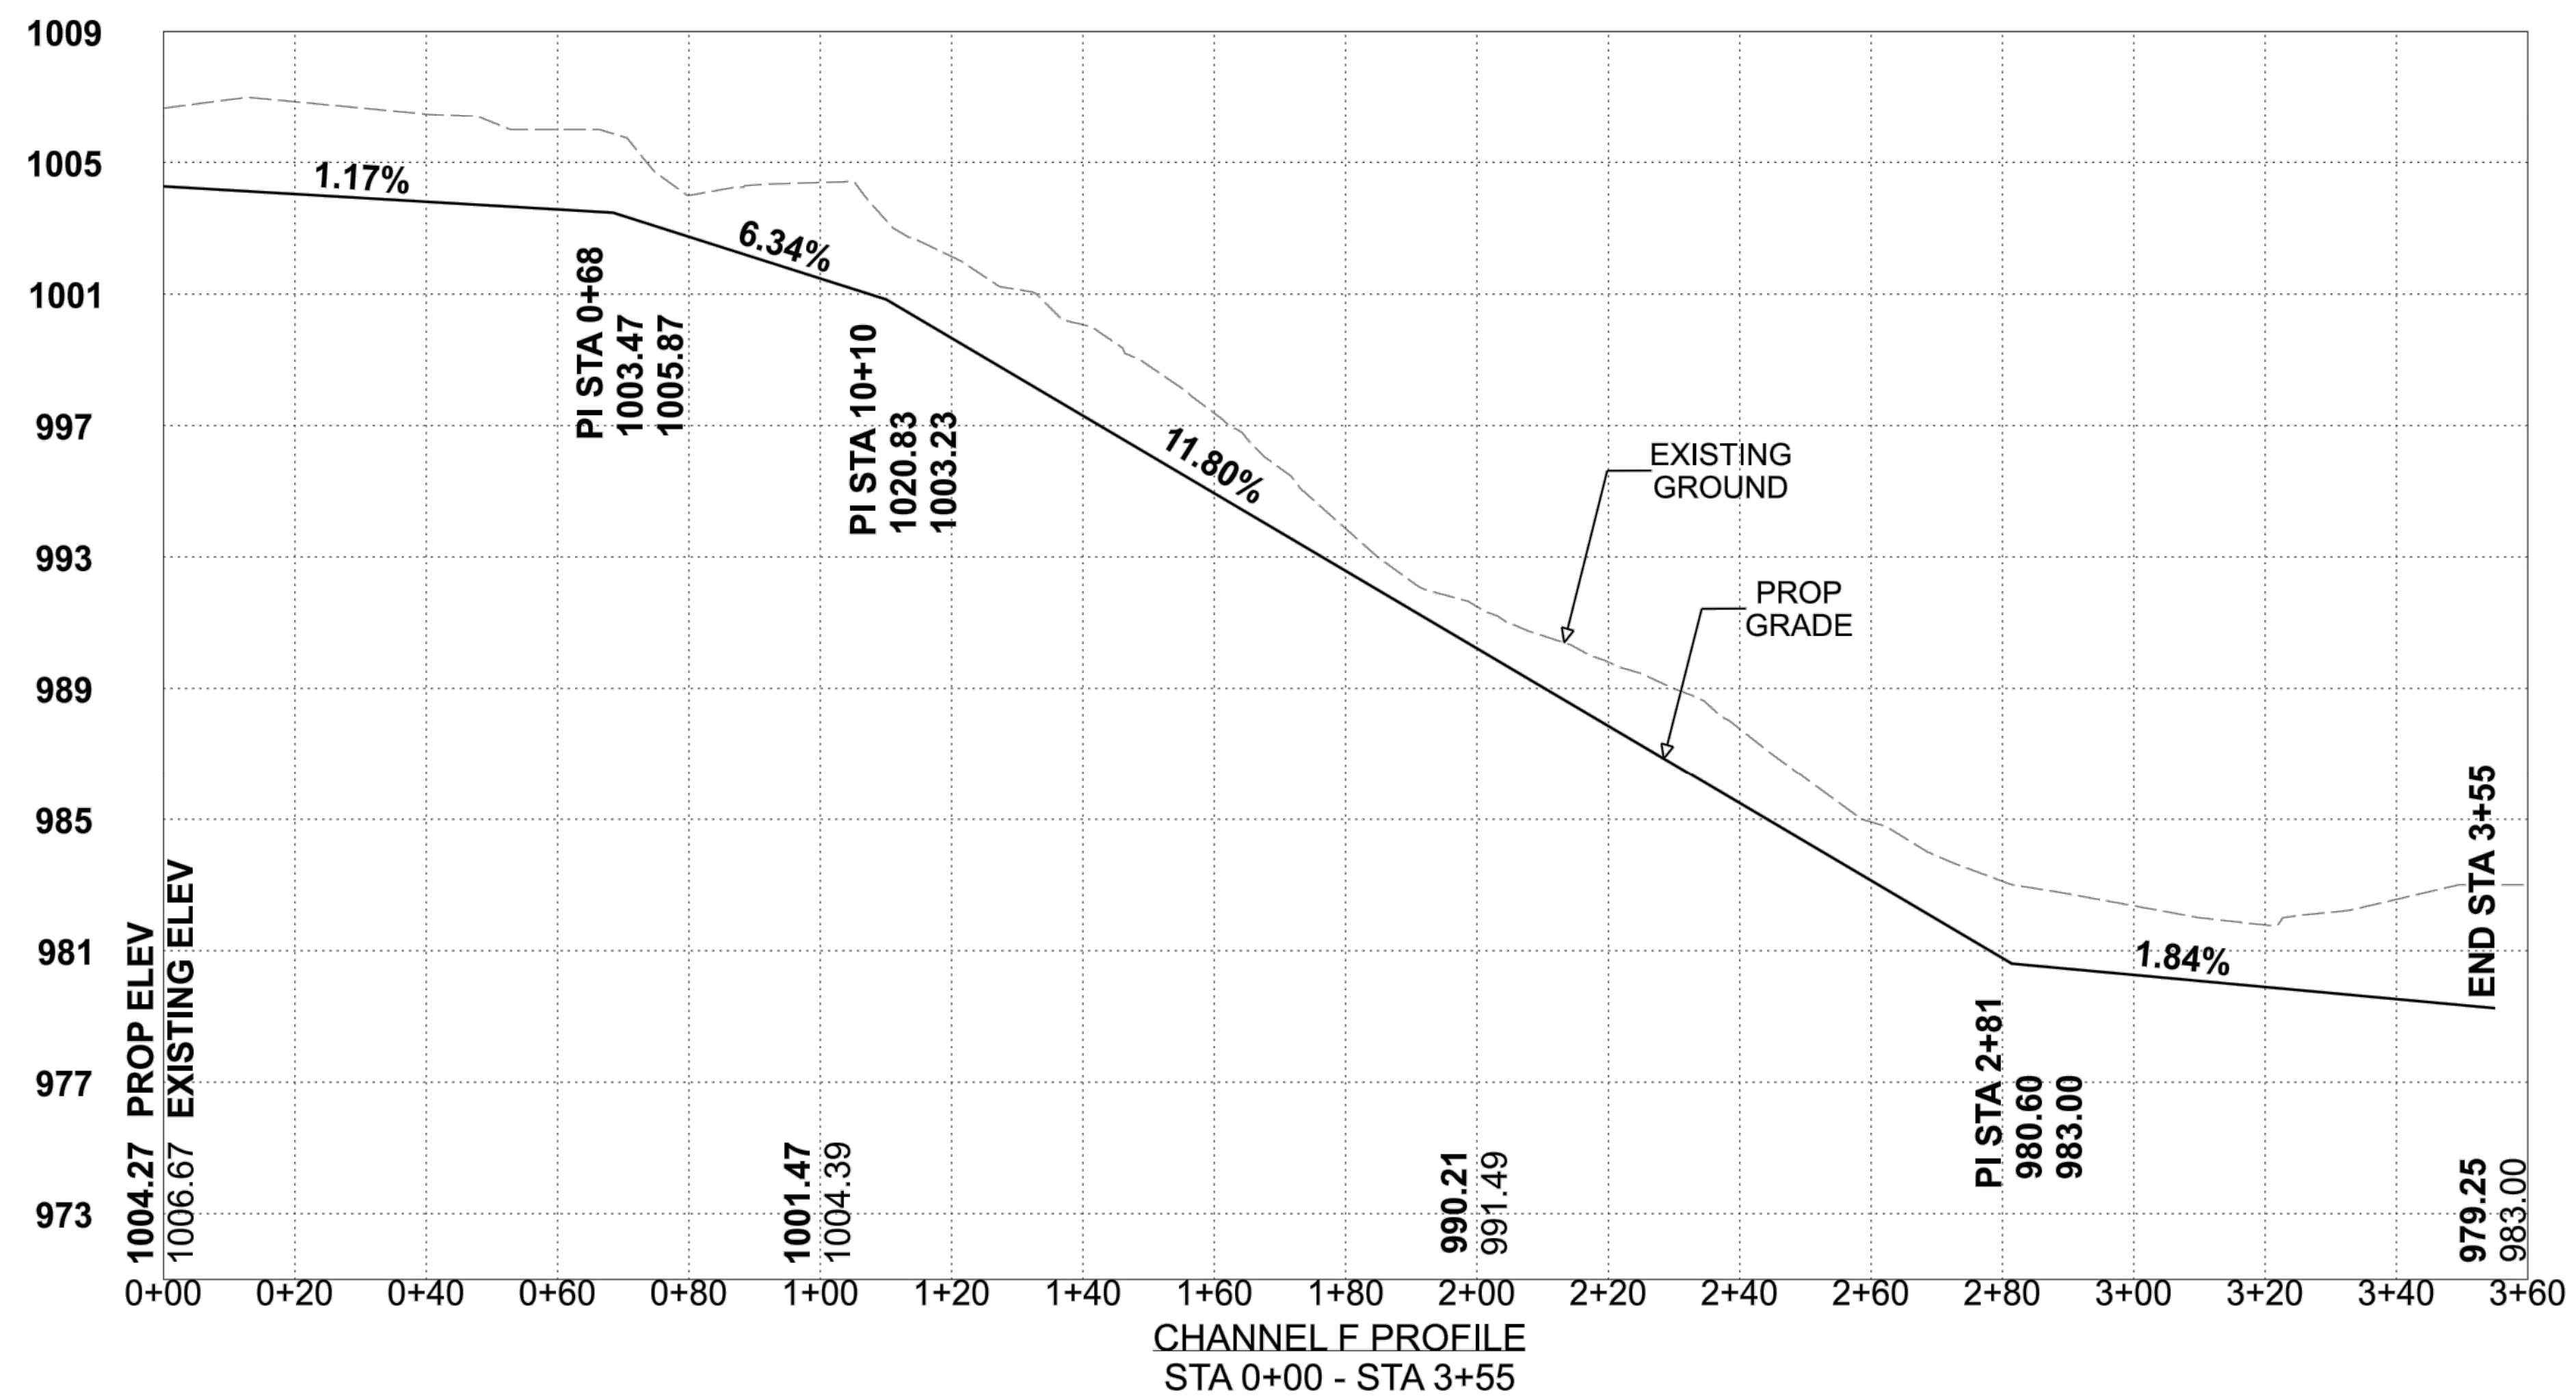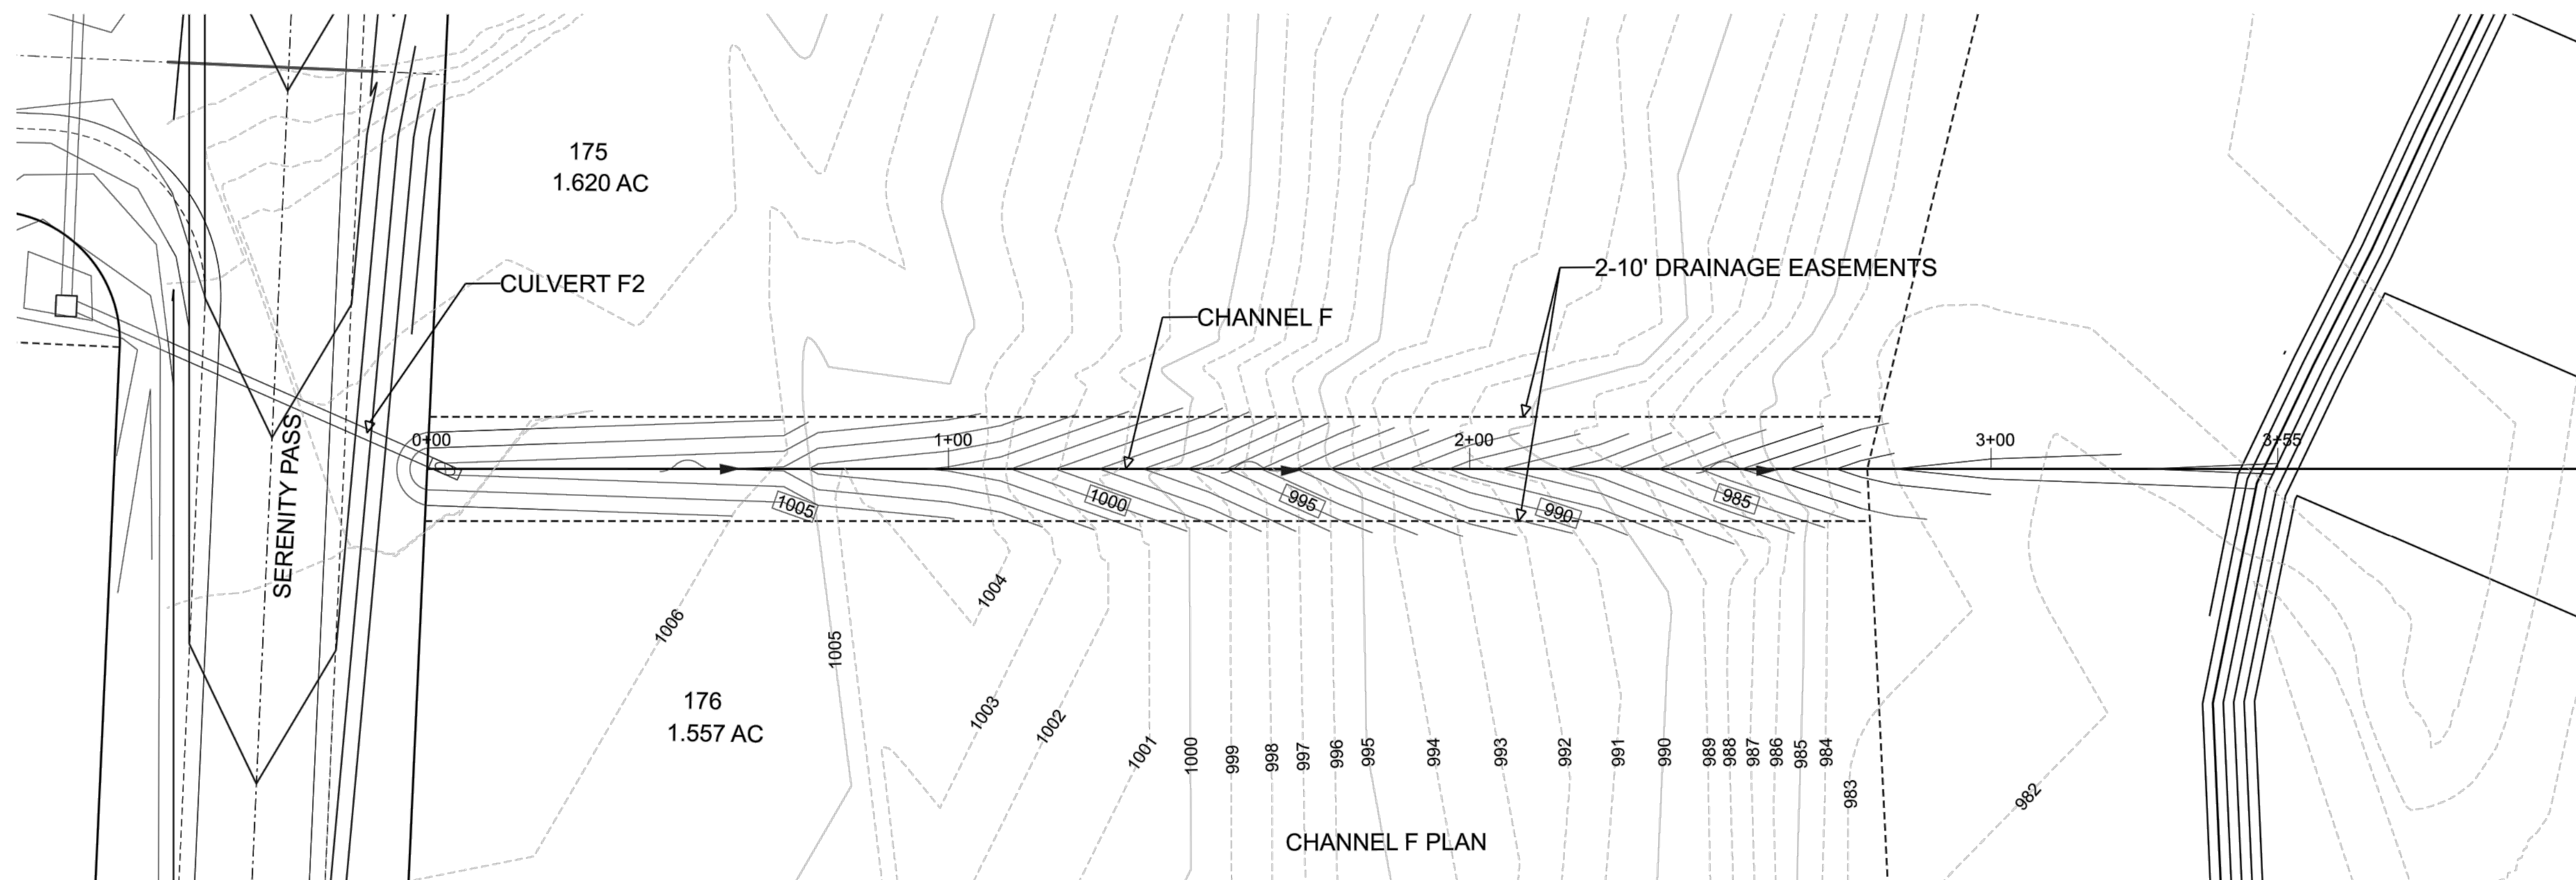


 **GALLEGOS  
ENGINEERING,  
INC.**

FIRM REGISTRATION # F-003884

SAN ANTONIO, TEXAS    [www.gallegoseng.com](http://www.gallegoseng.com)    PH: 210.641.0812

REVISIONS				
NO.	DATE	DESCRIPTION	BY	



SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS


CHANNEL F PLAN & PROFILE  
STA 0+00 - STA 3+55  
GALE ESTATES, L.L.C.



1. THIS PLAN SHOWS EXISTING CONTOURS WHICH ARE TAKEN FROM ACTUAL FIELD WORK TOPOGRAPHY SURVEY CONDUCTED BY URBAN SURVEYING, INC.
2. CONTRACTOR MUST ENSURE ALL DISTURBED AREAS ARE GRADED TO DRAIN PROPERLY AFTER CONSTRUCTION HAS BEEN COMPLETED.
3. PROPOSED GRADING AROUND THE BUILDING(S) MUST BE GRADED FOR POSITIVE DRAINAGE AWAY FROM THE CONCRETE FOUNDATIONS WITH MIN. 2% SLOPE.
4. ALL FILL SLOPE SHOULD BE EQUAL OR LESS THAN A 3H:1V SLOPE, UNLESS OTHERWISE NOTED.
5. IF AN ELEVATION DISCREPANCY IS FOUND, CONTRACTOR MUST NOTIFY ENGINEER IMMEDIATELY BEFORE COMMENCING CONSTRUCTION; OTHERWISE PROCEEDING WITHOUT GALLEGOS ENGINEERING PERMISSION WILL CONSTITUTE CONTRACTOR PROCEEDING AT THEIR OWN RISK. OWNER NOT RESPONSIBLE FOR PAYING TO REWORK AREAS THAT CONTRACTOR PROCEEDED WITHOUT GALLEGOS ENGINEERING APPROVAL.
6. CONTRACTOR SHALL VEGETATE FILL/CUT SLOPES, LANDSCAPE AREAS, OR OTHER DISTURBED AREAS DUE TO CONSTRUCTION WITH SOD OR SEEDING. SEE GENERAL NOTES ON COVER SHEET AND OR LANDSCAPE ARCHITECT PLANS FOR FURTHER INFORMATION.
7. CONTRACTOR TO MATCH EXISTING ELEVATIONS AT ALL EXISTING PAVEMENT TIE-INS.
8. SEE GENERAL DETAILS FOR FILL COMPACTION REQUIREMENTS FOR PAVEMENT AREAS. FILL OUTSIDE THE PAVEMENT AREAS TO BE COMPACTED TO 90% PROCTOR MAX. DRY DENSITY.

CONTRACTOR AND/OR CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR STRUCTURAL DESIGN / GEOTECHNICAL / SAFETY / EQUIPMENT CONSULTANT, IF ANY, SHALL REVIEW THESE PLANS AND AVAILABLE GEOTECHNICAL INFORMATION AND THE ANTICIPATED INSTALLATION SITE(S) WITHIN THE PROJECT WORK AREA IN ORDER TO IMPLEMENT CONTRACTOR'S TRENCH SAFETY PROTECTION SYSTEMS, PROGRAMS AND/OR PROCEDURES FOR THE PROJECT DESCRIBED IN THE CONTRACT DOCUMENTS. THE CONTRACTOR'S IMPLEMENTATION OF THESE SYSTEMS, PROGRAMS AND/OR PROCEDURES SHALL PROVIDE FOR ADEQUATE TRENCH EXCAVATION SAFETY PROTECTION THAT COMPLY WITH AS A MINIMUM, OSHA STANDARDS FOR TRENCH EXCAVATIONS. SPECIFICALLY, CONTRACTOR AND/OR CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR SAFETY CONSULTANT SHALL IMPLEMENT A TRENCH SAFETY PROGRAM IN ACCORDANCE WITH OSHA STANDARDS GOVERNING THE PRESENCE AND ACTIVITIES OF INDIVIDUALS WORKING IN AND AROUND TRENCH EXCAVATION.

1. THE LOCATIONS AND DEPTHS OF EXISTING UTILITIES SHOWN ON THESE PLANS ARE APPROXIMATE ONLY. ACTUAL LOCATIONS AND DEPTHS OF UTILITIES MUST BE VERIFIED BY CONTRACTOR PRIOR TO CONSTRUCTION. ANY AND ALL DAMAGE DURING CONSTRUCTION SHALL BE REPAIRED BY THE CONTRACTOR AT THEIR SOLE EXPENSE.
2. ALL MATERIALS AND CONSTRUCTION PROCEDURES SHALL COMPLY WITH THE CITY OF SAN ANTONIO STANDARD SPECIFICATIONS FOR PUBLIC WORKS CONSTRUCTION (LATEST EDITION), AND TCEQ REGULATIONS.
3. CONTRACTOR SHALL CALL TEXAS ONE CALL SYSTEM @ (800) 245-4545 PRIOR TO CONSTRUCTION NEAR AREAS OF EXCAVATION.
4. 48 HOURS PRIOR TO CONSTRUCTION, CONTRACTOR SHALL NOTIFY THE ALL UTILITY COMPANIES SO THEY CAN LOCATE AND TAG THEIR OWN UNDERGROUND UTILITIES (SEE CONTACTS ON COVER SHEET).

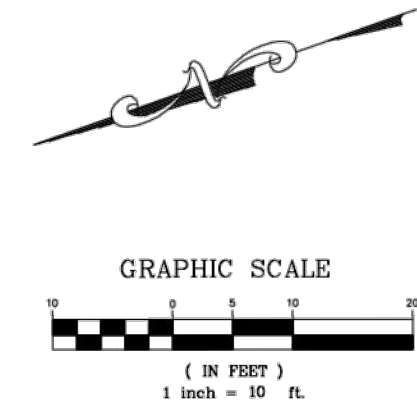

CAUTION!!!  
CONTACT:

THE LOCATION OF EXISTING UNDERGROUND UTILITIES ARE SHOWN IN AN APPROXIMATE WAY ONLY. THE CONTRACTOR SHALL DETERMINE THE EXACT LOCATION OF ALL EXISTING UTILITIES BEFORE COMMENCING WORK. HE AGREES TO BE FULLY RESPONSIBLE FOR ANY AND ALL DAMAGES WHICH MIGHT OCCUR BY HIS FAILURE TO EXACTLY LOCATE AND PRESERVE ANY AND ALL UNDERGROUND UTILITIES.

REVISONS				
NO.	DATE	DESCRIPTION	BY	

PROJ. #:	DATE:	DGN. BY:	DWN. BY:	CHKD. BY:
U5-SER	03/06/23	S.G.	S.G.	R.M.G.



**GALLEGOS  
ENGINEERING,  
INC.**

FIRM REGIS.

**SAN ANTONIO, TEXAS    www.gallegoseng.com    PH: 210.641.0812**

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

## DRIVEWAY DETAILS


GALE ESTATES, L.L.C.

*SHEET* 15  
*OF* 24




S:\Projects\00-GENERAL\00-ACS Serenity Unit\5\Drawings\Sheets\18-15-GRD-RIPRAP DETS.dwg


## EMBANKMENT

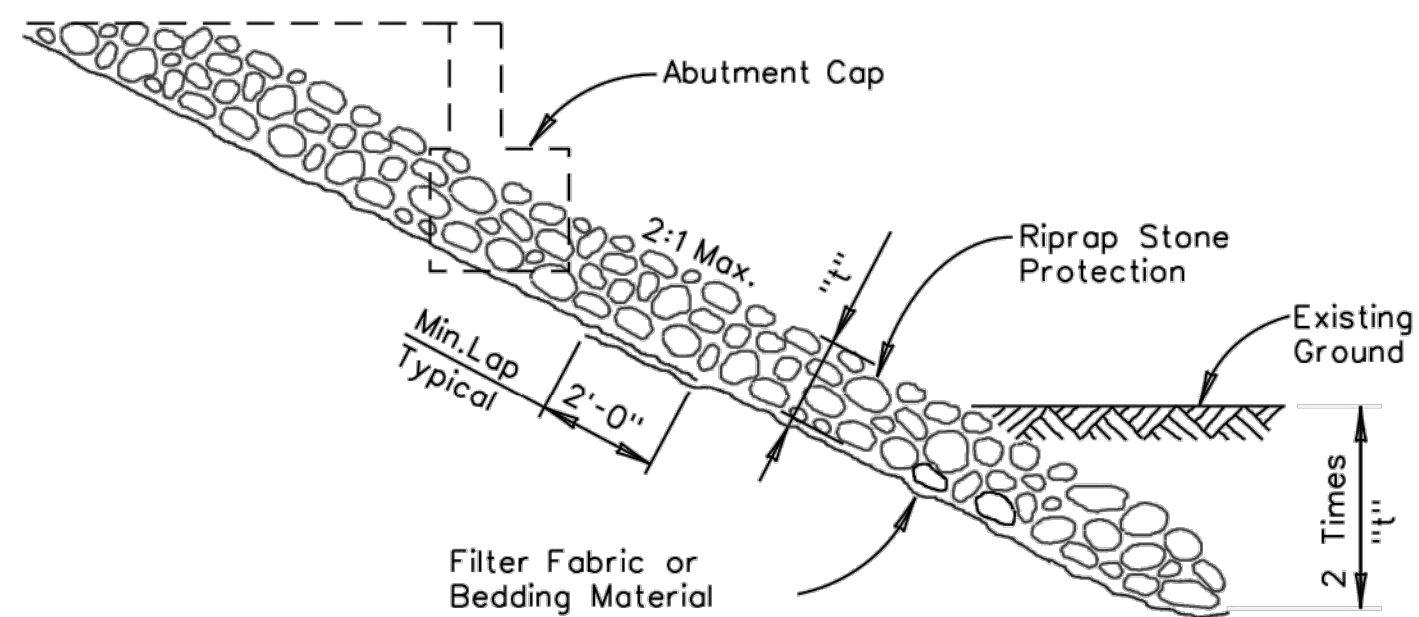

TOE DETAIL ①

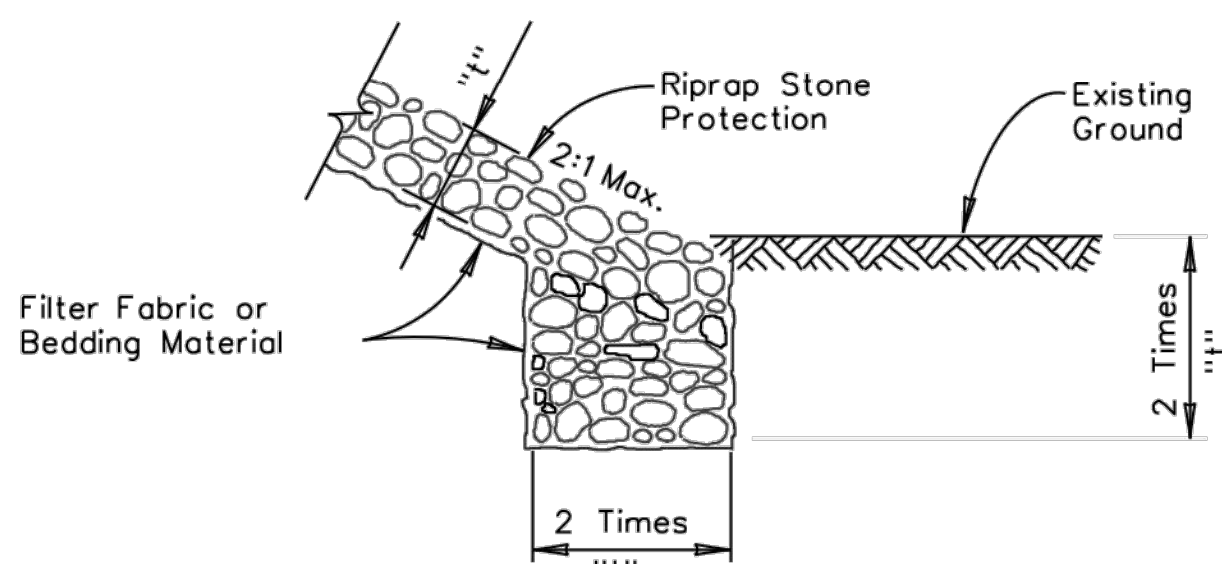


TOE DETAIL ①  
(ALTERNATE)

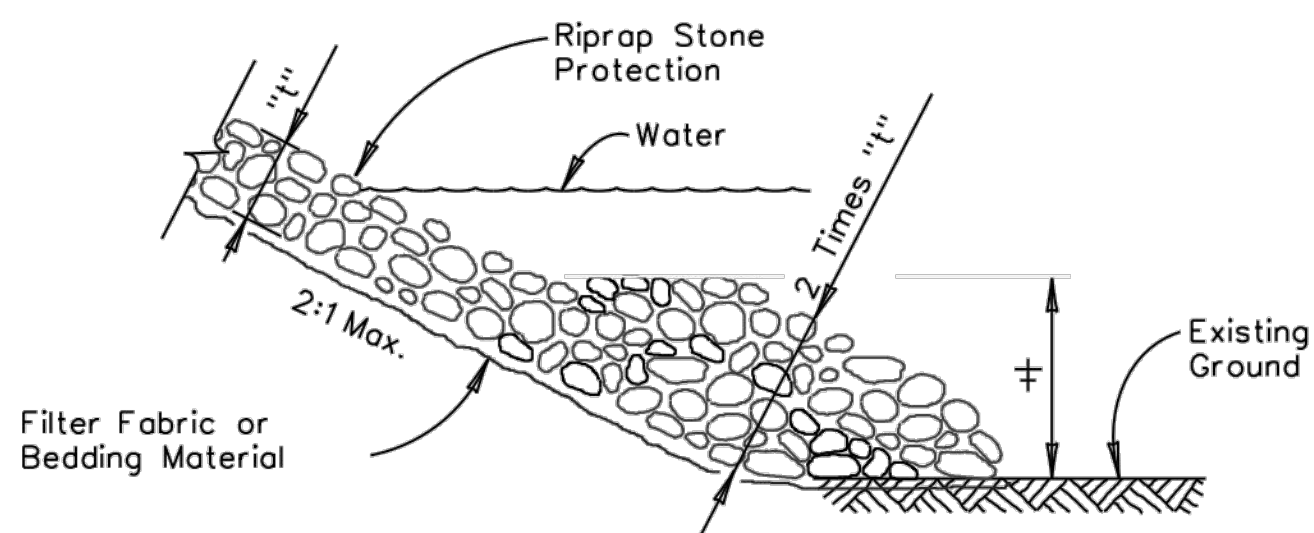

TOE DETAIL ①  
UNDER WATER

± 2 times the thickness ("t") or maximum expected scour considering site history if available.


## PIER

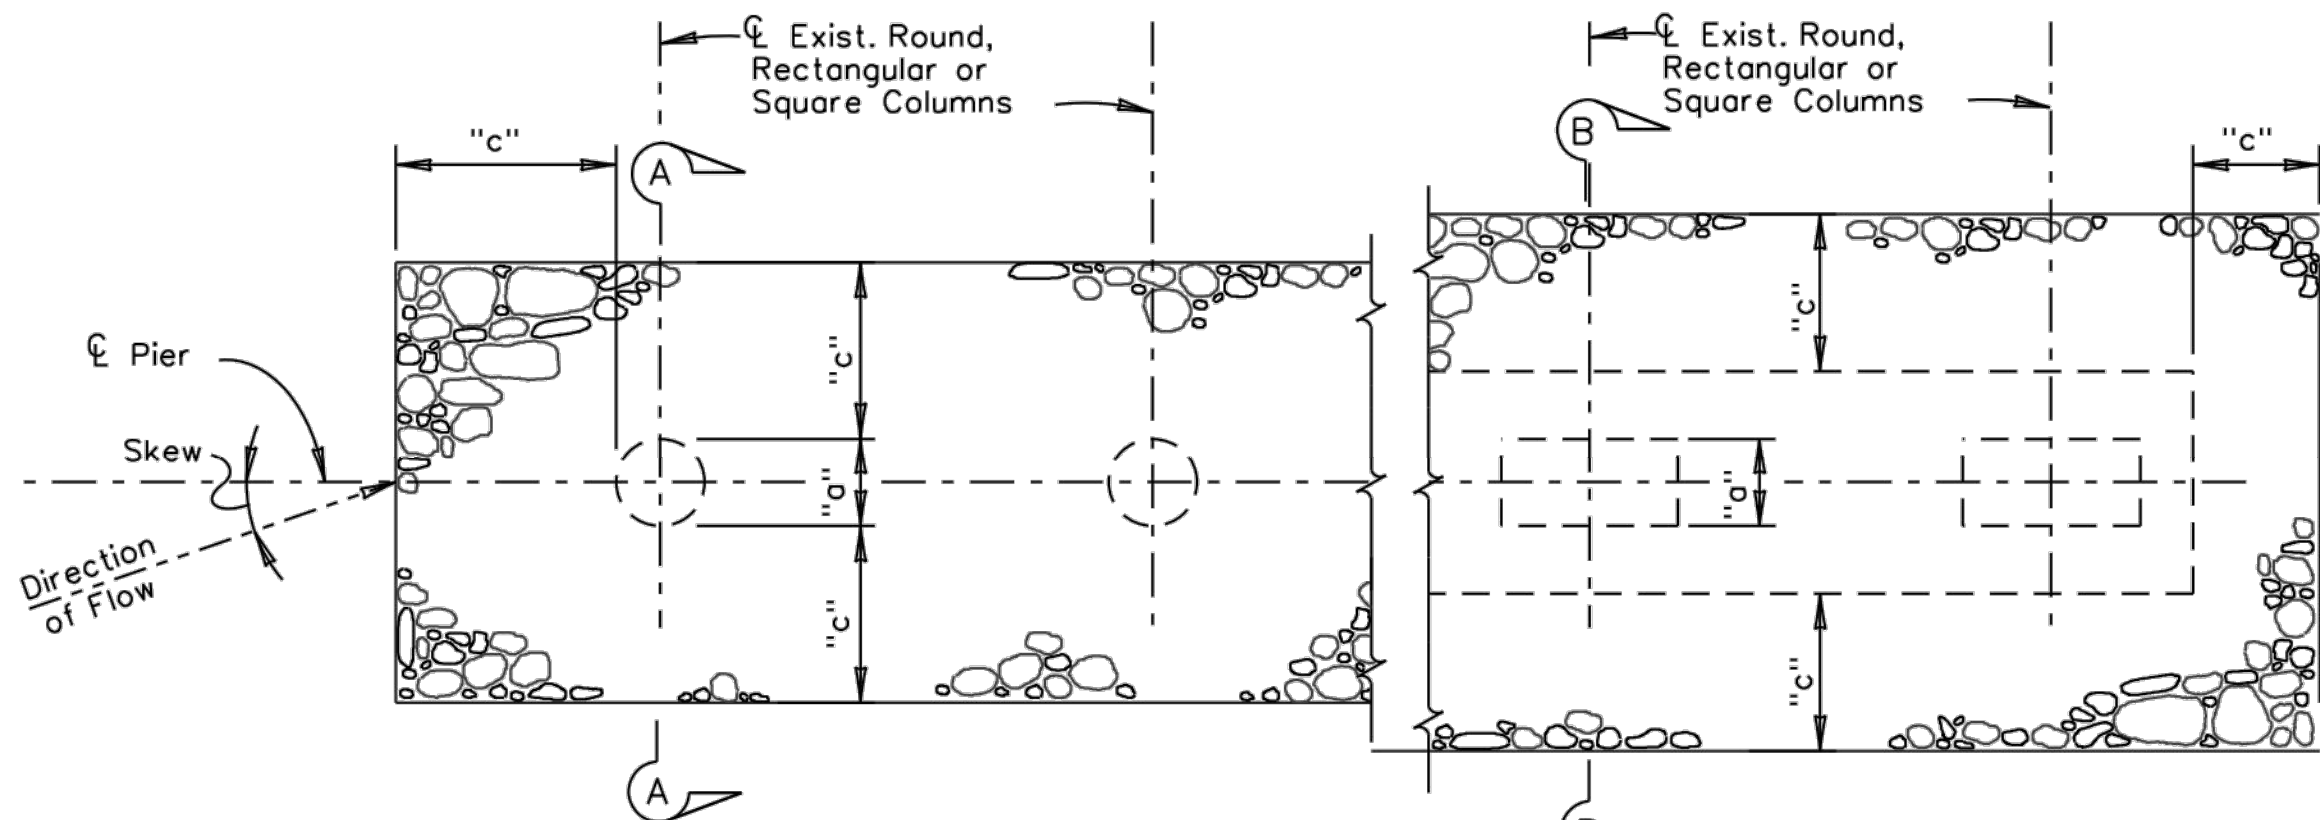

COLUMN ON DRILLED SHAFT  
OR PILING

COLUMN ON SPREAD FOOTING


## PLAN VIEW

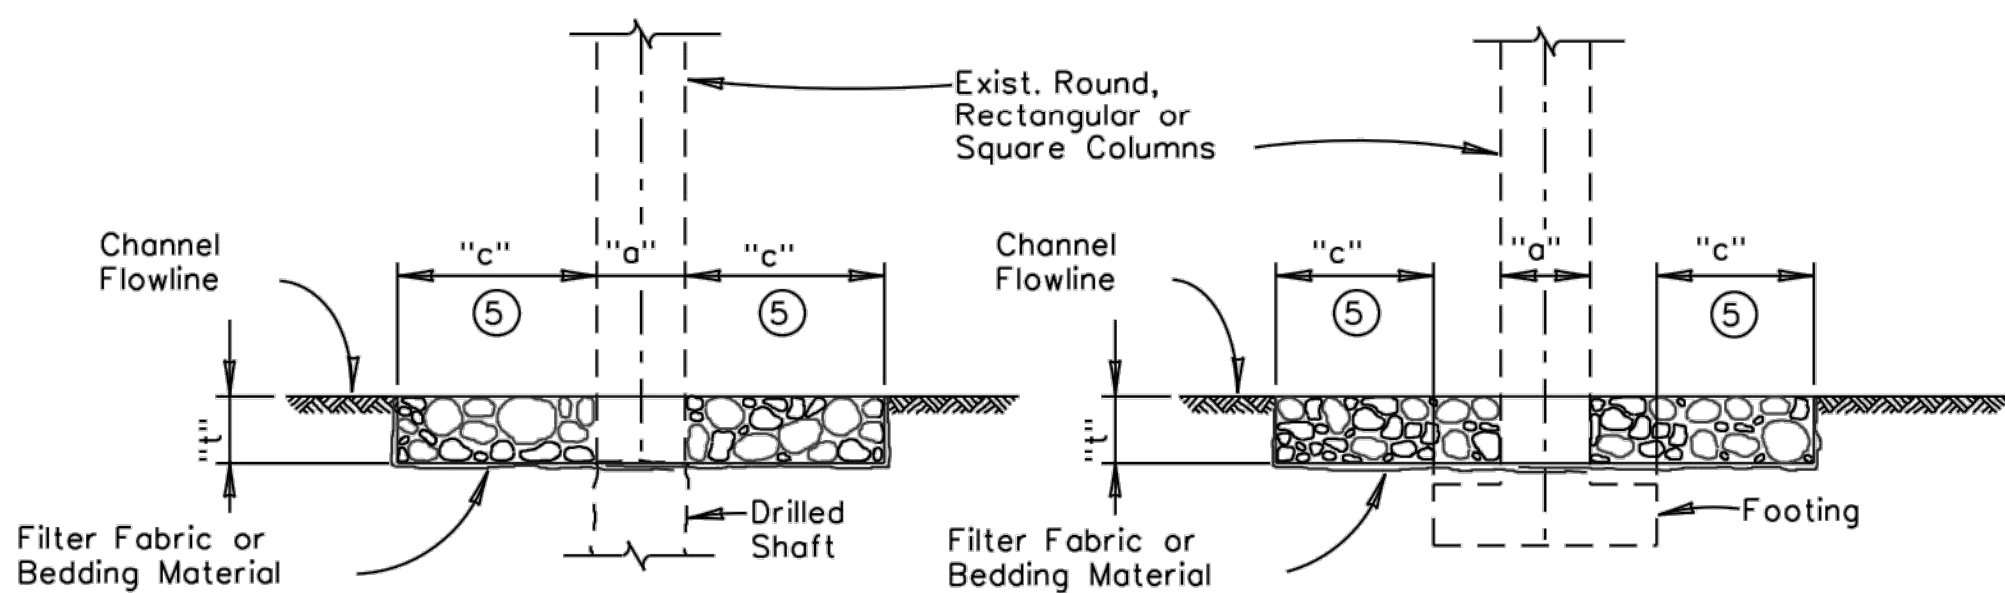

SECTION A-A

SECTION B-B


## ELEVATION

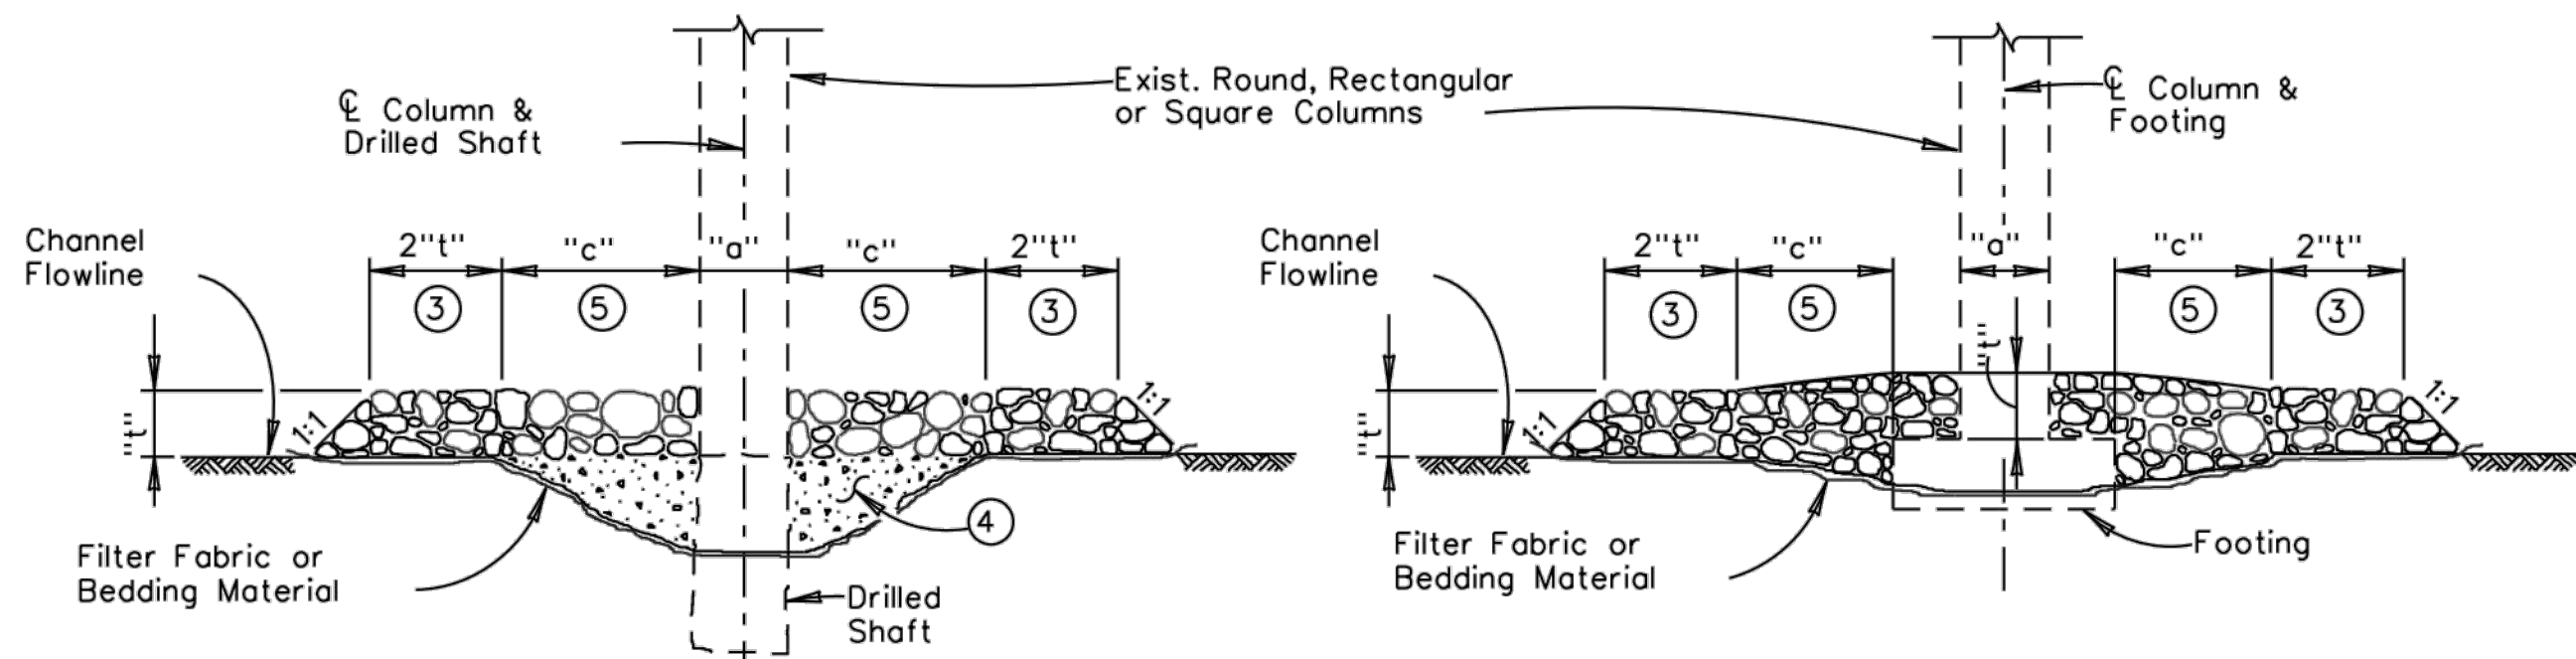

SECTION A-A

SECTION B-B

## ELEVATION UNDER WATER OR SCOUR CRITICAL

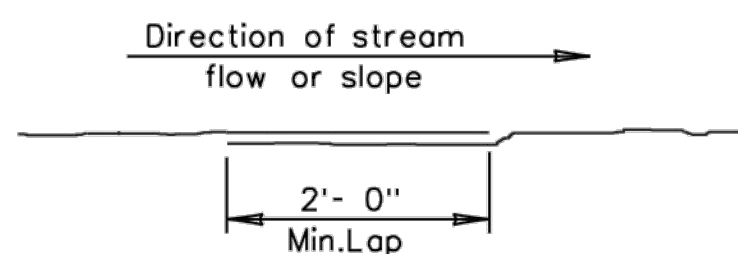

FILTER FABRIC LAP

### NOTES:

- ① Toe required at all boundaries of stone protection except where placed next to a structure such as an abutment or pier.
- ② Bedding material is not required if filter fabric is used. Filter Fabric will be Type 2 (6 oz/sy) as per DMS 6200.
- ③ In areas where excavation in the channel will exacerbate scour, an additional width of stone protection is required as shown.
- ④ Scour damage may be filled with a material having a gradation equal to the bedding material but will not be more coarse than stone protection being placed, as specified in item 432 "RIPRAP", approval of the engineer is required.
- ⑤ Surface of stone protection will slope away from the pier, but not exceed 2:1.

### GENERAL NOTES:

Refer to item 432 for the gradation of stone protection and bedding material, alternate gradations are not permitted. Placement of stone protection will not be performed in a manner that will cause segregation such as dumping or pushing material in place.

See Layout for limits and thickness of riprap specified, design table provided below is a guide for the designer. All work will be performed in accordance with item 432.

### DESIGN TABLE:

Minimum specific gravity for stone protection is 2.40  
Minimum thickness permissible is 12 inches, channel velocities (V) for a given thickness and gradation will not exceed the limits indicated in the table below.

- "t" = Thickness of revetment
- "a" = Column width
- Skew = Angle between direction of flow and center of pier
- "c" =  $2'a/\cos(\text{skew})$
- "v" = Stream velocity

	ABUTMENT OR CHANNEL BANK	REVETMENT TYPE	
		RECT.NOSE	ROUND NOSE
"t" in.	"v"(max.) ft/s	"v"(max.) ft/s	"v"(max.) ft/s
12	5.8	6.0	6.8
15	6.5	6.8	7.7
18	7.1	7.2	8.2
21	7.7	7.7	8.7
24	8.2	7.8	8.8
30	9.2	9.1	10.3

### SAN ANTONIO DISTRICT STANDARD



## FLEXIBLE RIPRAP STONE PROTECTION EMBANKMENTS AND PIERS

FRR (SP)

T:\Engdata\Standards\StoneProtect.dgn		PREPARED BY AND FOR USE OF TxDOT.			
ORIGINAL DRAWING DATE: SEPT. 2007	STATE DISTRICT REGION	FEDERAL AD PROJECT	SHEET		
DN: JHK	09-01-08	SAT 6			
CK: JGD		COUNTY	CONTROL	SECTION	JOB HIGHWAY
DN: MRM					
CK: JHK					

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

RIPRAP DETAILS

GALE ESTATES, L.L.C.

SHEET 16  
OF 24

FIRM REGISTRATION # F48084



SAN ANTONIO, TEXAS www.gallecoseng.com PH: 210.641.0812









1. CASTING NUMBER AND MANUFACTURER'S I.D. ON LID AND RING.
2. LOAD BEARING CAPABILITY OF HS-20 MINIMUM.
3. THE LOAD BEARING SURFACES SHALL BE MACHINE GROUND.
4. THE COMBINED WEIGHT OF THE MANHOLE RING AND COVER MUST BE AT LEAST 260 LBS.

\* FOR CONTRACTOR'S INFORMATION ONLY.  
QUANTITIES VARY WITH "H".  
SEE INLET & MANHOLE SUMMARY SHEETS FOR "H".


1. ALL BARS INTERCEPTING THE RING AND COVER OPENING AND PIPE OPENINGS. SHALL BE FIELD CUT
2. CONCRETE SHALL BE CLASS "A", 3000 PSI IN 28 DAYS.
3. ALL DIMENSIONS RELATING TO REINFORCING STEEL ARE TO CENTER OF BARS.
4. ALL EXPOSED CORNERS SHALL HAVE 3/4" CHAMFER
5. PAYMENT FOR ALL EXCAVATION, BACKFILLING, CONCRETE, REINFORCING STEEL, RING, AND COVER SHALL BE INCLUDED IN THE UNIT COST OF ITEM 403 "STORM SEWER JUNCTION BOXES AND INLETS".

FIRM REGISTRATION # F-003084

## 4-WAY INLET STANDARDS

GALE ESTATES, L.L.C.




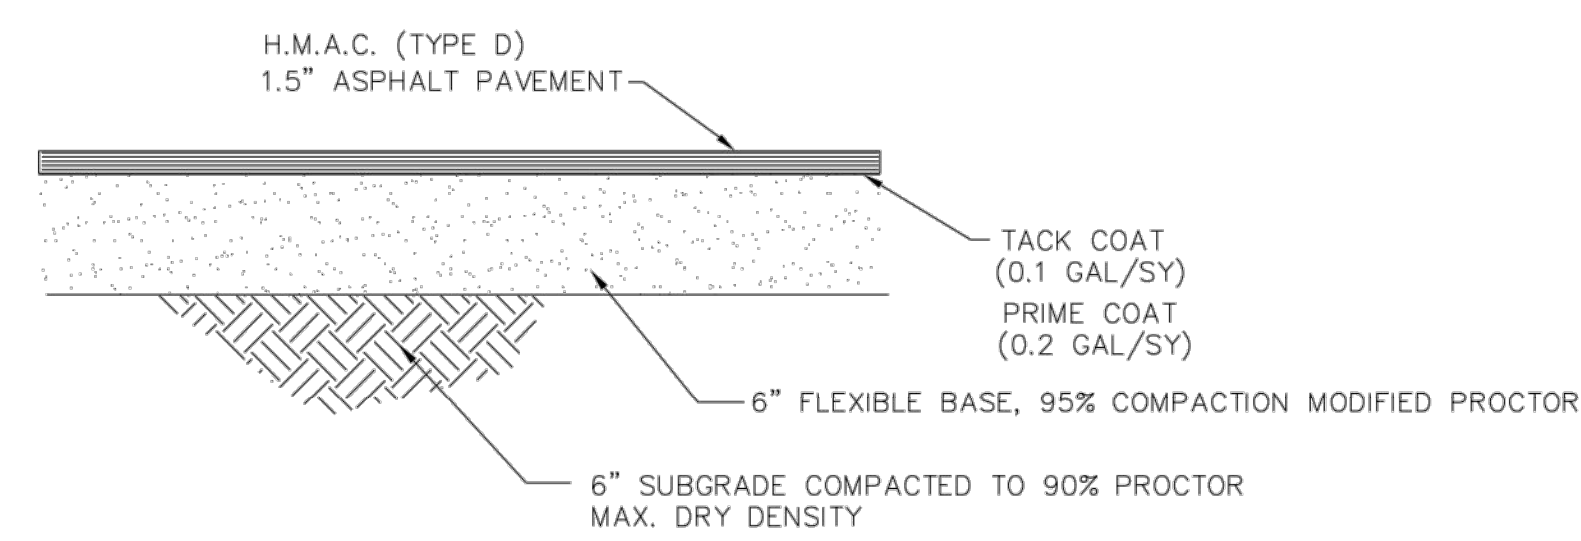

LOCAL STREET	
PAVEMENT MATERIAL	THICKNESS, (IN)
TYPE D, HOT MIX ASPHALTIC CONCRETE, TXDOT ITEM 340	1.5
TACK COAT - TXDOT ITEM 340 - 0.1 GALLONS PER SQUARE YARD	-
PRIME COAT - TXDOT ITEM 310 - 0.2 GALLONS PER SQUARE YARD	-
CRUSHED LIMESTONE BASE, TXDOT ITEM 247, TYPE A, GRADE 1 OR 2	6


\*28 POUNDS LIME PER SQUARE YARD

REGULAR ASPHALT PAVEMENT  
SECTION DETAIL  
N.T.S.

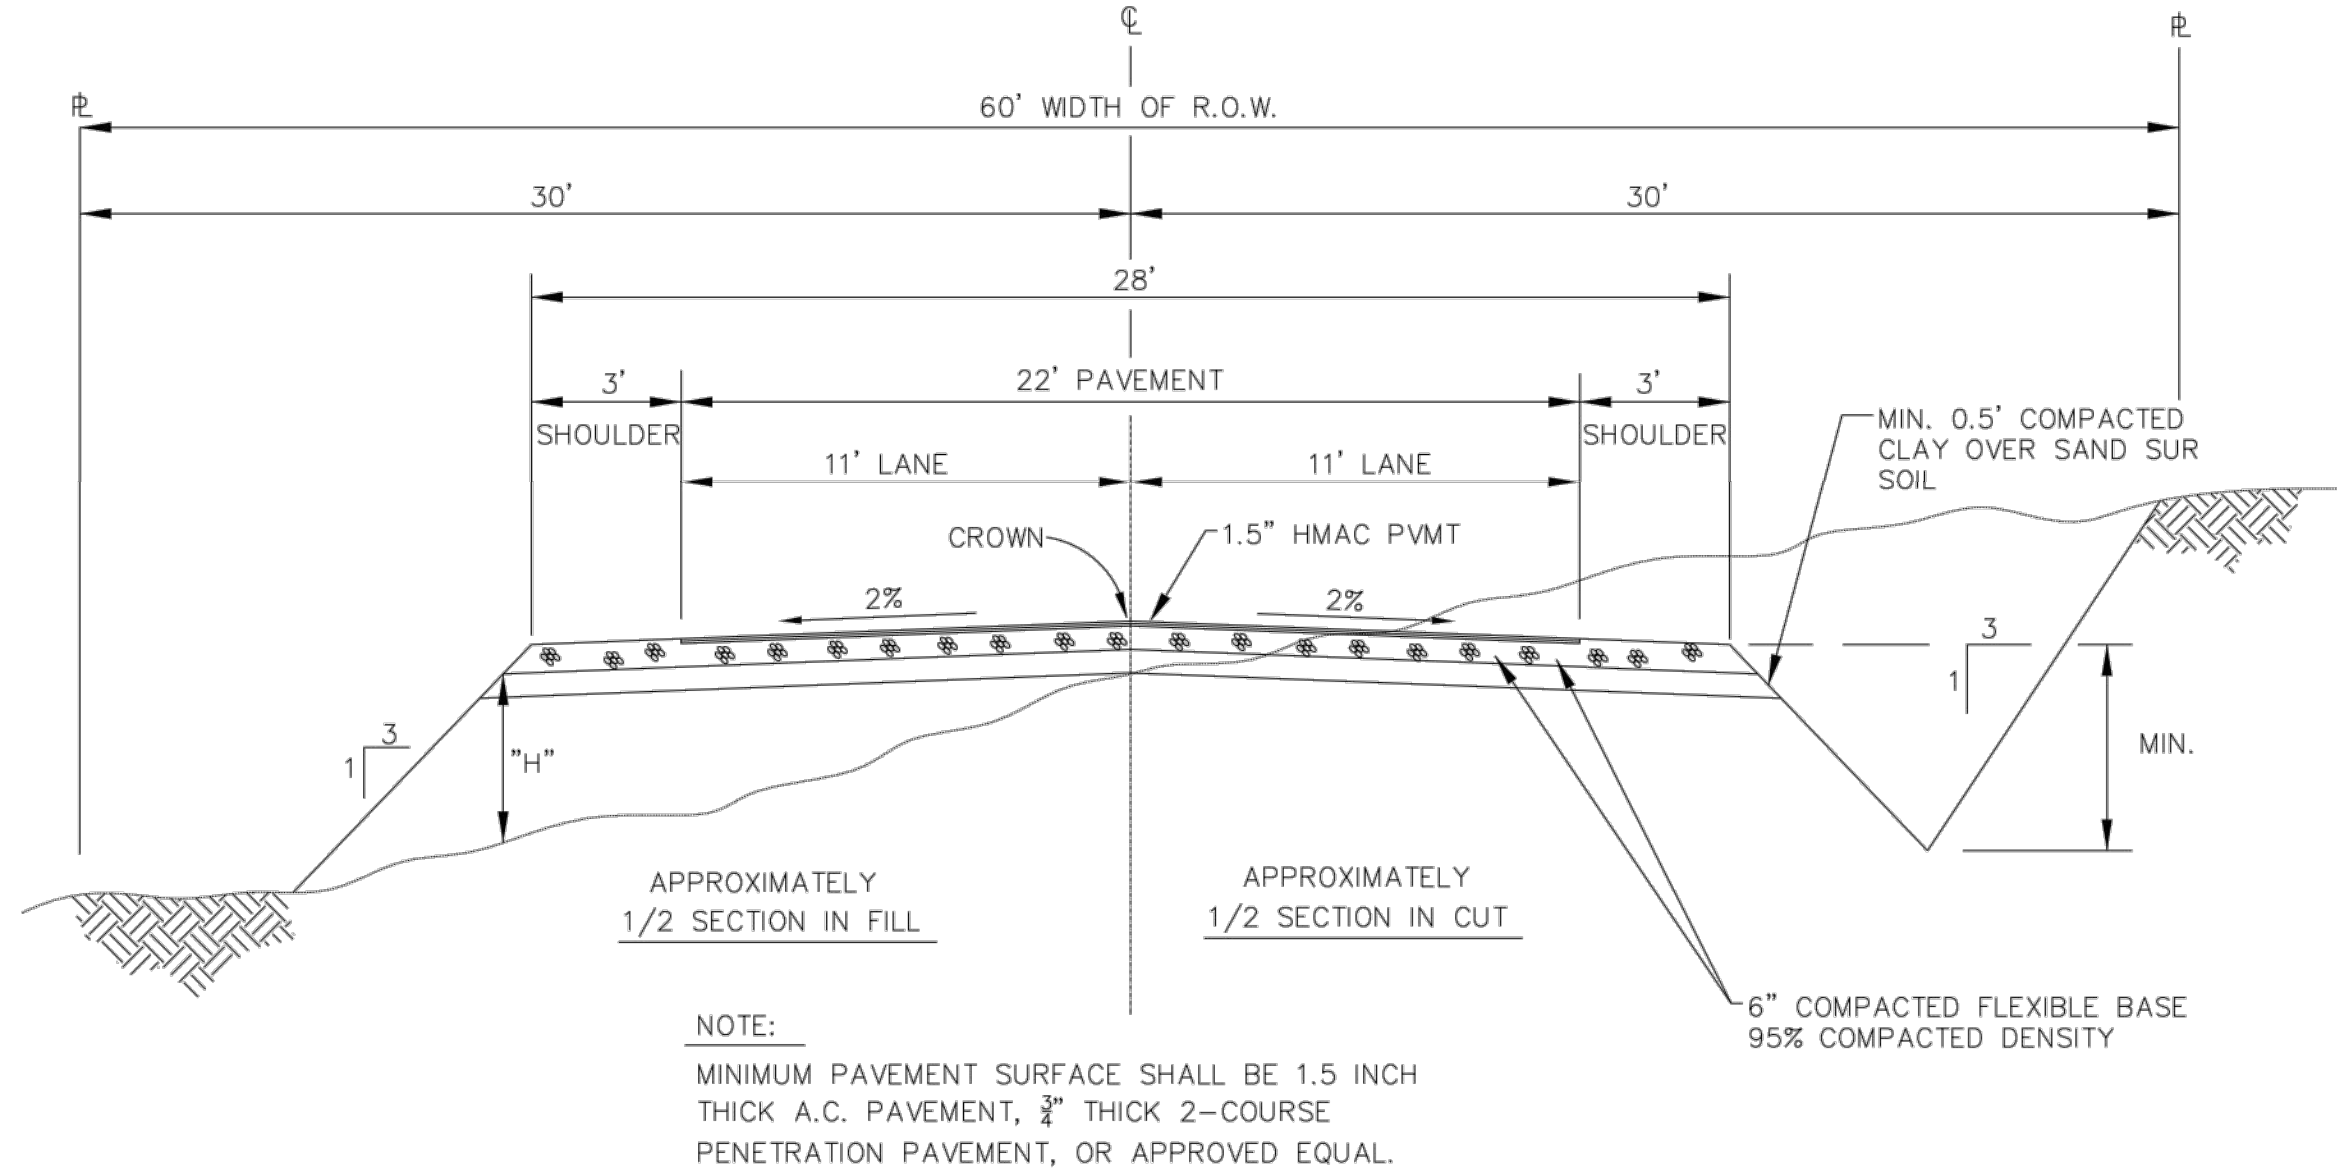


NOTE:  
MINIMUM PAVEMENT SURFACE SHALL BE 1.5 INCH THICK A.C. PAVEMENT, 3/4" THICK 2-COURSE PENETRATION PAVEMENT, OR APPROVED EQUAL.

TYPICAL STREET SECTION  
N.T.S.

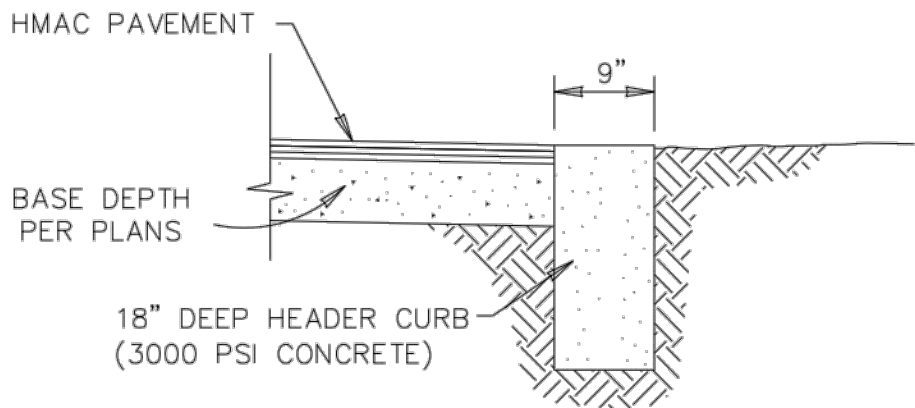


\* PROVIDE HEADER CURB PER PLANS.


HEADER CURB  
N.T.S.

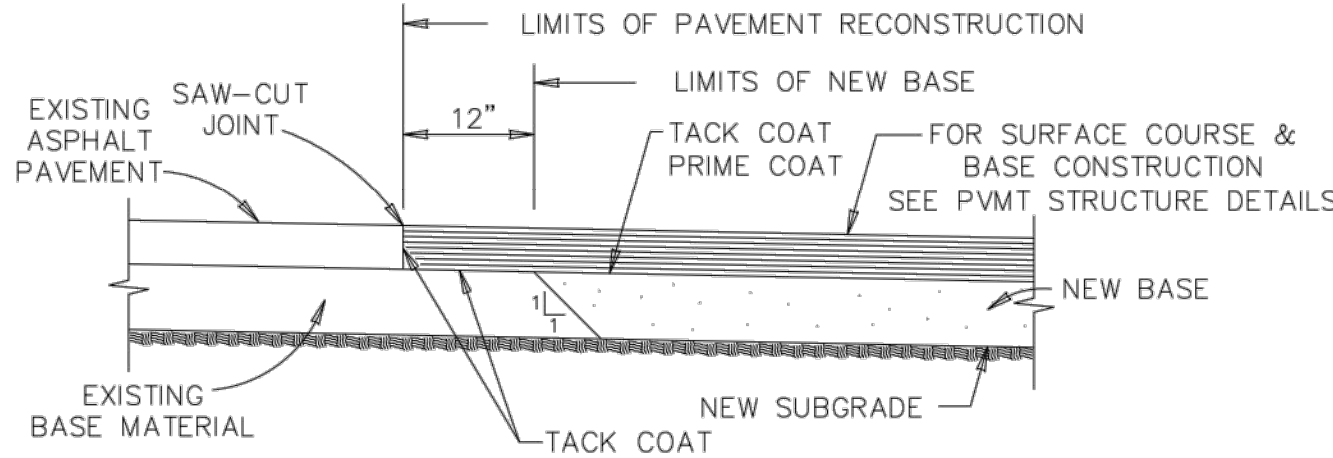

PAVEMENT JUNCTION DETAILS  
N.T.S.

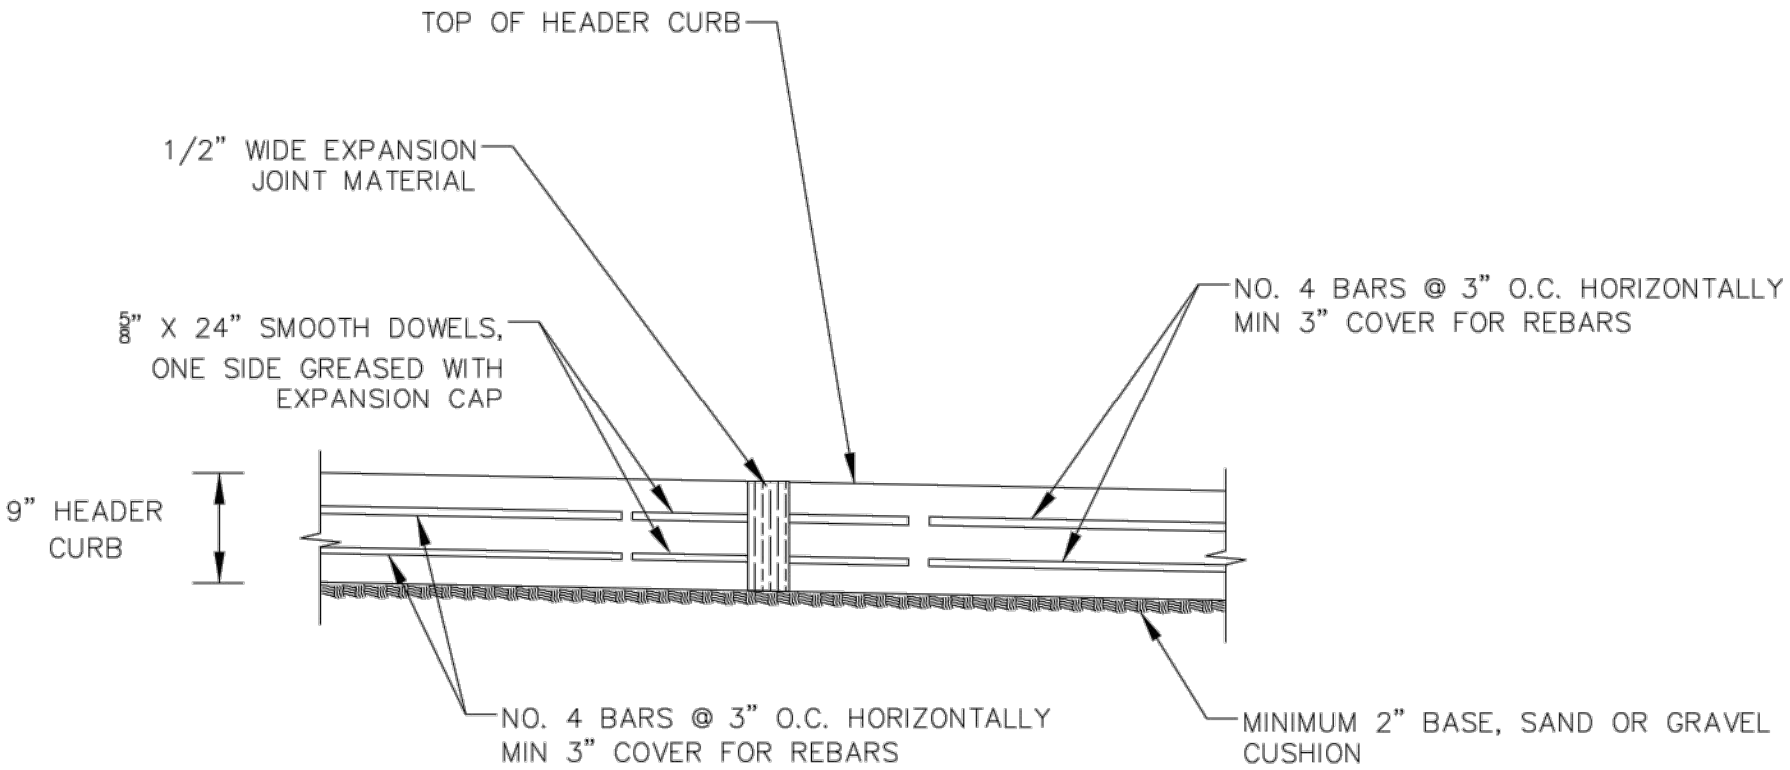

HEADER CURB EXPANSION JOINT DETAILS  
N.T.S.

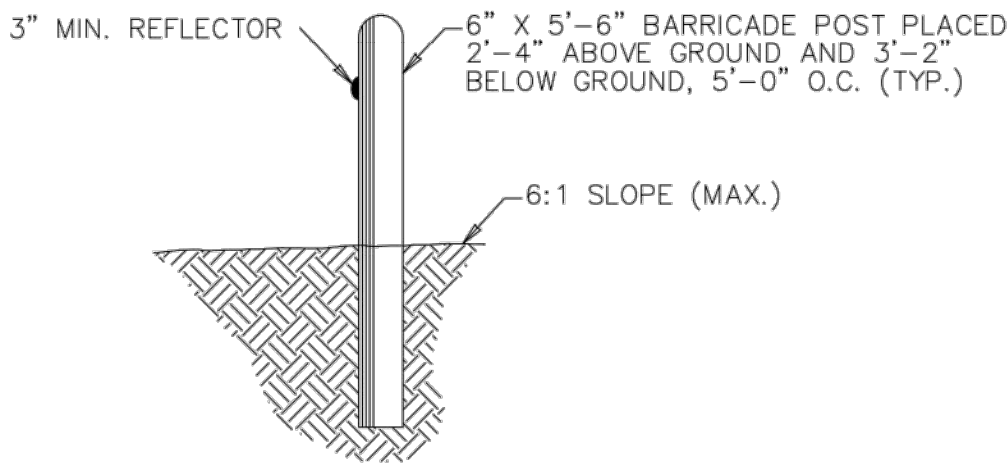

TIMBER POST DETAIL  
N.T.S.

GENERAL NOTES :  
1) ALL CONSTRUCTION SHALL CONFORM TO THE COMAL COUNTY SUBDIVISION REGULATIONS.  
2) FILL TO BE PLACED IN LIFTS, PER COMAL COUNTY SUBDIVISION REGULATIONS.

S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEETS\18-15-GRD-GEN DETAILS.dwg

REVISIONS	
NO.	DESCRIPTION
DATE	BY
PROJ. #	DATE
DES. BY	CHKD. BY
DWN. BY	S.G.
03/06/23	U5-SER
S.G.	R.M.G.

FIRM REGISTRATION # F40804

**GALLECOS ENGINEERING, INC.**

SAN ANTONIO, TEXAS www.gallecoseng.com PH: 210.641.0812

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLECOS, P.E. 86916 APRIL 6, 2023 ALTERATION OF A SEALED DOCUMENT WITHOUT THE SIGNATURE OF THE REGISTERED PROFESSIONAL ENGINEER IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT

**RICHARD M. GALLECOS**  
P.E. 86916  
REGISTERED PROFESSIONAL ENGINEER  
STATE OF TEXAS



SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

**GENERAL DETAILS**

GALE ESTATES, L.L.C.



S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEETS\S19-U5-TRAFFIC SIGNAGE-PLAN.dwg

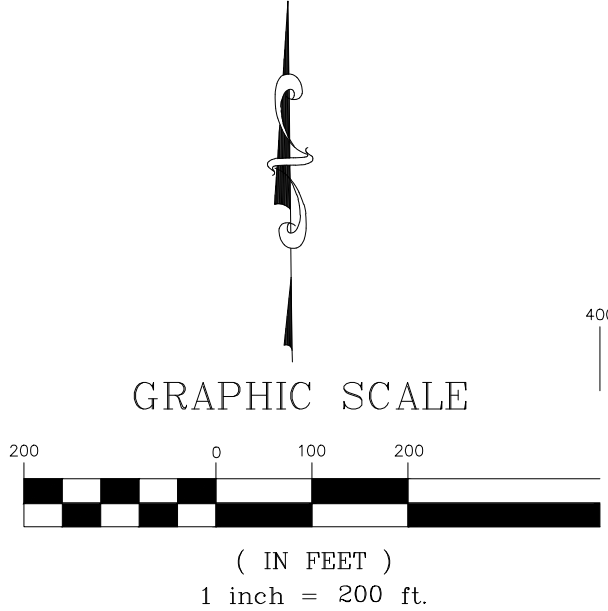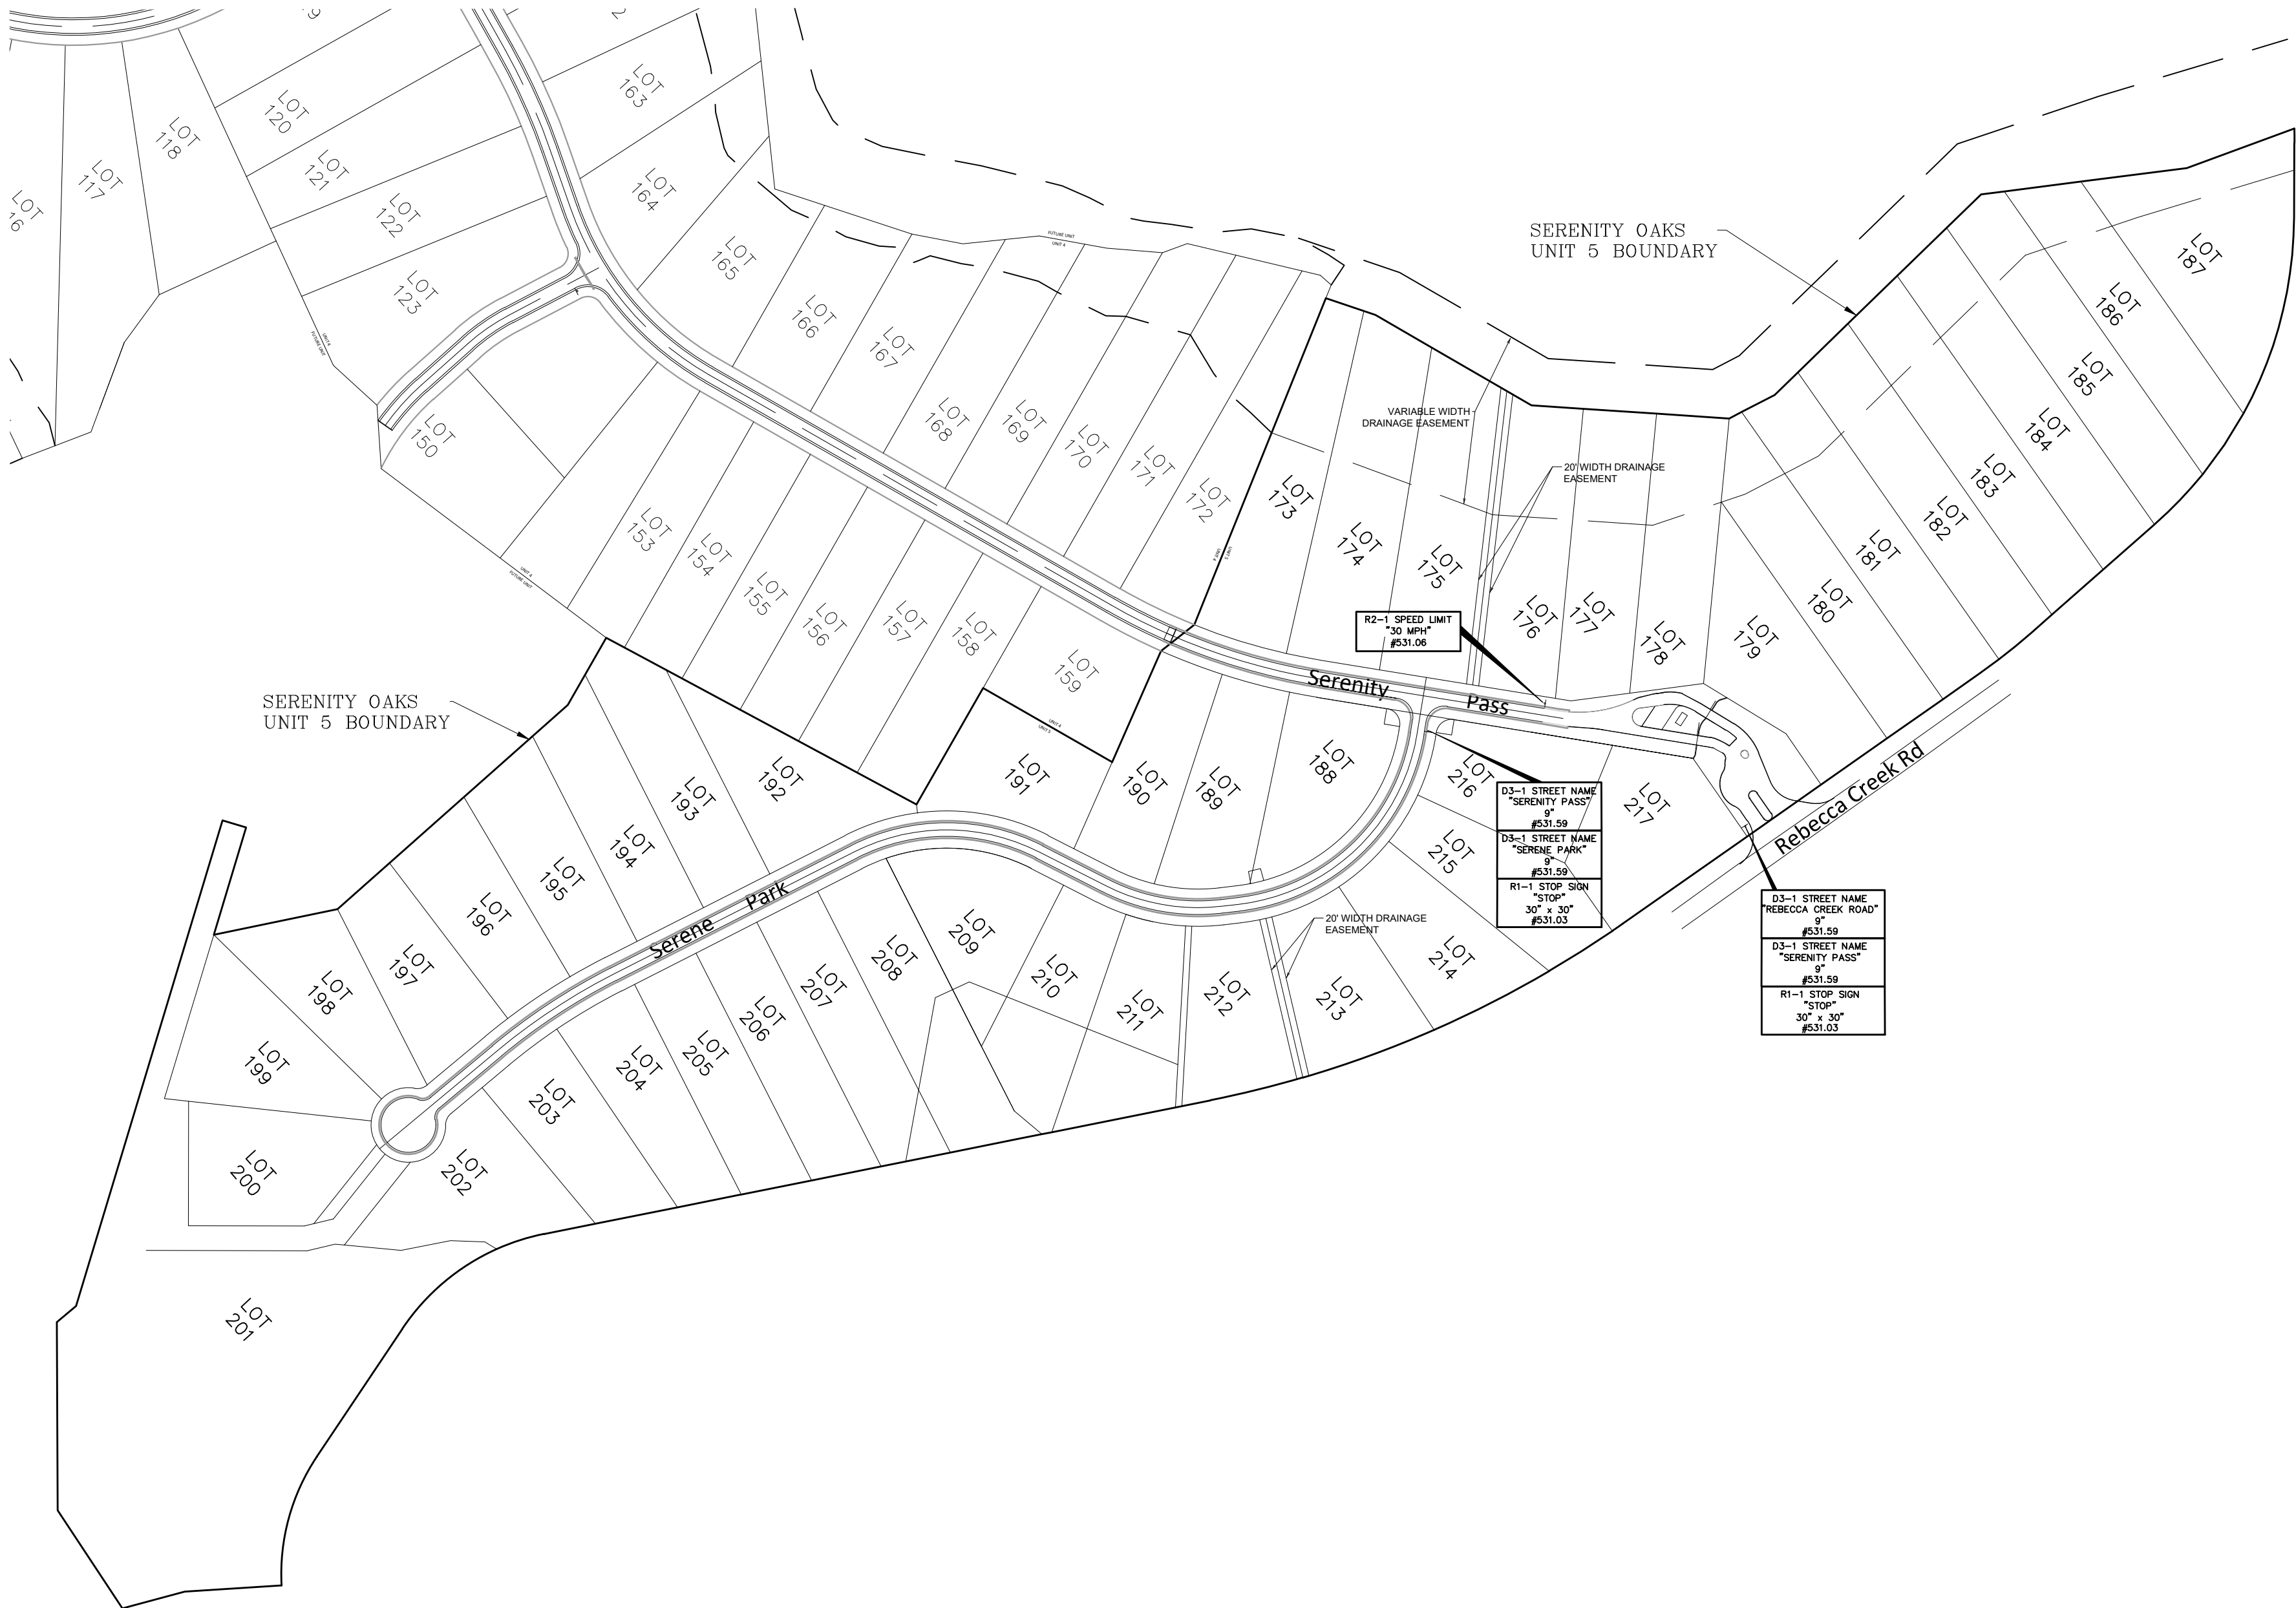

NOTES

- ALL TRAFFIC SIGNS SHALL BE MANUFACTURED AND INSTALLED ACCORDING TO THE TEXAS MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (T.M.U.T.C.D.).
- INSTALL SIGNS SUCH THAT THEIR VIEW IS NOT BLOCKED BY LOW HANGING VEGETATION, UTILITY POLES, OTHER TRAFFIC SIGNS, ETC.
- ALL PAVEMENT MARKINGS SHALL COMPLY WITH THE T.M.U.T.C.D.
- ALL PERMANENT REGULATORY AND WARNING SIGNS ARE TO BE PROVIDED AND INSTALLED BY THE DEVELOPER TO COUNTY SPECIFICATIONS. COMAL COUNTY WILL INSTALL STREET NAME PLATES.

SIGNING AND PAVEMENT MARKING PLAN NOTES

- COMAL COUNTY WILL INSTALL COUNTY ROAD SIGNS AND INVOICE THE OWNER. THE CONTRACTOR IS TO INSTALL ALL TxDOT SIGNS AND PAVEMENT MARKINGS, ALL ROAD SIGNS AND PAVEMENT MARKINGS SHALL BE INSTALLED IN ACCORDANCE WITH THE APPROVED ENGINEERING PLANS, THE COUNTY WILL INSPECT ALL SIGNS AT FINAL INSPECTION.
- THE CONTRACTOR SHALL INSTALL ALL PAVEMENT MARKINGS IN ACCORDANCE WITH APPROVED ENGINEERING PLANS. THE CONTRACTOR SHALL NOTIFY THE COUNTY AT LEAST 24 HOURS PRIOR TO THE INSTALLATION OF ALL SEALER AND PAVEMENT MARKINGS. THE COUNTY WILL INSPECT ALL MARKINGS AT FINAL APPLICATION.

SIGN QUANTITIES	
DESCRIPTION	QUANTITY
(R1-1) STOP	EACH 2
(R2-1) SPEED LIMIT	EACH 1
(D3-1) 9" STREET NAME	EACH 4

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

TRAFFIC SIGNAGE PLAN  
GALE ESTATES, L.L.C.

SHEET 19  
OF 24

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLECOS, P.E. 88916 APRIL 8, 2023 ALTERATION OF A SEALED DOCUMENT WITHOUT THE SIGNATURE OF THE DESIGNER OR ENGINEER IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT

FIRM REGISTRATION # F-00004

GALLECOS ENGINEERING, INC.  
 SAN ANTONIO, TEXAS www.gallegoseng.com PH: 210.641.0812

REVISIONS					
NO.	DATE	DESCRIPTION	BY		
PROJ. #:	DATE:	DES. BY:	DWN. BY:	CHECK. BY:	R.M.G.
U5-SER	03/06/23	S.G.	S.G.		



(Descriptive Codes correspond to project estimate and quantities sheets)

Post Type \_\_\_\_\_

FRP = Fiberglass Reinforced Plastic Pipe (see SMD (FRP))  
TWT = Thin-Walled Tubing (see SMD (TWT))  
10BWG = 10 BWG Tubing (see SMD (SLIP-1) to (SLIP-3))  
S80 = Schedule 80 Pipe (see SMD (SLIP-1) to (SLIP-3))

Number of Posts (1 or 2)

Anchor Type

- UA = Universal Anchor - Concrete (see SMD (FRP) and (TWT))
- UB = Universal Anchor - Bolted down (see SMD (FRP) and (TWT))
- WS = Wedge Anchor Steel - (see SMD (TWT))
- WP = Wedge Anchor Plastic (see SMD (TWT))
- SA = Slipbase - Concrete (see SMD (SLIP-1) to (SLIP-3))
- SB = Slipbase - Bolted Down (see SMD (SLIP-1) to (SLIP-3))

### Sign Mounting Designation

P = Prefab. "Plain" (see SMD (SLIP-1) to (SLIP-3), (TWT), (FRP))  
 T = Prefab. "T" (see SMD (SLIP-1) to (SLIP-3), (TWT))  
 U = Prefab. "U" (see SMD (SLIP-1) to (SLIP-3))  
 IF REQUIRED  
 1EXT or 2EXT = Number of Extensions (see SMD (SLIP-1) to (SLIP-3), (TWT))  
 BM = Extruded Wind Beam (see SMD (SLIP-1) to (SLIP-3))  
 WC = 1.12 #/ft Wing Channel (see SMD (SLIP-1) to (SLIP-3))  
 EXAL = Extruded Aluminum Sign Panels (see SMD (SLIP-3))

Diagram illustrating the non-breakaway portion of the support structure (i.e., stub) for a vehicle seat back. The diagram shows a side view of the seat back with a label "TX-207" on the lower part of the backrest. A horizontal line indicates the "Ground Surface". A dimension of "4\" max." is shown for the height of the non-breakaway portion above the ground surface. A dimension of "60\"" is shown for the length of the non-breakaway portion along the ground surface.

To avoid vehicle undercarriage snagging, any substantial remains of a breakaway support, when it is broken away, should not project more than 4 inches above a 60-inch chord (i.e., typical space between wheel paths).

The diagram illustrates the placement of a 'HIGHWAY INTERSECTION AHEAD' sign on a paved shoulder. It is divided into two sections based on shoulder width:


- LESS THAN 6 FT. WIDE:** The sign is placed at a distance of at least 12 ft from the travel lane edge. The sign itself has a width of 7.5 ft max and 7.0 ft min. The shoulder width is indicated as 0 to 6 ft.
- GREATER THAN 6 FT. WIDE:** The sign is placed at a distance of at least 6 ft from the travel lane edge. The sign width remains 7.5 ft max and 7.0 ft min.

The diagram illustrates a T-intersection with a 'Travel Lane' and a 'Paved Shoulder'. A callout box shows a double-headed arrow symbol. Dimensions are provided for the lane width and the offset from the shoulder to the centerline of the intersecting road.

- Travel Lane width: 12 ft min
- Offset from shoulder to centerline: 6 ft min
- Offset from shoulder to edge of intersecting road: 7.5 ft max, 7.0 ft min

When this sign is needed at the end of a two-lane, two way roadway, the right edge of the sign should be in line with the centerline of the roadway. Place as close to ROW as practical.

No more than 2 sign posts should be located within a 7 ft. circle.

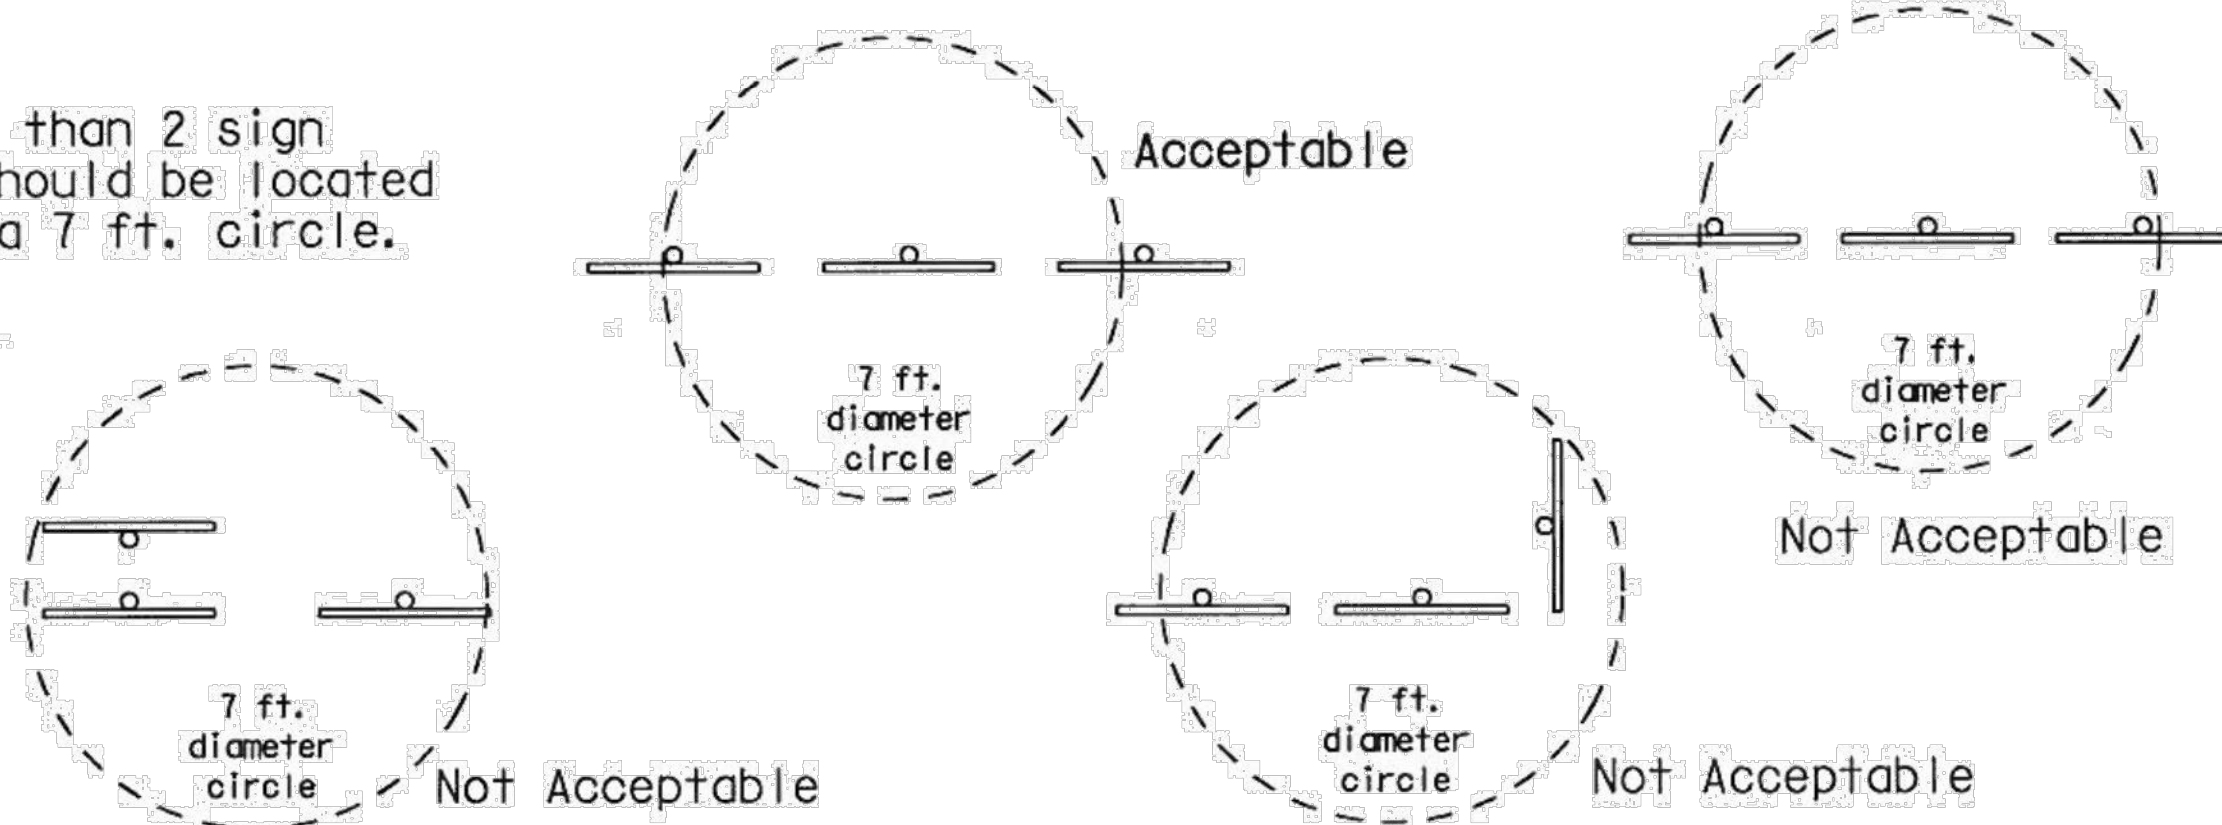

**Single Signs**

U-bolt

Sign Post

Sign Clamp

Nut, lock washer

Nylon washer, flat washer, lock washer, nut

Sign Panel

**Back-to-Back Signs**

Nylon washer, flat washer, lock washer, nut

Sign Panel

Nut, lock washer

Sign Post

Sign Clamp

Clamp Bolt

Sign Panel

Nylon washer, flat washer, lock washer, nut

Sign Bolt

Bolts used to mount sign panels to the clamp are 5/16-18 UNC galvanized square head with nut, nylon washer, flat washer and lock washer. The bolt length is 1 inch for aluminum.

When two sign clamps are used to mount signs back-to-back, use a 5/16-18 UNC galvanized hex head per ASTM A307 with nut and helical-spring lock washer. The approximate bolt lengths for various post sizes and sign clamp types are given in the table at right. The bolt length may need to be adjusted depending upon field conditions.

Sign clamps may be either the specific size clamp or the universal clamp.

Pipe Diameter	Approximate Bolt Length	
	Specific Clamp	Universal Clamp
2" nominal	3"	3 or 3 1/2"
2 1/2" nominal	3 or 3 1/2"	3 1/2 or 4"
3" nominal	3 1/2 or 4"	4 1/2"

7.5 ft max  
7.0 ft min \*

Travel Lane

Paved Shoulder

14 FT 4 IN

LOW CLEARANCE

35 M.P.H.

EAST FARM ROAD 3713

EAST FARM ROAD 3713

316

When a supplemental plaque or secondary sign is used, the 7 ft sign height is measured to the bottom of the supplemental plaque or secondary sign.

A diagram of a diamond-shaped sign with the text "HIGHWAY INTERSECTION AHEAD". The sign is mounted on a post. The dimensions are specified as follows: the width of the sign is 2 ft min on both sides; the height of the sign is 7.5 ft max and 7.0 ft min; and the sign is positioned 2 ft min from the face of the curb on both sides.

The diagram shows a side view of a highway with a 'Travel Lane' and a 'Paved Shoulder'. A diamond-shaped sign reading 'HIGHWAY INTERSECTION AHEAD' is positioned on the shoulder. A horizontal arrow labeled 'Maximum possible' indicates the distance from the sign face to the intersection. Vertical dimension lines show the sign's height as '7.5 ft max' and '7.0 ft min \*'. A dashed line indicates the sign's offset from the shoulder edge, labeled '\*\*\*'.

Right-of-way restrictions may be created by rocks, water, vegetation, forest, buildings, a narrow island, or other factors.

In situations where a lateral restriction prevents the minimum horizontal clearance from the edge of the travel lane, signs should be placed as far from the travel lane as practical.

\*\*\* Post may be shorter if protected by guardrail or if Engineer determines the post could not be hit due to extreme slope.

\* Signs shall be mounted using the following condition that results in the greatest sign elevation:

- (1) a minimum of 7 to a maximum of 7.5 feet above the edge of the travel lane or
- (2) a minimum of 7 to a maximum of 7.5 feet above the grade at the base of the support when sign is installed on the backslope.

The maximum values may be increased when directed by the Engineer.

See the Traffic Operations Division website for detailed drawings of sign clamps, Triangular Slipbase System components and Wedge Anchor System components.

The website address is:  
<http://www.txdot.gov/publications/traffic.htm>




SIGN MOUNTING DETAILS  
SMALL ROADSIDE SIGNS  
GENERAL NOTES & DETAILS

SMD (GEN)-08

© TxDOT July 2002		M: TxDOT		C: TxDOT		M: TxDOT		C: TxDOT	
9-08	REVISIONS	CONTRACT	SECTION	JULY		HIGHWAY			
		DISTRICT	COUNTY				SHEET NO.		



## TRIANGULAR SLIPBASE INSTALLATION GENERAL REQUIREMENTS

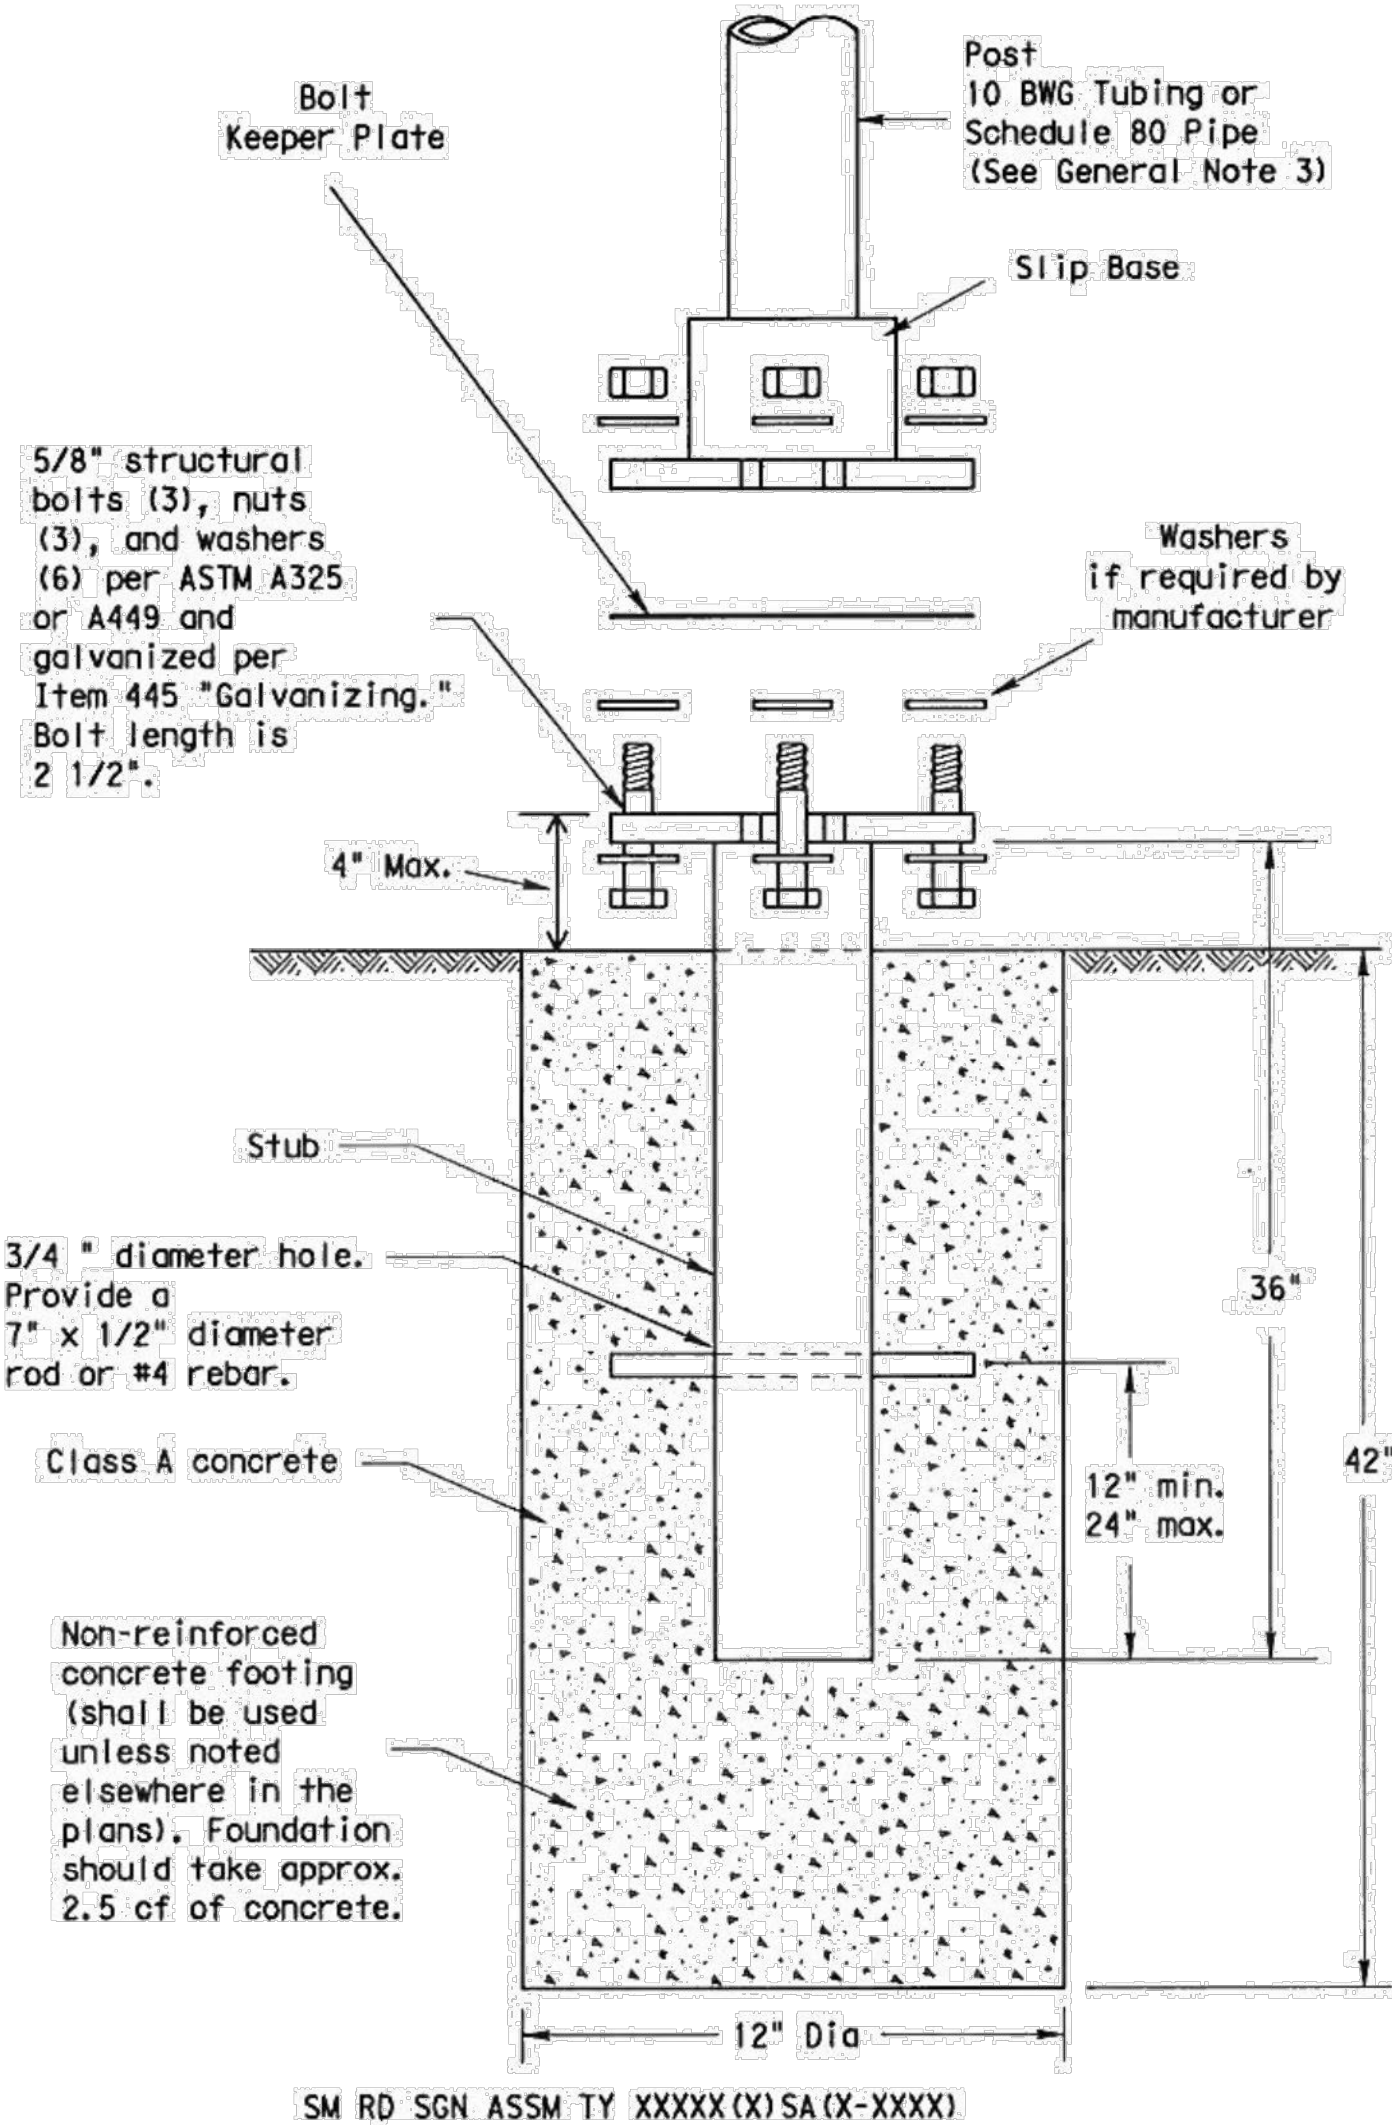

**NOTE**

There are various devices approved for the Triangular Slipbase System. Please reference the Material Producer List for approved slip base systems. [http://www.txdot.gov/business/producer\\_list.htm](http://www.txdot.gov/business/producer_list.htm) The devices shall be installed per manufacturers' recommendations. Installation procedures shall be provided to the Engineer by Contractor.

GENERAL NOTES:

1. Slip base shall be permanently marked to indicate manufacturer. Method, design, and location of marking are subject to approval of the TxDOT Traffic Standards Engineer.
2. Material used as post with this system shall conform to the following specifications:
  - 10 BWG Tubing (2.875" outside diameter)
    - 0.134" nominal wall thickness
    - Seamless or electric-resistance welded steel tubing or pipe
    - Steel shall be HSLAS Gr 55 per ASTM A1011 or ASTM A1008
    - Other steels may be used if they meet the following:
      - 55,000 PSI minimum yield strength
      - 70,000 PSI minimum tensile strength
      - 20% minimum elongation in 2"
    - Wall thickness (uncoated) shall be within the range of 0.122" to 0.138"
    - Outside diameter (uncoated) shall be within the range of 2.867" to 2.883"
    - Galvanization per ASTM A123 or ASTM A653 G210. For precoated steel tubing (ASTM A653), recoat tube outside diameter weld seam by metallizing with zinc wire per ASTM B833.
  - Schedule 80 Pipe (2.875" outside diameter)
    - 0.276" nominal wall thickness
    - Steel tubing per ASTM A500 Gr C
    - Other seamless or electric-resistance welded steel tubing or pipe with equivalent outside diameter and wall thickness may be used if they meet the following:
      - 46,000 PSI minimum yield strength
      - 62,000 PSI minimum tensile strength
      - 21% minimum elongation in 2"
    - Wall thickness (uncoated) shall be within the range of 0.248" to 0.304"
    - Outside diameter (uncoated) shall be within the range of 2.855" to 2.895"
    - Galvanization per ASTM A123
3. See the Traffic Operations Division website for detailed drawings of sign clamps and Texas Universal Triangular Slipbase System components. The website address is:  
<http://www.txdot.gov/publications/traffic.htm>
4. Sign supports shall not be spliced except where shown. Sign support posts shall not be spliced.

## ASSEMBLY PROCEDURE


## Foundation

1. Prepare 12-inch diameter by 42-inch deep hole. If solid rock is encountered, the depth of the foundation may be reduced such that it is embedded a minimum of 18 inches into the solid rock.
2. The Engineer may permit batches of concrete less than 2 cubic yards to be mixed with a portable, motor-driven concrete mixer. For small placements less than 0.5 cubic yards, hand mixing in a suitable container may be allowed by Engineer. Concrete shall be Class A.
3. Push the pipe end of the slip base stub into the center of the concrete. Rotate the stub back and forth while pushing it down into the concrete to assure good contact between the concrete and stub. Continue to work the stub into the concrete until it is between 2 to 4 inches above the ground.
4. Plumb the stub. Allow a minimum of 4 days to set, unless otherwise directed by the Engineer.
5. The triangular slipbase system is multidirectional and is designed to release when struck from any direction.


## Support t

1. Cut support so that the bottom of the sign will be 7 to 7.5 feet above the edge of the travelway (i.e., edge of the closest lane) when slip plate is below the edge of pavement or 7 to 7.5 feet above slip plate when the slip plate is above the edge of the travelway. The cut shall be plumb and straight.
2. Attach sign to support using connections shown. When multiple signs are installed on the same support, ensure the minimum clearance between each sign is maintained. See SMD (SLIP-2) for clearances based on sign types.

## CONCRETE ANCHOR

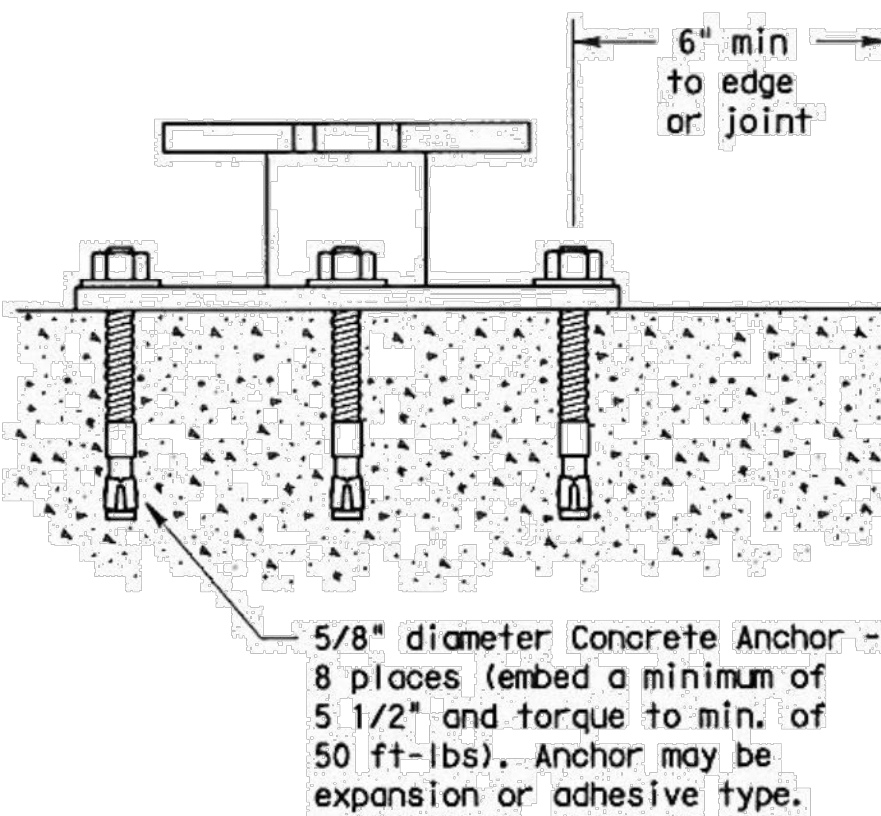

Concrete anchor consists of 5/8" diameter stud bolt with UNC series bolt threads on the upper end. Heavy hex nut per ASTM A563, and hardened washer per ASTM F436. The stud bolt shall have a minimum yield and ultimate tensile strength of 50 and 75 KSI, respectively. Nuts, bolts and washers shall be galvanized per Item 445, "Galvanizing." Adhesive type anchors shall have stud bolts installed with Type III epoxy per DMS-6100, "Epoxyes and Adhesives." Adhesive anchors may be loaded after adequate epoxy cure time per the manufacturer's recommendations. Top of bolt shall extend at least flush with top of the nut when installed. The anchor, when installed in 4000 psi normal-weight concrete with a 5 1/2" minimum embedment, shall have a minimum allowable tension and shear of 3900 and 3100 psi, respectively.

 *Texas Department of Transportation*  
*Traffic Operations Division*

SIGN MOUNTING DETAILS  
SMALL ROADSIDE SIGNS  
TRIANGULAR SLIPBASE SYSTEM

SMD (SLIP-1) -08

© TxDOT July 2002		Pl: TXDOT	Ck: TXDOT	Pl: TXDOT	Ck: TXDOT
9-08	REVISIONS	CUAT	SECT	JUG	HIGHWAY
		DIST		COUNTY	SHEET NO.



SAN ANTONIO, TEXAS [www.gallegoseng.com](http://www.gallegoseng.com) PH: 210.641.0812







S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEETS\523-05-DET POND.dwg

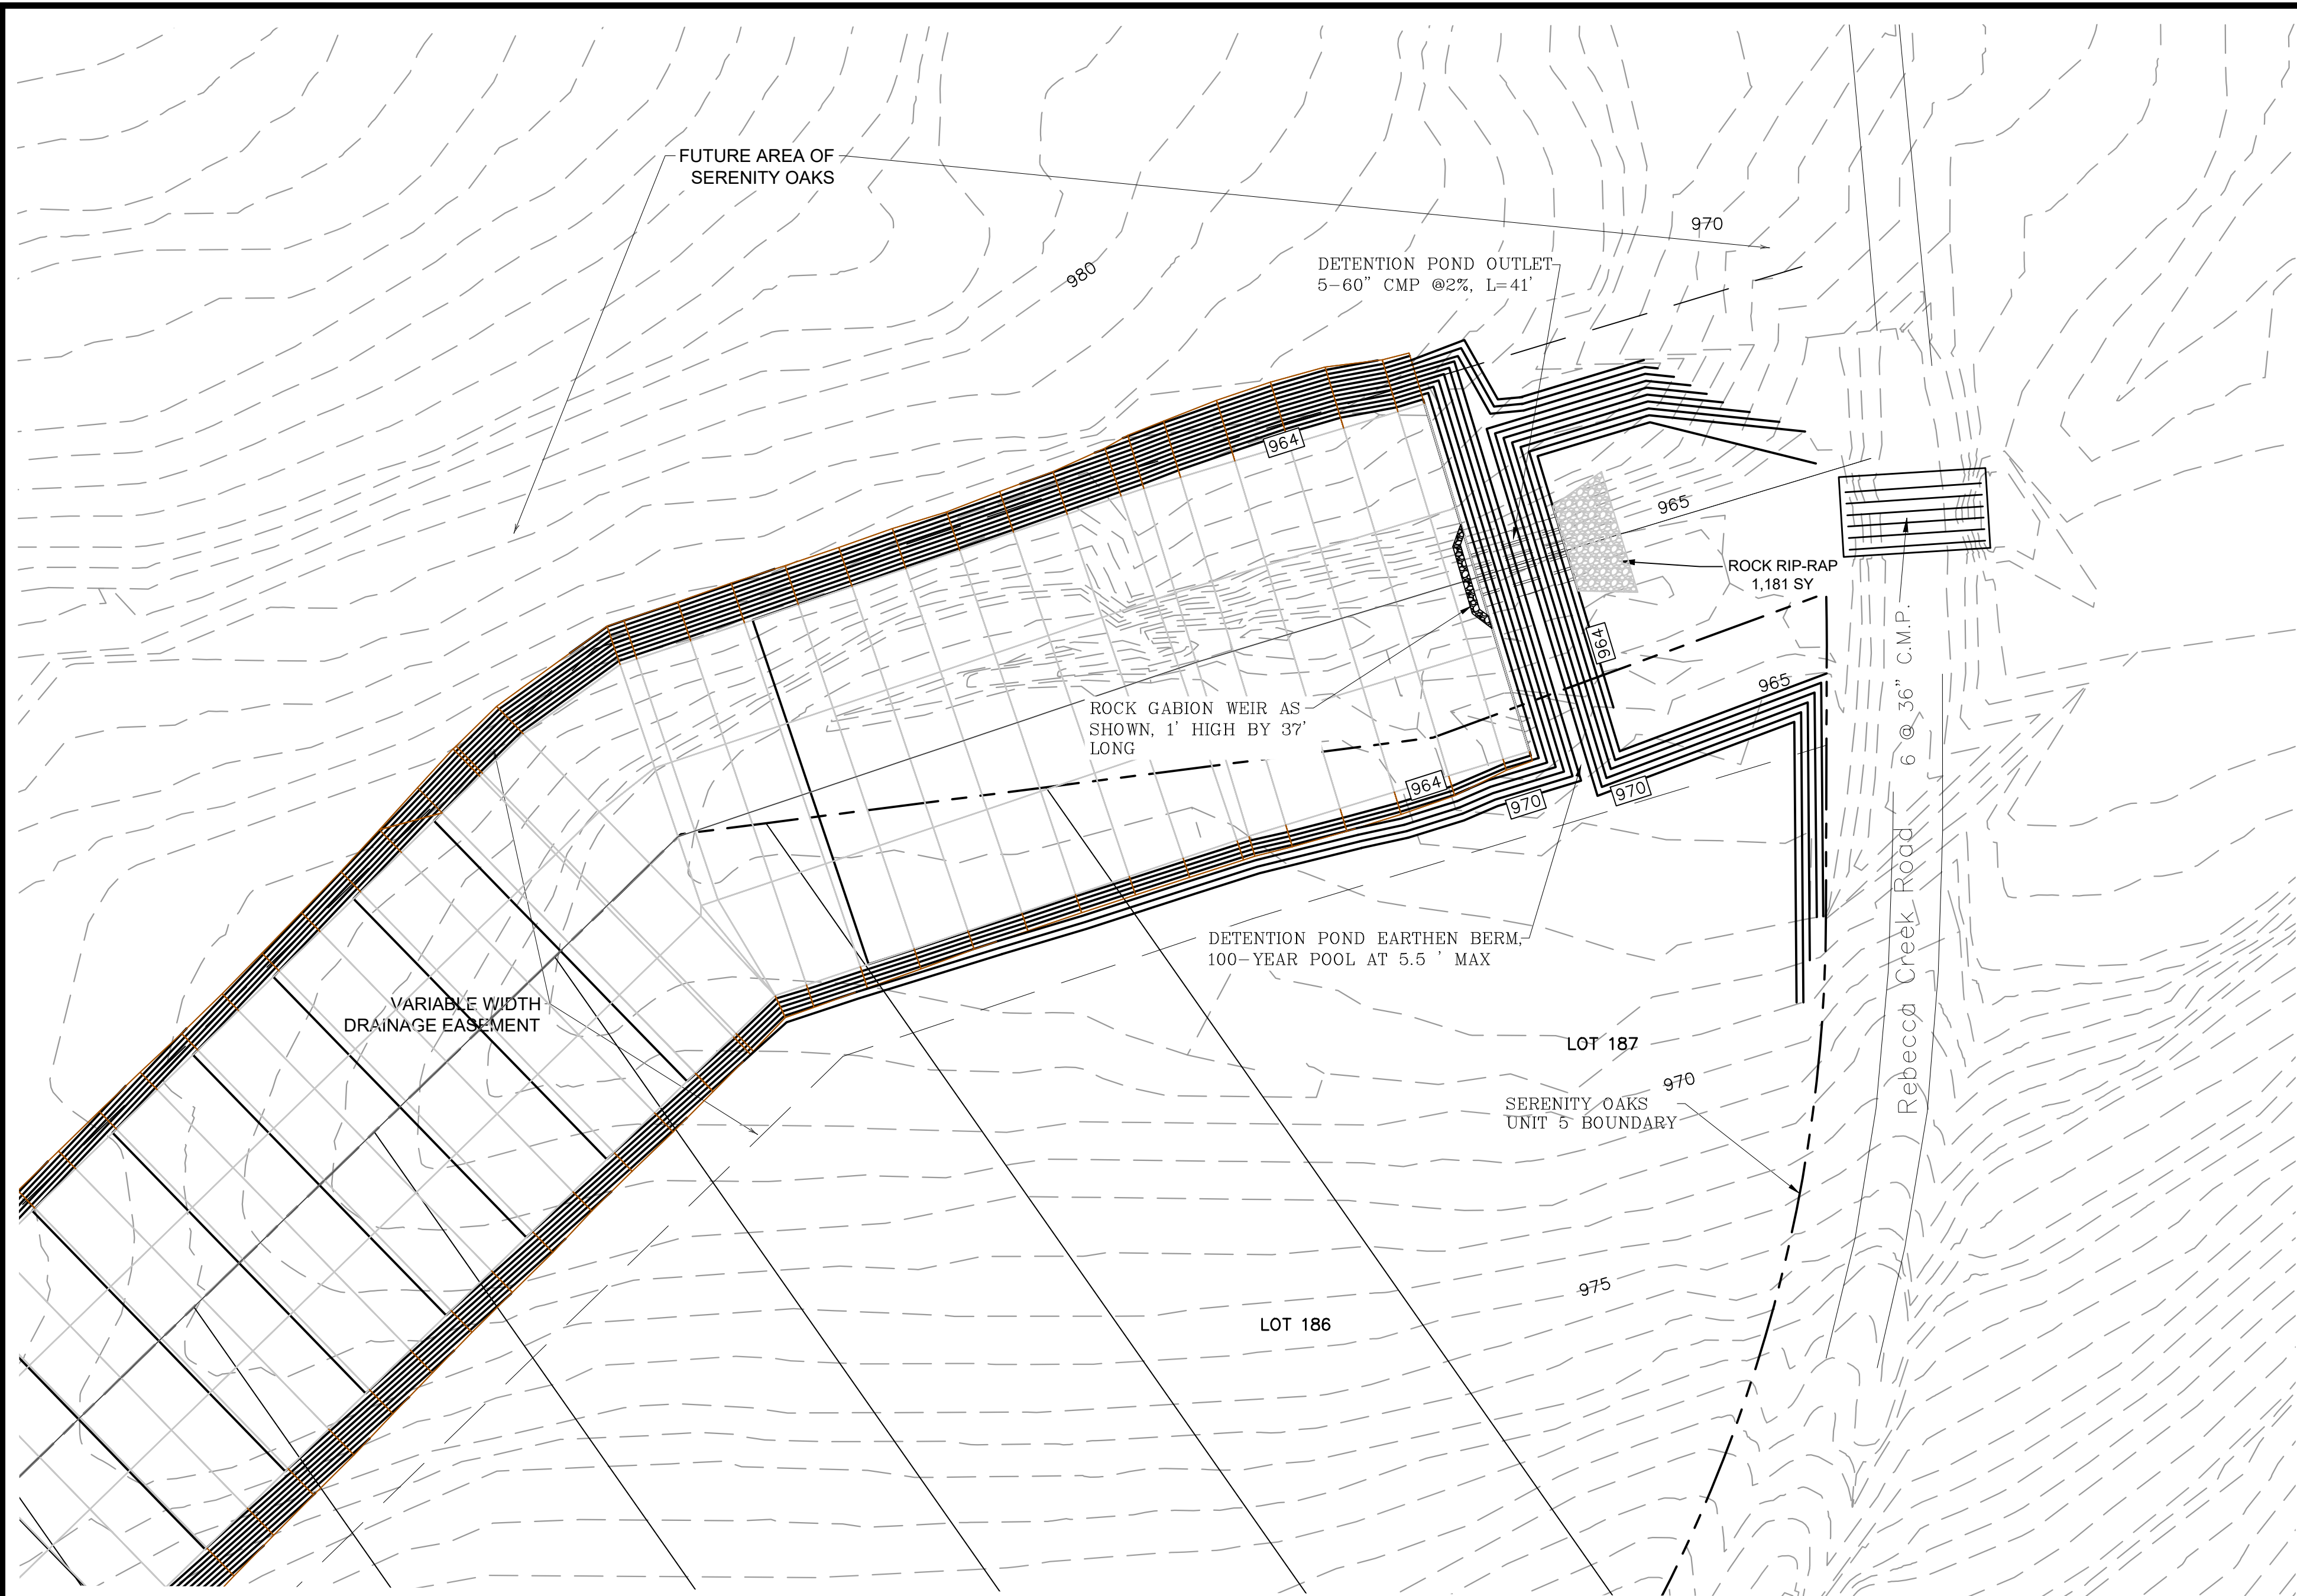

## 10.2 RIPRAP APRON

The most commonly used device for outlet protection, primarily for culverts 1500 mm (60 in) or smaller, is a riprap apron. An example schematic of an apron taken from the Federal Lands Division of the Federal Highway Administration is shown in Figure 10.4.


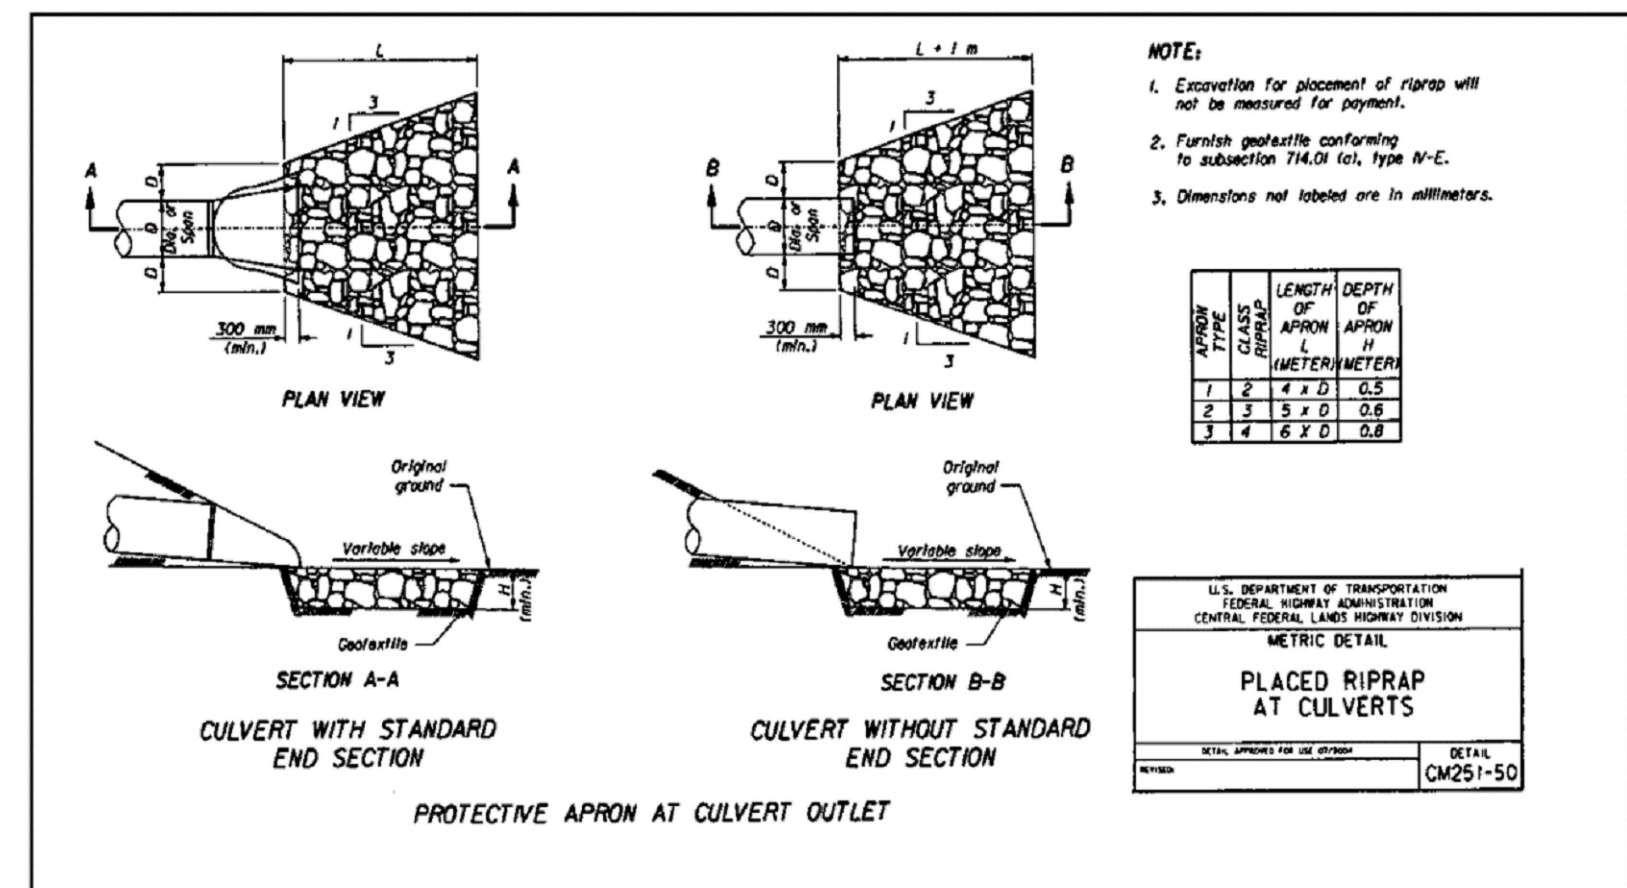


Figure 10.4. Placed Riprap at Culverts (Central Federal Lands Highway Division)  
TYPICAL CULVERT ENERGY DISSIPATION DETAIL  
FOR CONSTRUCTION DIMENSIONS

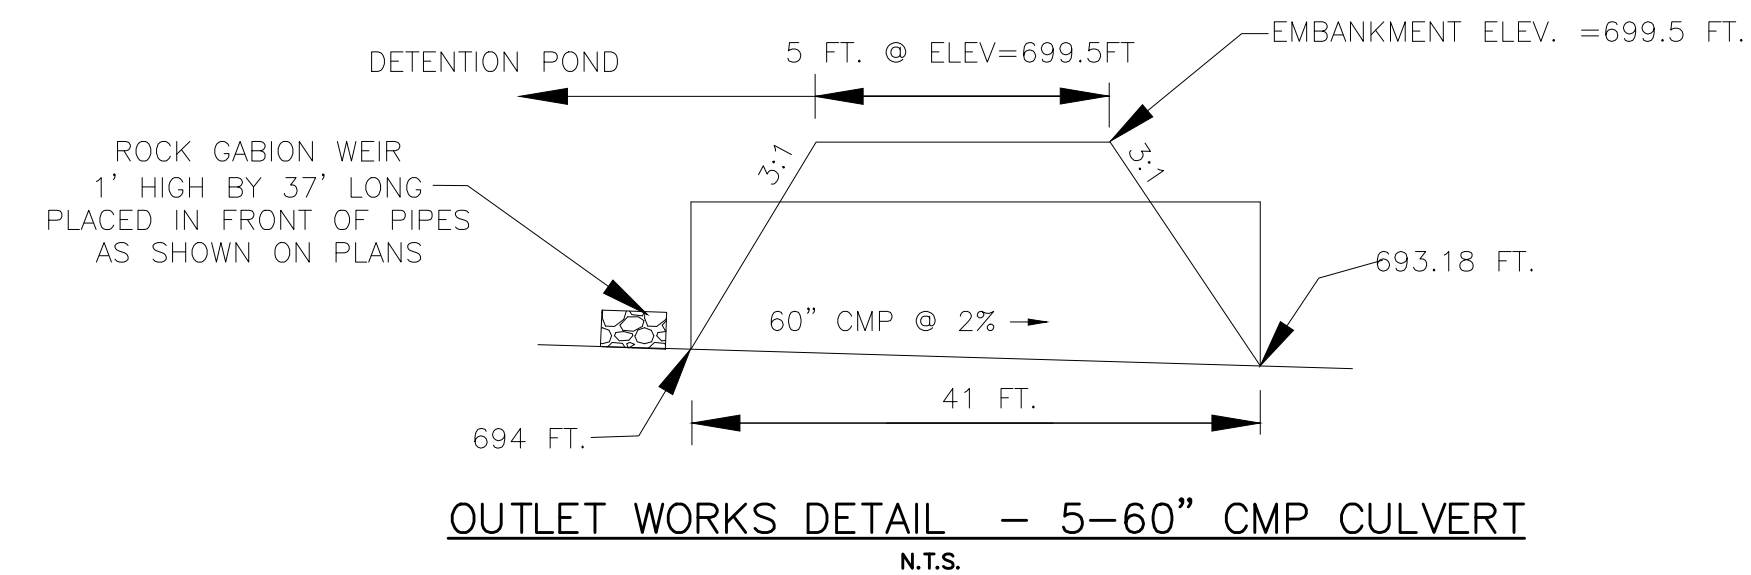

NOTE:  
CONTRACTOR TO COMPACT DETENTION BASIN EMBANKMENT FILL  
TO 95% STANDARD PROCTOR DENSITY.

REVISIONS			
NO.	DATE	DESCRIPTION	BY

PROJ. #	DATE	DES. BY	DWN. BY	CHECK. BY
05-SER	09/30/22			

FIRM REGISTRATION # F-10084

**GALLECOS ENGINEERING, INC.**

SAN ANTONIO, TEXAS www.gallecoseng.com PH: 210.641.0812

THE SEAL APPEARING ON THIS DOCUMENT IS AUTHORIZED BY RICHARD M. GALLECOS, P.E. 88916 NOVEMBER 2, 2022 ALTERATION OF A SEALED DOCUMENT WITHOUT THE SIGNATURE OF THE LICENSEE IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

DETENTION POND PLAN  
GALE ESTATES, L.L.C.

SHEET 23  
OF 24







# Temporary Stormwater Section

## Texas Commission on Environmental Quality

for Regulated Activities on the Edwards Aquifer Recharge Zone and Relating to 30 TAC §213.5(b)(4)(A), (B), (D)(I) and (G); Effective June 1, 1999

***To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.***

***Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.***

## Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Temporary Stormwater Section** is hereby submitted for TCEQ review and executive director approval. The application was prepared by:

Print Name of Customer/Agent: Richard M. Gallegos, P.E.

Date: January 5, 2025

Signature of Customer/Agent:



Regulated Entity Name: Serenity Oaks Subdivision, Unit 5

## Project Information

### Potential Sources of Contamination

*Examples: Fuel storage and use, chemical storage and use, use of asphaltic products, construction vehicles tracking onto public roads, and existing solid waste.*

1. Fuels for construction equipment and hazardous substances which will be used during construction:

☐ The following fuels and/or hazardous substances will be stored on the site: \_\_\_\_\_

These fuels and/or hazardous substances will be stored in:

- ☐ Aboveground storage tanks with a cumulative storage capacity of less than 250 gallons will be stored on the site for less than one (1) year.

- ☐ Aboveground storage tanks with a cumulative storage capacity between 250 gallons and 499 gallons will be stored on the site for less than one (1) year.
- ☐ Aboveground storage tanks with a cumulative storage capacity of 500 gallons or more will be stored on the site. An Aboveground Storage Tank Facility Plan application must be submitted to the appropriate regional office of the TCEQ prior to moving the tanks onto the project.
- ☒ Fuels and hazardous substances will not be stored on the site.
- 2. ☒ **Attachment A - Spill Response Actions.** A site specific description of the measures to be taken to contain any spill of hydrocarbons or hazardous substances is attached.
- 3. ☐ Temporary aboveground storage tank systems of 250 gallons or more cumulative storage capacity must be located a minimum horizontal distance of 150 feet from any domestic, industrial, irrigation, or public water supply well, or other sensitive feature.
- 4. ☒ **Attachment B - Potential Sources of Contamination.** A description of any activities or processes which may be a potential source of contamination affecting surface water quality is attached.

### ***Sequence of Construction***

- 5. ☒ **Attachment C - Sequence of Major Activities.** A description of the sequence of major activities which will disturb soils for major portions of the site (grubbing, excavation, grading, utilities, and infrastructure installation) is attached.
  - ☒ For each activity described, an estimate (in acres) of the total area of the site to be disturbed by each activity is given.
  - ☒ For each activity described, include a description of appropriate temporary control measures and the general timing (or sequence) during the construction process that the measures will be implemented.
- 6. ☒ Name the receiving water(s) at or near the site which will be disturbed or which will receive discharges from disturbed areas of the project: Un-Named Tributaries of the Guadalupe River

### ***Temporary Best Management Practices (TBMPs)***

*Erosion control examples: tree protection, interceptor swales, level spreaders, outlet stabilization, blankets or matting, mulch, and sod. Sediment control examples: stabilized construction exit, silt fence, filter dikes, rock berms, buffer strips, sediment traps, and sediment basins. Please refer to the Technical Guidance Manual for guidelines and specifications. All structural BMPs must be shown on the site plan.*

- 7. ☒ **Attachment D – Temporary Best Management Practices and Measures.** TBMPs and measures will prevent pollution of surface water, groundwater, and stormwater. The construction-phase BMPs for erosion and sediment controls have been designed to retain sediment on site to the extent practicable. The following information is attached:



- ☒ A description of how BMPs and measures will prevent pollution of surface water, groundwater or stormwater that originates upgradient from the site and flows across the site.
  - ☒ A description of how BMPs and measures will prevent pollution of surface water or groundwater that originates on-site or flows off site, including pollution caused by contaminated stormwater runoff from the site.
  - ☒ A description of how BMPs and measures will prevent pollutants from entering surface streams, sensitive features, or the aquifer.
  - ☒ A description of how, to the maximum extent practicable, BMPs and measures will maintain flow to naturally-occurring sensitive features identified in either the geologic assessment, TCEQ inspections, or during excavation, blasting, or construction.
8. ☐ The temporary sealing of a naturally-occurring sensitive feature which accepts recharge to the Edwards Aquifer as a temporary pollution abatement measure during active construction should be avoided.
- ☐ **Attachment E - Request to Temporarily Seal a Feature.** A request to temporarily seal a feature is attached. The request includes justification as to why no reasonable and practicable alternative exists for each feature.
- ☒ There will be no temporary sealing of naturally-occurring sensitive features on the site.
9. ☒ **Attachment F - Structural Practices.** A description of the structural practices that will be used to divert flows away from exposed soils, to store flows, or to otherwise limit runoff discharge of pollutants from exposed areas of the site is attached. Placement of structural practices in floodplains has been avoided.
10. ☒ **Attachment G - Drainage Area Map.** A drainage area map supporting the following requirements is attached:
- ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin will be provided.
  - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a smaller sediment basin and/or sediment trap(s) will be used.
  - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin or other equivalent controls are not attainable, but other TBMPs and measures will be used in combination to protect down slope and side slope boundaries of the construction area.
  - ☐ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. A smaller sediment basin and/or sediment trap(s) will be used in combination with other erosion and sediment controls within each disturbed drainage area.

- ☒ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. Erosion and sediment controls other than sediment basins or sediment traps within each disturbed drainage area will be used.
11. ☐ **Attachment H - Temporary Sediment Pond(s) Plans and Calculations.** Temporary sediment pond or basin construction plans and design calculations for a proposed temporary BMP or measure have been prepared by or under the direct supervision of a Texas Licensed Professional Engineer. All construction plans and design information must be signed, sealed, and dated by the Texas Licensed Professional Engineer. Construction plans for the proposed temporary BMPs and measures are attached.
- ☒ N/A
12. ☒ **Attachment I - Inspection and Maintenance for BMPs.** A plan for the inspection of each temporary BMP(s) and measure(s) and for their timely maintenance, repairs, and, if necessary, retrofit is attached. A description of the documentation procedures, recordkeeping practices, and inspection frequency are included in the plan and are specific to the site and/or BMP.
13. ☒ All control measures must be properly selected, installed, and maintained in accordance with the manufacturer's specifications and good engineering practices. If periodic inspections by the applicant or the executive director, or other information indicate a control has been used inappropriately, or incorrectly, the applicant must replace or modify the control for site situations.
14. ☒ If sediment escapes the construction site, off-site accumulations of sediment must be removed at a frequency sufficient to minimize offsite impacts to water quality (e.g., fugitive sediment in street being washed into surface streams or sensitive features by the next rain).
15. ☒ Sediment must be removed from sediment traps or sedimentation ponds not later than when design capacity has been reduced by 50%. A permanent stake will be provided that can indicate when the sediment occupies 50% of the basin volume.
16. ☒ Litter, construction debris, and construction chemicals exposed to stormwater shall be prevented from becoming a pollutant source for stormwater discharges (e.g., screening outfalls, picked up daily).

## ***Soil Stabilization Practices***

*Examples: establishment of temporary vegetation, establishment of permanent vegetation, mulching, geotextiles, sod stabilization, vegetative buffer strips, protection of trees, or preservation of mature vegetation.*

17. ☒ **Attachment J - Schedule of Interim and Permanent Soil Stabilization Practices.** A schedule of the interim and permanent soil stabilization practices for the site is attached.

- 18. ☒ Records must be kept at the site of the dates when major grading activities occur, the dates when construction activities temporarily or permanently cease on a portion of the site, and the dates when stabilization measures are initiated.
- 19. ☒ Stabilization practices must be initiated as soon as practicable where construction activities have temporarily or permanently ceased.

### ***Administrative Information***

- 20. ☒ All structural controls will be inspected and maintained according to the submitted and approved operation and maintenance plan for the project.
- 21. ☒ If any geologic or manmade features, such as caves, faults, sinkholes, etc., are discovered, all regulated activities near the feature will be immediately suspended. The appropriate TCEQ Regional Office shall be immediately notified. Regulated activities must cease and not continue until the TCEQ has reviewed and approved the methods proposed to protect the aquifer from any adverse impacts.
- 22. ☒ Silt fences, diversion berms, and other temporary erosion and sediment controls will be constructed and maintained as appropriate to prevent pollutants from entering sensitive features discovered during construction.





**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 29, 2024

**PILOT-SCALE FIELD TESTING PLAN  
SERENITY OAKS, UNIT 5**

**NOT APPLICABLE TO THIS PLAN.**

**ATTACHMENT O**



## **GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

December 29, 2024

### **MINIMIZING SURFACE STREAM CONTAMINATION SERENITY OAKS, UNIT 5**

The pre-developed condition flows, proceed south and southeasterly to existing swales and improved earthen channels to the Guadalupe River south-southeast of this tract. A CMP Culvert transfer the runoff across proposed subdivision streets to improved earthen channels and seasonal tributaries of the Guadalupe River. This Unit completed the final, large detention basin sized for the remainder of the Development to maintain storm flows to pre-construction conditions.


The proposed Single-Family Residential Subdivision will generate an insignificant increase in stormwater runoff, which after exiting each residential lot; will be carried by roadside ditches and drainage pipe to the two aforementioned tributaries and on in a southerly direction to the Guadalupe.

All post-developed surface runoff is to be directed to the roadside ditches of the proposed streets and then to earthen channels.

All silt bearing or otherwise contaminated stormwater discharge will be treated at the point source by pertinent TCEQ recommended TBMPs until all pavement is in place and areas to have permanent vegetation are restored.

See Attachment "X", Page CZP 1, Drainage Area Map and Exhibit 2 for the total 100-year inundation line based on calculations for Pre & Post Developed Stormwater flows.



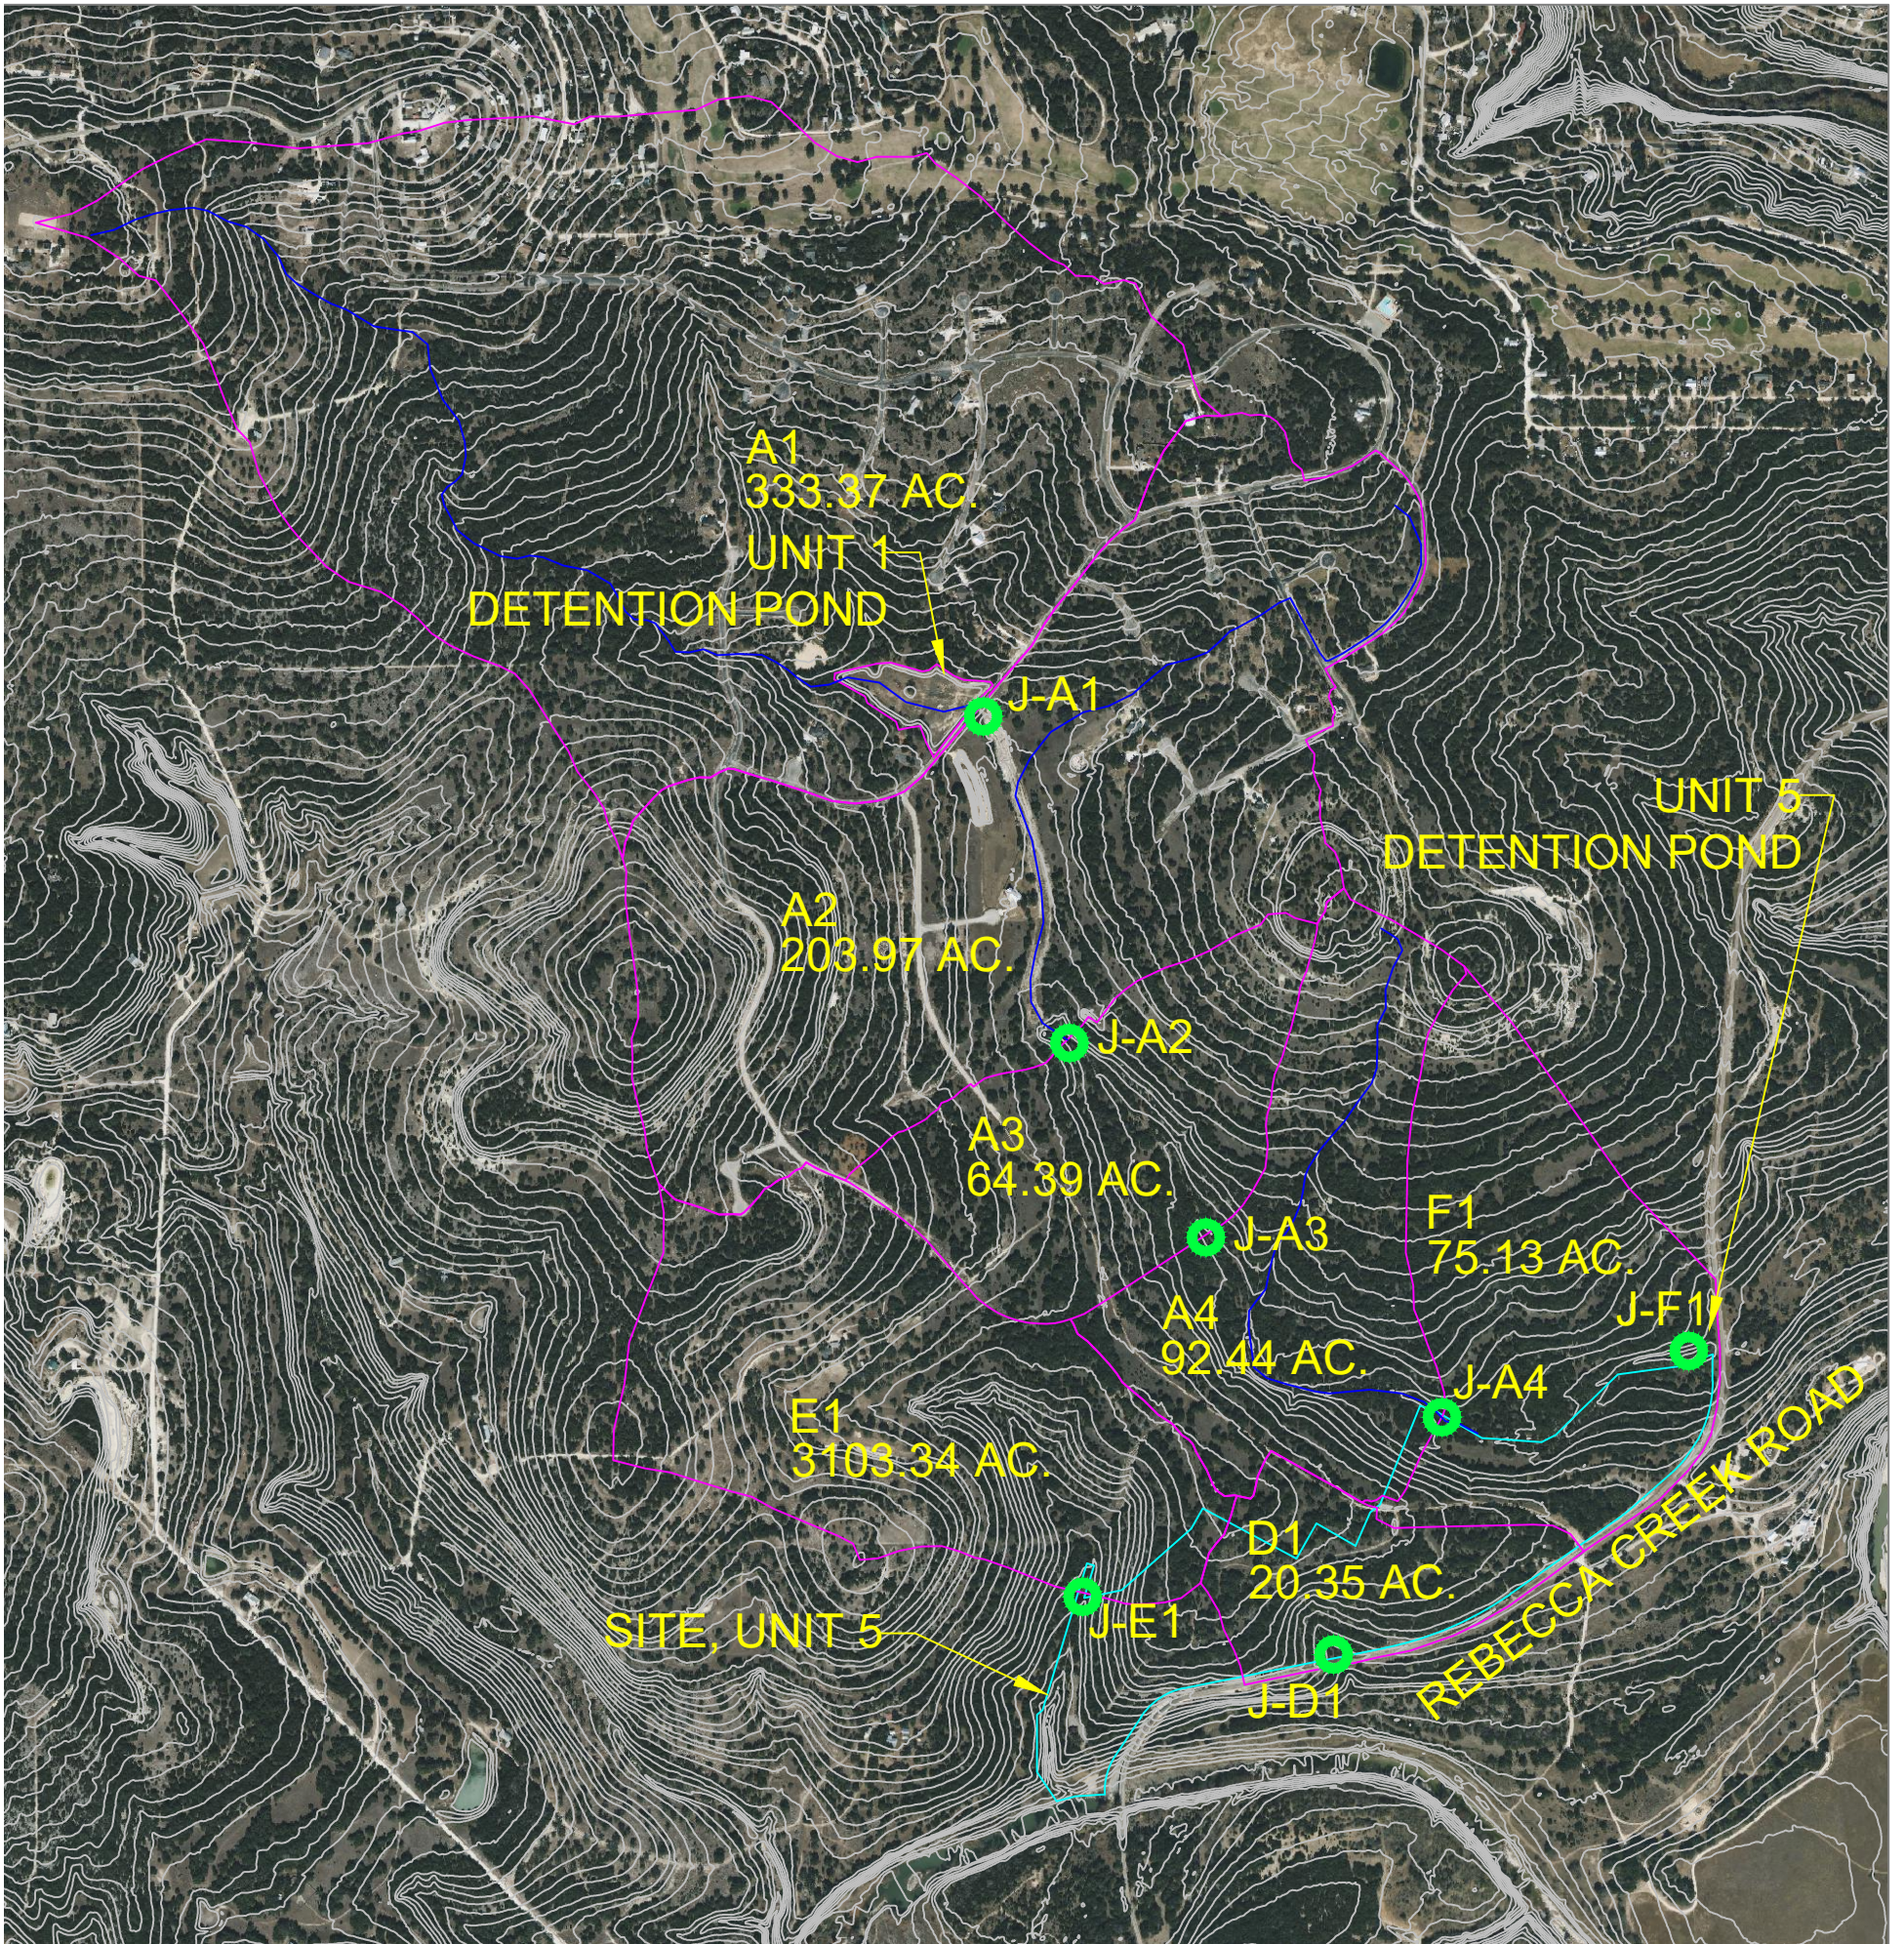


SERENITY OAKS, UNIT 5 SUBDIVISION  
65 ACRES  
COMAL COUNTY, TEXAS

STORM WATER MANAGEMENT PLAN  
DRAINAGE AREA MAP -POST DEVELOPMENT




S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEETS\Exhibit-7-Post Inundation.dwg




REVISIONS			
NO.	DATE	DESCRIPTION	BY

PROJ. #	DATE	DES. BY	DWN. BY	CHECK. BY	R.M.G.
05-SER	03/06/23				

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLECOS, P.E. 86916 APRIL 6, 2023 ALTERATION OF A SEALED DOCUMENT WITHOUT THE SIGNATURE OF THE REGISTERED PROFESSIONAL ENGINEER IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT



PRM REGISTRATION # F-00084



GALLECOS ENGINEERING, INC.

SAN ANTONIO, TEXAS    www.gallegoseng.com    PH: 210.641.0812

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

POST CONSTRUCTION INUNDATION MAP  
GALE ESTATES, L.L.C.


SHEET 7  
OF 7



S:\Projects\00-GENERAL\00-ACS Serenity Unit 5\DWG\SHEET\CFZP02-US-SHPP-12-27-24.dwg



LOCATION MAP  
NOT TO SCALE

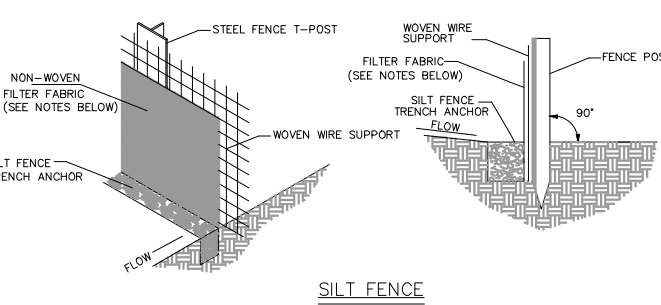

SILT FENCE

GENERAL NOTES:

- The maximum height of the filter fabric should range between 18 and 36 inches above the ground surface (depending on the amount of upslope ponding expected).
- Posts should be spaced 8 to 10 feet apart when a woven wire support fence is used and not more than 6 feet apart when extra strength filter fabric (without a woven wire support fence) is used. The posts should be embedded a minimum of 18 inches.
- A trench should be excavated 4 to 8 inches wide and 4 to 12 inches deep along the upslope side of the line of posts.
- If standard strength filter fabric is to be used, the optional woven wire support should be fastened to the upslope side of the posts. Extend the woven wire support to the bottom of the trench. The filter fabric should be fastened using 4 every spaced staples or T-clips to the woven wire support fence, and 8 to 20 inches of the fabric should extend into the trench.
- Extra strength filter fabric does not require a woven wire support fence. Fastened the filter fabric directly to the posts and extend 8 to 20 inches of the fabric into the trench.
- Where joints in the filter fabric are required, the filter fabric 6-inch overlap and securely secured.
- Do not attach filter fabric to trees.
- Backfill the anchor trench with compacted soil or 0.75 inch minimum diameter gravel placed over the filter fabric.
- Remove silt fence when the construction site is completely stabilized.
- Inspect silt fence daily during periods of prolonged rainfall, immediately after each rainfall event, and weekly during periods of no rainfall. Make any required repairs immediately.
- Sediment must be removed when it reaches a depth of 6". Take care to avoid damaging the fence during cleanout.
- Silt fences should not be removed until the upslope area has been permanently stabilized. Contaminated sediment deposits must be removed and disposed of off-site in accordance with applicable regulations. Uncontaminated sediment remaining in place after the silt fence has been removed should be dressed to conform with the existing grade, and stabilized.
- Place silt fence along a line of uniform elevation, perpendicular to the direction of flow.

MATERIALS:

- Fence posts may be either 4" min. steel or wood posts spaced at 6" to 8". Softwood shall be 2" min. dia. or nominal 2" x 4". Hard wood posts shall have a min. cross section 1.5" x 1.5".
- Synthetic filter fabric should be a pervious sheet of polypropylene, nylon, polyester, or polyethylene yarn conforming to the requirements below:


SYNTHETIC FILTER FABRIC REQUIREMENTS

Physical Property	Requirements
Minimum Weight	3.5 ounces per square yard (ASTM 3786-84)
Min. Mullen Burst Strength	200 lbs. per square foot (ASTM 3786-84)
Minimum flow through rate	100 GPM/SF of frontal area (ASTM 4491-85)

- Barlap of 10 ounces per square yard of fabric can also be used.
- The filter fabric should be purchased in continuous rolls to minimize joints.

MAINTENANCE:

- Inspect regularly and after every storm. Make any repairs necessary to ensure the measure is in good working order.
- Sediment should be removed and the structure restored to its original dimensions when sediment has accumulated to a depth of 6".
- Clean or remove and replace the stone filter or filter fabric if they become clogged.
- Silt protection should remain in place and operational until the drainage area is stabilized.

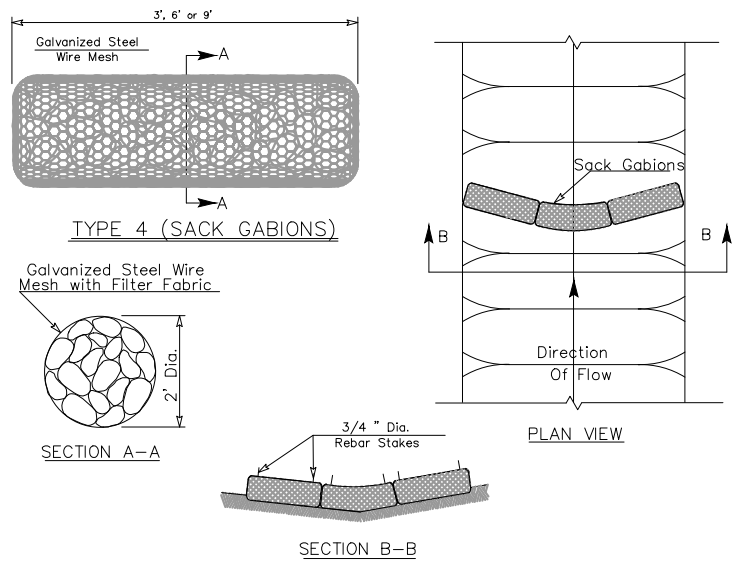

GENERAL NOTES:

- The top of the sack gabions should be level and oriented perpendicular to the direction of flow.
- Filter fabric material shall be fastened to woven wire support.
- Filter fabric material should meet the following specifications:
  - Resistant to ultraviolet light. Fabric should be non-woven geotextile with minimum weight of 3.5 ounces per square yard, minimum mullen burst strength of 200 pounds per square inch and a flow through rate of 120 gallons per minute per square foot of frontal area.
  - Stone size: 4-4" x 4" open graded crushed limestone.
  - Inspect weekly or after each rainfall event and repair or replace as needed.
  - When silt reaches a depth of 6 inches or more above natural ground, silt shall be removed and disposed in an approved manner that will not contribute to re-erosion. Contaminated sediment must be removed and disposed of off-site in accordance with applicable regulations.
- Remove sack gabions after construction site is completely stabilized.

INSTALLATION:



- Layout the perpendicular to flow direction.
- Clear the area of debris, rocks or plants that will interfere with installation.
- Place wire mesh and filter fabric on the ground along the proposed installation with enough overlap to completely encircle the finished size of the berm.
- Place the rock along the center of the woven wire mesh taking care not to damage the filter fabric.
- Wrap the structure with the previously placed woven wire mesh secure enough so that when walked across the structure retains it's shape.
- Secure with tie wire.

MATERIALS:


- Synthetic filter fabric should contain ultraviolet ray inhibitors and stabilizers to provide a minimum of 70% strength retained after 500 hours.
- Barlap of 10 ounces per square yard of fabric may also be used.
- The filter fabric should be purchased in continuous rolls to minimize joints.
- Woven wire support sheathing shall be a minimum 20 gauge with 1 inch openings.

MAINTENANCE:

- Inspect regularly and after every storm. Make any repairs necessary to ensure the sack gabions are in good working order.
- Sediment should be removed and the structure restored to its original dimensions when sediment has accumulated to a depth of 6".
- Clean or remove and replace the stone filter or filter fabric if they become clogged.
- Sack Gabions should remain in place and operational until the drainage area is stabilized.

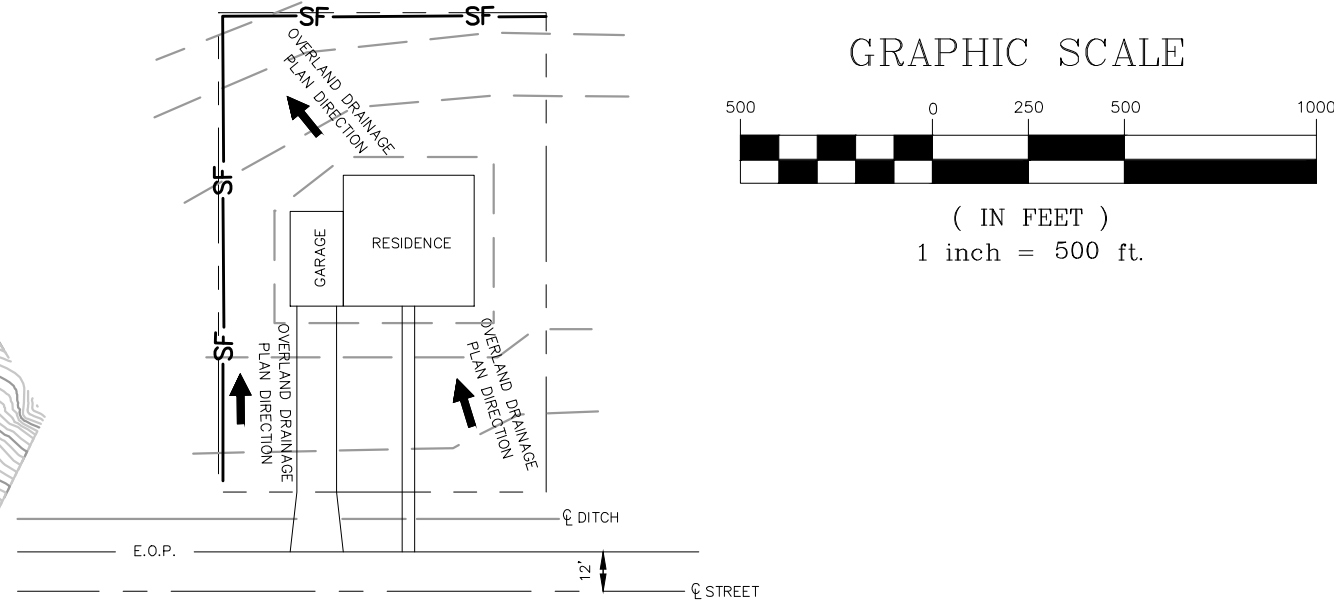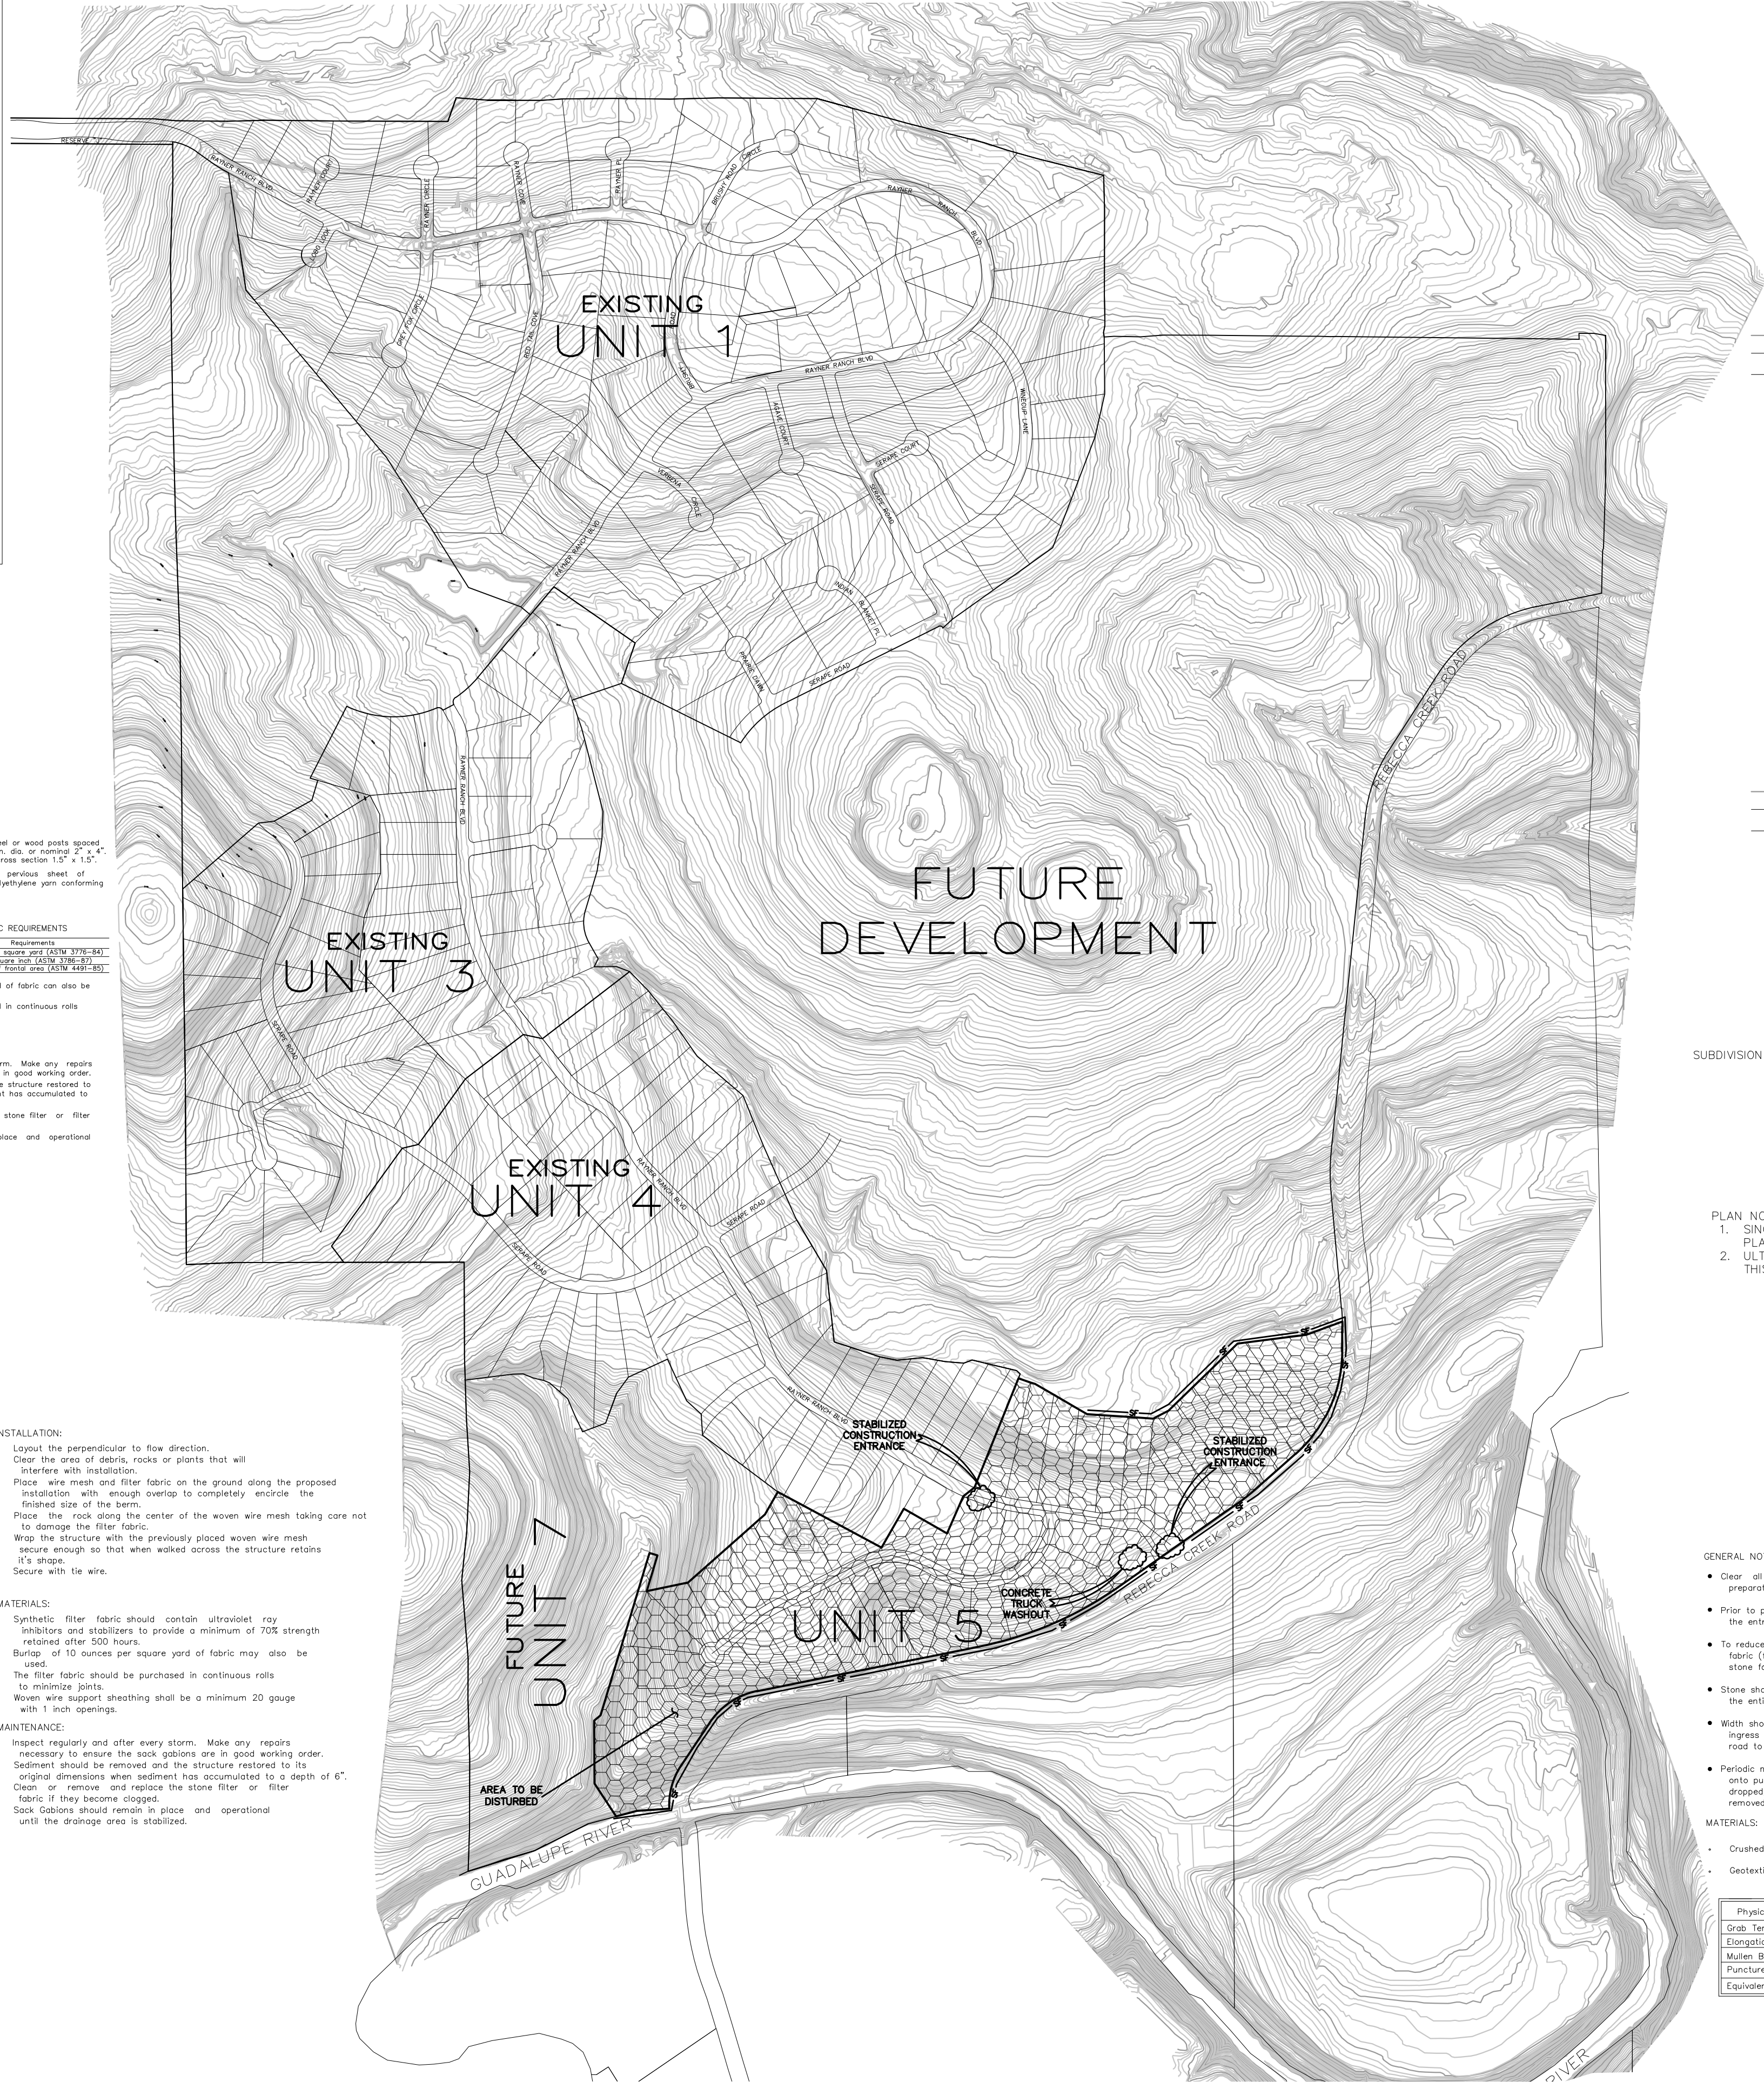

TYPICAL LOT  
EROSION/SEDIMENT  
CONTROL DETAIL  
NOT TO SCALE

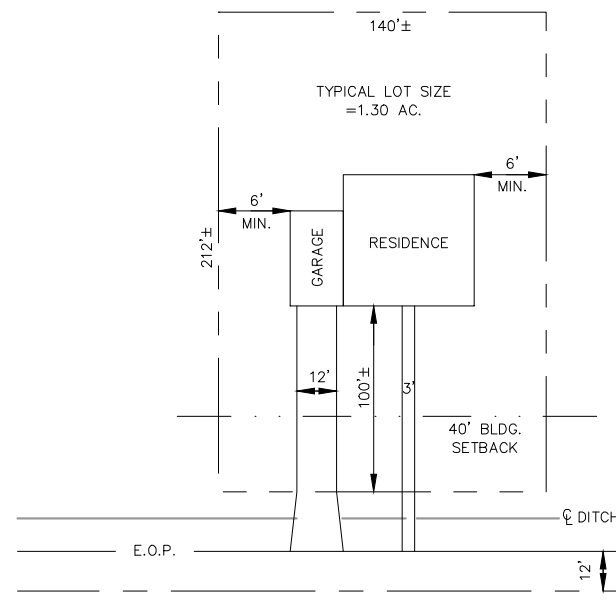

TYPICAL LOT DETAIL  
NOT TO SCALE

IMPERVIOUS COVER CALCS.

RESIDENCE	±2,500 S.F.
GARAGE	±500 S.F.
DRIVEWAY	±1,500 S.F.
WALK	±--- S.F.
TOTAL	±4,500 S.F.

SUBDIVISION RESIDENTIAL TOTAL: 44 LOTS X 4,500 S.F. = 198,000 S.F.

STREET PAVEMENT TOTAL: 177,240 S.F.


SUB-TOTAL IMPERVIOUS COVER: 375,240 S.F. = 8.61 ACRES

TOTAL ACREAGE FOR UNIT 5: 65.15 ACRES

TOTAL IMPERVIOUS COVER FOR UNIT 5: 13.2%

PLAN NOTES:

- SINCE DETERMINATION OF SLOPE STABILITY IS DIFFICULT ON THIS SITE PLAN, ALL SURFACES NOT PAVED SHALL BE SLOPE STABILIZED.
- ULTIMATE GRADES SHALL ADHERE TO EXISTING GRADES SHOWN ON THIS SHEET.

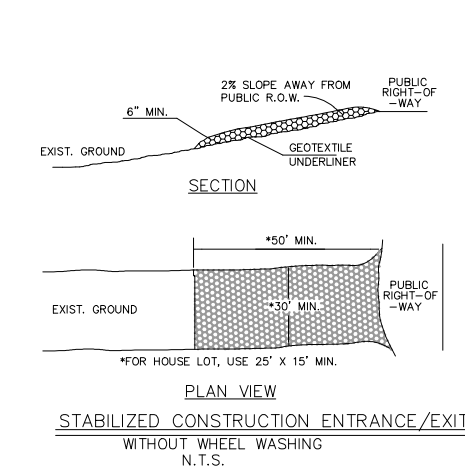

GENERAL NOTES:

- Clear all vegetation, roots and all other obstructions in preparation for grading.
- Prior to placing geotextile (filter fabric) make sure that the entrance is properly graded and compacted.
- To reduce maintenance and loss of aggregate place geotextile fabric (filter cloth) over the existing ground before placing the stone for the entrance.
- Stone should be placed to a depth of 6-inches or greater for the entire width and length.
- Width should be not less than full width of all points of ingress or egress. Flore the entrance where it meets existing road to provide a turning radius.
- Periodic maintenance will be required to prevent tracking onto public right-of-way or any roadway. All sediment spilled, dropped, or tracked onto any public right-of-way must be removed immediately.

MATERIALS:

- Crushed stone 4-inches – 8-inches in diameter.
- Geotextile (filter fabric) with the properties listed below.

Physical Property	Requirements
Grab Tensile Strength	220 lbs. (ASTM D4632)
Elongation Failure	60% (ASTM D4632)
Mullen Burst Strength	430 lbs. (ASTM D3786)
Puncture Strength	125 lbs. (ASTM D4633)
Equivalent Opening	Size 40-80 (US Std Sieve)(ASTM D4751)

- Texas Commission on Environmental Quality  
Contributing Zone Plan  
General Construction Notice
- Written construction notification should be provided to the appropriate TCEQ regional office no later than 48 hours prior to commencement of the regulated activity. Information should include the date on which the regulated activity will commence, the name of the approved plan for the regulated activity, and the name of the prime contractor with the name and telephone number of the contact person.
  - All contractors conducting regulated activities associated with this project should be provided with complete copies of the approved Contributing Zone Plan and the TCEQ letter indicating the specific conditions of its approval. During the course of these regulated activities, the contractor shall keep copies of the approved plan and approval letter on-site.
  - No temporary aboveground hydrocarbon and hazardous substance storage tank system may be installed within 150 feet of a domestic, industrial, irrigation, or public water supply well.
  - Prior to commencing construction, all temporary erosion and sedimentation (E&S) control measures must be properly selected, installed, and maintained in accordance with the manufacturer's specifications and good engineering practices. Controls specified in the E&S Plan of the approved Sediment Control Zone Plan are required during construction. If inspectors indicate a control has been used inappropriately, or incorrectly, the applicant must replace or modify the control for site stabilization. The controls must remain in place until disturbed areas are revegetated and the areas have become permanently stabilized.
  - If sediment escapes the construction site, off-site accumulations of sediment must be removed at a frequency sufficient to minimize off-site impacts to water quality (e.g., fugitive sediment in street being washed into surface streams or sensitive features by the next rain).
  - Sediment must be removed from sediment traps or sedimentation ponds not later than when design capacity has been reduced by 50%. A permanent date must be provided that can indicate when the sediment occupies 50% of the basin volume.
  - Litter, construction debris, and construction chemicals exposed to stormwater shall be prevented from becoming a pollutant source for stormwater discharges (e.g., screening outlets, picked up daily).
  - All spills (excavated material) generated from the project site and stored on-site must have proper E&S controls installed.
  - Stabilization measures shall be initiated as soon as practicable in portions of the site where construction activities have temporarily or permanently ceased, and construction activities will not resume within 21 days. When the initiation of stabilization measures by the 14th day is precluded by weather conditions, stabilization measures shall be initiated as soon as practicable.
  - The following records should be maintained and made available to the TCEQ upon request: the dates when major grading activities occur; the dates when construction activities temporarily or permanently cease on a portion of the site; and the dates when stabilization measures are initiated.
  - The holder of any approved Contributing Zone plan must notify the appropriate regional office in writing and obtain approval from the executive director prior to initiating any of the following:
    - any physical or operational modification of any best management practices or structures), including but not limited to temporary or permanent ponds, dikes, berms, fill fences, and diversionary structures.
    - any change that would significantly impact the ability to prevent pollution of the Edwards Aquifer and hydrologically connected surface water; or
    - any development of land previously identified in a contributing zone plan as undeveloped.

Approved by TCEQ Regional Office  
2800 S. H. 36, Suite 100  
Austin, Texas 78746-5712  
Phone (512) 389-3929  
Fax (512) 389-3795  
Texas Regional Office  
14200 Jackson Road  
San Antonio, Texas 78233-4480  
Phone (214) 440-3066  
Fax (214) 440-4325

THESE GENERAL CONSTRUCTION NOTES MUST BE INCLUDED ON THE CONSTRUCTION PLANS PROVIDED TO THE CONTRACTOR AND ALL SUBCONTRACTORS.

SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

CZP SITE PLAN

GALE ESTATES, L.L.C.

SHEET CZP-2

OF 3

FIRM REGISTRATION # F408044

GALLEGOS  
ENGINEERING,  
INC.

THE SEAL APPEARING ON  
THIS DOCUMENT WAS  
AUTHORIZED BY  
RICHARD M. GALLEGOS, P.E. 86916  
JANUARY 4, 2025  
ATTENTION OF A SEALED DOCUMENT  
WITH NO LESS THAN 90 DAYS BEFORE  
IS AN OFFENSE UNDER THE  
TEXAS ENGINEERING PRACTICE ACT







**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH  
210-641-2037 FAX

# **STORM WATER POLLUTION PREVENTION PLAN (SWPPP)**

PROJECT NAME:

**SERENITY OAKS, UNIT 5  
Comal County, TX**

PREPARED FOR:

**Gale Estates, LLC  
15315 San Pedro  
San Antonio, TX 78232**

PREPARED BY:

**Richard M. Gallegos, P.E.  
GALLEGOS ENGINEERING, INC.**

**FIRM REGISTRATION # F-003084**

**P.O. Box 690067  
San Antonio, TX 78269  
[rg@gallegoseng.com](mailto:rg@gallegoseng.com)**

**DATE: JULY 10, 2022**





# LARGE CONSTRUCTION SITE NOTICE

FOR THE  
Texas Commission on Environmental Quality (TCEQ)  
Stormwater Program  
**TPDES GENERAL PERMIT TXR150000**

## ***“PRIMARY OPERATOR” NOTICE***

This notice applies to construction sites operating under Part II.E.3. of the TPDES General Permit Number TXR150000 for discharges of stormwater runoff from construction sites equal to or greater than five acres, including the larger common plan of development. The information on this notice is required in Part III.D.2. of the general permit. Additional information regarding the TCEQ stormwater permit program may be found on the internet at:

[http://www.tceq.state.tx.us/nav/permits/wq\\_construction.html](http://www.tceq.state.tx.us/nav/permits/wq_construction.html)

Site-Specific TPDES Authorization Number:	
Operator Name:	
Contact Name and Phone Number:	
Project Description: <i>Physical address or description of the site's location, and estimated start date and projected end date, or date that disturbed soils will be stabilized.</i>	
Location of Stormwater Pollution Prevention Plan:	



## **TEXAS COMMISSION ON ENVIRONMENTAL QUALITY**

Construction General Permit Stormwater Pollution Prevention Plan (SWP3)  
Worksheets  
December 2013

### **Texas Pollutant Discharge Elimination Systems (TPDES)**

#### **Construction Stormwater General Permit (TXR150000)**

#### **Stormwater Pollution Prevention Plan (SWP3)**

Company: GALE ESTATES, LLC

Role: DEVELOPER

Project Name: SERENITY OAKS, UNIT 5

and/or Other Operators:

Plan Date: July 2022



## Table of Contents

Section	Tab	Page
Certification Page: Primary and/or Secondary operator		
<b>Site/Project Description:</b>		
1. Nature of Construction and List of Pollutants <i>Part III, Sect. F.1. (a-b)</i>	3	4
2. Schedule or Sequence of Major Grading Activities <i>Part III, Sect. F.1.(c)</i>	4	5
3. Acreage, Material Storage, and Soil Type <i>Part III, Sect.F.1. (d-e)</i>	5	6
4. Location Map <i>Part III, Sect. F.1.(f)</i>	6	7
5. Detailed Site Map <i>Part III, Sect. F.1.g.(i)-(viii)</i>	7	8
6. Site Description, Support Facilities <i>Part III, Sect. F.1.(h - i)</i>	8	9
7. Copy of TXR140000, NOI, certificate, and/or site notice	9	10
<b>Description of Best Management Practices:</b>		
8. Best Management Practices (BMPs), Erosion and Sediment Controls <i>Part III, Sect. F.2.a.(i)-(ii) and F.2. (c)</i>	10	11
9. BMPs, Off-site Transfer of Pollutant Controls <i>Part III, Sect. F.2.a.(iii)</i>	11	12
10. BMPs, Erosion Control and Stabilization Practices <i>Part III, Sect. F.2.b.(i)</i>	12	13
11. Dates of Major Grading Activities and Construction Stoppage <i>Part III, Sect. F.2.b.ii (A)-(C), (iii)</i>	13	14
12. Sediment Control Practices <i>Part III, Sect. F.2. (c)</i>	14	15
13. Permanent Stormwater Controls <i>Part III, Sect. F.3</i>	15	16
14. Other Stormwater Controls <i>Part III, Sect. F.4.(a)-(d)</i>	16	17-18
15. Inspection of Controls Worksheets <i>Part III, Sect. F.7</i>	17	19-20
16. List of BMPs for Eligible Non-Stormwater Discharges <i>Part III, Sect. F.8</i>	18	21
17. Stormwater runoff from Concrete Batch Plants <i>Part IV</i>	19	22
18. Concrete Truck Washout Requirements, <i>Part V</i>	20	23

## Certification Page

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Sign as required by 30 TAC 305.128

Signed: \_\_\_\_\_

JASON GALE  
OFFICER

Date: 07/10/2022

## If plan is shared by more than one entity:

Signed: \_\_\_\_\_

name  
title

Date: \_\_\_\_\_ TPDES#: \_\_\_\_\_

Signed: \_\_\_\_\_

name  
title

Date: \_\_\_\_\_ TPDES#: \_\_\_\_\_

Signed: \_\_\_\_\_

name  
title

Date: \_\_\_\_\_ TPDES#: \_\_\_\_\_

## Primary Operators

GALE ESTATES, LLC

\_\_\_\_\_

\_\_\_\_\_



## Site Description

### Section 1

#### Nature of Construction and List of Pollutants

##### *Part III, Sect. F.1. (a)*

#### Description of the general nature of construction activities:

Construction of residential streets and drainage channels to serve 44 large residential lots.

Pollutant: Oil and grease.

Source: Construction equipment and trucks.

Pollutant: Sediment. Source: Disturbed soil.

##### *Part III, Sect. F.1. (b)*

#### List of ALL potential pollutants and their sources:

<i>Potential Pollutants</i>	<i>Source</i>
Oil, Grease, Diesel Fuel & Gasoline.	Construction Equipment on or near areas to be cleared, graded and/or excavated.
Sediment	Stormwater runoff from areas cleared, graded and/or excavated.
Asphalt Cement (CRS-2 Cationic Emulsified Asphalt) for Double Penetration Seal Coat Aggregate Binder.	Road Surfaces.
Concrete Truck Wash Out.	Concrete Residential Slab & Drainage Riprap.

## Section 2

### Construction Schedule

#### *Part III Sect. F.1. (c)*

Description of the intended schedule, or a sequence of the major activities that will be disturbing soil for the major portions of the site. Add or subtract rows as needed.

<i>Name of Operator</i>	<i>Phase of Project Projected dates Month/year</i>	<i>Activity Disturbing Soil clearing, excavation, etc.</i>	<i>Location on-site where activity will be conducted</i>	<i>Acreage being disturbed</i>



### Section 3

#### Acreage, Material Storage, and Soil Type

##### *Part III, Sect. F.1. (d)*

The total acreage of the entire property and the total acreage where construction activity will occur. Include off-site material storage areas, overburden and stockpiles of dirt or aggregates, and borrow areas.

<i>Material Storage</i>	<i>Material (s)</i>	<i>Acreage</i>	<i>Location</i>
Off-site	None	0	
On-site	Crushed Rd. Base	3.023	Lots 180-190 or Contractor Preference
Overburden/Stockpiles of Dirt	None	0	
Borrow Areas	Rocky Overburden	2.7	Improved Drain Channels
Other areas used as part of the project	None	0	
<b>Total acreage of project property:</b>	<b>65.16</b>	<b>Total acreage of disturbed soil:</b>	<b>8.32</b>

##### *Part III Sect. F.1. (e)*

Description of the soil type (e.g., loamy, clayey, sandy, rocky) or the quality of any discharge from the site.

## **Section 4**

### **Location Map**

*Part III Sect. F.1. (f)*

**Attached Map**



## **Section 5**

### **Detailed Site Map(s)**

*Part III Sect. F.1.g (i)-(viii)*

**Attach Map(s)**

## Section 6

### Site Description – Support Facilities

#### *Part III Sect. F.1. (h)*

A description of the activities and their locations of any asphalt plants, concrete batch plants or other activity supporting this construction site.

<i>Facility</i>	<i>Description</i>	<i>Location</i>
Asphalt Plant	<b>Asphalt Cement (CRS-2 Cationic Emulsified Asphalt) for Double Penetration Seal Coat Aggregate Binder.</b>	<b>Delivered daily from refinery.</b>
Concrete Batch Plant	<b>Drainage Structure &amp; House Slab Readymix Concrete.</b>	<b>Delivered daily from local commercial batch plants. Such as Ingram Readymix.</b>
Other Support Activity	<b>MC-30 Rd. Base Prime Coat</b>	<b>Delivered &amp; Distributed as Needed.</b>

#### *Part III Sect. F.1. (i)*

List of receiving waters at or near the site that will be disturbed or that will receive discharges from the project's disturbed areas.

<i>Name of Receiving</i>	<i>Will Receiving Water Be Disturbed?</i>	<i>Location of Receiving water</i>
<b>Guadalupe River</b>	<b>No</b>	<b>Near Rebecca Creek Rd. Crossing.</b>



## **Section 7**

**Copies of Construction General Permit (CGP) TXR150000  
or description of location of CGP  
NOI, certificate, and/or site notice**

## Best Management Practices

### Section 8

#### Best Management Practices (BMPs) Erosion and Sediment Controls

##### *Part III Section F.2.a.(i)-(ii) and F.2. (c)*

Description of Erosion and Sediment Controls designed to retain sediment. Add as many rows as needed.

<i><b>BMPs Installed</b></i>	<i><b>Location(s) On-Site</b></i>	<i><b>Inspection/Maintenance Schedule</b></i>	<i><b>Modifications/Replacement Activities</b></i>
Silt Fence	See Plans	Bi-weekly & after each 2" or great Rain Event.	Replace all damaged & washed out fence.
Rock Berms	See Plans	Monthly	Replace when blocked by sediment to a depth of 1'.
Stabilized Construction Entrance/Exit	See Plans	Weekly	Replace when silt reaches the top course of aggregate.
Sack Gabion	See Plans	Monthly	Replace when blocked by sediment to a depth of 1'.

<i><b>Are there sedimentation basins or traps?*</b> If yes, list the measures taken to reduce the pollutants transported off-site by pumping activities.</i>	<b>Yes</b> <input checked="" type="checkbox"/>	<b>No</b> <input type="checkbox"/>
<i><b>Prevention Measure</b></i>	<i><b>Location On-Site</b></i>	<i><b>Implementation Date</b></i>
<b>Per BMP Best Practices</b>	Channel	Prior to Construction

\* Part III Section F.6. (c) Sediment must be removed from sediment traps and basins no later than the time that the design capacity has been reduced by 50 percent.

## Section 9

### BMPs, Off-Site Transfer of Pollutant Controls

#### *Part III Section F.2.a. (iii)*

List of good housekeeping practices implemented to limit the off-site transport of litter, construction debris, and construction materials.

<b><i>Litter Controls:</i></b>	
<b><i>Good Housekeeping Activity</i></b>	<b><i>Location(s) On-Site</i></b>
Street ROW clearing & burning. Provided no “Burn Ban” is in effect.	On site within ROWs.
<b><i>Construction Debris Controls:</i></b>	
<b><i>Good Housekeeping Activity</i></b>	<b><i>Location(s) On-Site</i></b>
Wrecked Conc. Forms & CMP remnants.	Removed from site weekly.
<b><i>Construction Material Controls:</i></b>	
<b><i>Good Housekeeping Activity</i></b>	<b><i>Location(s) On-Site</i></b>
Scrap Building materials.	Each Home Builder to remove from site Monthly.



## Section 10

### BMPs, Stabilization and Erosion Control Practices

#### *Part III Section F.2.b. (i)*

Stabilization and erosion control practices may include, but are not limited to: establishing temporary or permanent vegetation, mulching, geotextiles, sod stabilization, vegetative buffer strips, and protecting existing trees and vegetation. List practices used where they are located, when they will be implemented, and whether they are temporary (interim) or permanent.

<i>Stabilization Practices</i>	<i>Location On-Site</i>	<i>Implementation Date</i>	<i>Interim or Permanent</i>
<b>Install Geotextile Fabric</b>	<b>Under Stabilized Construction Entrance</b>	<b>Per Contractor</b>	<b>Temporary (Interim)</b>

## Section 11

### Dates of Major Grading Activities and Construction Stoppage

#### *Part III Section F.2.b. (ii) (A)-(C), (iii)*

If you do not list activities below, either attach documentation or state where records for the activities can be accessed:

Documentation attached? Yes ☐ No ☐

Where can documentation be found (if not included in SWP3)?

Contact Person              Phone Number

#### **Dates when major grading activities will occur and locations on-site:**

<i>Activity</i>	<i>Location</i>	<i>Dates when Activity is Scheduled</i>
See Section 2		

#### **Dates when construction activity will temporarily or permanently cease:**

<i>Location on-site</i>	<i>Date activity is to be stopped</i>	<i>Temporary or Permanent?</i>	<i>Stabilization Initiation Date</i>
August 2023			

## Section 12

### Sediment Control Practices

#### Part III Section F.2. (c)

Will the project disturb 10 acres or more at one time? Yes ☒ No ☐

If yes, is it feasible to install a sediment basin? Yes ☐ No ☒

Calculate the volume of runoff from a 2-year, 24 hour storm event. Volume of sediment basin:

In determining feasibility have you considered (attach any additional justification in determining feasibility):

<i>Site Factor</i>	<i>Considered?</i>	<i>Site Factor</i>	<i>Considered?</i>
Site Soils	Rock	Precipitation pattern	
Slope	4 to 5 % Avg.	Site geometry	
Available area		Site vegetation	
Public safety		Geotechnical factors	
Groundwater depth		Infiltration capacity	
Other? (list)		Other? (list)	

Based on above information, sedimentation basin will ☐ be used **OR** ☐ is not feasible.

**If a sediment basin is not feasible, list of alternative structural control practices that will be used:**

<i>Article II. Structural Control</i>	<i>Used? Yes/No</i>	<i>Location On-Site</i>
A series of smaller sediment basins	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Silt fences	Yes <input checked="" type="checkbox"/> No <input type="checkbox"/>	
Vegetative buffer strips	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Sediment traps	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Other (list): Rock Berms	Yes <input checked="" type="checkbox"/> No <input type="checkbox"/>	
Other (list):	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Other (list):	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Other (list):	Yes <input type="checkbox"/> No <input type="checkbox"/>	



## Section 13

### Permanent Stormwater Controls

#### *Part III Section F.3*

The following measures will be constructed to control post-construction runoff:

<i>Control Measure</i>	<i>Location on Project Site</i>	<i>Control runoff from what areas</i>

## Section 14

### Other Stormwater Controls

#### *Part III Section F.4. (a)*

Control to minimize dust generation and off-site tracking of sediment:

<i>Control Practice Used</i>	<i>Location(s) On-Site</i>
Stabilized Construction Entrance/Exit	Serenity Pass.
Site Contractor's Water Truck	Job Site

#### *Part III Section F.4. (b)*

The following construction and waste materials will be stored on-site:

<i>Materials Stored On-Site</i>	<i>Average Amount Stored</i>	<i>Location On-Site</i>	<i>Controls Used to Prevent Pollutants</i>
Crushed Limestone Base	Unknown	Lot 190	Silt Fence Around Stockpile.

### Other Stormwater Controls

#### *Part III Section F.4. (c)- (d)*

Describe pollutant sources from areas other than construction (make additional copies of this worksheet as needed):

<i>Type of pollutant source</i>	<i>Pollutant(s)</i>	<i>Control(s) or measure(s) used to minimize pollutants</i>
Site Work Contractor	Traffic generated road dust	Site Work Contractor will have

<i>Type of pollutant source</i>	<i>Pollutant(s)</i>	<i>Control(s) or measure(s) used to minimize pollutants</i>
		a water truck available for dust control.

Describe the velocity dissipation devices that will be placed at discharge locations and/or along the length of any outfall channels:

<i>Dissipation Device (hay bales, silt fence, pond, etc.)</i>	<i>Outfall Discharging to (MS4, bar ditch, creek/stream)</i>	<i>At Outfall or Channel (distance interval for channel)</i>



## Section 15

### Inspection of Controls Worksheets/Report

#### *Part III Section F.7.*

Complete this worksheet every seven days; **OR**, every 14 days and within 24 hours of a 2 inch rainfall event, and retain in your SWP3.

**Inspector (name/title):**      **Inspection Date:**      **Day:**      **Time:**      **am/pm**

**Scope of inspection:** 14 Day Inspection ☐ or Weekly Inspection ☐

**Day of week normally conducted:** \_\_\_\_\_ **0.5 inch Rainfall Event** ☐

<i>Inspection Type:</i>	<i>Inspected? (Y/N)</i>	<i>Areas of Concern (Describe in detail in the narrative section)</i>
Disturbed Soil Areas	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Material Storage Areas	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Structural Controls	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Sediment & Erosion Controls	Yes <input type="checkbox"/> No <input type="checkbox"/>	
Entrance(s) and Exit(s)	Yes <input type="checkbox"/> No <input type="checkbox"/>	

#### **Discharges:**

<i>Nature of discharge (silt, gravel, sand, other pollutant)</i>	<i>Location on-site discharge</i>



## Inspection of Controls Worksheets (contd.)

### Part III Section F.7.

Best Management Practices Inspected: Add additional rows if needed.

<i><b>BMP and Location</b></i>	<i><b>OK (no action required)</b></i>	<i><b>BMP failed (describe failure)</b></i>	<i><b>Required Maintenance (describe corrective actions needed)</b></i>
	<input type="checkbox"/>		
	<input type="checkbox"/>		
	<input type="checkbox"/>		
	<input type="checkbox"/>		
	<input type="checkbox"/>		
	<input type="checkbox"/>		

#### Additional BMPs Needed

<b>Location</b>	<b>Best Management Practice</b>	<b>Replacing Existing BMP?</b>

## Inspection Narrative Description/Certification

### Part III Section F.7.

Complete this worksheet every seven days; **OR**, every 14 days and within 24 hours of a 2 inch rainfall event and retain in your SWP3.

Describe the inspector's qualifications to conduct the inspections:

Describe how your inspection was conducted:

Describe all incidents of non-compliance (i.e. major discharges, BMP failures):

"I certify that the facility or site is in compliance with the stormwater pollution prevention plan and this permit."

I further certify that I am authorized to sign this report under TCEQ rules at 30 TAC 305.128 (relating to Signatories to Reports)

Name/Title:

Date:



## Section 16

### Eligible Non-Stormwater Discharges (listed in Part II.3. [a]-[h])

#### *Part III, Sect. F.8*

<i>Eligible Non-stormwater Discharge</i>	<i>Used? Yes/No</i>	<i>Pollution Prevention Measure(s)</i>	<i>Implementation Date</i>
Fire Fighting Activities	Yes <input type="checkbox"/> No <input type="checkbox"/>		
Fire Hydrant Flushing	Yes <input type="checkbox"/> No <input type="checkbox"/>		
Washing of Vehicles, Buildings, or Pavement without detergents or soap (see description in Part II.3.[c])	Yes <input type="checkbox"/> No <input type="checkbox"/>		
Dust Control	Yes <input type="checkbox"/> No <input type="checkbox"/>		
Potable Water Sources (water line flushing)	Yes <input type="checkbox"/> No <input type="checkbox"/>		
Air Conditioning Condensate	Yes <input type="checkbox"/> No <input type="checkbox"/>		
Uncontaminated Ground/Spring Water	Yes <input type="checkbox"/> No <input type="checkbox"/>		
Other? (List)	Yes <input type="checkbox"/> No <input type="checkbox"/>		

List any other non-stormwater discharge permitted by a separate NPDES, TPDES, or TCEQ Permit.

<i>Non-stormwater Discharge</i>	<i>Pollution Prevention Measure</i>	<i>Implementation Date</i>



## **Section 17**

### **Stormwater Runoff from Concrete Batch Plants**

#### ***Part IV***

See Instructions for information regarding Concrete Batch Plants associated with Construction Projects.



## **Section 18**

### **Concrete Truck Washout Requirements**


#### ***Part V***

Location of concrete washout area on site and description of BMPs established to prevent the concrete wash out water from contributing to groundwater contamination or entering the waters of the state.






ESTIMATED STORM WATER POLLUTION PREVENTION PLAN & TEMPORARY SEDIMENTATION AND EROSION CONTROL PLAN QUANTITIES		
SERENITY OAKS, UNIT 5		
ITEM	UNIT	QUANTITY
STABILIZED CONSTRUCTION ENTRANCE	EACH	2
SILT FENCE	L.F.	5,880
CONCRETE TRUCK WASHOUT	EACH	1

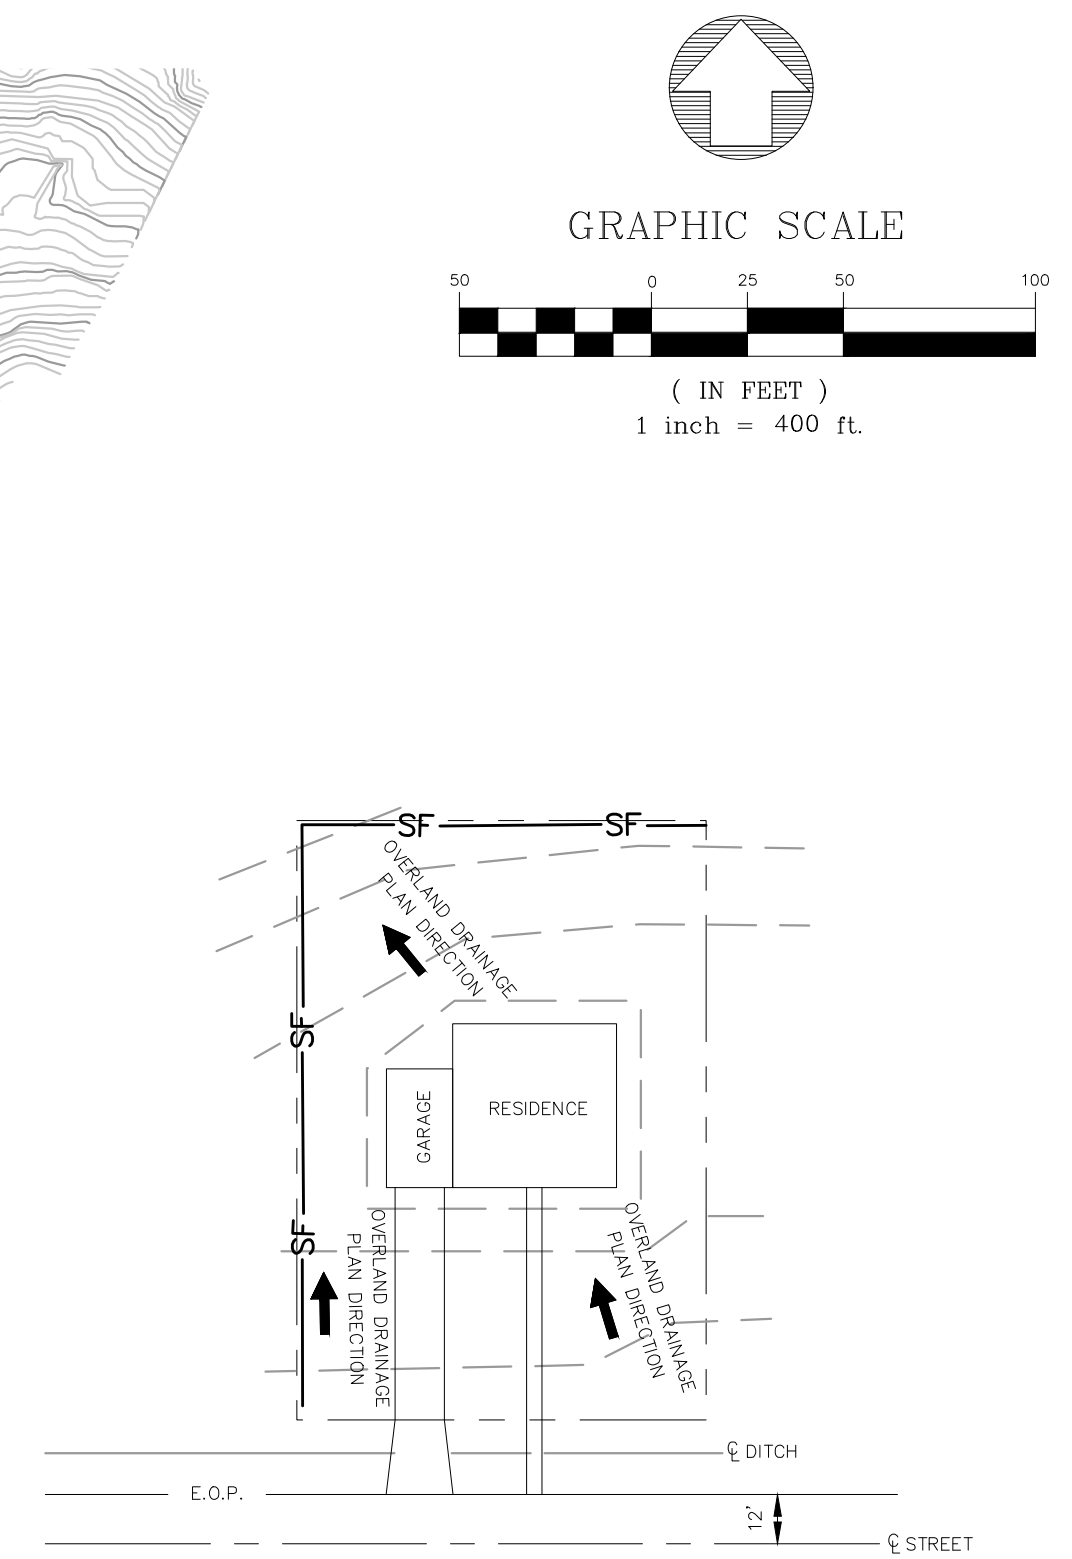

TYPICAL LOT  
EROSION/SEDIMENT  
CONTROL DETAIL  
NOT TO SCALE

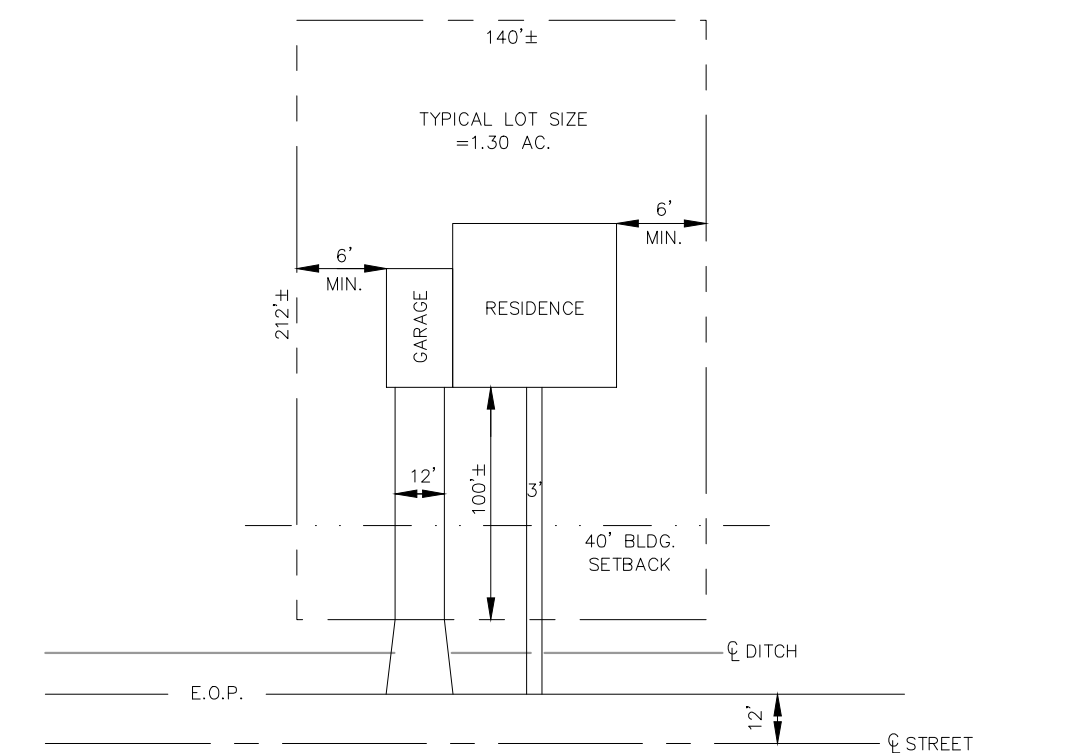

TYPICAL LOT DETAIL

NOT TO SCALE

<u>IMPERVIOUS COVER CALCS.</u>	
RESIDENCE	±2,500 S.F.
GARAGE	±500 S.F.
DRIVEWAY	±1,500 S.F.
WALK	±---- S.F.
<u>TOTAL</u>	<u>±4,500 S.F.</u>

SUBDIVISION RESIDENTIAL TOTAL: 44 LOTS X 4,500 S.F.  
= 198,000 S.F.

STREET PAVEMENT TOTAL: 177,240 S.F.

SUB-TOTAL IMPERVIOUS COVER: 375,240 S.F. = 8.61 ACRES

TOTAL ACREAGE FOR UNIT 5: 65.15 ACRES

TOTAL IMPERVIOUS COVER FOR UNIT 5: 13.2%

REVISIONS				
NO.	DATE	DESCRIPTION	BY	

FIRM REGISTRATION # F-003084



SAN ANTONIO, TEXAS    [www.gallegoseng.com](http://www.gallegoseng.com)    PH: 210.641.0812

THE SEAL APPEARING ON  
THIS DOCUMENT WAS  
AUTHORIZED BY  
RICHARD M. GALLEGO, P.E. 86916  
APRIL 8, 2023  
ALTERATION OF A SEALED DOCUMENT  
WITHOUT PROPER NOTIFICATION  
TO THE RESPONSIBLE ENGINEER  
IS AN OFFENSE UNDER THE  
TEXAS ENGINEERING PRACTICE ACT



SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

STORM WATER POLLUTION  
PREVENTION PLAN  
GALE ESTATES, L.L.C.

GALE ESIAIES, L.L.C.

HEET 3  
OF 24



S:\Projects\00--GENERAL\00--ACS Serenity Unit 5\DWG\SHEET\504--U5--SWPPP NAR.dwg

SITE DESCRIPTION

PROJECT: SERENITY OAKS SUBDIVISION UNIT 5  
A PROPOSED SINGLE FAMILY RESIDENTIAL DEVELOPMENT LOCATED IN THE COUNTY OF COMAL, LOCATED OFF RAYNER RANCH ROAD.

PROJECT DESCRIPTION:  
THE CONSTRUCTION OF STREETS, DRAINAGE, WATER, AND UTILITY FACILITIES NECESSARY FOR THE DEVELOPMENT OF A SINGLE-FAMILY RESIDENTIAL SUBDIVISION.

MAJOR SOIL DISTURBING ACTIVITIES:  
ACTIVITIES ASSOCIATED WITH STREET, DRAIN, & UTILITY CONSTRUCTION--TRENCHING, STOCKPILING SPOILS AND EXCAVATION.

TOTAL PROJECT AREA: ± 89.96 ACRES  
TOTAL AREA TO BE DISTURBED: ± 89.96 ACRES

WEIGHTED RUNOFF COEFFICIENT (AFTER CONSTRUCTION): 0.62

EXISTING CONDITION OF SOIL & VEGETATIVE COVER AND % OF EXISTING VEGETATIVE COVER:

THE SOIL TYPE(S) ON SITE ARE AS FOLLOWS:  
1. ROCK WITH SOME TOP SOIL.

NAME OF RECEIVING WATERS: TRIBUTARY OF GUADALUPE RIVER

SOIL STABILIZATION PRACTICES:

- TEMPORARY SEEDING
- PERMANENT PLANTING, SODDING, OR SEEDING
- MULCHING
- SOIL RETENTION BLANKET
- BUFFER ZONES
- ☒ PRESERVATIVE OF NATURAL RESOURCES

OTHER:

STRUCTURAL PRACTICES:

- ☒ SILT FENCES
- HAY BALES
- ☒ ROCK BERMS
- DIVERSION, INTERCEPTOR, OR PERIMETER DIKES
- DIVERSION, INTERCEPTOR, OR PERIMETER SWALES
- DIVERSION, DIKE AND SWALE COMBINATIONS
- PIPE SLOPE DRAINS
- PAVED FLUMES
- ☒ ROCK BEDDING AT CONSTRUCTION EXIT
- TIMBER MATTING AT CONSTRUCTION EXIT
- CHANNEL LINERS
- SEDIMENT TRAPS
- SEDIMENT BASINS
- CURB INLET GRAVEL FILTER
- STONE OUTLET STRUCTURES
- CURBS AND GUTTERS
- STORM SEWERS
- VELOCITY CONTROL DEVICES

OTHER:

NARRATIVE – SEQUENCE OF CONSTRUCTION (STORM WATER MANAGEMENT) ACTIVITIES:

STRUCTURAL PRACTICES, AS APPLICABLE, WILL BE INSTALLED PRIOR TO EACH PHASE OF THE PROJECT AND MAINTAINED DURING THE CONSTRUCTION OF THAT PHASE. SOIL STABILIZATION PRACTICES WILL CLOSELY FOLLOW COMPLETION AND ACCEPTANCE OF CONSTRUCTION FOR EACH PROJECT PHASE.

STORM WATER MANAGEMENT:

THE CONTRACTOR WILL INSTALL AND MAINTAIN SEDIMENTATION AND EROSION CONTROL MEASURES AS SPECIFIED IN THE STORM WATER POLLUTION PREVENTION PLAN, TEMPORARY SEDIMENTATION & EROSION CONTROL PLAN, AND AS DIRECTED BY AUTHORIZED OFFICIALS.

CONTRACTOR TO PLACE EXCAVATED MATERIAL ON THE HIGH SIDE OF THE TRENCH.

SITE DESCRIPTION

OTHER EROSION AND SEDIMENT CONTROLS:

MAINTENANCE:  
ALL EROSION AND SEDIMENT CONTROLS WILL BE MAINTAINED IN GOOD WORKING ORDER. IF A REPAIR IS NECESSARY, IT WILL BE DONE AT THE EARLIEST DATE POSSIBLE, BUT NO LATER THAN 7 CALENDAR DAYS AFTER THE SURROUNDING EXPOSED GROUND HAS DRIED SUFFICIENTLY TO PREVENT FURTHER DAMAGE FROM HEAVY EQUIPMENT.

INSPECTION:  
AN INSPECTION WILL BE PERFORMED BY THE CONTRACTOR EVERY 2 WEEKS AS WELL AS AFTER EVERY HALF INCH OR MORE OF RAIN (AS RECORDED ON A NON-FREEZING RAIN GAUGE TO BE LOCATED AT THE PROJECT SITE). THE CONTROLS WILL BE REVISED AS NECESSARY.

WASTE MATERIALS:  
ALL WASTE MATERIAL WILL BE COLLECTED AND STORED IN A METAL DUMPSTER. THE DUMPSTER WILL MEET ALL STATE AND LOCAL CITY SOLID WASTE MANAGEMENT REGULATIONS. ALL TRASH AND CONSTRUCTION DEBRIS FROM THE SITE WILL BE DEPOSITED IN THE DUMPSTER. THE DUMPSTER WILL BE EMPTIED AS NECESSARY OR AS REQUIRED BY LOCAL REGULATION, AND THE TRASH WILL BE HUALED TO A LOCAL DUMP. NO CONSTRUCTION WASTE MATERIAL WILL BE BURIED ON SITE.

HAZARDOUS WASTE (INCLUDING SPILL REPORTING):  
AT A MINIMUM, ANY PRODUCTS IN THE FOLLOWING CATEGORIES ARE CONSIDERED TO BE HAZARDOUS:  
  
PAINTS, ACIDS FOR CLEANING MASONARY SURFACES, CLEANING SOLVENTS ASPHALT PRODUCTS, CHEMICAL ADDITIVES FOR SOIL STABILIZATION, OR CONCRETE CURING COMPOUNDS AND ADDITIVES. IN THE EVENT OF A SPILL WHICH MAY BE HAZARDOUS, THE SPILL COORDINATOR SHOULD BE CONTACTED IMMEDIATELY.

SANITARY WASTE:  
ALL SANITARY WASTE WILL BE COLLECTED FROM THE PORTABLE UNITS AS NECESSARY OR AS REQUIRED BY LOCAL REGULATION BY A LICENSED SANITARY WASTE MANAGEMENT CONTRACTOR.

OFFSITE VEHICLE TRACKING:

- HAUL ROADS DAMPENED FOR DUST CONTROL
- LOADED HAUL TRUCKS TO BE COVERED WITH TARPULIN
- EXCESS DIRT ON ROAD REMOVED DAILY
- ☒ STABILIZED CONSTRUCTION ENTRANCE

OTHER:

REMARKS:

OWNER’S CERTIFICATION

I CERTIFY UNDER PENALTY OF LAW THAT THIS DOCUMENT AND ALL ATTACHMENTS WERE PREPARED UNDER MY SUPERVISION IN ACCORDANCE WITH SYSTEM DESIGNED TO ASSURE THAT QUALIFIED PERSONAL PROPERLY GATHER AND EVALUATE THE INFORMATION SUBMITTED. BASED ON MY INQUIRY OF THE PERSON OR PERSONS WHO MANAGE THE SYSTEM, OR THOSE PERSONS DIRECTLY RESPONSIBLE FOR GATHERING THE INFORMATION SUBMITTED IS, TO THE BEST OF MY KNOWLEDGE AND BELIEF, TRUE, ACCURATE, AND COMPLETE. I AM AWARE THAT THERE ARE SIGNIFICANT PENALTIES FOR SUBMITTING FALSE INFORMATION, INCLUDING THE POSSIBILITY OF FINE AND IMPRISONMENT FOR KNOWING VIOLATIONS.

OWNER DATE

CONTRACTOR’S CERTIFICATION

I CERTIFY UNDER PENALTY OF LAW THAT I UNDERSTAND THE TERMS AND CONDITIONS OF THE GENERAL TEXAS POLLUTANT DISCHARGE ELIMINATION SYSTEM (TPDES) PERMIT THAT AUTHORIZES THE STORM WATER DISCHARGES ASSOCIATED WITH INDUSTRIAL ACTIVITY FROM THE CONSTRUCTION SITE IDENTIFIED AS PART OF THIS CERTIFICATION PLAN.

SIGNATURE (CONTRACTOR) DATE

REVISIONS			
NO.	DATE	DESCRIPTION	BY
PROJ. #:	DATE:	DRAWN BY:	CHECKED BY:
U5-SER	09/30/22	S.G.	R.M.G.

FIRM REGISTRATION # F-40804



GALLEGOS

ENGINEERING,

INC.

SAN ANTONIO, TEXAS    www.gallegoseng.com    PH: 210.641.0812

THE SEAL APPEARING ON THIS DOCUMENT WAS AUTHORIZED BY RICHARD M. GALLEGOS, P.E. 86916 NOVEMBER 2, 2022 ALTERATION OF A SEALED DOCUMENT WITHOUT REPRODUCTION OF THE LICENSEE'S SIGNATURE IS AN OFFENSE UNDER THE TEXAS ENGINEERING PRACTICE ACT




SERENITY OAKS SUBDIVISION, UNIT 5  
COMAL COUNTY, TEXAS

STORM WATER POLLUTION  
PREVENTION PLAN

GALE ESTATES, L.L.C.

SHEET 4  
OF 24



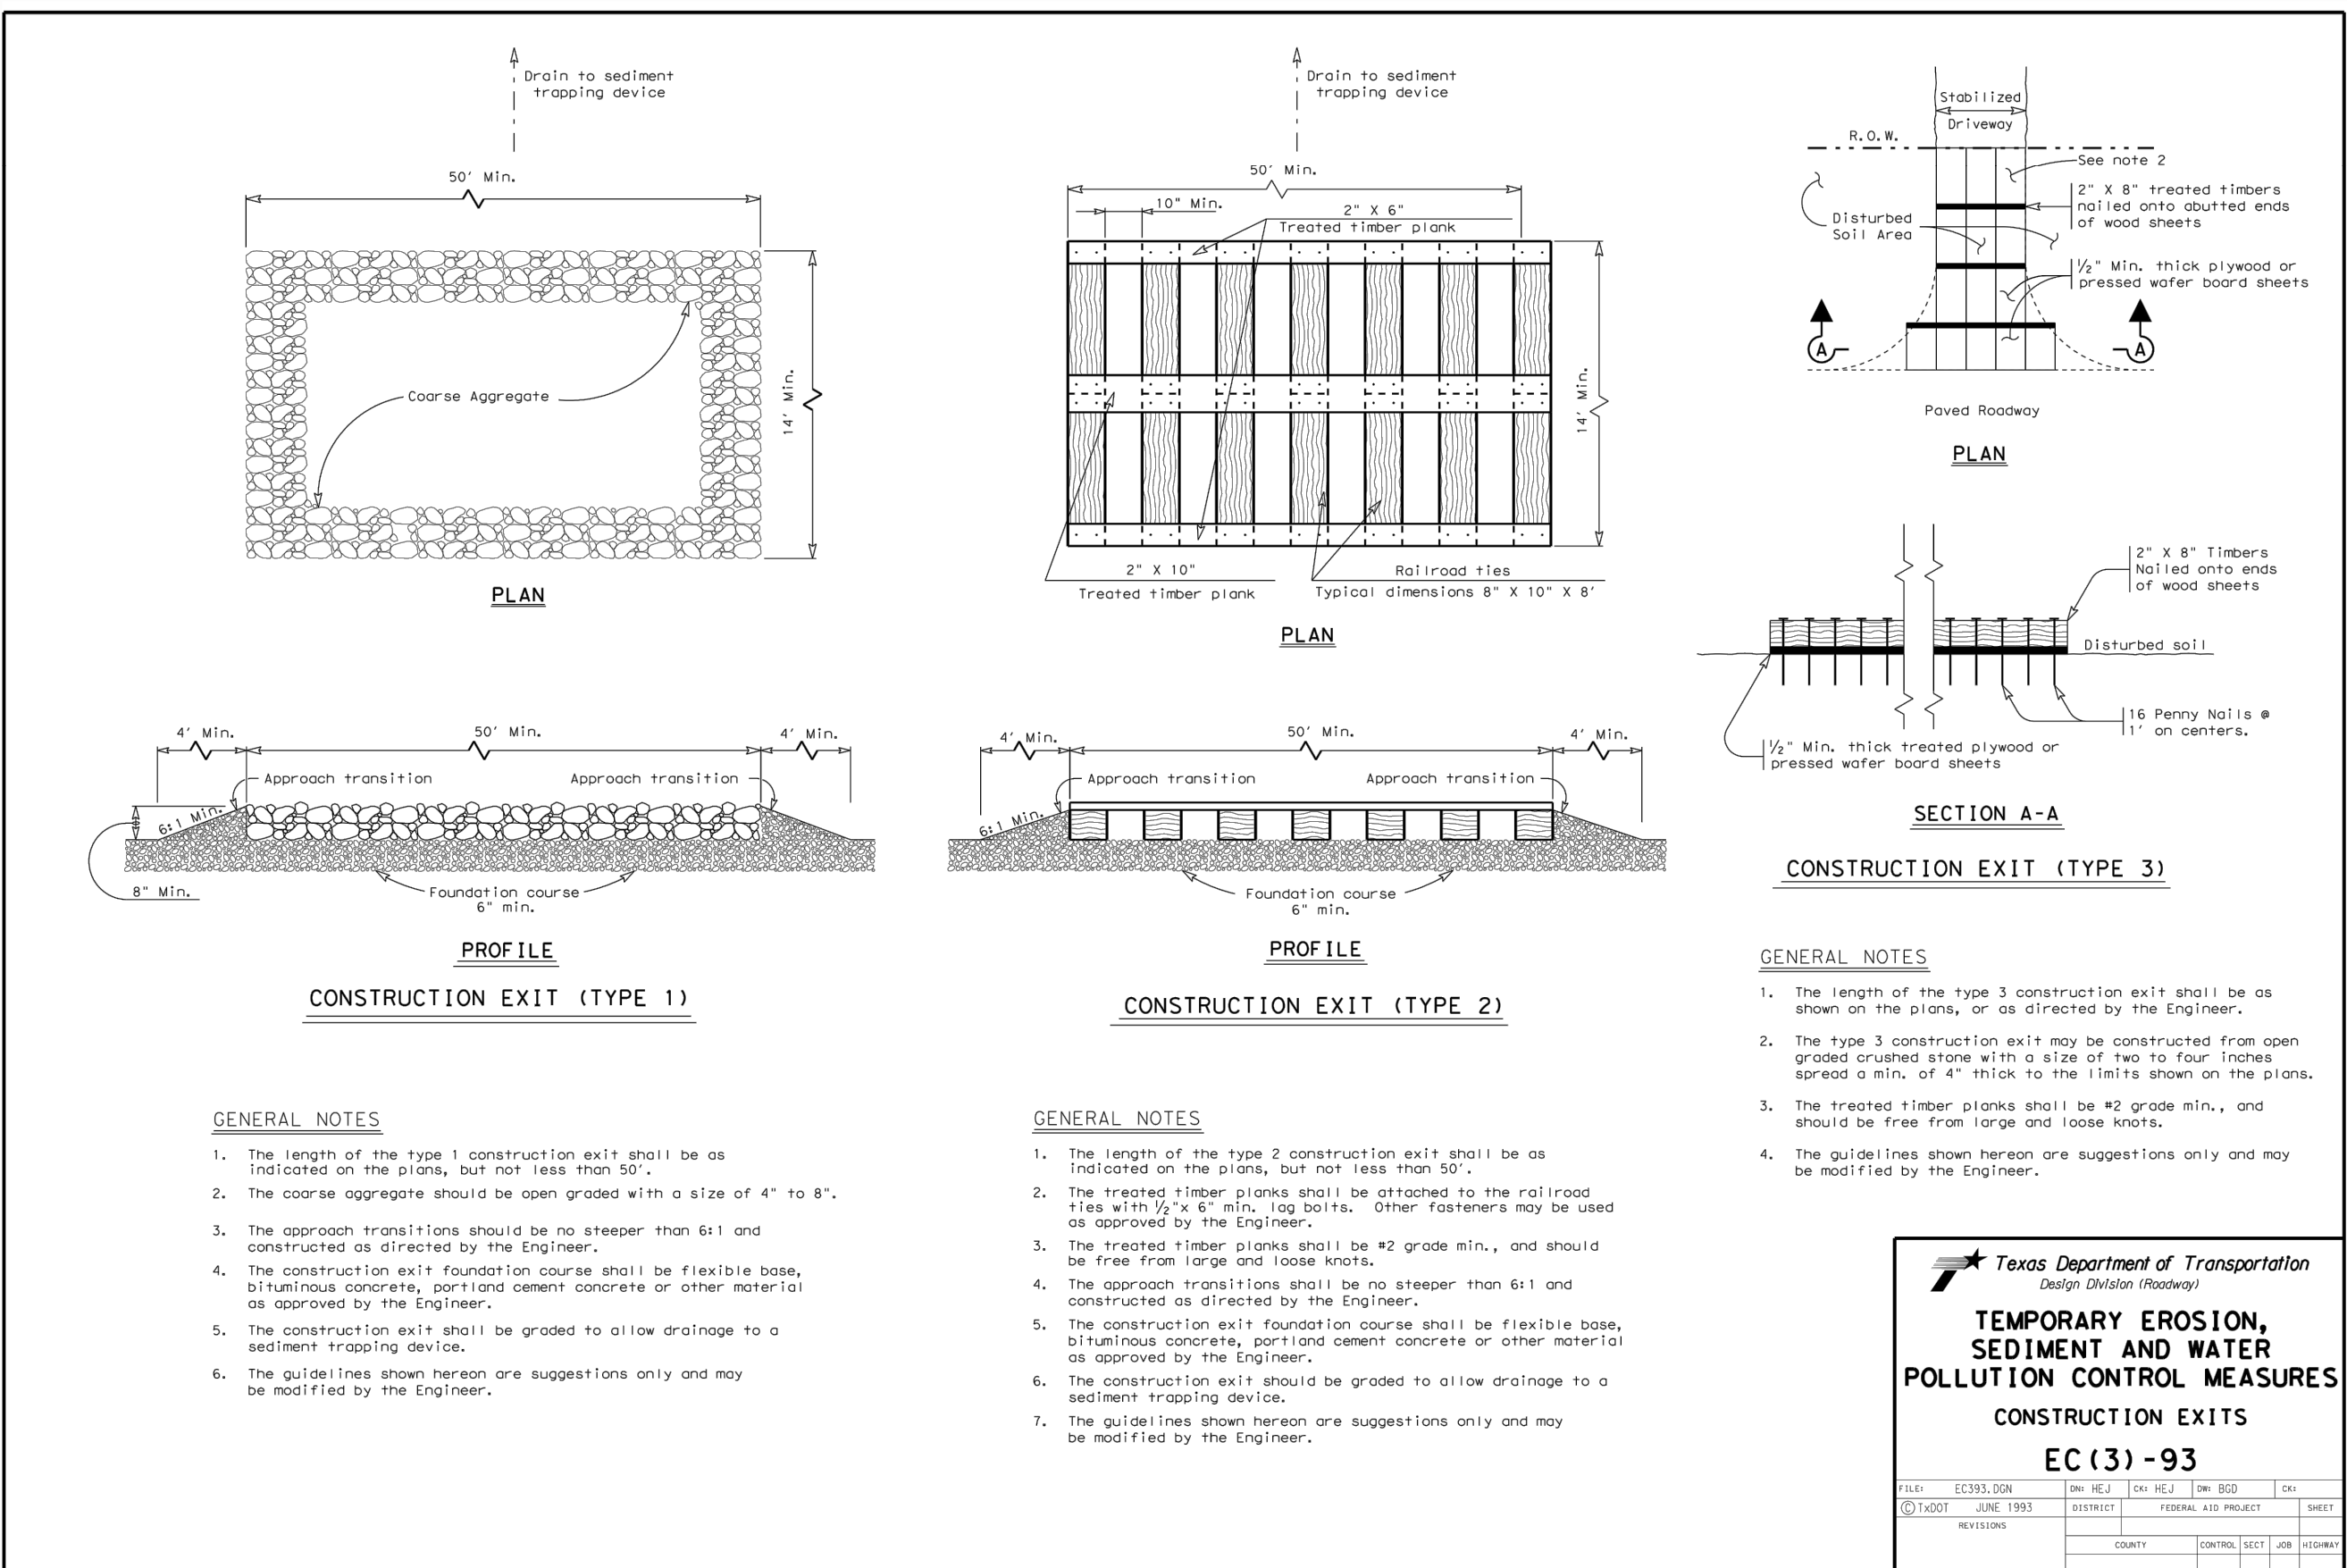



## Texas Commission on Environmental Quality

### Construction Notice of Intent

#### Site Information (Regulated Entity)

What is the name of the site to be authorized?	Serenity Oaks Subdivision, Unit 5
Does the site have a physical address?	No
Because there is no physical address, describe how to locate this site:	Located 2.4 miles east on Rebecca Creek Rd from the intersection with Hwy 281 North of Spring Branch Tx, Rt 1.4 miles south-southeast on Rayner Ranch Road
City	Spring Branch
State	TX
ZIP	78070
County	COMAL
Latitude (N) (##.#####)	29.89676
Longitude (W) (-###.#####)	-98.37012
Primary SIC Code	1521
Secondary SIC Code	
Primary NAICS Code	
Secondary NAICS Code	

#### Regulated Entity Site Information

What is the Regulated Entity's Number (RN)?	RN106475122
What is the name of the Regulated Entity (RE)?	SERENITY OAKS UNIT 3
Does the RE site have a physical address?	No
Because there is no physical address, describe how to locate this site:	2.4 MI E OF HWY 281 ON REBECCA CRK RD 1.4 ON RAYNO
City	SPRING BRANCH
State	TX
ZIP	78070
County	COMAL
Latitude (N) (##.#####)	
Longitude (W) (-###.#####)	
Facility NAICS Code	236115
What is the primary business of this entity?	SINGLE FAMILY RESIDENTIAL

#### Customer (Applicant) Information

How is this applicant associated with this site?	Operator
What is the applicant's Customer Number (CN)?	CN603643685
Type of Customer	Corporation



**Full legal name of the applicant:**

Legal Name	Gale Estates, LLC
Texas SOS Filing Number	800739775
Federal Tax ID	
State Franchise Tax ID	32023056974
State Sales Tax ID	
Local Tax ID	
DUNS Number	
Number of Employees	0-20
Independently Owned and Operated?	Yes
I certify that the full legal name of the entity applying for this permit has been provided and is legally authorized to do business in Texas.	Yes

**Responsible Authority Contact**

Organization Name	Gale Estates, LLC
Prefix	MR
First	Jason
Middle	
Last	Gale
Suffix	
Credentials	
Title	President

**Responsible Authority Mailing Address**

Enter new address or copy one from list:

Address Type	Domestic
Mailing Address (include Suite or Bldg. here, if applicable)	15315 SAN PEDRO AVE
Routing (such as Mail Code, Dept., or Attn:)	
City	SAN ANTONIO
State	TX
ZIP	78232
Phone (###-###-####)	2104945237
Extension	
Alternate Phone (###-###-####)	
Fax (###-###-####)	
E-mail	acs1@satx.rr.com

## Application Contact

**Person TCEQ should contact for questions about this application:**

Same as another contact?	
Organization Name	Gallegos Engineering
Prefix	



First	Richard
Middle	Michael
Last	Gallegos
Suffix	
Credentials	
Title	President
Enter new address or copy one from list:	
<b>Mailing Address</b>	
Address Type	Domestic
Mailing Address (include Suite or Bldg. here, if applicable)	101 FAWN DR
Routing (such as Mail Code, Dept., or Attn:)	
City	SHAVANO PARK
State	TX
ZIP	78231
Phone (###-###-####)	2108344563
Extension	
Alternate Phone (###-###-####)	
Fax (###-###-####)	
E-mail	rg@gallegoseng.com

## CNOI General Characteristics

1 Is the project or site located on Indian Country Lands?	No
2 Is the project or site associated to a facility that is licensed for the storage of high-level radioactive waste by the United States Nuclear Regulatory Commission under 10 CFR Part 72?	No
3 Is your construction activity associated with an oil and gas exploration, production, processing, or treatment, or transmission facility?	No
4 Is the project or site associated to a quarrying facility that is located within either the John Graves Scenic Riverway or Coke Stevenson Scenic Riverway, as defined in 30 TAC 311.71?	No
5 What is the Primary Standard Industrial Classification (SIC) Code that best describes the construction activity being conducted at the site?	1521
6 If applicable, what is the Secondary SIC Code(s)?	
7 What is the total number of acres that the construction project or site will disturb under the control of the primary operator?	65.15
8 What is the construction project or site type?	Single-family residential
9 Is the project part of a larger common plan of development or sale?	Yes
10 What is the estimated start date of the project?	01/06/2025
11 What is the estimated end date of the project?	12/31/2025
12 Will concrete truck washout be performed at the site?	Yes
13 What is the name of the first water body(s) to receive the stormwater runoff or potential runoff from the site?	Tributary of Guadalupe River



14 What is the segment number(s) of the classified water body(s) that the discharge will eventually reach?	1806
15 Is the discharge into a Municipal Separate Storm Sewer System (MS4)?	No
16 Is the discharge or potential discharge within the Recharge Zone, Contributing Zone, or Contributing Zone within the Transition Zone of the Edwards Aquifer, as defined in 30 TAC Chapter 213?	Yes
16.1 I certify that the copy of the TCEQ-approved Plan required by the Edwards Aquifer Rule (30 TAC Chapter 213) that is included or referenced in the Stormwater Pollution Prevention Plan will be implemented.	Yes
17 I certify that a stormwater pollution prevention plan (SWP3) has been developed, will be implemented prior to construction, and to the best of my knowledge and belief is compliant with any applicable local sediment and erosion control plans, as required in the general permit TXR150000. Note: For multiple operators who prepare a shared SWP3, the confirmation of an operator may be limited to its obligations under the SWP3 provided all obligations are confirmed by at least one operator.	Yes
18 I certify that I have obtained a copy and understand the terms and conditions of the Construction General Permit (TXR150000).	Yes
19 I understand that a Notice of Termination (NOT) must be submitted when this authorization is no longer needed.	Yes

## Certification

I certify that I am authorized under 30 Texas Administrative Code Subchapter 305.44 to sign this document and can provide documentation in proof of such authorization upon request.

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

1. I am Richard M Gallegos, the owner of the STEERS account ER086300.
2. I have the authority to sign this data on behalf of the applicant named above.
3. I have personally examined the foregoing and am familiar with its content and the content of any attachments, and based upon my personal knowledge and/or inquiry of any individual responsible for information contained herein, that this information is true, accurate, and complete.
4. I further certify that I have not violated any term in my TCEQ STEERS participation agreement and that I have no reason to believe that the confidentiality or use of my password has been compromised at any time.
5. I understand that use of my password constitutes an electronic signature legally equivalent to my written signature.
6. I also understand that the attestations of fact contained herein pertain to the implementation, oversight and enforcement of a state and/or federal environmental program and must be true and complete to the best of my knowledge.
7. I am aware that criminal penalties may be imposed for statements or omissions that I know or have reason to believe are untrue or misleading.
8. I am knowingly and intentionally signing Construction Notice of Intent.
9. My signature indicates that I am in agreement with the information on this form, and authorize its submittal to the TCEQ.

OPERATOR Signature: Richard M Gallegos OPERATOR



Customer Number:	CN603643685
Legal Name:	Gale Estates, LLC
Account Number:	ER086300
Signature IP Address:	24.162.10.57
Signature Date:	2025-01-06
Signature Hash:	68998B14339AF35C48BB522D85F9B14E567EDB327AA4D5FA6EE8F4EAD512FAF8
Form Hash Code at time of Signature:	D3431B7645CC5CB56287EF53764A1EDEDE94D38AA41A0CE72028F6AB5691D781

## Fee Payment

Transaction by:	The application fee payment transaction was made by ER086300/Richard M Gallegos
Paid by:	The application fee was paid by RICHARD MICHAEL GALLEGOS
Fee Amount:	\$225.00
Paid Date:	The application fee was paid on 2025-01-06
Transaction/Voucher number:	The transaction number is 582EA000641976 and the voucher number is 739141

## Submission

Reference Number:	The application reference number is 742251
Submitted by:	The application was submitted by ER086300/Richard M Gallegos
Submitted Timestamp:	The application was submitted on 2025-01-06 at 14:33:24 CST
Submitted From:	The application was submitted from IP address 24.162.10.57
Confirmation Number:	The confirmation number is 616454
Steers Version:	The STEERS version is 6.85

## Additional Information

Application Creator: This account was created by Richard M Gallegos



Bobby Janecka, *Commissioner*  
Catarina R. Gonzales, *Commissioner*  
Kelly Keel, *Executive Director*



## TEXAS COMMISSION ON ENVIRONMENTAL QUALITY

*Protecting Texas by Reducing and Preventing Pollution*

January 6, 2025

Dear Applicant:

Re: TPDES General Permit for Construction Stormwater Runoff (TXR150000)  
Notice of Intent Authorization

Your Notice of Intent (NOI) application for authorization under the general permit for discharge of stormwater associated with construction activities has been received. Pursuant to authorization from the Executive Director of the Texas Commission on Environmental Quality, the Division Deputy Director of the Water Quality Division has issued the enclosed Certificate.

Please refer to the attached certificate for the authorization number that was assigned to your project/site and the effective date. Please use this number to reference this project/site for future communications with the Texas Commission on Environmental Quality (TCEQ).

Authorization under the Edwards Aquifer Protection Program is required before construction can begin where the site is located within the Edwards Aquifer Recharge Zone, Contributing Zone, or Contributing Zone within the Transition Zone. See <https://www.tceq.texas.gov/permitting/eapp/viewer.html> for additional information.

**It is the responsibility of the Operator to notify the TCEQ Stormwater Processing Center of any change in address supplied on the original Notice of Intent by submitting a Notice of Change.**

A Notice of Termination must be submitted when permit coverage is no longer needed.

For questions related to processing of your application you may contact the Stormwater Processing Center by email at [SWPERMIT@tceq.texas.gov](mailto:SWPERMIT@tceq.texas.gov) or by telephone at (512) 239-3700. If you have any technical questions regarding the general permit, you may contact the stormwater technical staff by email at [SWGPA@tceq.texas.gov](mailto:SWGPA@tceq.texas.gov) or by telephone at (512) 239-4671. Also, you may obtain information on the stormwater web site at <https://www.tceq.texas.gov/permitting/stormwater>.

Sincerely,

A handwritten signature in black ink, appearing to read "R. Sadlier", with a long, sweeping horizontal line extending to the right.

Robert Sadlier, Deputy Director  
Water Quality Division





**TEXAS COMMISSION ON ENVIRONMENTAL QUALITY**  
**Texas Pollutant Discharge Elimination System**  
**Stormwater Construction General Permit**

The Notice of Intent (NOI) for the facility listed below was received on January 6, 2025. The intent to discharge stormwater associated with construction activity under the terms and conditions imposed by the Texas Pollutant Discharge Elimination System (TPDES) stormwater Construction General Permit (CGP) TXR150000 is acknowledged. Your facility's unique TPDES CGP stormwater authorization number is:

**TXR1534TE**

Coverage Effective: January 06, 2025

The TCEQ's stormwater CGP requires certain stormwater pollution prevention and control measures, possible monitoring and reporting, and periodic inspections. Among the conditions and requirements of this permit, you must have prepared and implemented a stormwater pollution prevention plan (SWP3) that is tailored to your construction site. As a facility authorized to discharge under the stormwater CGP, all terms and conditions must be complied with to maintain coverage and avoid possible penalties.

**Project/Site Information:**

RN106475122  
Serenity Oaks Subdivision Unit 5  
Located 2.4 Miles East On Rebecca Creek Rd From The Intersection  
With Hwy 281 North of Spring Branch Tx, Rt 1.4 Miles South-  
Southeast On Rayner Ranch Road  
Spring Branch, TX 78070  
Comal County

**Operator:**

CN603643685  
Gale Estates, LLC  
15315 San Pedro Ave  
San Antonio, TX 78232

**This CGP and all authorizations expire on March 5, 2028, unless otherwise amended.** If you have any questions related to processing of your application, you may contact the Stormwater Processing Center by **email at [SWPERMIT@tceq.texas.gov](mailto:SWPERMIT@tceq.texas.gov) or by telephone at (512) 239-3700**. For technical issues, you may contact the stormwater technical staff by **email at [SWGP@tceq.texas.gov](mailto:SWGP@tceq.texas.gov) or by telephone at (512) 239-4671**. Also, you may obtain information on the TCEQ web site at <https://www.tceq.texas.gov/goto/wq-dpa>. A copy of this document should be kept with your SWP3.

A handwritten signature in black ink, appearing to read "K. Keel".

Issued Date: January 06, 2025

---

FOR THE COMMISSION



**Agent Authorization Form**  
For Required Signature  
Edwards Aquifer Protection Program  
Relating to 30 TAC Chapter 213  
Effective June 1, 1999

I Jason Gale,  
Print Name  
President,  
Title - Owner/President/Other  
of Gale Estates, LLC,  
Corporation/Partnership/Entity Name  
have authorized Richard M. Gallegos, P.E.,  
Print Name of Agent/Engineer  
of Gallegos Engineering, Inc.,  
Print Name of Firm

to represent and act on the behalf of the above named Corporation, Partnership, or Entity for the purpose of preparing and submitting this plan application to the Texas Commission on Environmental Quality (TCEQ) for the review and approval consideration of regulated activities.

I also understand that:

1. The applicant is responsible for compliance with 30 Texas Administrative Code Chapter 213 and any condition of the TCEQ's approval letter. The TCEQ is authorized to assess administrative penalties of up to \$10,000 per day per violation.
2. For those submitting an application who are not the property owner, but who have the right to control and possess the property, additional authorization is required from the owner.
3. Application fees are due and payable at the time the application is submitted. The application fee must be sent to the TCEQ cashier or to the appropriate regional office. The application will not be considered until the correct fee is received by the commission.
4. A notarized copy of the Agent Authorization Form must be provided for the person preparing the application, and this form must accompany the completed application.
5. No person shall commence any regulated activity on the Edwards Aquifer Recharge Zone, Contributing Zone or Transition Zone until the appropriate application for the activity has been filed with and approved by the Executive Director.

SIGNATURE PAGE:


[Signature]  
Applicant's Signature

1-2-2025  
Date

THE STATE OF Texas §  
County of Brewer §

BEFORE ME, the undersigned authority, on this day personally appeared Jason Gale known to me to be the person whose name is subscribed to the foregoing instrument, and acknowledged to me that (s)he executed same for the purpose and consideration therein expressed.

GIVEN under my hand and seal of office on this 2<sup>nd</sup> day of January, 2025



Lidia S. Ortega  
NOTARY PUBLIC  
Lidia S. Ortega  
Typed or Printed Name of Notary

MY COMMISSION EXPIRES: 02-07-2027



# Application Fee Form

## Texas Commission on Environmental Quality

Name of Proposed Regulated Entity: SERENITY OAKS SUBDIVISION, UNIT 5

Regulated Entity Location: 15315 SAN PEDRO, SAN ANTONIO, TX 78232

Name of Customer: GALE ESTATES, LLC

Contact Person: JASON GALE

Phone: 210-494-5237

Customer Reference Number (if issued): CN 603643685

Regulated Entity Reference Number (if issued): RN 105893432

### Austin Regional Office (3373)

☐ Hays

☐ Travis

☐ Williamson

### San Antonio Regional Office (3362)

☐ Bexar

☐ Medina

☐ Uvalde

☒ Comal

☐ Kinney

Application fees must be paid by check, certified check, or money order, payable to the **Texas Commission on Environmental Quality**. Your canceled check will serve as your receipt. **This form must be submitted with your fee payment.** This payment is being submitted to:

☐ Austin Regional Office

☒ San Antonio Regional Office

☐ Mailed to: TCEQ - Cashier

☐ Overnight Delivery to: TCEQ - Cashier

Revenues Section

Mail Code 214

P.O. Box 13088

Austin, TX 78711-3088

12100 Park 35 Circle

Building A, 3rd Floor

Austin, TX 78753

(512)239-0357

### Site Location (Check All That Apply):

☐ Recharge Zone

☒ Contributing Zone

☐ Transition Zone

<i>Type of Plan</i>	<i>Size</i>	<i>Fee Due</i>
Water Pollution Abatement Plan, Contributing Zone Plan: One Single Family Residential Dwelling	Acres	\$
Water Pollution Abatement Plan, Contributing Zone Plan: Multiple Single Family Residential and Parks	65.15 Acres	\$ 6,500
Water Pollution Abatement Plan, Contributing Zone Plan: Non-residential	Acres	\$
Sewage Collection System	L.F.	\$
Lift Stations without sewer lines	Acres	\$
Underground or Aboveground Storage Tank Facility	Tanks	\$
Piping System(s)(only)	Each	\$
Exception	1 Each	\$
Extension of Time	Each	\$

Signature: \_\_\_\_\_

Date: January 5, 2025



# Application Fee Schedule

Texas Commission on Environmental Quality

Edwards Aquifer Protection Program 30 TAC Chapter 213 (effective 05/01/2008)

## ***Water Pollution Abatement Plans and Modifications***

### ***Contributing Zone Plans and Modifications***

<b><i>Project</i></b>	<b><i>Project Area in Acres</i></b>	<b><i>Fee</i></b>
One Single Family Residential Dwelling	< 5	\$650
Multiple Single Family Residential and Parks	< 5	\$1,500
	5 < 10	\$3,000
	10 < 40	\$4,000
	40 < 100	\$6,500
	100 < 500	\$8,000
	≥ 500	\$10,000
Non-residential (Commercial, industrial, institutional, multi-family residential, schools, and other sites where regulated activities will occur)	< 1	\$3,000
	1 < 5	\$4,000
	5 < 10	\$5,000
	10 < 40	\$6,500
	40 < 100	\$8,000
	≥ 100	\$10,000

### ***Organized Sewage Collection Systems and Modifications***

<b><i>Project</i></b>	<b><i>Cost per Linear Foot</i></b>	<b><i>Minimum Fee- Maximum Fee</i></b>
Sewage Collection Systems	\$0.50	\$650 - \$6,500

### ***Underground and Aboveground Storage Tank System Facility Plans and Modifications***

<b><i>Project</i></b>	<b><i>Cost per Tank or Piping System</i></b>	<b><i>Minimum Fee- Maximum Fee</i></b>
Underground and Aboveground Storage Tank Facility	\$650	\$650 - \$6,500

### ***Exception Requests***

<b><i>Project</i></b>	<b><i>Fee</i></b>
Exception Request	\$500

### ***Extension of Time Requests***

<b><i>Project</i></b>	<b><i>Fee</i></b>
Extension of Time Request	\$150





**GALLEGOS ENGINEERING, INC.**

P.O. BOX 690067  
SAN ANTONIO, TEXAS 78269

210-641-0812 PH

January 20, 2025

**CHECK OR PAYMENT FOR CZP REVIEW  
SERENITY OAKS, UNIT 5**

Payment will be made via online payment per TCEQ website.



# TCEQ Core Data Form

For detailed instructions on completing this form, please read the Core Data Form Instructions or call 512-239-5175.

## SECTION I: General Information

<b>1. Reason for Submission</b> (If other is checked please describe in space provided.)		
<input checked="" type="checkbox"/> New Permit, Registration or Authorization (Core Data Form should be submitted with the program application.)		
<input type="checkbox"/> Renewal (Core Data Form should be submitted with the renewal form)		<input type="checkbox"/> Other
<b>2. Customer Reference Number</b> (if issued)	<a href="#">Follow this link to search for CN or RN numbers in Central Registry**</a>	<b>3. Regulated Entity Reference Number</b> (if issued)
CN 603643685		RN 106475122

## SECTION II: Customer Information

<b>4. General Customer Information</b>		<b>5. Effective Date for Customer Information Updates</b> (mm/dd/yyyy)							
<input type="checkbox"/> New Customer <input checked="" type="checkbox"/> Update to Customer Information <input type="checkbox"/> Change in Regulated Entity Ownership									
<input type="checkbox"/> Change in Legal Name (Verifiable with the Texas Secretary of State or Texas Comptroller of Public Accounts)									
<i>The Customer Name submitted here may be updated automatically based on what is current and active with the Texas Secretary of State (SOS) or Texas Comptroller of Public Accounts (CPA).</i>									
<b>6. Customer Legal Name</b> (If an individual, print last name first: eg: Doe, John)			<i>If new Customer, enter previous Customer below:</i>						
Gale Estates, LLC									
<b>7. TX SOS/CPA Filing Number</b>	<b>8. TX State Tax ID</b> (11 digits)	<b>9. Federal Tax ID</b> (9 digits) 208039985	<b>10. DUNS Number</b> (if applicable)						
<b>11. Type of Customer:</b>		<input checked="" type="checkbox"/> Corporation <input type="checkbox"/> Individual Partnership: <input type="checkbox"/> General <input type="checkbox"/> Limited							
Government: <input type="checkbox"/> City <input type="checkbox"/> County <input type="checkbox"/> Federal <input type="checkbox"/> Local <input type="checkbox"/> State <input type="checkbox"/> Other		<input type="checkbox"/> Sole Proprietorship <input type="checkbox"/> Other:							
<b>12. Number of Employees</b>		<b>13. Independently Owned and Operated?</b>							
<input checked="" type="checkbox"/> 0-20 <input type="checkbox"/> 21-100 <input type="checkbox"/> 101-250 <input type="checkbox"/> 251-500 <input type="checkbox"/> 501 and higher		<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No							
<b>14. Customer Role</b> (Proposed or Actual) – as it relates to the Regulated Entity listed on this form. Please check one of the following									
<input checked="" type="checkbox"/> Owner <input type="checkbox"/> Operator <input type="checkbox"/> Owner & Operator <input type="checkbox"/> Other: <input type="checkbox"/> Occupational Licensee <input type="checkbox"/> Responsible Party <input type="checkbox"/> VCP/BSA Applicant									
<b>15. Mailing Address:</b>	15315 San Pedro								
	City	San Antonio	State	TX	ZIP	78232	ZIP + 4	3719	
<b>16. Country Mailing Information</b> (if outside USA)					<b>17. E-Mail Address</b> (if applicable)				
					acs1@satx.rr.com				



<b>18. Telephone Number</b> ( 210 ) 494-5237	<b>19. Extension or Code</b>	<b>20. Fax Number (if applicable)</b> ( 210 ) 494-0913
---	------------------------------	---

## SECTION III: Regulated Entity Information

<b>21. General Regulated Entity Information</b> (If 'New Regulated Entity' is selected, a new permit application is also required.)								
<input checked="" type="checkbox"/> New Regulated Entity <input type="checkbox"/> Update to Regulated Entity Name <input type="checkbox"/> Update to Regulated Entity Information								
<i>The Regulated Entity Name submitted may be updated, in order to meet TCEQ Core Data Standards (removal of organizational endings such as Inc, LP, or LLC).</i>								
<b>22. Regulated Entity Name</b> (Enter name of the site where the regulated action is taking place.)								
Serenity Oaks Subdivision, Unit 5								
<b>23. Street Address of the Regulated Entity:</b>  (No PO Boxes)	Unassigned							
	City		State		ZIP		ZIP + 4	
<b>24. County</b>								

If no Street Address is provided, fields 25-28 are required.

<b>25. Description to Physical Location:</b>	Located 2.4 miles east on Rebecca Ck. Rd. from intersection of Hwy 281 North of Spring Branch, TX, Rt. 1.4 miles south-southeast on Rayner Ranch Blvd.							
<b>26. Nearest City</b>					<b>State</b>	<b>Nearest ZIP Code</b>		
Spring Branch					TX	78070		
<i>Latitude/Longitude are required and may be added/updated to meet TCEQ Core Data Standards. (Geocoding of the Physical Address may be used to supply coordinates where none have been provided or to gain accuracy).</i>								
<b>27. Latitude (N) In Decimal:</b>		29.89676N			<b>28. Longitude (W) In Decimal:</b>		98.37012W	
Degrees	Minutes	Seconds	Degrees	Minutes	Seconds			
<b>29. Primary SIC Code</b> (4 digits)	<b>30. Secondary SIC Code</b> (4 digits)		<b>31. Primary NAICS Code</b> (5 or 6 digits)		<b>32. Secondary NAICS Code</b> (5 or 6 digits)			
1521	None		236115		None			
<b>33. What is the Primary Business of this entity?</b> (Do not repeat the SIC or NAICS description.)								
General Contractors - Single-Family Home								
<b>34. Mailing Address:</b>	Gale Estates, LLC							
	15315 San Pedro							
	City	San Antonio	State	TX	ZIP	78232	ZIP + 4	3719
<b>35. E-Mail Address:</b>	acs1@satx.rr.com							
<b>36. Telephone Number</b>	<b>37. Extension or Code</b>				<b>38. Fax Number (if applicable)</b>			
( 210 ) 494-5237					( 210 ) 494-913			

**39. TCEQ Programs and ID Numbers** Check all Programs and write in the permits/registration numbers that will be affected by the updates submitted on this form. See the Core Data Form instructions for additional guidance.


<input type="checkbox"/> Dam Safety	<input type="checkbox"/> Districts	<input checked="" type="checkbox"/> Edwards Aquifer	<input type="checkbox"/> Emissions Inventory Air	<input type="checkbox"/> Industrial Hazardous Waste
<input type="checkbox"/> Municipal Solid Waste	<input type="checkbox"/> New Source Review Air	<input type="checkbox"/> OSSF	<input type="checkbox"/> Petroleum Storage Tank	<input type="checkbox"/> PWS
<input type="checkbox"/> Sludge	<input type="checkbox"/> Storm Water	<input type="checkbox"/> Title V Air	<input type="checkbox"/> Tires	<input type="checkbox"/> Used Oil
<input type="checkbox"/> Voluntary Cleanup	<input type="checkbox"/> Wastewater	<input type="checkbox"/> Wastewater Agriculture	<input type="checkbox"/> Water Rights	<input type="checkbox"/> Other:

## **SECTION IV: Preparer Information**

<b>40. Name:</b>	Richard M. Gallegos, P.E.	<b>41. Title:</b>	President
<b>42. Telephone Number</b>	<b>43. Ext./Code</b>	<b>44. Fax Number</b>	<b>45. E-Mail Address</b>
( 210 ) 641-0812		( ) -	rg@gallegoseng.com

## **SECTION V: Authorized Signature**

**46.** By my signature below, I certify, to the best of my knowledge, that the information provided in this form is true and complete, and that I have signature authority to submit this form on behalf of the entity specified in Section II, Field 6 and/or as required for the updates to the ID numbers identified in field 39.

<b>Company:</b>	Gallegos Engineering, Inc.	<b>Job Title:</b>	President
<b>Name (In Print):</b>	Richard M. Gallegos	<b>Phone:</b>	( 210 ) 641- 0812
<b>Signature:</b>		<b>Date:</b>	1/5/25
