

CONTRIBUTING ZONE PLAN EXCEPTION REQUEST FOR C.I.S.D. SMITHSON VALLEY HIGH SCHOOL

PREPARED FOR:



JUNE 2024

PREPARED BY:



- *Engineers*
- *Surveyors*
- *Planners*

Moy Tarin Ramirez Engineers, LLC

12770 Cimarron Path, Suite 100 San Antonio, Texas 78249

TBPE Firm #5297 • TBPLS Firm #10131500

Phone 210-698-5051 • Fax 210-698-5085

C.I.S.D. SMITHSON VALLEY HIGH SCHOOL CONTRIBUTING ZONE PLAN EXCEPTION REQUEST

TABLE OF CONTENTS

I. EDWARDS AQUIFER APPLICATION COVER

II. CONTRIBUTING ZONE EXCEPTION REQUEST FORM

- a. ATTACHMENT A – ROAD MAP
- b. ATTACHMENT B – USGS QUADRANGLE MAP
- c. ATTACHMENT C – PROJECT NARRATIVE
- d. ATTACHMENT D – NATURE OF EXCEPTION
- e. ATTACHMENT E – EQUIVALENT WATER QUALITY PROTECTION

III. TEMPORARY STORMWATER SECTION

- a. ATTACHMENT A – SPILL RESPONSE ACTIONS
- b. ATTACHMENT B – POTENTIAL SOURCES OF CONTAMINATION
- c. ATTACHMENT C – SEQUENCE OF MAJOR ACTIVITIES
- d. ATTACHMENT D – TEMPORARY BEST MANAGEMENT PRACTICES AND MEASURES
- e. ATTACHMENT F – STRUCTURAL PRACTICES
- f. ATTACHMENT G – DRAINAGE AREA MAP
- g. ATTACHMENT I – INSPECTION AND MAINTENANCE FOR BMPs
- h. ATTACHMENT J – SCHEDULE OF INTERIM AND PERMANENT SOIL STABILIZATION PRACTICES

IV. CONSTRUCTION PLANS

V. AGENT AUTHORIZATION FORM

VI. APPLICATION FEE FORM

VII. TCEQ CORE DATA FORM

Texas Commission on Environmental Quality

Edwards Aquifer Application Cover Page

Our Review of Your Application

The Edwards Aquifer Program staff conducts an administrative and technical review of all applications. The turnaround time for administrative review can be up to 30 days as outlined in 30 TAC 213.4(e). Generally administrative completeness is determined during the intake meeting or within a few days of receipt. The turnaround time for technical review of an administratively complete Edwards Aquifer application is 90 days as outlined in 30 TAC 213.4(e). Please know that the review and approval time is directly impacted by the quality and completeness of the initial application that is received. In order to conduct a timely review, it is imperative that the information provided in an Edwards Aquifer application include final plans, be accurate, complete, and in compliance with [30 TAC 213](#).

Administrative Review

1. [Edwards Aquifer applications](#) must be deemed administratively complete before a technical review can begin. To be considered administratively complete, the application must contain completed forms and attachments, provide the requested information, and meet all the site plan requirements. The submitted application and plan sheets should be final plans. Please submit one full-size set of plan sheets with the original application, and half-size sets with the additional copies.

To ensure that all applicable documents are included in the application, the program has developed tools to guide you and web pages to provide all forms, checklists, and guidance. Please visit the below website for assistance: <http://www.tceq.texas.gov/field/eapp>.

2. This Edwards Aquifer Application Cover Page form (certified by the applicant or agent) must be included in the application and brought to the administrative review meeting.
3. Administrative reviews are scheduled with program staff who will conduct the review. Applicants or their authorized agent should call the appropriate regional office, according to the county in which the project is located, to schedule a review. The average meeting time is one hour.
4. In the meeting, the application is examined for administrative completeness. Deficiencies will be noted by staff and emailed or faxed to the applicant and authorized agent at the end of the meeting, or shortly after. Administrative deficiencies will cause the application to be deemed incomplete and returned.

An appointment should be made to resubmit the application. The application is re-examined to ensure all deficiencies are resolved. The application will only be deemed administratively complete when all administrative deficiencies are addressed.

5. If an application is received by mail, courier service, or otherwise submitted without a review meeting, the administrative review will be conducted within 30 days. The applicant and agent will be contacted with the results of the administrative review. If the application is found to be administratively incomplete, it can be retrieved from the regional office or returned by regular mail. If returned by mail, the regional office may require arrangements for return shipping.
6. If the geologic assessment was completed before October 1, 2004 and the site contains “possibly sensitive” features, the assessment must be updated in accordance with the *Instructions to Geologists* (TCEQ-0585 Instructions).

Technical Review

1. When an application is deemed administratively complete, the technical review period begins. The regional office will distribute copies of the application to the identified affected city, county, and groundwater conservation district whose jurisdiction includes the subject site. These entities and the public have 30 days to provide comments on the application to the regional office. All comments received are reviewed by TCEQ.

2. A site assessment is usually conducted as part of the technical review, to evaluate the geologic assessment and observe existing site conditions. The site must be accessible to our staff. The site boundaries should be clearly marked, features identified in the geologic assessment should be flagged, roadways marked and the alignment of the Sewage Collection System and manholes should be staked at the time the application is submitted. If the site is not marked the application may be returned.
3. We evaluate the application for technical completeness and contact the applicant and agent via Notice of Deficiency (NOD) to request additional information and identify technical deficiencies. There are two deficiency response periods available to the applicant. There are 14 days to resolve deficiencies noted in the first NOD. If a second NOD is issued, there is an additional 14 days to resolve deficiencies. If the response to the second notice is not received, is incomplete or inadequate, or provides new information that is incomplete or inadequate, the application must be withdrawn or if not withdrawn the application will be denied and the application fee will be forfeited.
4. The program has 90 calendar days to complete the technical review of the application. If the application is technically adequate, such that it complies with the Edwards Aquifer rules, and is protective of the Edwards Aquifer during and after construction, an approval letter will be issued. Construction or other regulated activity may not begin until an approval is issued.

Mid-Review Modifications

It is important to have final site plans prior to beginning the permitting process with TCEQ to avoid delays.

Occasionally, circumstances arise where you may have significant design and/or site plan changes after your Edwards Aquifer application has been deemed administratively complete by TCEQ. This is considered a "Mid-Review Modification". Mid-Review Modifications may require redistribution of an application that includes the proposed modifications for public comment.

If you are proposing a Mid-Review Modification, two options are available to you:

- You can withdraw your application, and your fees will be refunded or credited for a resubmittal.
- TCEQ can continue the technical review of the application as it was submitted, and a modification application can be submitted at a later time.

If the application is withdrawn, the resubmitted application will be subject to the administrative and technical review processes and will be treated as a new application. The application will be redistributed to the effected jurisdictions.

Please contact the regional office if you have questions. If your project is located in Williamson, Travis, or Hays County, contact TCEQ's Austin Regional Office at 512-339-2929. If your project is in Comal, Bexar, Medina, Uvalde, or Kinney County, contact TCEQ's San Antonio Regional Office at 210-490-3096

Please fill out all required fields below and submit with your application.

1. Regulated Entity Name: Cisd SMITHSON VALLEY HIGH SCHOOL					2. Regulated Entity No.: 103932638				
3. Customer Name: Comal ISD					4. Customer No.: 600249825				
5. Project Type: (Please circle/check one)	New	Modification			Extension	Exception			
6. Plan Type: (Please circle/check one)	WPAP	CZP	SCS	UST	AST	EXP	EXT	Technical Clarification	Optional Enhanced Measures
7. Land Use: (Please circle/check one)	Residential	Non-residential			8. Site (acres):			95.4 acres	
9. Application Fee:	\$500	10. Permanent BMP(s):				Existing (3) Extended Detention Ponds			
11. SCS (Linear Ft.):	N/A	12. AST/UST (No. Tanks):				N/A			
13. County:	Comal	14. Watershed:				Dripping Springs Creek			

Application Distribution

Instructions: Use the table below to determine the number of applications required. One original and one copy of the application, plus additional copies (as needed) for each affected incorporated city, county, and groundwater conservation district are required. Linear projects or large projects, which cross into multiple jurisdictions, can require additional copies. Refer to the "Texas Groundwater Conservation Districts within the EAPP Boundaries" map found at:

http://www.tceq.texas.gov/assets/public/compliance/field_ops/eapp/EAPP%20GWCD%20map.pdf

For more detailed boundaries, please contact the conservation district directly.

Austin Region			
County:	Hays	Travis	Williamson
Original (1 req.)	—	—	—
Region (1 req.)	—	—	—
County(ies)	—	—	—
Groundwater Conservation District(s)	<input type="checkbox"/> Edwards Aquifer Authority <input type="checkbox"/> Barton Springs/ Edwards Aquifer <input type="checkbox"/> Hays Trinity <input type="checkbox"/> Plum Creek	<input type="checkbox"/> Barton Springs/ Edwards Aquifer	NA
City(ies) Jurisdiction	<input type="checkbox"/> Austin <input type="checkbox"/> Buda <input type="checkbox"/> Dripping Springs <input type="checkbox"/> Kyle <input type="checkbox"/> Mountain City <input type="checkbox"/> San Marcos <input type="checkbox"/> Wimberley <input type="checkbox"/> Woodcreek	<input type="checkbox"/> Austin <input type="checkbox"/> Bee Cave <input type="checkbox"/> Pflugerville <input type="checkbox"/> Rollingwood <input type="checkbox"/> Round Rock <input type="checkbox"/> Sunset Valley <input type="checkbox"/> West Lake Hills	<input type="checkbox"/> Austin <input type="checkbox"/> Cedar Park <input type="checkbox"/> Florence <input type="checkbox"/> Georgetown <input type="checkbox"/> Jerrell <input type="checkbox"/> Leander <input type="checkbox"/> Liberty Hill <input type="checkbox"/> Pflugerville <input type="checkbox"/> Round Rock

San Antonio Region					
County:	Bexar	Comal	Kinney	Medina	Uvalde
Original (1 req.)	—	<u>X</u>	—	—	—
Region (1 req.)	—	<u>X</u>	—	—	—
County(ies)	—	<u>X</u>	—	—	—
Groundwater Conservation District(s)	<input type="checkbox"/> Edwards Aquifer Authority <input type="checkbox"/> Trinity-Glen Rose	<input checked="" type="checkbox"/> Edwards Aquifer Authority	<input type="checkbox"/> Kinney	<input type="checkbox"/> EAA <input type="checkbox"/> Medina	<input type="checkbox"/> EAA <input type="checkbox"/> Uvalde
City(ies) Jurisdiction	<input type="checkbox"/> Castle Hills <input type="checkbox"/> Fair Oaks Ranch <input type="checkbox"/> Helotes <input type="checkbox"/> Hill Country Village <input type="checkbox"/> Hollywood Park <input type="checkbox"/> San Antonio (SAWS) <input type="checkbox"/> Shavano Park	<input type="checkbox"/> Bulverde <input type="checkbox"/> Fair Oaks Ranch <input type="checkbox"/> Garden Ridge <input type="checkbox"/> New Braunfels <input type="checkbox"/> Schertz	NA	<input type="checkbox"/> San Antonio ETJ (SAWS)	NA

I certify that to the best of my knowledge, that the application is complete and accurate. This application is hereby submitted to TCEQ for administrative review and technical review.

Sean Smith, P.E.

Print Name of Customer/Authorized Agent

Signature of Customer/Authorized Agent

Date

6/17/24

****FOR TCEQ INTERNAL USE ONLY****

Date(s) Reviewed:		Date Administratively Complete:	
Received From:		Correct Number of Copies:	
Received By:		Distribution Date:	
EAPP File Number:		Complex:	
Admin. Review(s) (No.):		No. AR Rounds:	
Delinquent Fees (Y/N):		Review Time Spent:	
Lat./Long. Verified:		SOS Customer Verification:	
Agent Authorization Complete/Notarized (Y/N):		Fee Check:	Payable to TCEQ (Y/N):
Core Data Form Complete (Y/N):			Signed (Y/N):
Core Data Form Incomplete Nos.:			Less than 90 days old (Y/N):

Contributing Zone Exception Request Form

Texas Commission on Environmental Quality

for Regulated Activities on the Contributing Zone to the Edwards Aquifer and Relating to 30 TAC §213.24(1), Effective June 1, 1999

To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.

Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.

Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Contributing Zone Exception Request Form** is hereby submitted for TCEQ review and executive director approval. The request was prepared by:

Print Name of Customer/Agent: Sean Smith, P.E.

Date: 6/17/2024

Signature of Customer/Agent:



Regulated Entity Name: CISD SMITHSON VALLEY HIGH SCHOOL

Project Information

1. County: Comal
2. Stream Basin: Upper Cibolo Creek
3. Groundwater Conservation District (if applicable): Trinity Glen Rose
4. Customer (Applicant):

Contact Person: Jeffrey Smith

Entity: Comal Independent School District

Mailing Address: 1404 IH 35 North

City, State: New Braunfels, Texas

Telephone: (830) 221-2101

Email Address: jeffrey.smith@comalisd.org

Zip: 78130

Fax: _____

5. Agent/Representative (If any):

Contact Person: Sean Smith, P.E.

Entity: Moy Tarin Ramirez Engineers, LLC

Mailing Address: 12770 Cimarron Path, Suite 100

City, State: San Antonio, Texas

Zip: 78249

Telephone: (210) 698-5051

Fax: _____

Email Address: ssmith@mtrengineers.com

6. Project Location

☐ This project is inside the city limits of _____.

☐ This project is outside the city limits but inside the ETJ (extra-territorial jurisdiction) of _____.

☒ This project is not located within any city limits or ETJ.

7. ☒ The location of the project site is described below. Sufficient detail and clarity has been provided so that the TCEQ's Regional staff can easily locate the project and site boundaries for a field investigation.

The SmithsonValley High School campus is located approximately 1.5 miles east of the intersection of US 281 and SH-46 on the south side of SH-46.

8. ☒ **Attachment A - Road Map.** A road map showing directions to and location of the project site is attached. The map clearly shows the boundary of the project site.

9. ☒ **Attachment B - USGS Quadrangle Map.** A copy of the USGS Quadrangle Map (Scale: 1" = 2000') is attached. The map(s) should clearly show:

☒ Project site boundaries.

☒ USGS Quadrangle Name(s).

10. ☒ **Attachment C - Project Narrative.** A detailed narrative description of the proposed project is provided at the end of this form. The project description is consistent throughout the application and contains, at a minimum, the following details:

☒ Area of the site

☒ Offsite areas

☒ Impervious cover

☒ Permanent BMP(s)

☒ Proposed site use

☒ Site history

☒ Previous development

☒ Area(s) to be demolished

11. Existing project site conditions are noted below:

☐ Existing commercial site

☐ Existing industrial site


☐ Existing residential site

- ☐ Existing paved and/or unpaved roads
- ☐ Undeveloped (Cleared)
- ☐ Undeveloped (Undisturbed/Not cleared)
- ☒ Other: Existing High School


12. ☒ **Attachment D - Nature Of Exception.** A narrative description of the nature of each exception requested is attached. All provisions of 30 TAC §213 Subchapter B for which an exception is being requested have been identified in the description.
13. ☒ **Attachment E - Equivalent Water Quality Protection.** Documentation demonstrating equivalent water quality protection for surface streams which enter the Edwards Aquifer is attached.

Administrative Information

14. ☒ Submit one (1) original and one (1) copy of the application, plus additional copies as needed for each affected incorporated city, groundwater conservation district, and county in which the project will be located. The TCEQ will distribute the additional copies to these jurisdictions.
15. ☒ The applicant understands that prior approval under this section must be obtained from the executive director for the exception to be authorized.



SCALE: 1"=2000'

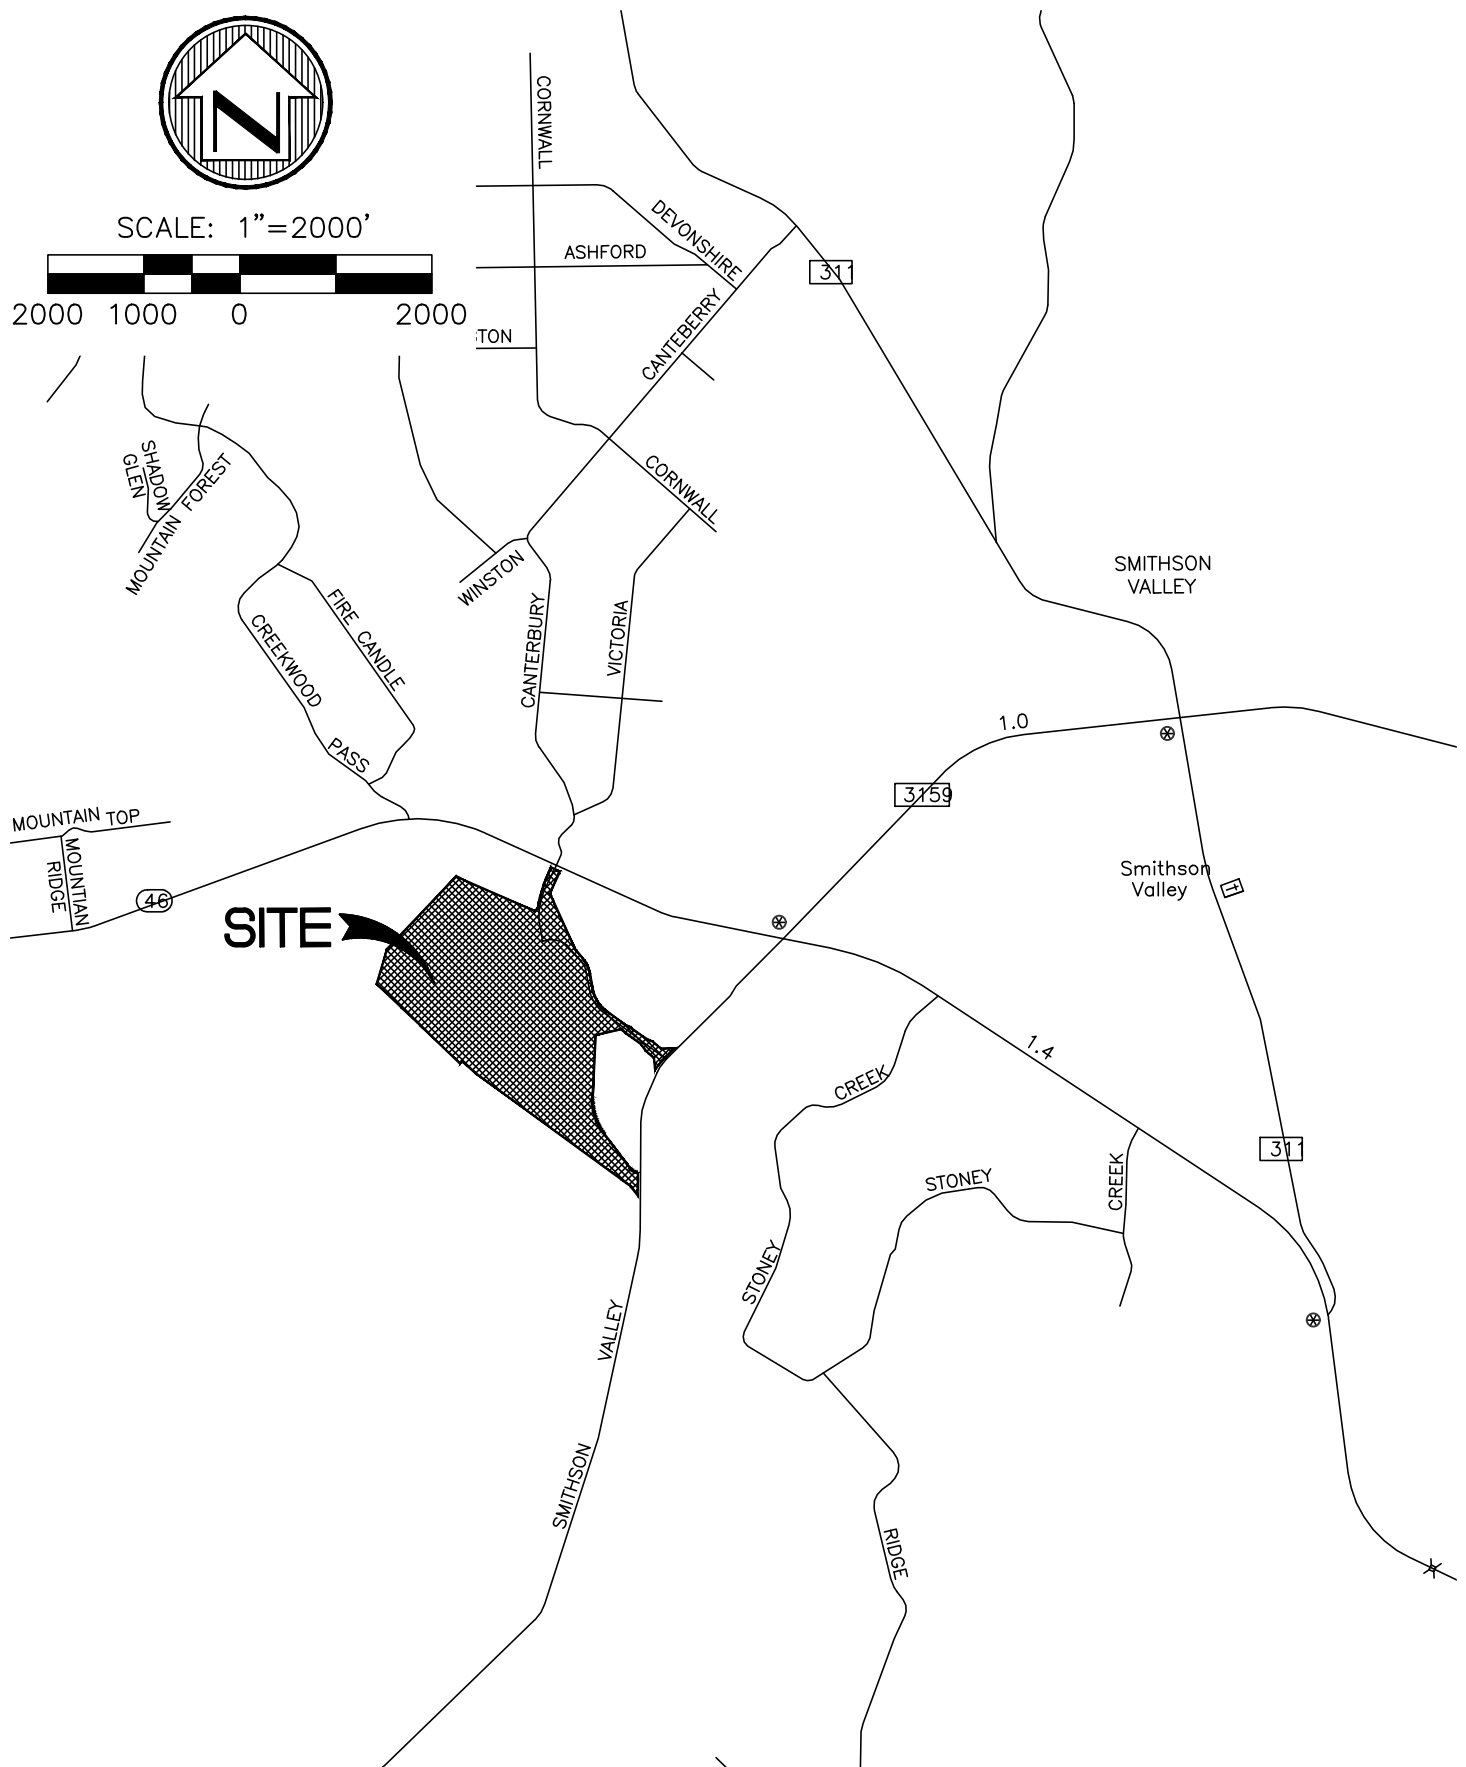

Moy Tarin Ramirez Engineers, LLC

TBPELS ENGINEERING F-5287/SURVEYING F-10131500

12770 CIMARRON PATH, SUITE 100
SAN ANTONIO, TEXAS 78249

TEL: (210) 698-5051
FAX: (210) 698-5085


- Engineers
- Surveyors
- Planners

**COMAL INDEPENDENT SCHOOL DISTRICT
2023 BASEBALL UPGRADES
ATTACHMENT A - LOCATION MAP**


PROJ. #: 24050

JUNE 2024

EXHIBIT 1



SCALE: 1"=2000'

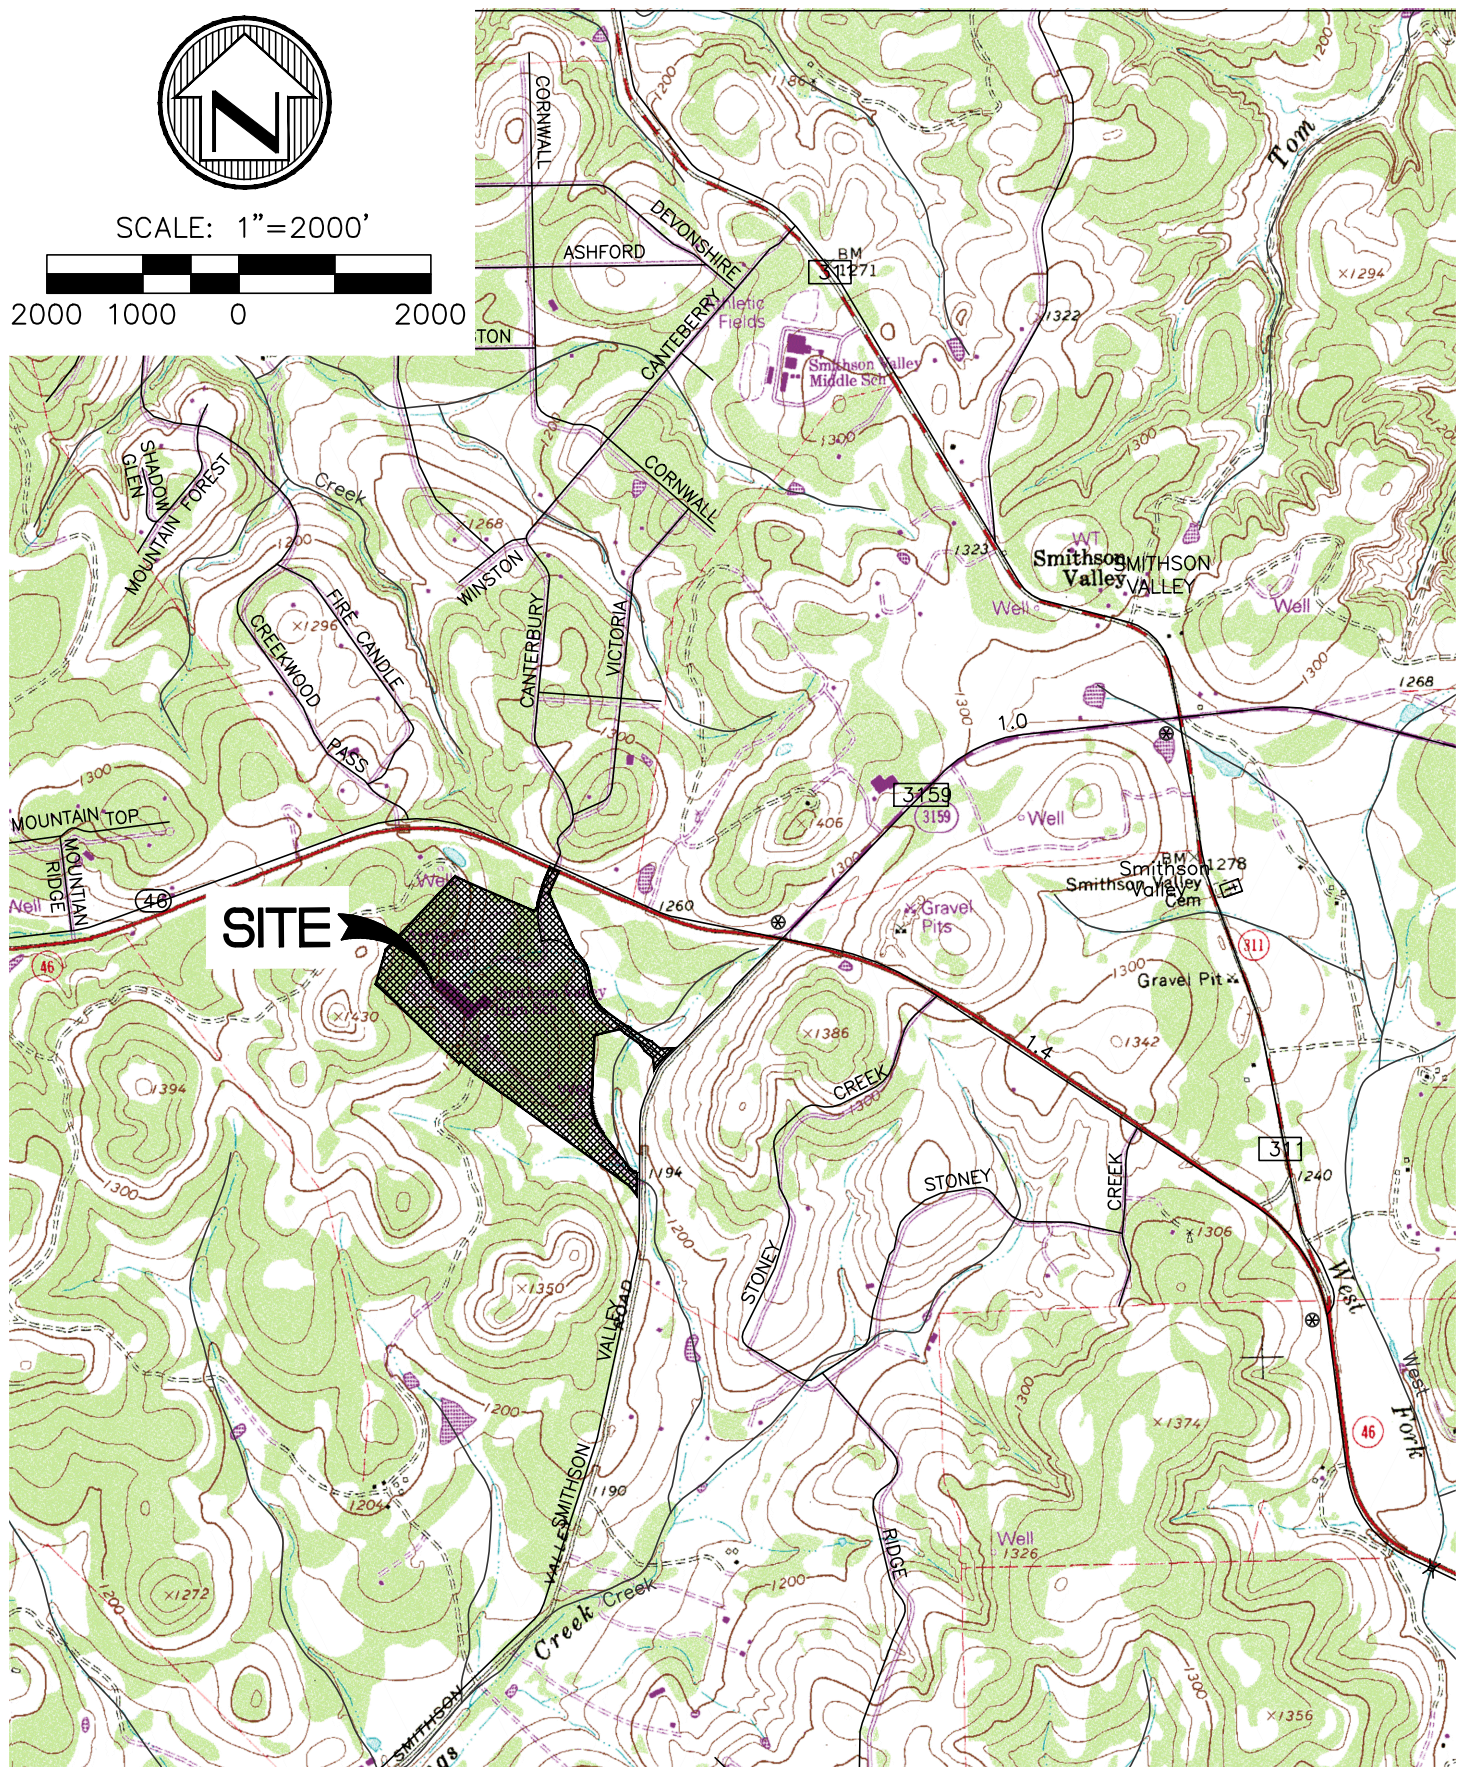

Moy Tarin Ramirez Engineers, LLC

TBPELS ENGINEERING F-5287/SURVEYING F-10131500

12770 CIMARRON PATH, SUITE 100
SAN ANTONIO, TEXAS 78249

TEL: (210) 698-5051
FAX: (210) 698-5085

- Engineers
- Surveyors
- Planners

**COMAL INDEPENDENT SCHOOL DISTRICT
2023 BASEBALL UPGRADES
ATTACHMENT B - USGS EXHIBIT**

PROJ. #: 24050

JUNE 2024

EXHIBIT 2

ATTACHMENT C

PROJECT DESCRIPTION

This project consists of the demolition and reconstruction/re-location of the existing baseball field fencing and associated light poles as well as the demolition of the existing dugouts and other miscellaneous site improvements. There will not be an increase in impervious cover to the site as a result of the improvements proposed with this project. Therefore, there are no proposed permanent BMPs with this project and there are no proposed modifications to the existing permanent BMPs with this project. Temporary BMP's will be provided and are shown on the accompanying Storm Water Pollution Prevention Plan (SWPPP).

The overall acreage of the Smithson Valley High School property is 95.4 acres, and the campus is located at 14001 TX-46, Spring Branch, Texas 78070. The site is situated over the Edwards Aquifer Contributing Zone. We have delineated a 1.7-acre project area within the overall property boundary for purposes of this exception request, also shown on the SWPPP. All work associated with this exception request will be performed within the 1.7-acre project area.

ATTACHMENT D

NATURE OF EXCEPTION

This application is requesting an exception to the submission of a Contributing Zone Plan (CZP) Modification. This project consists of the demolition and reconstruction/re-location of the existing baseball field fencing and associated light poles as well as the demolition of the existing dugouts and other miscellaneous site improvements. The proposed project will not impact the on-site impervious cover or existing drainage patterns.

The original Contributing Zone Plan (CZP) was approved on July 12th, 2001. There have been four modifications to the original CZP with the most recent one having been approved on April 9th, 2019.

The existing Permanent Best Management Practices (BMPs) will not be modified in any with this project.

ATTACHMENT E

EQUIVALENT WATER QUALITY PROTECTION

The original CZP approval letter listed an impervious cover of 19.40 acres prior to the effective rule date of 30 TAC Chapter 213, Subchapter B.

A CZP application was approved by letter dated July 12, 2001, that consisted of renovations and expansions that included new classrooms, a gym expansion, tennis courts, asphalt band field, parking areas, sidewalks, and access drives. The improvements added 6.87 acres of impervious cover, increasing the total on-site impervious cover to 26.27 acres.

A CZP Modification was approved by letter dated July 1, 2002, and included the construction of 1.08 acres of additional parking area. The improvements increased the total on-site impervious cover to 27.35 acres.

A second CPS modification was approved by letter dated April 24, 2009, that increased the total site area to 91.6 acres. The project consisted of improvements that included building additions, parking areas and drives, addition to the storm sewer system, and three extended detention basins. The improvements added 15.45 acres of impervious cover, increasing the total on-site impervious cover to 42.8 acres.

A third CZP modification was approved by letter dated October 28, 2016, that increased the total site area to 95.4 acres. The project included the renovations of an existing baseball field house, replacement of six structures at the softball and football fields, a new agriculture barn consisting of two new structures, drainage improvements, and modifications to the three existing extended detention basins. The project added 1.57 acres of impervious cover, increasing the total on-site impervious cover to 44.37 acres.

A fourth CZP modification was approved by letter dated April 9, 2019, that consisted of the reconstruction of the track/football field, construction of additional flatwork around the existing track/football field, and the addition of concrete flatwork to provide a high jump area. The project added 0.366 acres of impervious cover, increasing the total on-site impervious cover to 44.73 acres (46.89 percent) with pre-existing impervious cover totaling 19.40 acres.

The proposed project will not be increasing the currently approved impervious cover, therefore additional treatment/permanent Best Management Practices (BMPs) are not being added to this project. The current drainage patterns and BMPs will not be affected by the proposed project.

Temporary Stormwater Section

Texas Commission on Environmental Quality

for Regulated Activities on the Edwards Aquifer Recharge Zone and Relating to 30 TAC §213.5(b)(4)(A), (B), (D)(I) and (G); Effective June 1, 1999

To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.

Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.

Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Temporary Stormwater Section** is hereby submitted for TCEQ review and executive director approval. The application was prepared by:

Print Name of Customer/Agent: Sean Smith, P.E.

Date: 6/17/2024

Signature of Customer/Agent:



Regulated Entity Name: CISD SMITHSON VALLEY HIGH SCHOOL

Project Information

Potential Sources of Contamination

Examples: Fuel storage and use, chemical storage and use, use of asphaltic products, construction vehicles tracking onto public roads, and existing solid waste.

1. Fuels for construction equipment and hazardous substances which will be used during construction:

☐ The following fuels and/or hazardous substances will be stored on the site: _____

These fuels and/or hazardous substances will be stored in:

- ☐ Aboveground storage tanks with a cumulative storage capacity of less than 250 gallons will be stored on the site for less than one (1) year.

- ☐ Aboveground storage tanks with a cumulative storage capacity between 250 gallons and 499 gallons will be stored on the site for less than one (1) year.
- ☐ Aboveground storage tanks with a cumulative storage capacity of 500 gallons or more will be stored on the site. An Aboveground Storage Tank Facility Plan application must be submitted to the appropriate regional office of the TCEQ prior to moving the tanks onto the project.
- ☒ Fuels and hazardous substances will not be stored on the site.
- 2. ☒ **Attachment A - Spill Response Actions.** A site specific description of the measures to be taken to contain any spill of hydrocarbons or hazardous substances is attached.
- 3. ☒ Temporary aboveground storage tank systems of 250 gallons or more cumulative storage capacity must be located a minimum horizontal distance of 150 feet from any domestic, industrial, irrigation, or public water supply well, or other sensitive feature.
- 4. ☒ **Attachment B - Potential Sources of Contamination.** A description of any activities or processes which may be a potential source of contamination affecting surface water quality is attached.

Sequence of Construction

- 5. ☒ **Attachment C - Sequence of Major Activities.** A description of the sequence of major activities which will disturb soils for major portions of the site (grubbing, excavation, grading, utilities, and infrastructure installation) is attached.
 - ☒ For each activity described, an estimate (in acres) of the total area of the site to be disturbed by each activity is given.
 - ☒ For each activity described, include a description of appropriate temporary control measures and the general timing (or sequence) during the construction process that the measures will be implemented.
- 6. ☒ Name the receiving water(s) at or near the site which will be disturbed or which will receive discharges from disturbed areas of the project: Upper Cibolo Creek

Temporary Best Management Practices (TBMPs)

Erosion control examples: tree protection, interceptor swales, level spreaders, outlet stabilization, blankets or matting, mulch, and sod. Sediment control examples: stabilized construction exit, silt fence, filter dikes, rock berms, buffer strips, sediment traps, and sediment basins. Please refer to the Technical Guidance Manual for guidelines and specifications. All structural BMPs must be shown on the site plan.

- 7. ☒ **Attachment D – Temporary Best Management Practices and Measures.** TBMPs and measures will prevent pollution of surface water, groundwater, and stormwater. The construction-phase BMPs for erosion and sediment controls have been designed to retain sediment on site to the extent practicable. The following information is attached:

- ☒ A description of how BMPs and measures will prevent pollution of surface water, groundwater or stormwater that originates upgradient from the site and flows across the site.
 - ☒ A description of how BMPs and measures will prevent pollution of surface water or groundwater that originates on-site or flows off site, including pollution caused by contaminated stormwater runoff from the site.
 - ☒ A description of how BMPs and measures will prevent pollutants from entering surface streams, sensitive features, or the aquifer.
 - ☒ A description of how, to the maximum extent practicable, BMPs and measures will maintain flow to naturally-occurring sensitive features identified in either the geologic assessment, TCEQ inspections, or during excavation, blasting, or construction.
8. ☒ The temporary sealing of a naturally-occurring sensitive feature which accepts recharge to the Edwards Aquifer as a temporary pollution abatement measure during active construction should be avoided.
- ☐ **Attachment E - Request to Temporarily Seal a Feature.** A request to temporarily seal a feature is attached. The request includes justification as to why no reasonable and practicable alternative exists for each feature.
- ☒ There will be no temporary sealing of naturally-occurring sensitive features on the site.
9. ☒ **Attachment F - Structural Practices.** A description of the structural practices that will be used to divert flows away from exposed soils, to store flows, or to otherwise limit runoff discharge of pollutants from exposed areas of the site is attached. Placement of structural practices in floodplains has been avoided.
10. ☒ **Attachment G - Drainage Area Map.** A drainage area map supporting the following requirements is attached:
- ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin will be provided.
 - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a smaller sediment basin and/or sediment trap(s) will be used.
 - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin or other equivalent controls are not attainable, but other TBMPs and measures will be used in combination to protect down slope and side slope boundaries of the construction area.
 - ☐ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. A smaller sediment basin and/or sediment trap(s) will be used in combination with other erosion and sediment controls within each disturbed drainage area.

- ☒ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. Erosion and sediment controls other than sediment basins or sediment traps within each disturbed drainage area will be used.
11. ☐ **Attachment H - Temporary Sediment Pond(s) Plans and Calculations.** Temporary sediment pond or basin construction plans and design calculations for a proposed temporary BMP or measure have been prepared by or under the direct supervision of a Texas Licensed Professional Engineer. All construction plans and design information must be signed, sealed, and dated by the Texas Licensed Professional Engineer. Construction plans for the proposed temporary BMPs and measures are attached.
- ☒ N/A
12. ☒ **Attachment I - Inspection and Maintenance for BMPs.** A plan for the inspection of each temporary BMP(s) and measure(s) and for their timely maintenance, repairs, and, if necessary, retrofit is attached. A description of the documentation procedures, recordkeeping practices, and inspection frequency are included in the plan and are specific to the site and/or BMP.
13. ☒ All control measures must be properly selected, installed, and maintained in accordance with the manufacturer's specifications and good engineering practices. If periodic inspections by the applicant or the executive director, or other information indicate a control has been used inappropriately, or incorrectly, the applicant must replace or modify the control for site situations.
14. ☒ If sediment escapes the construction site, off-site accumulations of sediment must be removed at a frequency sufficient to minimize offsite impacts to water quality (e.g., fugitive sediment in street being washed into surface streams or sensitive features by the next rain).
15. ☒ Sediment must be removed from sediment traps or sedimentation ponds not later than when design capacity has been reduced by 50%. A permanent stake will be provided that can indicate when the sediment occupies 50% of the basin volume.
16. ☒ Litter, construction debris, and construction chemicals exposed to stormwater shall be prevented from becoming a pollutant source for stormwater discharges (e.g., screening outfalls, picked up daily).

Soil Stabilization Practices

Examples: establishment of temporary vegetation, establishment of permanent vegetation, mulching, geotextiles, sod stabilization, vegetative buffer strips, protection of trees, or preservation of mature vegetation.

17. ☒ **Attachment J - Schedule of Interim and Permanent Soil Stabilization Practices.** A schedule of the interim and permanent soil stabilization practices for the site is attached.

- 18. ☒ Records must be kept at the site of the dates when major grading activities occur, the dates when construction activities temporarily or permanently cease on a portion of the site, and the dates when stabilization measures are initiated.
- 19. ☒ Stabilization practices must be initiated as soon as practicable where construction activities have temporarily or permanently ceased.

Administrative Information

- 20. ☒ All structural controls will be inspected and maintained according to the submitted and approved operation and maintenance plan for the project.
- 21. ☒ If any geologic or manmade features, such as caves, faults, sinkholes, etc., are discovered, all regulated activities near the feature will be immediately suspended. The appropriate TCEQ Regional Office shall be immediately notified. Regulated activities must cease and not continue until the TCEQ has reviewed and approved the methods proposed to protect the aquifer from any adverse impacts.
- 22. ☒ Silt fences, diversion berms, and other temporary erosion and sediment controls will be constructed and maintained as appropriate to prevent pollutants from entering sensitive features discovered during construction.

ATTACHMENT A

SPILL RESPONSE ACTIONS

1. Housekeeping

- A. Minimize materials: An effort will be made to store only enough materials required to do the job.
- B. Storage: All materials stored on site will be stored in a neat, orderly manner in their appropriate containers in a covered area. If storage in a covered area is not feasible, then the materials will be covered with polyethylene or polypropylene sheeting to protect them from the elements.
- C. Labeling: Products will be kept in their original containers with the original manufacturer's label affixed to each container.
- D. Mixing: Substances will not be mixed with one another unless this is recommended by the manufacturer.
- E. Disposal: Whenever possible, all of a product will be used prior to disposal of the container. Manufacturer's recommendations will be followed for proper use and disposal of materials on site.
- F. Inspections: The site superintendent will inspect the site daily to ensure proper use and disposal of materials on site.
- G. Spoil Materials: Any excavated earth that will not be used for fill material and all demolished pavement will be hauled off site immediately and will be disposed of properly, in accordance with all applicable state/local regulations.

2. Product Specific Practices

- A. Petroleum Products: All on site vehicles will be monitored for leaks and will receive regular preventive maintenance to reduce the chance of leakage. If petroleum products will be present at the site, then they will be stored in tightly sealed containers which are clearly labeled. Any asphalt substances used on site will be applied according to the manufacturer's recommendations.
- B. Concrete Trucks: Ready/Transit Mix Trucks will not be allowed to wash out or discharge surplus concrete or drum wash water except in the designated location on site as shown on the SWPPP site plan.
- C. Paints: All containers will be tightly sealed and stored when not required for use. Excess paint will not be poured into storm sewer system or drainage channels, but will be properly disposed of according to manufacturers' instructions or state/local regulations.

- D. Fertilizers: Fertilizers will be applied only in the minimum amounts recommended by the manufacturer. Once applied, fertilizer will be worked into the soil to limit exposure to storm water. The fertilizer will be stored in a covered area, and any partially used bags will be transferred to a sealable plastic bin to avoid spills.

3. Spill Control and Response Measures

A spill prevention and response team will be designated by the site superintendent. In addition, the following practices will be followed for spill cleanup:

- A. Information: Manufacturers' recommended methods for spill cleanup will be clearly posted, and site personnel will be made aware of the procedures and location of the information and cleanup supplies.
- B. Equipment: Materials and equipment necessary for spill cleanup will be present on the site at all times. Equipment and materials will include, but not be limited to brooms, shovels, rags, gloves, goggles, absorbent materials (sand, sawdust, etc.) and plastic or metal trash containers specifically designed for this purpose. The materials and equipment necessary for spill cleanup will be dependent upon the nature and quantity of the material stored on site.
- C. Response: All spills will be cleaned up immediately upon discovery.

Cleanup

- (1) Clean up leaks and spills immediately
- (2) Use a rag for small spills on paved surfaces, a damp mop for general cleanup, and absorbent material for larger spills. If the spilled material is hazardous, then the used cleanup materials are also hazardous and must be disposed of as hazardous waste.
- (3) Never hose down or bury dry material spills. Clean up as much of the material as possible and dispose of properly. See the waste management BMPs in TCEQ Technical Guidance Manual RG-348 for specific information.

Minor Spills

- (1) Minor spills typically involve small quantities of oil, gasoline, paint, etc. which can be controlled by the first responder at the discovery of the spill.
- (2) Use absorbent materials on small spills rather than hosing down or burying the spill
- (3) Absorbent materials should be promptly removed and disposed of properly.
- (4) Follow the practice below for a minor spill:
- (5) Contain the spread of the spill.
- (6) Recover spilled materials.

(7) Clean the contaminated area and properly dispose of contaminated materials.

Semi-Significant Spills

Semi-significant spills still can be controlled by the first responder along with the aid of other personnel such as laborers and the foreman, etc. This response may require the cessation of all other activities.

Spills should be cleaned up immediately:

- (1) Contain spread of the spill.
- (2) Notify the project foreman immediately.
- (3) If the spill occurs on paved or impermeable surfaces, clean up using "dry" methods (absorbent materials, cat litter and/or rags). Contain the spill by encircling with absorbent materials and do not let the spill spread widely.
- (4) If the spill occurs in dirt areas, immediately contain the spill by constructing an earthen dike. Dig up and properly dispose of contaminated soil.
- (5) If the spill occurs during rain, cover the spill with tarps or other material to prevent contaminating runoff.

Significant/Hazardous Spills

For significant or hazardous spills that are in reportable quantities:

- (1) Notify the TCEQ by telephone as soon as possible and within 24 hours at 512-339-2929 (Austin) or 210-490-3096 (San Antonio) between 8 AM and 5 PM. After hours, contact the Environmental Release Hotline at 1-800-832-8224. It is the contractor's responsibility to have all emergency phone numbers at the construction site.
- (2) For spills of federal reportable quantities, in conformance with the requirements in 40 CFR parts 110, 119, and 302, the contractor should notify the National Response Center at (800) 424-8802.
- (3) Notification should first be made by telephone and followed up with a written report.
- (4) The services of a spills contractor or a Haz-Mat team should be obtained immediately. Construction personnel should not attempt to clean up until the appropriate and qualified staffs have arrived at the job site.
- (5) Other agencies which may need to be consulted include, but are not limited to, the City Police Department, County Sheriff Office, Fire Departments, etc.

D. Vehicle and Equipment Maintenance

- (1) If maintenance must occur onsite, use a designated area and a secondary containment, located away from drainage courses, to prevent the run-on of stormwater and the runoff of spills.

- (2) Regularly inspect onsite vehicles and equipment for leaks and repair immediately.
- (3) Check incoming vehicles and equipment (including delivery trucks, and employee and subcontractor vehicles) for leaking oil and fluids. Do not allow leaking vehicles or equipment onsite.
- (4) Always use secondary containment, such as a drain pan or drop cloth, to catch spills or leaks when removing or changing fluids.
- (5) Place drip pans or absorbent materials under paving equipment when not in use.
- (6) Use absorbent materials on small spills rather than hosing down or burying the spill. Remove the absorbent materials promptly and dispose of properly.
- (7) Promptly transfer used fluids to the proper waste or recycling drums. Don't leave full drip pans or other open containers lying around.
- (8) Oil filters disposed of in trash cans or dumpsters can leak oil and pollute stormwater. Place the oil filter in a funnel over a waste oil-recycling drum to drain excess oil before disposal. Oil filters can be recycled. Ask the oil supplier or recycler about recycling oil filters.
- (9) Store cracked batteries in a non-leaking secondary container. Do this with all cracked batteries even if you think all the acid has drained out. If you drop a battery, treat it as if it is cracked. Put it into the containment area until you are sure it is not leaking.

E. Vehicle and Equipment Fueling

- (1) If fueling must occur onsite, use designated areas, located away from drainage courses, to prevent the run-on of stormwater and the runoff of spills.
- (2) Discourage "topping off" of fuel tanks.
- (3) Always use secondary containment, such as a drain pan, when fueling to catch spills/leaks.

F. Safety: The spill area will be kept well ventilated, and personnel will wear appropriate protective clothing to prevent injury from contact with hazardous substances.

G. Reporting: Spills of toxic or hazardous material (if present on site) will be reported to the appropriate state or local government agency, regardless of the spill's size.

H. Record Keeping: The spill prevention plan will be modified to include measures to prevent this type of spill from recurring as well as improved methods for cleaning up any future spills. A description of each spill, what caused it, and the cleanup measures used will be kept with this plan.

ATTACHMENT B
POTENTIAL SOURCES OF CONTAMINATION

Potential Source	Oil, grease, fuel and hydraulic fluid contamination from construction equipment and vehicle dripping.
Preventive Measure	Vehicle maintenance, when possible, will be performed within a construction staging area specified by the General Contractor.
Potential Source	Miscellaneous trash and litter from construction workers and material wrappings.
Preventive Measure	Trash containers will be placed throughout the site to encourage proper trash disposal.
Potential Source	Construction debris.
Preventive Measure	Construction debris will be monitored daily by contractor. Debris will be collected weekly and placed in disposal bins. Situations requiring immediate attention will be addressed on a case by case basis.
Potential Source	Stormwater contamination from excess application of fertilizers, herbicides and pesticides.
Preventive Measure	Fertilizers, herbicides and pesticides will be applied only when necessary and in accordance with manufacturers directions.
Potential Source	Soil and mud from construction vehicle tires as they leave the site.
Preventive Measure	A stabilized construction exit shall be utilized as vehicles leave the site. Any soil, mud, etc. carried from the project onto public roads shall be cleaned up within 24 hours.
Potential Source	Sediment from soil, sand, gravel and excavated materials stockpiled on site.
Preventive Measure	Silt fence shall be installed on the downgradient side of all stockpiled materials. Reinforced rock berms shall be installed at all downstream discharge locations.

ATTACHMENT C
SEQUENCE OF MAJOR ACTIVITIES

Construction Sequencing

- A. Excavation.
- B. Demolition.
- C. Minor Grading.
- D. Seeding and soil stabilization.

ATTACHMENT D

TEMPORARY BEST MANAGEMENT PRACTICES AND MEASURES

Description of Temporary Best Management Practices:

Vegetation will be used as a temporary stabilization technique for all areas disturbed by construction, not covered in pavement, buildings, or other structures.

Sequence of installation during construction process for each phase of construction:

Vegetation as a temporary control will only be utilized in the event a disturbed area has been left denuded for more than 14 days.

Up gradient storm water flowing across the site:

There is minimum upgradient flow entering the construction area. All upgradient flow will be treated along with the stormwater generated onsite.

Onsite storm water flowing across and off the site:

The storm water originating onsite and flowing off the site will be treated through temporary BMPs. Silt fences will be installed at all locations where non-concentrated storm water exits the site.

Prevention of pollutants from entering surface streams, sensitive features and the aquifer:

The storm water originating onsite and flowing off the site will be treated using temporary BMPs prior to it entering surface streams, sensitive features and the aquifer. Silt fences will be installed at all locations where non-concentrated storm water may leave the site. These silt fences should filter the storm water prior to it leaving the site.

Maintaining flow to naturally-occurring sensitive features:

The storm water originating onsite and flowing off the site will continue to flow into the down gradient receiving waters. Any sensitive features downstream will continue to receive flow originating on the site. Prior to the flow leaving the site, it will be treated through temporary BMPs. These temporary BMPs should remove sediment, pollutants and debris if installed and maintained properly.

ATTACHMENT F
STRUCTURAL PRACTICES

Vegetation will be used as a temporary stabilization technique for all areas disturbed by construction, not covered by pavement, buildings, or other structures. Temporary stabilization shall consist of temporary seeding of disturbed areas that are denuded beyond 14 days without construction restart within 21 days. As a temporary control, the vegetation will be used to stabilize barren areas that are inactive for long periods of time.

ATTACHMENT G
DRAINAGE AREA MAP

On-site drainage patterns are going to remain unchanged as a result of the improvements proposed with this project. As a result, a drainage area map is not provided with this exception request.

ATTACHMENT I
INSPECTION AND MAINTENANCE FOR BMPS

Silt Fence

1. Inspect all fencing weekly, and after any rainfall.
2. Remove sediment when buildup reaches 6 inches, or install a second line of fencing parallel to the old fence.
3. Replace any torn fabric or install a second line of fencing parallel to the torn section.
4. Replace or repair any sections crushed or collapsed in the course of construction activity.

Bagged Gravel Inlet Filter

1. Inspections should be made weekly and after each rainfall. Repair or replacement should be made promptly as needed by the contractor.
2. Remove sediment when buildup reaches a depth of 3 inches. Removed sediment should be deposited in a suitable area and in such a manner that it will not erode.
3. Check placement of device to prevent gaps between device and curb.
4. Inspect filter fabric and patch or replace if torn or missing.
5. Structures should be removed, and the area stabilized only after the remaining drainage area has been properly stabilized.

CISD SMITHSON VALLEY HIGH SCHOOL

Responsible Party Form

Pollution Prevention Measure		Inspected	Corrective Action	
			Description	Date Completed
Silt Fence	Inspections			
	Fencing			
	Sediment Removal			
	Torn Fabric			
	Crushed/Collapsed Fencing			
Bagged Gravel Inlet Filters	Inspections			
	Replaced/Reshaped			
	Silt Removed			

Inspector's Name

Inspector's Signature

Name of Owner/Operator

Date

Note: Inspector is to attach a brief statement of his qualifications to this report.

ATTACHMENT J

SCHEDULE OF INTERIM AND PERMANENT SOIL STABILIZATION PRACTICES

Stabilization measures shall be initiated as soon as practicable in portions of the site where construction activities have temporarily or permanently ceased, but in no case more than 14 days after the construction activity in that portion of the site has temporarily or permanently ceased. Where the initiation of stabilization measures by the 14th day after construction activity temporarily or permanently ceases is precluded by weather conditions, stabilization measures shall be initiated as soon as practicable. Where construction activity on a portion of the site is temporarily ceased, and earth disturbing activities will be resumed within 21 days, temporary stabilization measures do not have to be initiated on that portion of the site. In areas experiencing droughts where the initiation of stabilization measures by the 14th day after construction activity has temporarily or permanently ceased is precluded by seasonal arid conditions, stabilization measures shall be initiated as soon as practicable.

Temporary stabilization shall consist of temporary seeding of disturbed areas that are denuded beyond 14 days without construction restart within 21 days.

As pad sites (buildings, sidewalks and pavement) are completed, permanent landscaping and sod shall be planted and irrigated. Curb and gutter will direct runoff into the permanent water quality basin.

Temporary vegetation stabilization techniques shall be in accordance with the TCEQ Technical Guidance Manual RG-248 (*Complying with the Edwards Aquifer Rules – Technical Guidance on Best Management Practices*), Chapter 1 Temporary Best Management Practices, Section 1.3.8 Temporary Vegetation, as follows:

Temporary Vegetation

Vegetation is used as a temporary or permanent stabilization technique for areas disturbed by construction, but not covered by pavement, buildings, or other structures. As a temporary control, vegetation can be used to stabilize stockpiles and barren areas that are inactive for long periods of time.

Vegetative techniques can and should apply to every construction project with few exceptions. Vegetation effectively reduces erosion in swales, stockpiles, berms, mild to medium slopes, and along roadways.

Other techniques may be required to assist in the establishment of vegetation. These other techniques include erosion control matting, mulches, surface roughening, swales and dikes to direct runoff around newly seeded areas, and proper grading to limit runoff velocities during construction. (NCTCOG, 1993b)

Materials:

The type of temporary vegetation used on a site is a function of the season and the availability of water for irrigation. For areas that are not irrigated, the year can be divided into two temporary planting seasons and one season for planting of permanent warm weather groundcovers. These periods are shown in Figure 1-19 for Bexar, Comal, Kinney, Medina, and Uvalde Counties. Appropriate temporary vegetation for these areas is shown in Table 1-4.

Other vegetation may perform as well as the recommended varieties, especially where irrigation is available. County agricultural extension agents are a good source for suggestions for other types of temporary vegetation. All seed should be high quality, U.S. Dept. of Agriculture certified seed.

Installation:

(1) Interim or final grading must be completed prior to seeding, minimizing all steep slopes. In addition, all necessary erosion structures such as dikes, swales, and diversions, should also be installed.

(2) Seedbed should be well pulverized, loose, and uniform.

(3) Fertilizer should be applied at the rate of 40 pounds of nitrogen and 40 pounds of phosphorus per acre, which is equivalent to about 1.0 pounds of nitrogen and phosphorus per 1000 square feet. Compost can be used instead of fertilizer and applied at the same time as the seed.

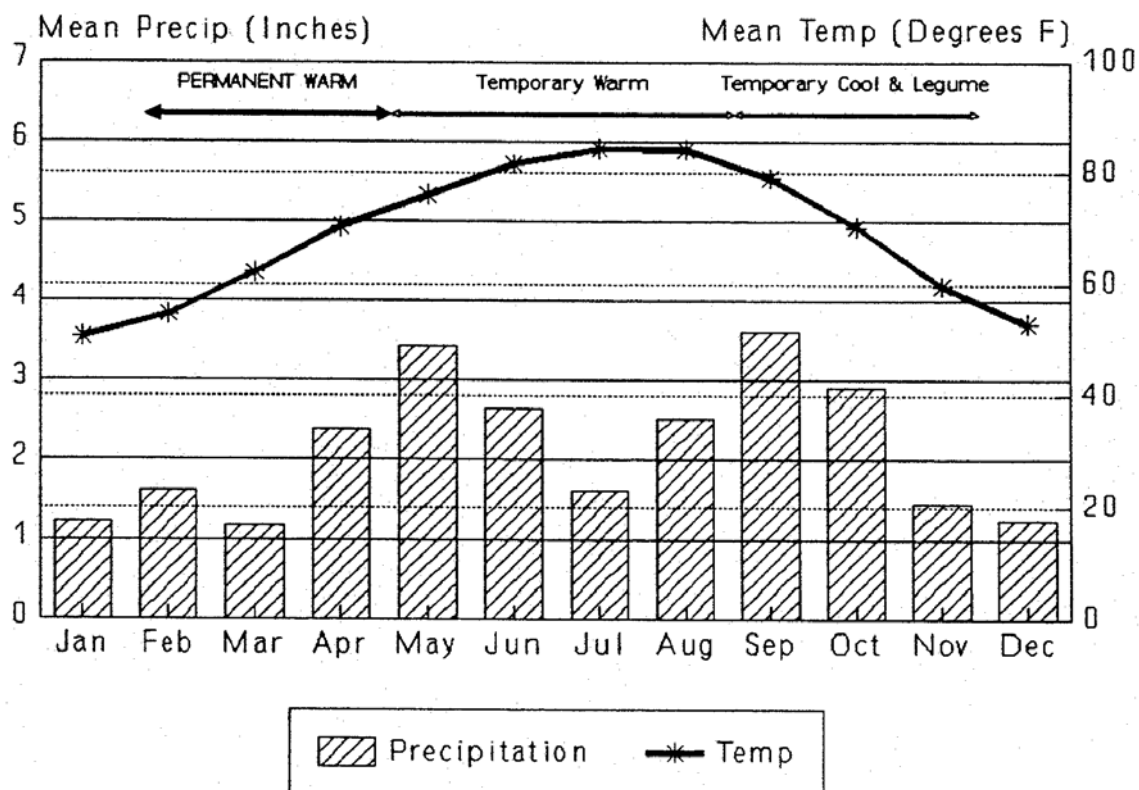


Figure 1-19 Planting Dates for Bexar, Comal, Kinney, Medina, and Uvalde Counties (Northcutt, 1993)

Table 1-4 Temporary Seeding for Bexar, Comal, Kinney, Medina, and Uvalde Counties (Northcutt, 1993)

Dates	Climate	Species (lb/ac)	
Sept 1 to Nov 30	Temporary Cool Season	Tall Fescue	4.0
		Oats	21.0
		Wheat (Red, Winter)	30.0
		Total	55.0
Sept 1 to Nov 30	Cool Season Legume	Hairy Vetch	8.0
May 1 to Aug 31	Temporary Warm Season	Foxtail Millet	30.0

(4) Seeding rates should be as shown in Table 1-4 or as recommended by the county agricultural extension agent.

(5) The seed should be applied uniformly with a cyclone seeder, drill, cultipacker seeder or hydroseeder (slurry includes seed, fertilizer and binder).

(6) Slopes that are steeper than 3:1 should be covered with appropriate soil stabilization matting as described in the following section to prevent loss of soil and seed.

Irrigation:

Temporary irrigation should be provided according to the schedule described below, or to replace moisture loss to evapotranspiration (ET), whichever is greater. Significant rainfall (on-site rainfall of ½" or greater) may allow watering to be postponed until the next scheduled irrigation.

Time Period	Irrigation Amount and Frequency
Within 2 hours of installation	Irrigate entire root depth, or to germinate seed
During the next 10 business days	Irrigate entire root depth every Monday, Wednesday, and Friday
During the next 30 business days or until Substantial Completion	Irrigate entire root depth a minimum of once per week, or as necessary to ensure vigorous growth
During the next 4 months or until Final Acceptance of the Project	Irrigate entire root depth once every two weeks, or as necessary to ensure vigorous growth

If cool weather induces plant dormancy, water only as necessary to maintain plant health.

Irrigate in a manner that will not erode the topsoil but will sufficiently soak the entire depth of roots.

Inspection and Maintenance Guidelines:

(1) Temporary vegetation should be inspected weekly and after each rain event to locate and repair any erosion.

(2) Erosion from storms or other damage should be repaired as soon as practical by regrading the area and applying new seed.

(3) If the vegetated cover is less than 80%, the area should be reseeded.



1. PROVIDE BAGGED GRAVEL INLET FILTERS AT ALL EXPOSED DRAINAGE STRUCTURES.
2. SOIL DISTURBANCES WILL OCCUR OVER THE ENTIRE SITE AS INDICATED ON PLAN.
3. LOCATIONS OF MAJOR STRUCTURAL AND NONSTRUCTURAL CONTROLS ARE LABELED.
4. THESE ARE THE TEMPORARY AND PERMANENT BEST MANAGEMENT PRACTICES.
5. SOIL STABILIZATION PRACTICES SHALL OCCUR OVER THE ENTIRE SITE WITH THE USE OF PAVEMENT, BUILDINGS, SIDEWALKS, GRASS SEED, MULCH, TREES, AND SHRUBS.
6. THERE ARE NO POLLUTION ZONES WHERE STORM WATER DISCHARGES TO SURFACE WATER.
7. CONTRACTOR SHALL MODIFY PLAN AS NECESSARY TO PROVIDE FOR PROPER STORM WATER MANAGEMENT THROUGHOUT THE PROJECT.
8. ALL MODIFICATIONS ARE TO BE NOTED ON CONTRACTOR'S COPY OF THE SURVEY DRAWING AND REPORT ON THE PROJECT SITE.
9. CONTRACTOR IS RESPONSIBLE FOR PROVIDING PROPER POLLUTION CONTROLS OF THE PROJECT THROUGHOUT THE ENTIRE CONSTRUCTION ACTIVITIES.

DATA ON INDICATED SUBSURFACE CONDITIONS ARE NOT INTENDED AS REPRESENTATIONS OR WARRANTIES OF ACCURACY OR CONTINUITY BETWEEN SOIL BORINGS. IT IS EXPRESSLY UNDERSTOOD THAT THE OWNER, ARCHITECT, AND/OR STRUCTURAL, CIVIL OR MECHANICAL, PLUMBING OR ELECTRICAL ENGINEER WILL NOT BE RESPONSIBLE FOR INTERPRETATIONS OR CONCLUSIONS DRAWN THEREFROM BY CONTRACTOR. DATA ARE MADE AVAILABLE FOR CONVENIENCE OF CONTRACTOR ONLY. CONTRACTOR, SUCH AS, BUT NOT LIMITED TO, SHALL NOT BE CONSIDERED TO BE A PART OF THESE CONTRACT DOCUMENTS. THE CONTRACTOR MAY, AT HIS OPTION, OBTAIN A COPY OF THE GEOTECHNICAL REPORT.

CONTRACTOR IS TO COORDINATE WITH LANDSCAPE
PLANS FOR FINAL TREE REMOVAL INSTRUCTIONS.

OWNER: COMAL INDEPENDENT SCHOOL DISTRICT
ADDRESS: 14001 TX-46
SPRING BRANCH, TEXAS 78070


	PROPERTY LINE
	EXISTING CONTOUR
	PROPOSED CONTOUR
	SILT FENCE
	ROCK BERM
	GRAVEL INLET FILTER
	CONSTRUCTION STAGING AREA
	CONCRETE WASHOUT PIT
	DRAINAGE FLOW ARROW

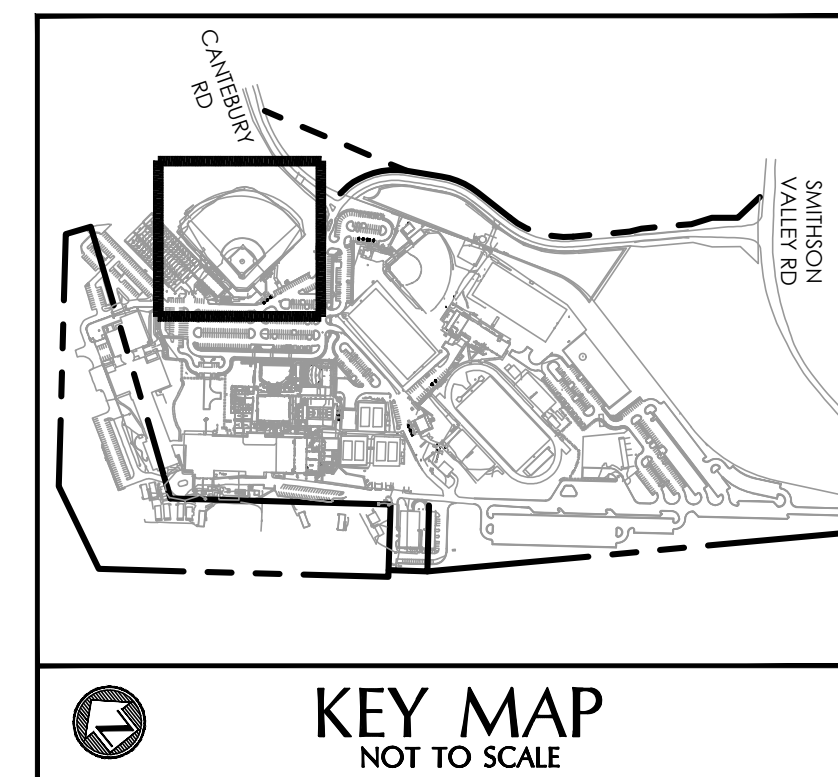

SCALE: 1"=30'



A horizontal graphic scale bar with alternating black and white segments. Below the bar, numerical labels indicate distances in feet: 30, 15, 0, and 15. The bar is divided into segments of 15 feet each, with the 0 mark in the center.

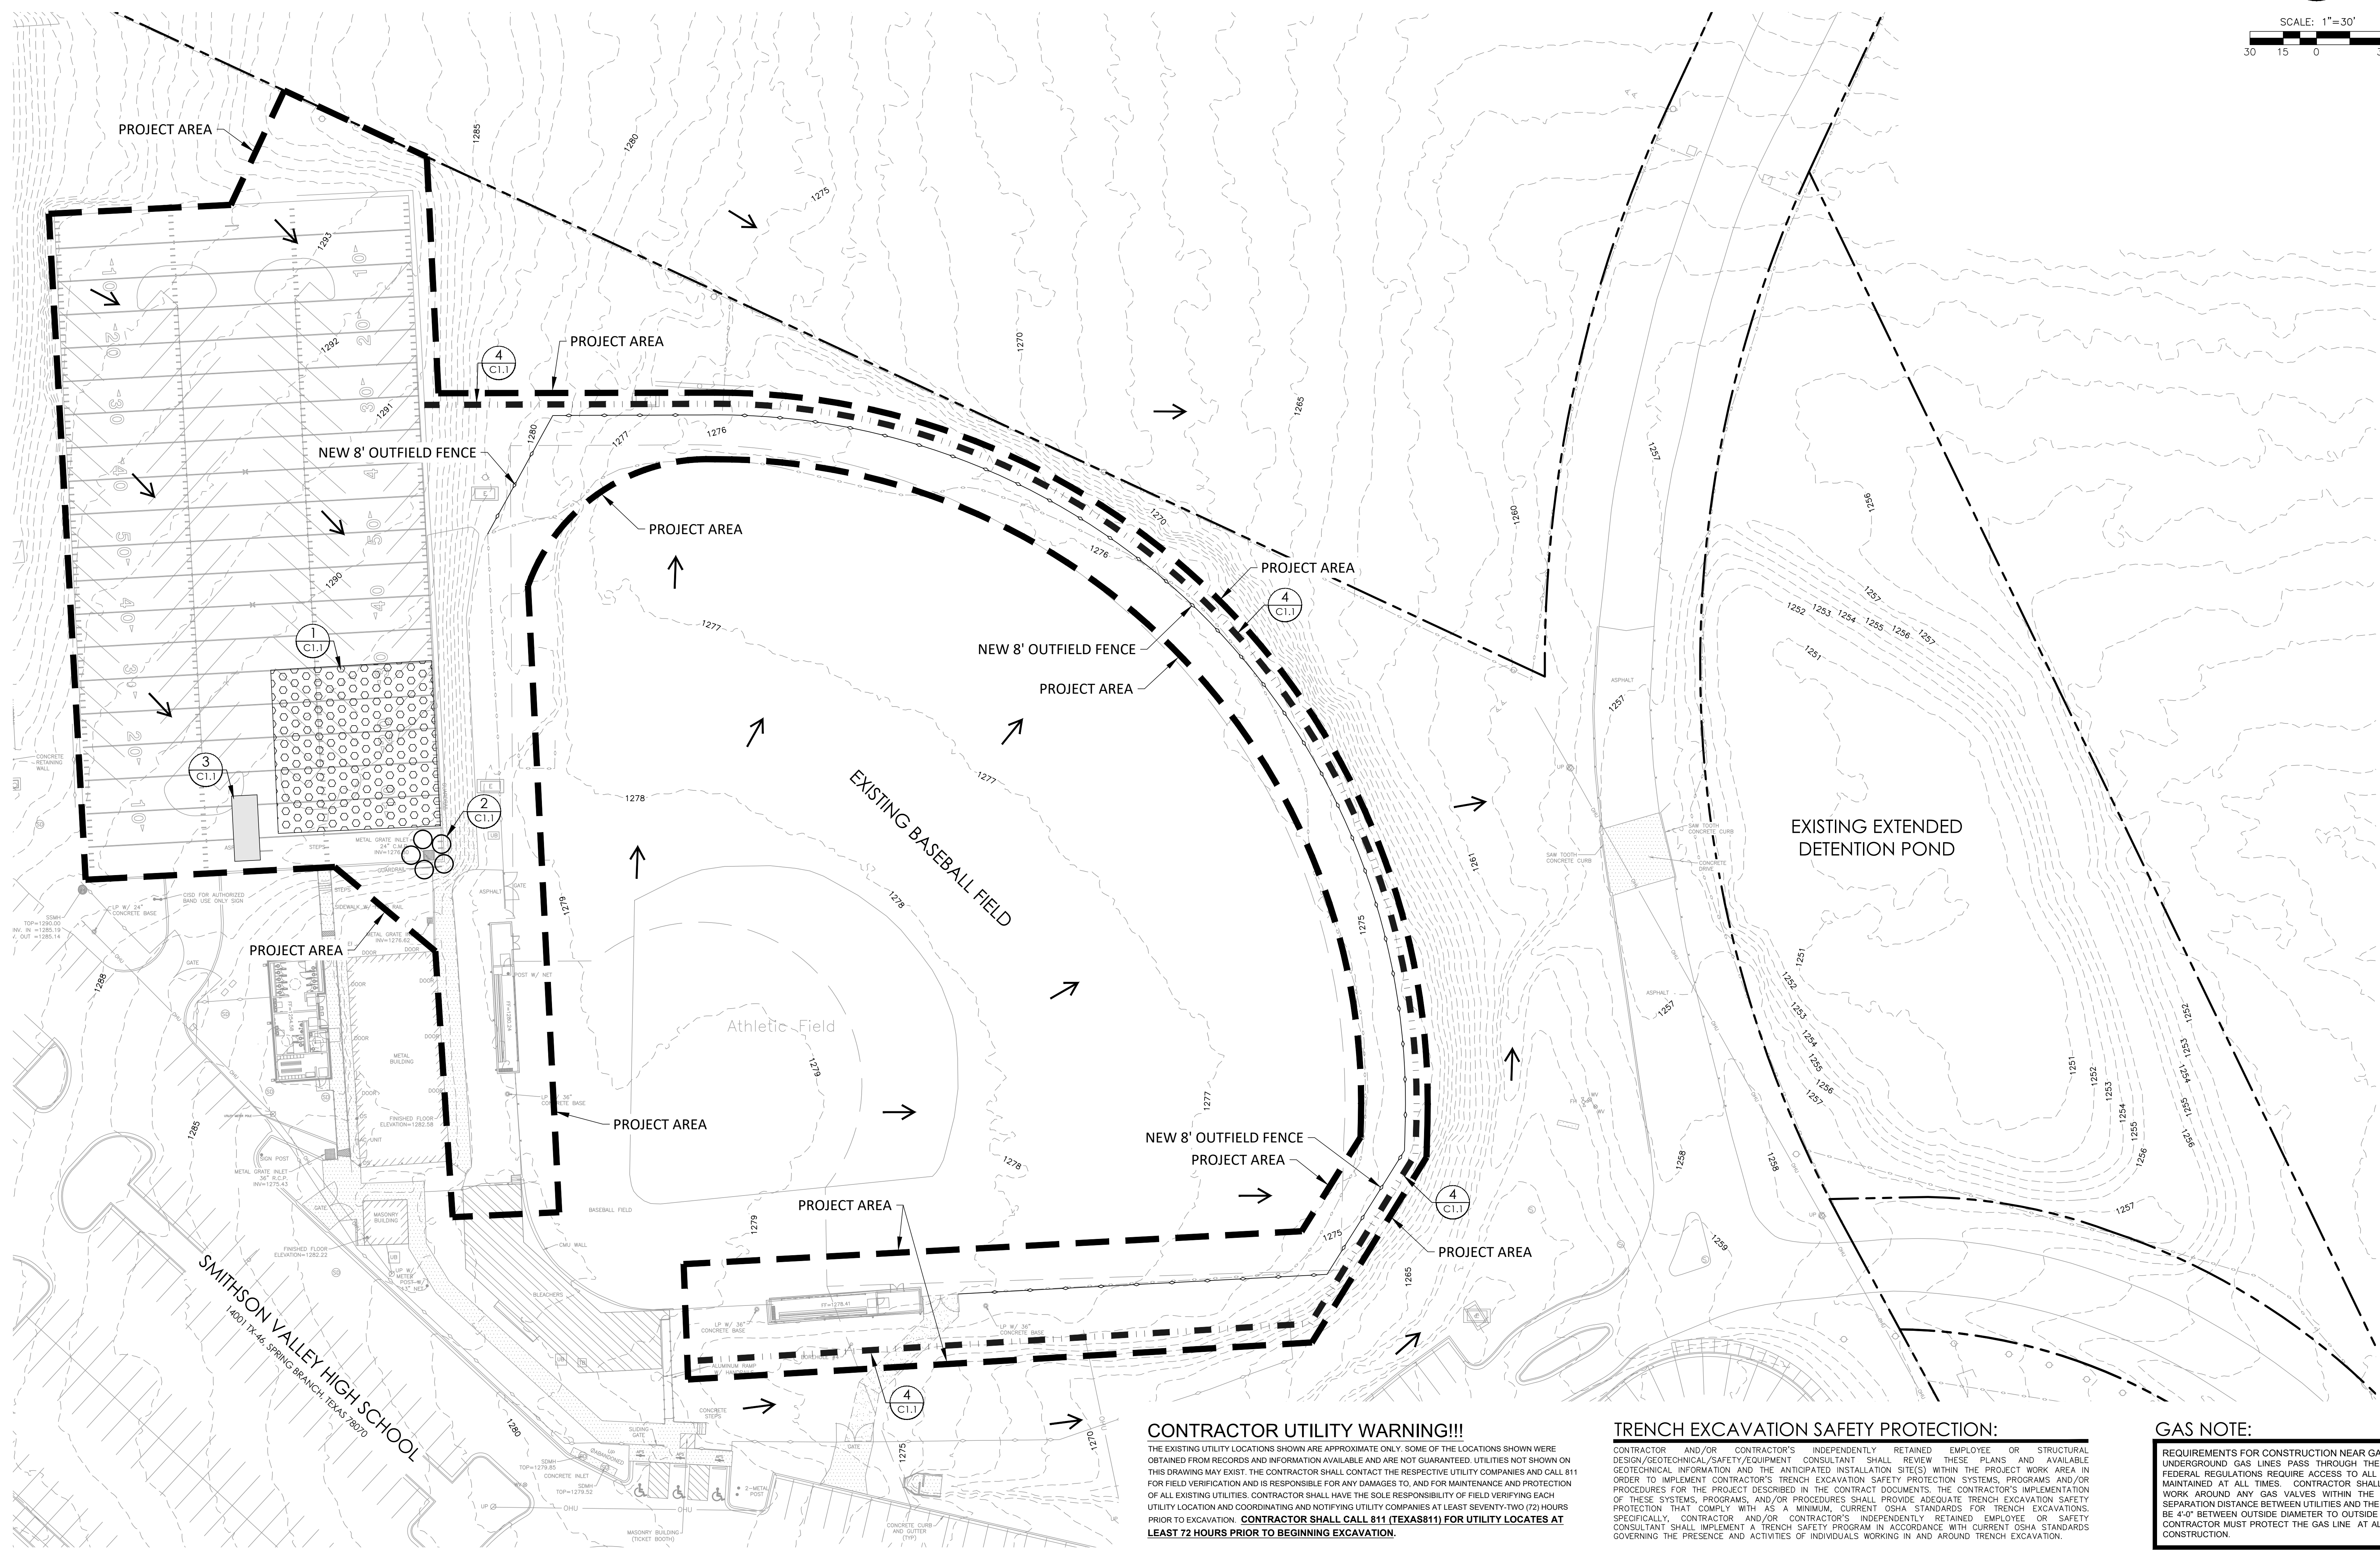


THE EXISTING UTILITY LOCATIONS SHOWN ARE APPROXIMATE ONLY. SOME OF THE LOCATIONS SHOWN WERE OBTAINED FROM RECORDS AND INFORMATION AVAILABLE AND ARE NOT GUARANTEED. UTILITIES NOT SHOWN ON THIS DRAWING MAY EXIST. THE CONTRACTOR SHALL CONTACT THE RESPECTIVE UTILITY COMPANIES AND CALL FOR FIELD VERIFICATION AND IS RESPONSIBLE FOR ANY DAMAGES TO, AND FOR MAINTENANCE AND PROTECTION OF ALL EXISTING UTILITIES. CONTRACTOR SHALL HAVE THE SOLE RESPONSIBILITY OF FIELD VERIFYING EACH UTILITY LOCATION AND COORDINATING AND NOTIFYING UTILITY COMPANIES AT LEAST SEVENTY-TWO (72) HOURS PRIOR TO EXCAVATION. **CONTRACTOR SHALL CALL 811 (TEXAS811) FOR UTILITY LOCATES AT LEAST 72 HOURS PRIOR TO BEGINNING EXCAVATION.**

CONTRACTOR AND/OR CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR STRUCTURAL DESIGN/GEOTECHNICAL SAFETY/EQUIPMENT CONSULTANT SHALL REVIEW THESE PLANS AND AVAILABLE GEOTECHNICAL INFORMATION AND THE ANTICIPATED INSTALLATION SITE(S) WITHIN THE PROJECT WORK AREA IN ORDER TO IMPLEMENT CONTRACTOR'S TRENCH EXCAVATION SAFETY PROTECTION SYSTEMS, PROGRAMS AND/OR PROCEDURES. CONTRACTOR SHALL SPECIFICALLY IDENTIFY AND ADDRESS ALL SAFETY CONCERNS ASSOCIATED WITH THESE SYSTEMS, PROGRAMS, AND/OR PROCEDURES. CONTRACTOR SHALL PROVIDE ADEQUATE TRENCH EXCAVATION SAFETY PROTECTION THAT COMPLY WITH AS A MINIMUM, CURRENT OSHA STANDARDS FOR TRENCH EXCAVATIONS. SPECIFICALLY, CONTRACTOR AND/OR CONTRACTOR'S INDEPENDENTLY RETAINED EMPLOYEE OR SAFETY CONSULTANT SHALL IDENTIFY AND ADDRESS ALL SAFETY CONCERNS ASSOCIATED WITH THE TRENCH EXCAVATION WORKING CONDITIONS AND ACTIVITIES. CONTRACTOR SHALL SPECIFICALLY IDENTIFY AND ADDRESS ALL SAFETY CONCERNS ASSOCIATED WITH THE TRENCH EXCAVATION WORKING CONDITIONS GOVERNING THE PRESENCE AND ACTIVITIES OF INDIVIDUALS WORKING IN AND AROUND TRENCH EXCAVATION.

REQUIREMENTS FOR CONSTRUCTION NEAR GAS:
UNDERGROUND GAS LINES PASS THROUGH THE SUBJECT SITE. FEDERAL REGULATIONS REQUIRE ACCESS TO ALL GAS VALVES BE MAINTAINED AT ALL TIMES. CONTRACTOR SHALL PROTECT AND WORK AROUND ANY GAS VALVES WITHIN THE PROJECT AREA. SEPARATION DISTANCE BETWEEN UTILITIES AND THE GAS MAIN SHALL BE 4'-0" BETWEEN OUTSIDE DIAMETER TO OUTSIDE DIAMETER. THE CONTRACTOR MUST PROTECT THE GAS LINE AT ALL TIMES DURING CONSTRUCTION.


[illegible]

**Engineers
Surveyors
Planners**



- Engineers
- Surveyors
- Planners



Moy Tarin Ramirez Engineers, LLC




COMAL INDEPENDENT SCHOOL DISTRICT
2023 BASEBALL UPGRADES

SHEET

C1.0

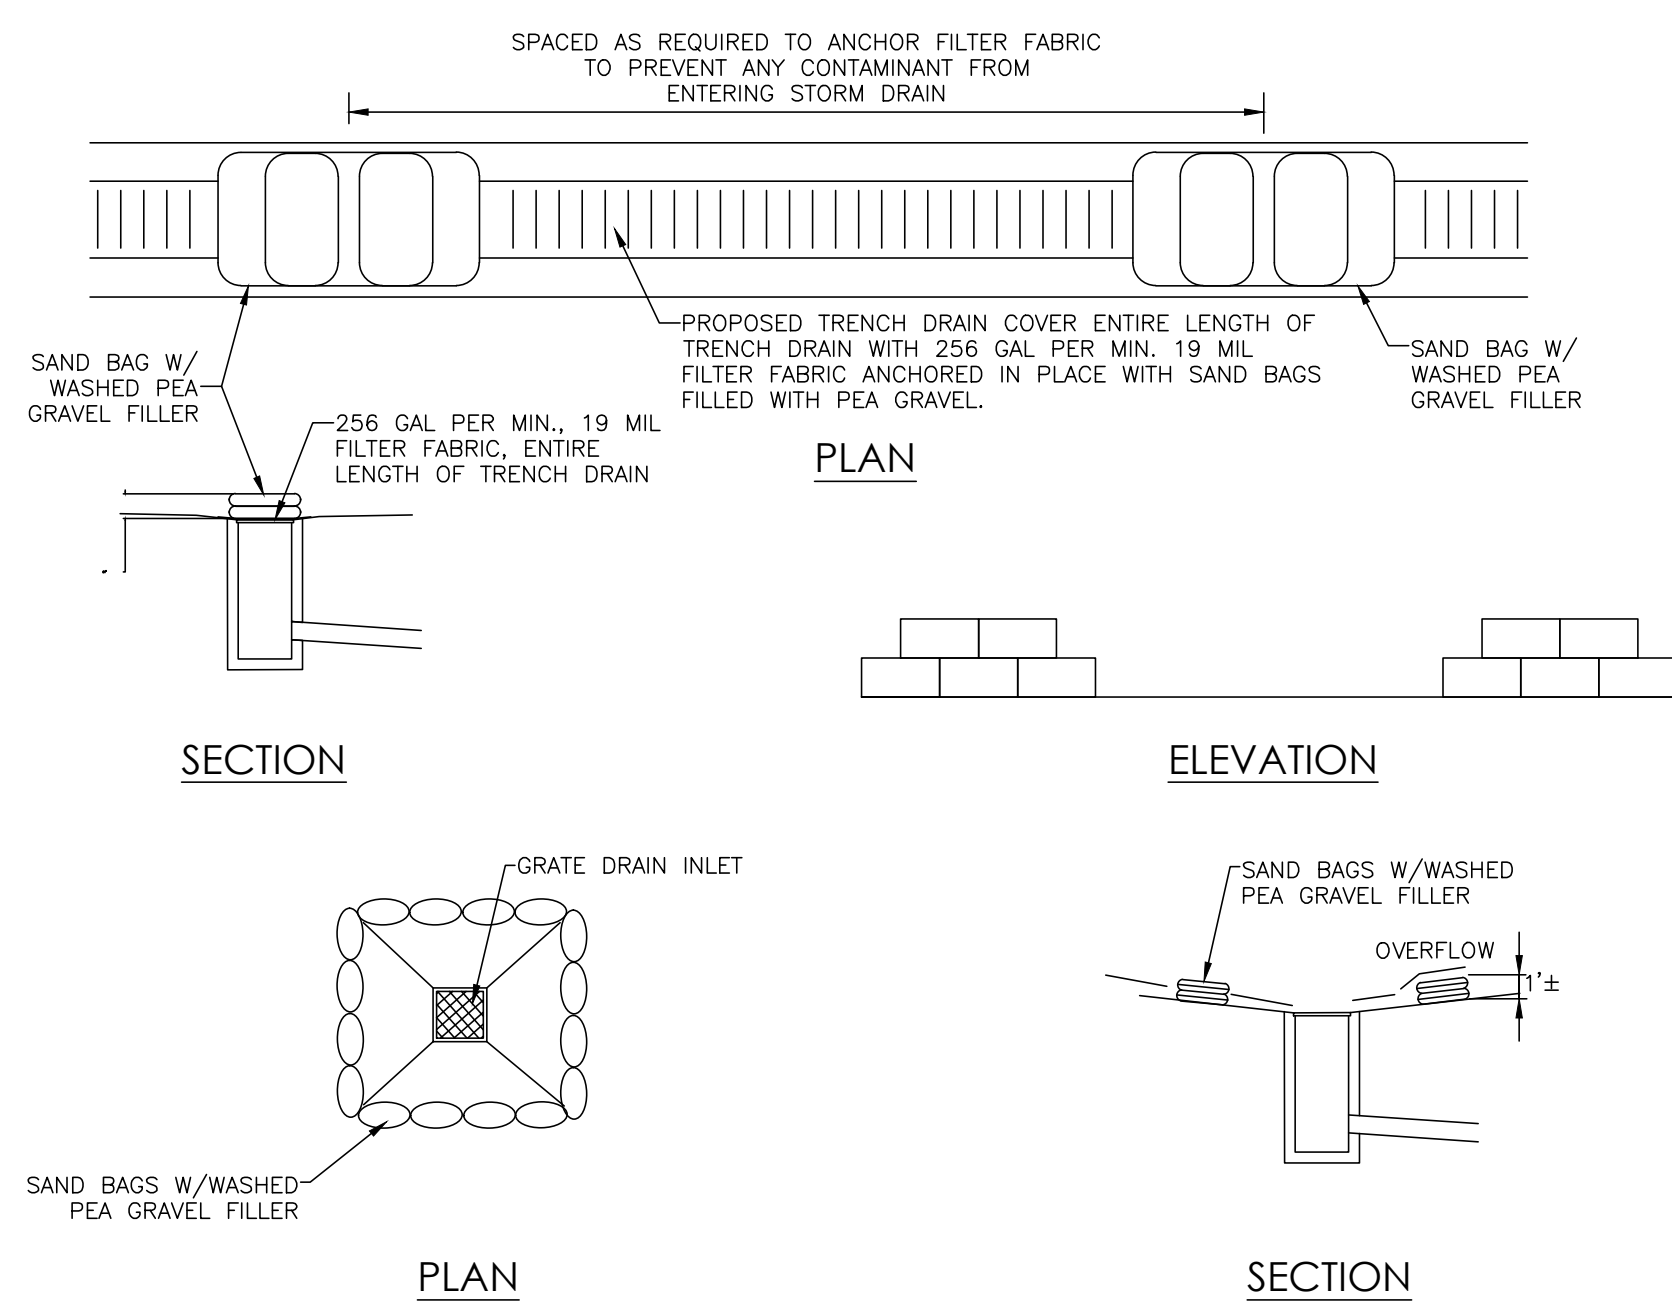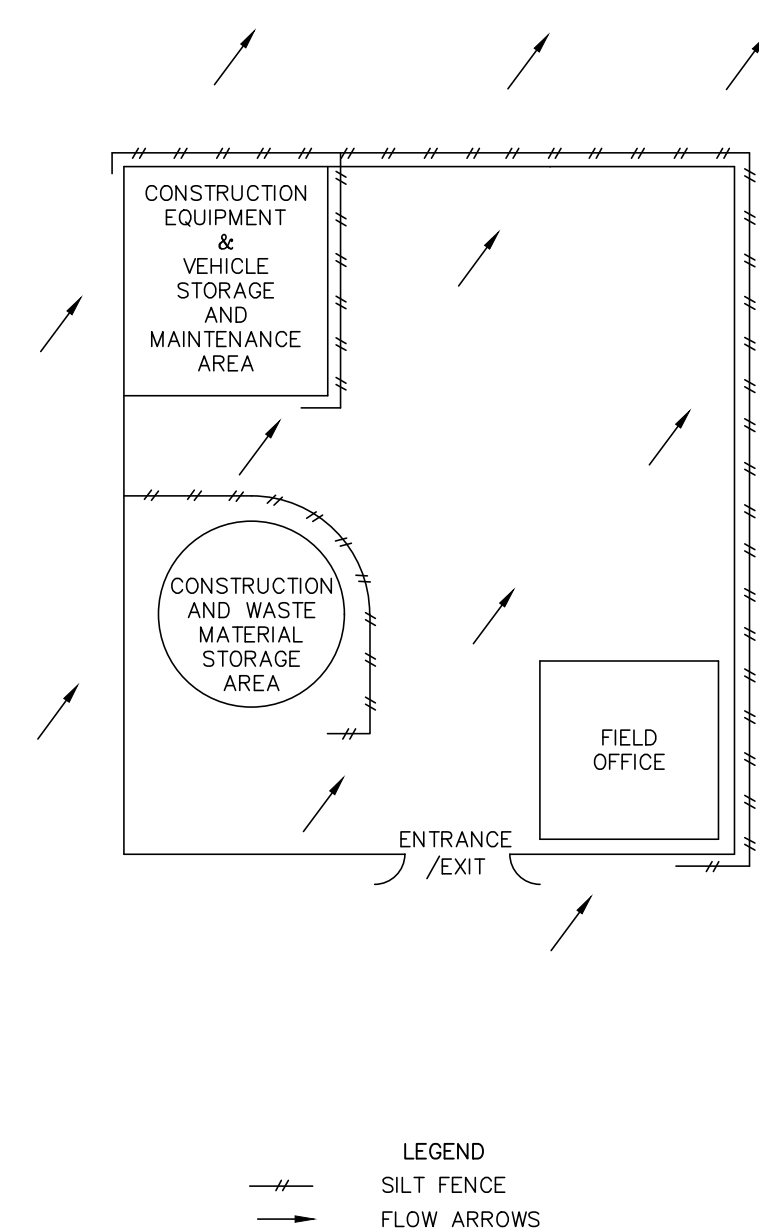


1. THE GRAVEL BAG MATERIAL SHOULD BE POLYPROPYLENE, POLYETHYLENE, POLYAMIDE OR COTTON BURLAP WOVEN FABRIC, MINIMUM UNIT WEIGHT 4 OZ/YD². MULLEN BURST STRENGTH EXCEEDING 300 PSI AND ULTRAWEAVE STABILITY EXCEEDING 70 PERCENT.
2. THE BAG LENGTH SHOULD BE 24 INCHES, WIDTH SHOULD BE 18 INCHES AND THICKNESS SHOULD BE 6 INCHES.
3. THE GRAVEL BAGS SHOULD BE FILLED WITH 3/4" GRAVEL.
4. WHEN A GRAVEL BAG IS FILLED WITH GRAVEL, THE OPEN END OF THE GRAVEL BAG SHOULD BE STAPLED OR TIED WITH NYLON OR POLY CORD.
5. THE GRAVEL BAGS SHOULD BE PLACED AS SHOWN ON THE DETAIL. THE GRAVEL BAGS SHALL BE STACKED TO FORM A CONTINUOUS BARRIER AROUND THE INLETS. THE BAGS SHOULD BE TIGHTLY ABUTTED AGAINST EACH OTHER TO PREVENT RUNOFF FROM FLOWING BETWEEN THE BAGS.
6. INSPECTION SHOULD BE MADE WEEKLY AND AFTER EACH RAINFALL. REPAIR OR REPLACEMENT SHOULD BE MADE PROMPTLY AS NEEDED BY THE CONTRACTOR.
7. CHECK PLACEMENT OF DEVICE TO PREVENT GAPS BETWEEN DEVICE AND CURB.
8. REMOVE SEDIMENT WHEN BUILDUP REACHES A DEPTH OF 3 INCHES. REMOVED SEDIMENT SHOULD BE DEPOSITED IN A SUITABLE AREA AND IN SUCH A MANNER THAT IT WILL NOT ERODE.
9. STRUCTURE SHOULD BE REMOVED AND THE AREA STABILIZED ONLY AFTER THE REMAINING DRAINAGE AREA HAS BEEN PROPERLY STABILIZED.

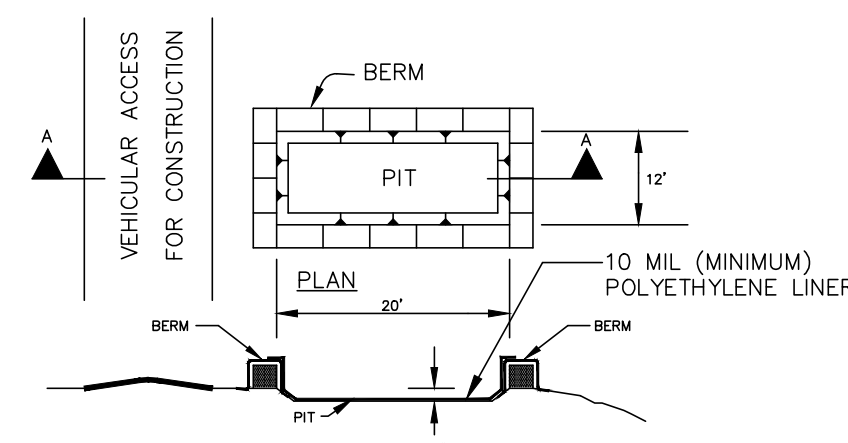


GENERAL NOTES

- DETAIL ABOVE ILLUSTRATES MINIMUM DIMENSIONS. PIT CAN BE INCREASED IN SIZE DEPENDING ON EXPECTED FREQUENCY OF USE.
- WASHOUT PIT SHALL BE LOCATED IN AN AREA EASILY ACCESSIBLE TO CONSTRUCTION TRAFFIC.
- WASHOUT PIT SHALL NOT BE LOCATED IN AREAS SUBJECT TO INUNDATION FROM STORM WATER RUNOFF.

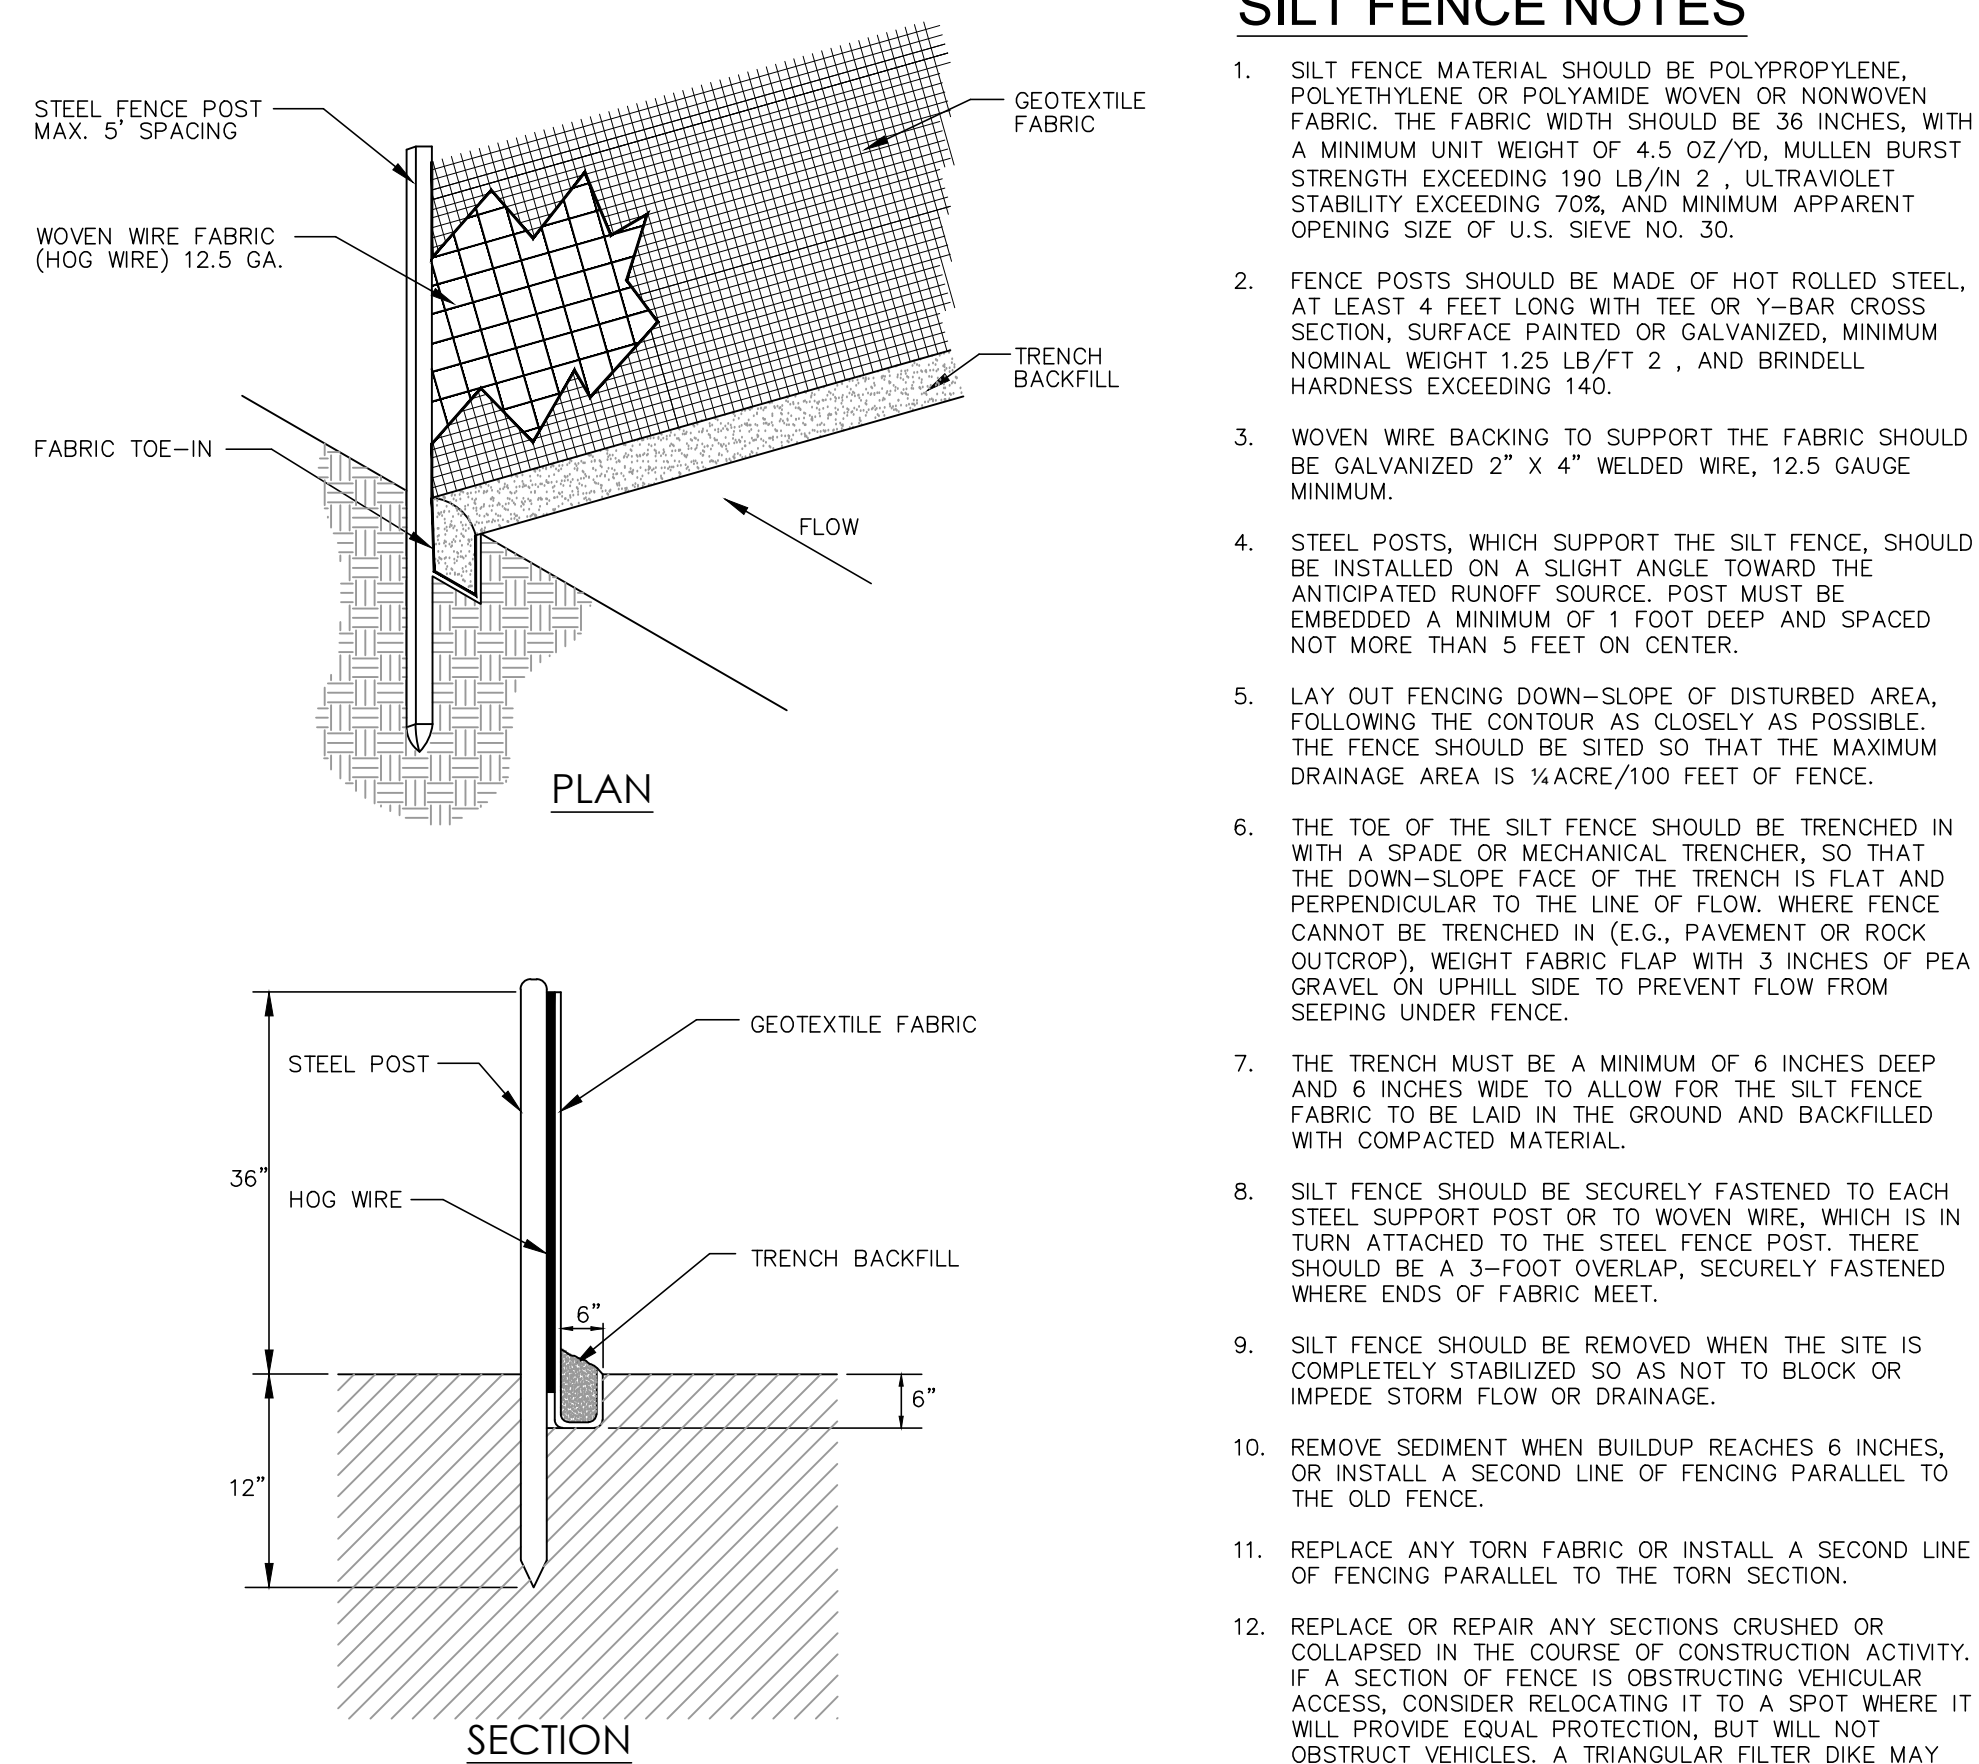


SILT FENCE NOTES

1. POLYETHYLENE MATERIAL SHOULD BE POLYPROPYLENE, SILT FENCE OR POLYAMIDE WOVEN OR NONWOVEN FABRIC. THE FABRIC SHOULD BE STRENGTHED WITH A MINIMUM UNIT TENSILE OF 4.5 OZ/YD, MULLEN BURNST TEST EXCEEDING 100 LB/YD 2, ULTRAVIOLET RADIATION RESISTANCE EXCEEDING 1000 HOURS APPARENT OPENING SIZE OF U.S. SIEVE NO. 30.
2. FENCE POSTS SHOULD BE MADE OF HOT ROLLED STEEL, 1/2" DIA. WITH AN INSTALLATION OF 12" DEEP. CROSS SECTION, SURFACE PAINTED OR GALVANIZED, MINIMUM NOMINAL WEIGHT 1.25 LB/YD 2, AND BRIDGELAP SHOULD EXCEED 12" MINIMUM.
3. WOMEN WERE BACKING TO SUPPORT THE FABRIC SHOULD BE GALVANIZED 2" X 4" WELDED WIRE, 12.5 GAUGE MINIMUM.
4. STEEL POSTS, WHICH SUPPORT THE SILT FENCE, SHOULD BE INSTALLED ON AN INCLINE TOWARD THE ANTICIPATED RUNOFF SOURCE. POSTS MUST BE SPACED AT A MINIMUM OF 10 FEET AND SPACED NOT MORE THAN 5 FEET ON CENTER.
5. LAY OUT FENCING DOWN-SLOPE OF DISTURBED AREA, FOLLOWING THE CONTOUR AS CLOSELY AS POSSIBLE. THE FABRIC SHOULD BE STRENGTHED TOWARD THE MAXIMUM DRAINAGE AREA IS 1/4"CR/100 FEET OF FENCE.
6. THE TOE OF THE SILT FENCE SHOULD BE TRENCHED IN WITH A SPADE OR MECHANICAL TRENCHER, SO THAT THE TRENCH SLOPE FACING THE FENCE IS DOWN-SLOPE AND PERPENDICULAR TO THE LINE OF FLOW. WHERE FENCE CANNOT BE TRENCHED, THE FABRIC SHOULD BE STRENGTHED (OUTCROP), WEAVE FABRIC FLAP WITH 3 INCHES OF FENCE ON UPHILL SIDE TO PREVENT FLOW FROM BEING DEFLECTED UNDER FENCE.
7. THE TRENCH MUST BE A MINIMUM OF 6 INCHES DEEP AND 6 INCHES WIDE TO ALLOW FOR THE SILT FENCE FABRIC TO BE LAID IN THE GROUND AND BACKFILLED AND COMPACTED WITH A ROLLER.
8. SILT FENCE SHOULD BE SECURELY FASTENED TO EACH SILT SUPPORT POST OR TO WOVEN WIRE, WHICH IS IN PLACE PRIOR TO THE INSTALLATION OF THE FENCE. THERE SHOULD BE A 3-FOOT OVERLAP, SECURELY FASTENED WHERE ENDS OF FABRIC MEET.
9. SILT FENCE SHOULD BE REMOVED WHEN THE SITE IS STABILIZED, STABILIZED SO AS NOT TO BLOCK OR IMPEDE STORM FLOW OR DRAINAGE.
10. REMOVE SEDIMENT WHEN BUILDUP REACHES 6 INCHES, OR INSTALL A SECOND LINE OF FENCING PARALLEL TO THE FIRST LINE.
11. REPLACE ANY TORN FABRIC OR INSTALL A SECOND LINE OF FENCING PARALLEL TO THE TORN SECTION.
12. REPLACE OR REPAIR ANY SECTIONS CRUSHED OR COLLAPSED IN THE COURSE OF CONSTRUCTION ACTIVITY. IF THE SECTION OF FENCING COLLAPSED, IT SHOULD BE COLLAPSED, CONSIDER RELOCATING IT TO A SPOT WHERE IT CAN BE USED TO FILL A TRENCH OR TO BE USED TO OBSTRUCT VEHICLES. A TRIANGULAR FILTER DICE MAY BE USED TO REPLACE A SILT FENCE AT COMMON VEHICLE ACCESS POINTS.

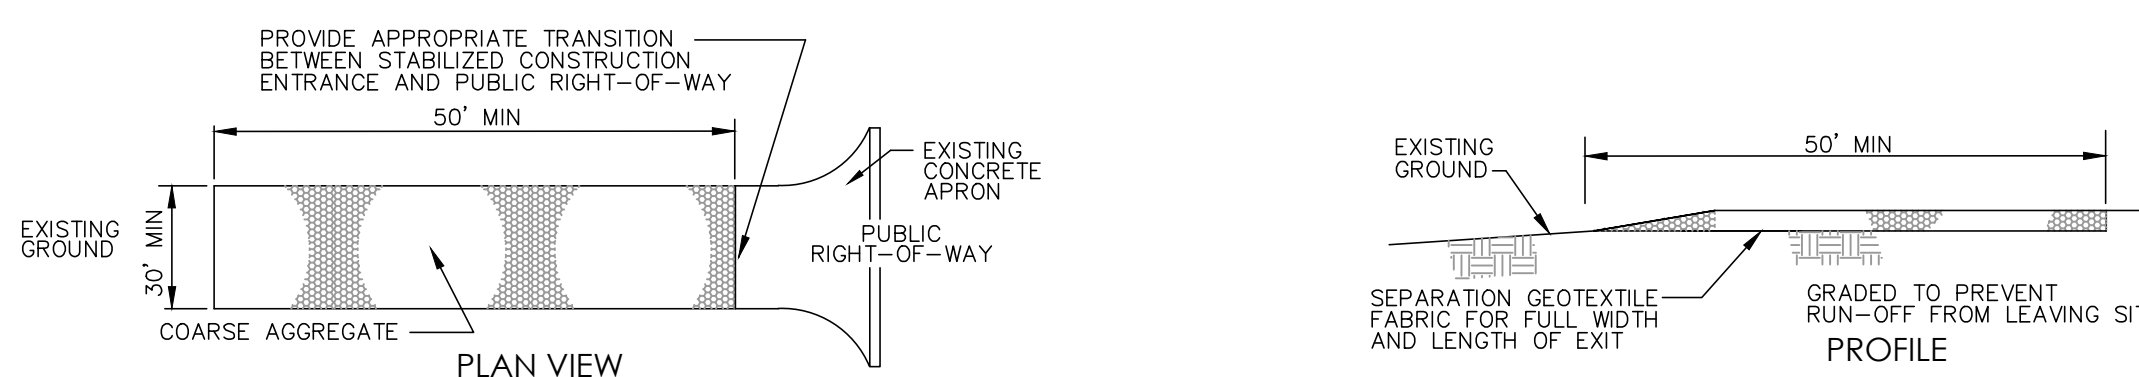


TEMPORARY CONSTRUCTION ENTRANCE/EXIT NOTES

1. THE AGGREGATE SHOULD CONSIST OF 4 TO 8 INCH WASHED STONE OVER A STABLE FOUNDATION.
2. THE AGGREGATE SHOULD BE PLACED WITH A MINIMUM THICKNESS OF 8 INCHES.
3. THE GEOTEXTILE FABRIC SHOULD BE DESIGNED SPECIFICALLY FOR USE AS A SOIL FILTRATION MEDIA WITH AN APPROXIMATE WEIGHT OF 6 OZ/YD 2 , A MULLEN BURST RATING OF 140 LB/IN 2 , AND AN EQUIVALENT OPENING SIZE GREATER THAN A NUMBER 50 SIEVE.
4. AVOID CURVES ON PUBLIC ROADS AND STEEP SLOPES. REMOVE VEGETATION AND OTHER OBJECTIONABLE MATERIAL FROM THE FOUNDATION AREA. GRADE CROWN FOUNDATION FOR POSITIVE DRAINAGE.
5. THE MINIMUM WIDTH OF THE ENTRANCE/EXIT SHOULD BE 12 FEET OR THE FULL WIDTH OF EXIT ROADWAY, WHICHEVER IS GREATER.
6. THE CONSTRUCTION ENTRANCE SHOULD BE AT LEAST 50 FEET LONG.
7. PLACE GEOTEXTILE FABRIC AND GRADE FOUNDATION TO IMPROVE STABILITY, ESPECIALLY WHERE WET CONDITIONS ARE ANTICIPATED.
8. PLACE STONE TO DIMENSIONS AND GRADE SHOWN. LEAVE SURFACE SMOOTH AND SLOPE FOR DRAINAGE.
9. THE ENTRANCE SHOULD BE MAINTAINED IN A CONDITION, WHICH WILL PREVENT TRACKING OR FLOWING OF SEDIMENT ONTO PUBLIC RIGHTS-OF-WAY. THIS MAY REQUIRE PERIODIC TOP DRESSING WITH ADDITIONAL STONE AS CONDITIONS DEMAND AND REPAIR AND/OR CLEANOUT OF ANY MEASURES USED TO TRAP SEDIMENT.
10. ALL SEDIMENT SPILLED, DROPPED, WASHED OR TRACKED ON TO PUBLIC RIGHTS-OF-WAY SHOULD BE REMOVED IMMEDIATELY BY CONTRACTOR.
11. WHEN NECESSARY, WHEELS SHOULD BE CLEANED TO REMOVE SEDIMENT PRIOR TO ENTRANCE ONTO PUBLIC RIGHT-OF-WAY.
12. WHEN WASHING IS REQUIRED, IT SHOULD BE DONE ON AN AREA STABILIZED WITH CRUSHED STONE THAT DRAINS INTO AN APPROVED SEDIMENT TRAP OR SEDIMENT BASIN.
13. ALL SEDIMENT SHOULD BE PREVENTED FROM ENTERING ANY STORM DRAIN, DITCH OR WATER COURSE.

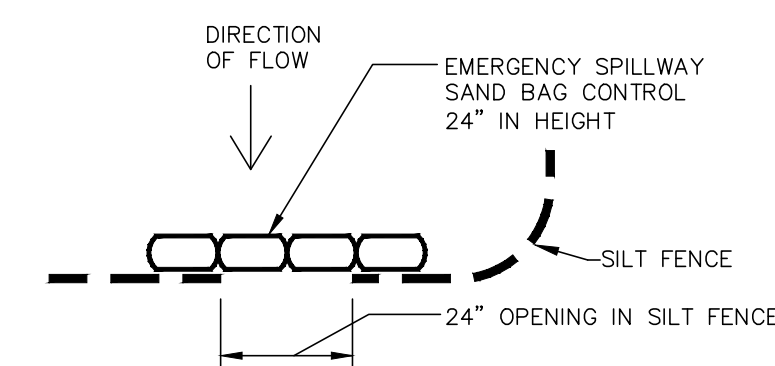

PLAN - SAND BAG CONTROL DETAIL

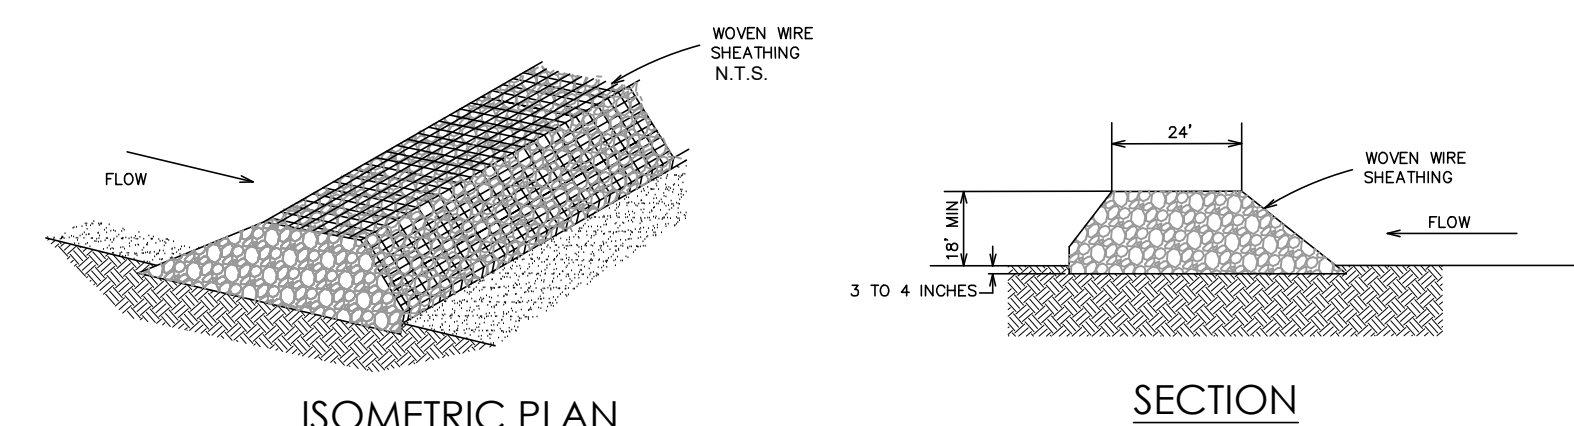

ROCK BERM NOTES

1. THE BERM STRUCTURE SHOULD BE SECURED WITH A WOVEN WIRE SHEATHING HAVING MAXIMUM OPENING OF 1 INCH AND A MINIMUM WIRE DIAMETER OF 20 GAUGE GALVANIZED AND SHOULD BE SECURED WITH SHOT RINGS.
2. CLEAN, OPEN GRADE 3 TO 8-INCH DIAMETER ROCK SHOULD BE USED, EXCEPT IN AREAS WHERE HIGH VELOCITIES OR LARGE VOLUMES OF FLOW ARE EXPECTED, WHERE 5-TO 8-INCH DIAMETER ROCKS MAY BE USED.
3. LAY OUT THE WOVEN WIRE SHEATHING PERPENDICULAR TO THE FLOW LINE.
4. BERM SHOULD HAVE A TOP WIDTH OF 2 FEET MINIMUM WITH SIDE SLOPES BEING 2:1 (H:V) OR FLATTER.
5. PLACE THE ROCK ALONG THE SHEATHING TO A HEIGHT NOT LESS THAN 18".
6. WRAP THE WIRE SHEATHING AROUND THE ROCK AND SECURE WITH THE WIRE SO THAT THE ENDS OF THE SHEATHING OVERLAP AT LEAST 2 INCHES, AND THE BERM RETAINS ITS SHAPE WHEN WALKED UPON.
7. BERM SHOULD BE BUILT ALONG THE CONTOUR AT ZERO PERCENT GRADE OR AS NEAR AS POSSIBLE.
8. THE ENDS OF THE BERM SHOULD BE TIED INTO EXISTING UPSLOPE GRADE AND THE BERM SHOULD BE BURIED IN A TRENCH APPROXIMATELY 3 TO 4 INCHES DEEP TO PREVENT FAILURE OF THE CONTROL.
9. INSPECTION SHOULD BE MADE WEEKLY AND AFTER EACH RAINFALL BY THE RESPONSIBLE PARTY; FOR INSTALLATIONS IN STREAMBEDS, ADDITIONAL DAILY INSPECTION SHOULD BE REQUIRED AS NEEDED DURING INSPECTION.
10. REMOVE SEDIMENT AND OTHER DEBRIS WHEN BUILDUP REACHES 6 INCHES AND DISPOSE OF THE ACCUMULATED SILT IN AN APPROVED MANNER AND REPAIR ANY LOOSE WIRE SHEATHING.
11. THE BERM SHOULD BE REPLACED WHEN THE STRUCTURE CEASES TO FUNCTION AS INTENDED DUE TO SILT ACCUMULATION AMONG THE ROCKS, WASHOUT, CONSTRUCTION TRAFFIC DAMAGE, ETC.
12. THE ROCK BERM SHOULD BE LEFT IN PLACE UNTIL ALL UPSTREAM AREAS ARE STABILIZED AND ACCUMULATED SILT REMOVED.

ROCK BERM

[illegible]

Agent Authorization Form
For Required Signature
Edwards Aquifer Protection Program
Relating to 30 TAC Chapter 213
Effective June 1, 1999

I John E. Chapman III,
Print Name
Superintendent,
Title - Owner/President/Other
of Comal Independent School District,
Corporation/Partnership/Entity Name
have authorized Moy Tarin Ramirez Engineers, LLC
Print Name of Agent/Engineer
of Moy Tarin Ramirez Engineers, LLC
Print Name of Firm

to represent and act on the behalf of the above named Corporation, Partnership, or Entity for the purpose of preparing and submitting this plan application to the Texas Commission on Environmental Quality (TCEQ) for the review and approval consideration of regulated activities.

I also understand that:

1. The applicant is responsible for compliance with 30 Texas Administrative Code Chapter 213 and any condition of the TCEQ's approval letter. The TCEQ is authorized to assess administrative penalties of up to \$10,000 per day per violation.
2. For those submitting an application who are not the property owner, but who have the right to control and possess the property, additional authorization is required from the owner.
3. Application fees are due and payable at the time the application is submitted. The application fee must be sent to the TCEQ cashier or to the appropriate regional office. The application will not be considered until the correct fee is received by the commission.
4. A notarized copy of the Agent Authorization Form must be provided for the person preparing the application, and this form must accompany the completed application.
5. No person shall commence any regulated activity on the Edwards Aquifer Recharge Zone, Contributing Zone or Transition Zone until the appropriate application for the activity has been filed with and approved by the Executive Director.

SIGNATURE PAGE:

[Signature]
Applicant's Signature

May 23, 2023
Date

THE STATE OF Texas §
County of Comal §

BEFORE ME, the undersigned authority, on this day personally appeared John Chapman III known to me to be the person whose name is subscribed to the foregoing instrument, and acknowledged to me that (s)he executed same for the purpose and consideration therein expressed.

GIVEN under my hand and seal of office on this 23 day of May, 2023



[Signature]
NOTARY PUBLIC
Susan Montgomery
Typed or Printed Name of Notary

MY COMMISSION EXPIRES: 2-19-2024

Application Fee Form

Texas Commission on Environmental Quality

Name of Proposed Regulated Entity: CISD SMITHSON VALLEY HIGH SCHOOL

Regulated Entity Location: 26715 S Glenrose Rd, San Antonio, TX 78260

Name of Customer: Comal ISD

Contact Person: Jeffrey Smith

Phone: (830) 221-2101

Customer Reference Number (if issued): CN 600249825

Regulated Entity Reference Number (if issued): RN 103932638

Austin Regional Office (3373)

☐ Hays

☐ Travis

☐ Williamson

San Antonio Regional Office (3362)

☐ Bexar

☐ Medina

☐ Uvalde

☒ Comal

☐ Kinney

Application fees must be paid by check, certified check, or money order, payable to the **Texas Commission on Environmental Quality**. Your canceled check will serve as your receipt. **This form must be submitted with your fee payment.** This payment is being submitted to:

☐ Austin Regional Office

☐ San Antonio Regional Office

☒ Mailed to: TCEQ - Cashier

☐ Overnight Delivery to: TCEQ - Cashier

Revenues Section

Mail Code 214

P.O. Box 13088

Austin, TX 78711-3088

12100 Park 35 Circle

Building A, 3rd Floor

Austin, TX 78753

(512)239-0357

Site Location (Check All That Apply):

☐ Recharge Zone

☒ Contributing Zone

☐ Transition Zone

Type of Plan	Size	Fee Due
Water Pollution Abatement Plan, Contributing Zone Plan: One Single Family Residential Dwelling	Acres	\$
Water Pollution Abatement Plan, Contributing Zone Plan: Multiple Single Family Residential and Parks	Acres	\$
Water Pollution Abatement Plan, Contributing Zone Plan: Non-residential	Acres	\$
Sewage Collection System	L.F.	\$
Lift Stations without sewer lines	Acres	\$
Underground or Aboveground Storage Tank Facility	Tanks	\$
Piping System(s)(only)	Each	\$
Exception	1 Each	\$ 500
Extension of Time	Each	\$

Signature: _____



Date: _____

6/17/24

Application Fee Schedule

Texas Commission on Environmental Quality

Edwards Aquifer Protection Program 30 TAC Chapter 213 (effective 05/01/2008)

Water Pollution Abatement Plans and Modifications

Contributing Zone Plans and Modifications

<i>Project</i>	<i>Project Area in Acres</i>	<i>Fee</i>
One Single Family Residential Dwelling	< 5	\$650
Multiple Single Family Residential and Parks	< 5	\$1,500
	5 < 10	\$3,000
	10 < 40	\$4,000
	40 < 100	\$6,500
	100 < 500	\$8,000
	≥ 500	\$10,000
Non-residential (Commercial, industrial, institutional, multi-family residential, schools, and other sites where regulated activities will occur)	< 1	\$3,000
	1 < 5	\$4,000
	5 < 10	\$5,000
	10 < 40	\$6,500
	40 < 100	\$8,000
	≥ 100	\$10,000

Organized Sewage Collection Systems and Modifications

<i>Project</i>	<i>Cost per Linear Foot</i>	<i>Minimum Fee- Maximum Fee</i>
Sewage Collection Systems	\$0.50	\$650 - \$6,500

Underground and Aboveground Storage Tank System Facility Plans and Modifications

<i>Project</i>	<i>Cost per Tank or Piping System</i>	<i>Minimum Fee- Maximum Fee</i>
Underground and Aboveground Storage Tank Facility	\$650	\$650 - \$6,500

Exception Requests

<i>Project</i>	<i>Fee</i>
Exception Request	\$500

Extension of Time Requests

<i>Project</i>	<i>Fee</i>
Extension of Time Request	\$150



TCEQ Use Only

TCEQ Core Data Form

For detailed instructions regarding completion of this form, please read the Core Data Form Instructions or call 512-239-5175.

SECTION I: General Information

1. Reason for Submission (If other is checked please describe in space provided.)		
<input checked="" type="checkbox"/> New Permit, Registration or Authorization (Core Data Form should be submitted with the program application.)		
<input type="checkbox"/> Renewal (Core Data Form should be submitted with the renewal form)	<input type="checkbox"/> Other	
2. Customer Reference Number (if issued)	Follow this link to search for CN or RN numbers in Central Registry**	3. Regulated Entity Reference Number (if issued)
CN 600249825		RN 103932638

SECTION II: Customer Information

4. General Customer Information		5. Effective Date for Customer Information Updates (mm/dd/yyyy)			
<input type="checkbox"/> New Customer		<input type="checkbox"/> Update to Customer Information		<input type="checkbox"/> Change in Regulated Entity Ownership	
<input type="checkbox"/> Change in Legal Name (Verifiable with the Texas Secretary of State or Texas Comptroller of Public Accounts)					
The Customer Name submitted here may be updated automatically based on what is current and active with the Texas Secretary of State (SOS) or Texas Comptroller of Public Accounts (CPA).					
6. Customer Legal Name (If an individual, print last name first: eg: Doe, John)				If new Customer, enter previous Customer below:	
7. TX SOS/CPA Filing Number		8. TX State Tax ID (11 digits)		9. Federal Tax ID (9 digits)	
				10. DUNS Number (if applicable)	
11. Type of Customer:		<input type="checkbox"/> Corporation		<input type="checkbox"/> Individual	
				Partnership: <input type="checkbox"/> General <input type="checkbox"/> Limited	
Government: <input type="checkbox"/> City <input type="checkbox"/> County <input type="checkbox"/> Federal <input type="checkbox"/> State <input type="checkbox"/> Other		<input type="checkbox"/> Sole Proprietorship		<input type="checkbox"/> Other:	
12. Number of Employees				13. Independently Owned and Operated?	
<input type="checkbox"/> 0-20 <input type="checkbox"/> 21-100 <input type="checkbox"/> 101-250 <input type="checkbox"/> 251-500 <input type="checkbox"/> 501 and higher				<input type="checkbox"/> Yes <input type="checkbox"/> No	
14. Customer Role (Proposed or Actual) – as it relates to the Regulated Entity listed on this form. Please check one of the following					
<input type="checkbox"/> Owner <input type="checkbox"/> Operator <input type="checkbox"/> Owner & Operator					
<input type="checkbox"/> Occupational Licensee <input type="checkbox"/> Responsible Party <input type="checkbox"/> Voluntary Cleanup Applicant <input type="checkbox"/> Other:					
15. Mailing Address:					
City					
State					
ZIP					
ZIP + 4					
16. Country Mailing Information (if outside USA)					
17. E-Mail Address (if applicable)					
18. Telephone Number		19. Extension or Code		20. Fax Number (if applicable)	
() -				() -	

SECTION III: Regulated Entity Information

21. General Regulated Entity Information (If 'New Regulated Entity' is selected below this form should be accompanied by a permit application)	
<input type="checkbox"/> New Regulated Entity <input type="checkbox"/> Update to Regulated Entity Name <input type="checkbox"/> Update to Regulated Entity Information	
The Regulated Entity Name submitted may be updated in order to meet TCEQ Agency Data Standards (removal of organizational endings such as Inc, LP, or LLC).	
22. Regulated Entity Name (Enter name of the site where the regulated action is taking place.)	
CISD SMITHSON VALLEY HIGH SCHOOL	

23. Street Address of the Regulated Entity: (No PO Boxes)	1404 IH 35 North, New Braunfels						
	City		State	TX	ZIP	78260	ZIP + 4
24. County	Comal						

Enter Physical Location Description if no street address is provided.

25. Description to Physical Location:							
26. Nearest City	State				Nearest ZIP Code		
Spring Branch	TX				78070		
27. Latitude (N) In Decimal:	29.804388		28. Longitude (W) In Decimal:	-98.358414			
Degrees	Minutes	Seconds	Degrees	Minutes	Seconds		
29	42	15.80	98	21	30.29		
29. Primary SIC Code (4 digits)	30. Secondary SIC Code (4 digits)		31. Primary NAICS Code (5 or 6 digits)	32. Secondary NAICS Code (5 or 6 digits)			
8211			611110				
33. What is the Primary Business of this entity? (Do not repeat the SIC or NAICS description.)							
High School							
34. Mailing Address:	14001 TX-46						
	City	Spring Branch	State	TX	ZIP	78070	ZIP + 4
35. E-Mail Address:	jeffrey.smith@comalisd.org						
36. Telephone Number	37. Extension or Code		38. Fax Number (if applicable)				
(830) 885-8500			() -				

39. TCEQ Programs and ID Numbers Check all Programs and write in the permits/registration numbers that will be affected by the updates submitted on this form. See the Core Data Form instructions for additional guidance.


<input type="checkbox"/> Dam Safety	<input type="checkbox"/> Districts	<input checked="" type="checkbox"/> Edwards Aquifer	<input type="checkbox"/> Emissions Inventory Air	<input type="checkbox"/> Industrial Hazardous Waste
<input type="checkbox"/> Municipal Solid Waste	<input type="checkbox"/> New Source Review Air	<input type="checkbox"/> OSSF	<input type="checkbox"/> Petroleum Storage Tank	<input type="checkbox"/> PWS
<input type="checkbox"/> Sludge	<input type="checkbox"/> Storm Water	<input type="checkbox"/> Title V Air	<input type="checkbox"/> Tires	<input type="checkbox"/> Used Oil
<input type="checkbox"/> Voluntary Cleanup	<input type="checkbox"/> Waste Water	<input type="checkbox"/> Wastewater Agriculture	<input type="checkbox"/> Water Rights	<input type="checkbox"/> Other:

SECTION IV: Preparer Information

40. Name:	Sean Smith, P.E.	41. Title:	Senior Vice President
42. Telephone Number	43. Ext./Code	44. Fax Number	45. E-Mail Address
(210) 698-5051		(210) 698-5085	ssmith@mtrengineers.com

SECTION V: Authorized Signature

46. By my signature below, I certify, to the best of my knowledge, that the information provided in this form is true and complete, and that I have signature authority to submit this form on behalf of the entity specified in Section II, Field 6 and/or as required for the updates to the ID numbers identified in field 39.

Company:	Moy Tarin Ramirez Engineers, LLC	Job Title:	Senior Vice President
Name (In Print):	Sean Smith, P.E.	Phone:	(210) 698- 5051
Signature:		Date:	
