

Texas Commission on Environmental Quality

Edwards Aquifer Application Cover Page

Our Review of Your Application

The Edwards Aquifer Program staff conducts an administrative and technical review of all applications. The turnaround time for administrative review can be up to 30 days as outlined in 30 TAC 213.4(e). Generally administrative completeness is determined during the intake meeting or within a few days of receipt. The turnaround time for technical review of an administratively complete Edwards Aquifer application is 90 days as outlined in 30 TAC 213.4(e). Please know that the review and approval time is directly impacted by the quality and completeness of the initial application that is received. In order to conduct a timely review, it is imperative that the information provided in an Edwards Aquifer application include final plans, be accurate, complete, and in compliance with [30 TAC 213](#).

Administrative Review

1. [Edwards Aquifer applications](#) must be deemed administratively complete before a technical review can begin. To be considered administratively complete, the application must contain completed forms and attachments, provide the requested information, and meet all the site plan requirements. The submitted application and plan sheets should be final plans. Please submit one full-size set of plan sheets with the original application, and half-size sets with the additional copies.

To ensure that all applicable documents are included in the application, the program has developed tools to guide you and web pages to provide all forms, checklists, and guidance. Please visit the below website for assistance: <http://www.tceq.texas.gov/field/eapp>.

2. This Edwards Aquifer Application Cover Page form (certified by the applicant or agent) must be included in the application and brought to the administrative review meeting.
3. Administrative reviews are scheduled with program staff who will conduct the review. Applicants or their authorized agent should call the appropriate regional office, according to the county in which the project is located, to schedule a review. The average meeting time is one hour.
4. In the meeting, the application is examined for administrative completeness. Deficiencies will be noted by staff and emailed or faxed to the applicant and authorized agent at the end of the meeting, or shortly after. Administrative deficiencies will cause the application to be deemed incomplete and returned.

An appointment should be made to resubmit the application. The application is re-examined to ensure all deficiencies are resolved. The application will only be deemed administratively complete when all administrative deficiencies are addressed.

5. If an application is received by mail, courier service, or otherwise submitted without a review meeting, the administrative review will be conducted within 30 days. The applicant and agent will be contacted with the results of the administrative review. If the application is found to be administratively incomplete, it can be retrieved from the regional office or returned by regular mail. If returned by mail, the regional office may require arrangements for return shipping.
6. If the geologic assessment was completed before October 1, 2004 and the site contains “possibly sensitive” features, the assessment must be updated in accordance with the *Instructions to Geologists* (TCEQ-0585 Instructions).

Technical Review

1. When an application is deemed administratively complete, the technical review period begins. The regional office will distribute copies of the application to the identified affected city, county, and groundwater conservation district whose jurisdiction includes the subject site. These entities and the public have 30 days to provide comments on the application to the regional office. All comments received are reviewed by TCEQ.
2. A site assessment is usually conducted as part of the technical review, to evaluate the geologic assessment and observe existing site conditions. The site must be accessible to our staff. The site boundaries should be

clearly marked, features identified in the geologic assessment should be flagged, roadways marked and the alignment of the Sewage Collection System and manholes should be staked at the time the application is submitted. If the site is not marked the application may be returned.

3. We evaluate the application for technical completeness and contact the applicant and agent via Notice of Deficiency (NOD) to request additional information and identify technical deficiencies. There are two deficiency response periods available to the applicant. There are 14 days to resolve deficiencies noted in the first NOD. If a second NOD is issued, there is an additional 14 days to resolve deficiencies. If the response to the second notice is not received, is incomplete or inadequate, or provides new information that is incomplete or inadequate, the application must be withdrawn or will be denied. Please note that because the technical review is underway, whether the application is withdrawn or denied **the application fee will be forfeited**.
4. The program has 90 calendar days to complete the technical review of the application. If the application is technically adequate, such that it complies with the Edwards Aquifer rules, and is protective of the Edwards Aquifer during and after construction, an approval letter will be issued. Construction or other regulated activity may not begin until an approval is issued.

Mid-Review Modifications

It is important to have final site plans prior to beginning the permitting process with TCEQ to avoid delays.

Occasionally, circumstances arise where you may have significant design and/or site plan changes after your Edwards Aquifer application has been deemed administratively complete by TCEQ. This is considered a “Mid-Review Modification”. Mid-Review Modifications may require redistribution of an application that includes the proposed modifications for public comment.

If you are proposing a Mid-Review Modification, two options are available:

- If the technical review has begun your application can be denied/withdrawn, your fees will be forfeited, and the plan will have to be resubmitted.
- TCEQ can continue the technical review of the application as it was submitted, and a modification application can be submitted at a later time.

If the application is denied/withdrawn, the resubmitted application will be subject to the administrative and technical review processes and will be treated as a new application. The application will be redistributed to the affected jurisdictions.

Please contact the regional office if you have questions. If your project is located in Williamson, Travis, or Hays County, contact TCEQ’s Austin Regional Office at 512-339-2929. If your project is in Comal, Bexar, Medina, Uvalde, or Kinney County, contact TCEQ’s San Antonio Regional Office at 210-490-3096

Please fill out all required fields below and submit with your application.

1. Regulated Entity Name: Vance Jackson Remote Parking Lot					2. Regulated Entity No.:				
3. Customer Name: Tessi Properties, LLC					4. Customer No.:				
5. Project Type: (Please circle/check one)	<input checked="" type="radio"/> New		Modification		Extension		Exception		
6. Plan Type: (Please circle/check one)	WPAP	<input checked="" type="radio"/> CZP	SCS	UST	AST	EXP	EXT	Technical Clarification	Optional Enhanced Measures
7. Land Use: (Please circle/check one)	Residential		<input checked="" type="radio"/> Non-residential			8. Site (acres):		7.50 acres	
9. Application Fee:	\$5,000		10. Permanent BMP(s):				Partial Sedimentation & Filtration System (Sand Basin)		
11. SCS (Linear Ft.):			12. AST/UST (No. Tanks):						
13. County:	Bexar		14. Watershed:				Upper SAR Watershed		

Application Distribution

Instructions: Use the table below to determine the number of applications required. One original and one copy of the application, plus additional copies (as needed) for each affected incorporated city, county, and groundwater conservation district are required. Linear projects or large projects, which cross into multiple jurisdictions, can require additional copies. Refer to the “Texas Groundwater Conservation Districts within the EAPP Boundaries” map found at:

http://www.tceq.texas.gov/assets/public/compliance/field_ops/eapp/EAPP%20GWCD%20map.pdf

For more detailed boundaries, please contact the conservation district directly.

Austin Region			
County:	Hays	Travis	Williamson
Original (1 req.)	—	—	—
Region (1 req.)	—	—	—
County(ies)	—	—	—
Groundwater Conservation District(s)	<input type="checkbox"/> Edwards Aquifer Authority <input type="checkbox"/> Barton Springs/ Edwards Aquifer <input type="checkbox"/> Hays Trinity <input type="checkbox"/> Plum Creek	<input type="checkbox"/> Barton Springs/ Edwards Aquifer	NA
City(ies) Jurisdiction	<input type="checkbox"/> Austin <input type="checkbox"/> Buda <input type="checkbox"/> Dripping Springs <input type="checkbox"/> Kyle <input type="checkbox"/> Mountain City <input type="checkbox"/> San Marcos <input type="checkbox"/> Wimberley <input type="checkbox"/> Woodcreek	<input type="checkbox"/> Austin <input type="checkbox"/> Bee Cave <input type="checkbox"/> Pflugerville <input type="checkbox"/> Rollingwood <input type="checkbox"/> Round Rock <input type="checkbox"/> Sunset Valley <input type="checkbox"/> West Lake Hills	<input type="checkbox"/> Austin <input type="checkbox"/> Cedar Park <input type="checkbox"/> Florence <input type="checkbox"/> Georgetown <input type="checkbox"/> Jerrell <input type="checkbox"/> Leander <input type="checkbox"/> Liberty Hill <input type="checkbox"/> Pflugerville <input type="checkbox"/> Round Rock

San Antonio Region					
County:	Bexar	Comal	Kinney	Medina	Uvalde
Original (1 req.)	<u>X</u>	—	—	—	—
Region (1 req.)	<u>X</u>	—	—	—	—
County(ies)	<u>X</u>	—	—	—	—
Groundwater Conservation District(s)	<input checked="" type="checkbox"/> Edwards Aquifer Authority <input checked="" type="checkbox"/> Trinity-Glen Rose	<input type="checkbox"/> Edwards Aquifer Authority	<input type="checkbox"/> Kinney	<input type="checkbox"/> EAA <input type="checkbox"/> Medina	<input type="checkbox"/> EAA <input type="checkbox"/> Uvalde
City(ies) Jurisdiction	<input type="checkbox"/> Castle Hills <input type="checkbox"/> Fair Oaks Ranch <input type="checkbox"/> Helotes <input type="checkbox"/> Hill Country Village <input type="checkbox"/> Hollywood Park <input checked="" type="checkbox"/> San Antonio (SAWS) <input type="checkbox"/> Shavano Park	<input type="checkbox"/> Bulverde <input type="checkbox"/> Fair Oaks Ranch <input type="checkbox"/> Garden Ridge <input type="checkbox"/> New Braunfels <input type="checkbox"/> Schertz	NA	<input type="checkbox"/> San Antonio ETJ (SAWS)	NA

I certify that to the best of my knowledge, that the application is complete and accurate. This application is hereby submitted to TCEQ for administrative review and technical review.

Kevin W. Love, P.E.

Print Name of Customer/Authorized Agent

Signature of Customer/Authorized Agent

Date

12/3/24

****FOR TCEQ INTERNAL USE ONLY****

Date(s) Reviewed:		Date Administratively Complete:	
Received From:		Correct Number of Copies:	
Received By:		Distribution Date:	
EAPP File Number:		Complex:	
Admin. Review(s) (No.):		No. AR Rounds:	
Delinquent Fees (Y/N):		Review Time Spent:	
Lat./Long. Verified:		SOS Customer Verification:	
Agent Authorization Complete/Notarized (Y/N):		Fee Check:	Payable to TCEQ (Y/N):
Core Data Form Complete (Y/N):			Signed (Y/N):
Core Data Form Incomplete Nos.:			Less than 90 days old (Y/N):

Contributing Zone Plan Application

Texas Commission on Environmental Quality

for Regulated Activities on the Contributing Zone to the Edwards Aquifer and Relating to 30 TAC §213.24(1), Effective June 1, 1999

To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.

Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.

Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Contributing Zone Plan Application** is hereby submitted for TCEQ review and Executive Director approval. The application was prepared by:

Print Name of Customer/Agent: Kevin W. Love, P.E.

Date: _____

Signature of Customer/Agent:

 12/3/24

Regulated Entity Name: Vance Jackson Remote Parking Lot

Project Information

1. County: Bexar
2. Stream Basin: Olmos Creek
3. Groundwater Conservation District (if applicable): Trinity Glen Rose GCD
4. Customer (Applicant):

Contact Person: Abigail Kampmann

Entity: Tessi Properties, LLC

Mailing Address: 153 Treeline Park, Suite 100

City, State: San Antonio, Texas

Telephone: 210-437-3961

Email Address: akampmann@principleauto.com

Zip: 78209

Fax: n/a

5. Agent/Representative (If any):

Contact Person: Kevin W. Love, P.E.

Entity: KLove Engineering, LLC

Mailing Address: 22610 US Highway 281 North, Ste. 204

City, State: San Antonio, Texas

Zip: 78258

Telephone: (210)485-5683

Fax: n/a

Email Address: klove@kloveengineering.com

6. Project Location:

- ☒ The project site is located inside the city limits of San Antonio.
- ☐ The project site is located outside the city limits but inside the ETJ (extra-territorial jurisdiction) of _____.
- ☐ The project site is not located within any city's limits or ETJ.

7. ☒ The location of the project site is described below. Sufficient detail and clarity has been provided so that the TCEQ's Regional staff can easily locate the project and site boundaries for a field investigation.

15480 Vance Jackson, San Antonio, TX 78249

8. ☒ **Attachment A - Road Map.** A road map showing directions to and the location of the project site is attached. The map clearly shows the boundary of the project site.

9. ☒ **Attachment B - USGS Quadrangle Map.** A copy of the official 7 ½ minute USGS Quadrangle Map (Scale: 1" = 2000") is attached. The map(s) clearly show:

- ☒ Project site boundaries.
- ☒ USGS Quadrangle Name(s).

10. ☒ **Attachment C - Project Narrative.** A detailed narrative description of the proposed project is attached. The project description is consistent throughout the application and contains, at a minimum, the following details:

- ☒ Area of the site
- ☒ Offsite areas
- ☒ Impervious cover
- ☒ Permanent BMP(s)
- ☒ Proposed site use
- ☒ Site history
- ☒ Previous development
- ☒ Area(s) to be demolished

11. Existing project site conditions are noted below:

- ☒ Existing commercial site
- ☐ Existing industrial site
- ☐ Existing residential site

- ☐ Existing paved and/or unpaved roads
☐ Undeveloped (Cleared)
☒ Undeveloped (Undisturbed/Not cleared)
☐ Other: _____

12. The type of project is:

- ☐ Residential: # of Lots: _____
☐ Residential: # of Living Unit Equivalents: _____
☒ Commercial
☐ Industrial
☐ Other: _____

13. Total project area (size of site): 7.50 Acres

Total disturbed area: 7.50 Acres

14. Estimated projected population: 0

15. The amount and type of impervious cover expected after construction is complete is shown below:

Table 1 - Impervious Cover

<i>Impervious Cover of Proposed Project</i>	<i>Sq. Ft.</i>	<i>Sq. Ft./Acre</i>	<i>Acres</i>
Structures/Rooftops	0	÷ 43,560 =	0
Parking	259,878	÷ 43,560 =	5.97
Other paved surfaces	0	÷ 43,560 =	0
Total Impervious Cover	259,878	÷ 43,560 =	5.97

Total Impervious Cover $5.97 \div \text{Total Acreage } 7.50 \times 100 = 79.60\%$ Impervious Cover

16. ☒ **Attachment D - Factors Affecting Surface Water Quality.** A detailed description of all factors that could affect surface water quality is attached. If applicable, this includes the location and description of any discharge associated with industrial activity other than construction.
17. ☒ Only inert materials as defined by 30 TAC 330.2 will be used as fill material.

For Road Projects Only

Complete questions 18 - 23 if this application is exclusively for a road project.

☐ N/A

18. Type of project:

- ☐ TXDOT road project.
- ☐ County road or roads built to county specifications.
- ☐ City thoroughfare or roads to be dedicated to a municipality.
- ☐ Street or road providing access to private driveways.

19. Type of pavement or road surface to be used:

- ☐ Concrete
- ☐ Asphaltic concrete pavement
- ☐ Other: _____

20. Right of Way (R.O.W.):

Length of R.O.W.: _____ feet.

Width of R.O.W.: _____ feet.

$L \times W = \text{_____ Ft}^2 \div 43,560 \text{ Ft}^2/\text{Acre} = \text{_____ acres.}$

21. Pavement Area:

Length of pavement area: _____ feet.

Width of pavement area: _____ feet.

$L \times W = \text{_____ Ft}^2 \div 43,560 \text{ Ft}^2/\text{Acre} = \text{_____ acres.}$

Pavement area _____ acres \div R.O.W. area _____ acres $\times 100 = \text{_____ \%}$ impervious cover.

22. ☐ A rest stop will be included in this project.

☐ A rest stop will not be included in this project.

23. ☐ Maintenance and repair of existing roadways that do not require approval from the TCEQ Executive Director. Modifications to existing roadways such as widening roads/adding shoulders totaling more than one-half (1/2) the width of one (1) existing lane require prior approval from the TCEQ.

Stormwater to be generated by the Proposed Project

24. ☒ **Attachment E - Volume and Character of Stormwater.** A detailed description of the volume (quantity) and character (quality) of the stormwater runoff which is expected to occur from the proposed project is attached. The estimates of stormwater runoff quality and quantity are based on area and type of impervious cover. Include the runoff coefficient of the site for both pre-construction and post-construction conditions.

Wastewater to be generated by the Proposed Project

25. ☒ Wastewater is to be discharged in the contributing zone. Requirements under 30 TAC §213.6(c) relating to Wastewater Treatment and Disposal Systems have been satisfied.

☐ N/A

26. Wastewater will be disposed of by:

☐ On-Site Sewage Facility (OSSF/Septic Tank):

☐ **Attachment F - Suitability Letter from Authorized Agent.** An on-site sewage facility will be used to treat and dispose of the wastewater from this site. The appropriate licensing authority's (authorized agent) written approval is attached. It states that the land is suitable for the use of private sewage facilities and will meet or exceed the requirements for on-site sewage facilities as specified under 30 TAC Chapter 285 relating to On-site Sewage Facilities.

☐ Each lot in this project/development is at least one (1) acre (43,560 square feet) in size. The system will be designed by a licensed professional engineer or registered sanitarian and installed by a licensed installer in compliance with 30 TAC Chapter 285.

☒ Sewage Collection System (Sewer Lines):

The sewage collection system will convey the wastewater to the Leon Creek Water Recycling Center (name) Treatment Plant. The treatment facility is:

☒ Existing.

☐ Proposed.

☐ N/A

Permanent Aboveground Storage Tanks(ASTs) ≥ 500 Gallons

Complete questions 27 - 33 if this project includes the installation of AST(s) with volume(s) greater than or equal to 500 gallons.

☒ N/A

27. Tanks and substance stored:

Table 2 - Tanks and Substance Storage

<i>AST Number</i>	<i>Size (Gallons)</i>	<i>Substance to be Stored</i>	<i>Tank Material</i>
1			
2			
3			
4			
5			

Total x 1.5 = _____ Gallons

28. ☐ The AST will be placed within a containment structure that is sized to capture one and one-half (1 1/2) times the storage capacity of the system. For facilities with more than

5 of 11

one tank system, the containment structure is sized to capture one and one-half (1 1/2) times the cumulative storage capacity of all systems.

- ☐ **Attachment G - Alternative Secondary Containment Methods.** Alternative methods for providing secondary containment are proposed. Specifications showing equivalent protection for the Edwards Aquifer are attached.

29. Inside dimensions and capacity of containment structure(s):

Table 3 - Secondary Containment

<i>Length (L)(Ft.)</i>	<i>Width(W)(Ft.)</i>	<i>Height (H)(Ft.)</i>	<i>L x W x H = (Ft3)</i>	<i>Gallons</i>

Total: _____ Gallons

30. Piping:

- ☐ All piping, hoses, and dispensers will be located inside the containment structure.
- ☐ Some of the piping to dispensers or equipment will extend outside the containment structure.
- ☐ The piping will be aboveground
- ☐ The piping will be underground

31. ☐ The containment area must be constructed of and in a material impervious to the substance(s) being stored. The proposed containment structure will be constructed of: _____.

32. ☐ **Attachment H - AST Containment Structure Drawings.** A scaled drawing of the containment structure is attached that shows the following:

- ☐ Interior dimensions (length, width, depth and wall and floor thickness).
- ☐ Internal drainage to a point convenient for the collection of any spillage.
- ☐ Tanks clearly labeled
- ☐ Piping clearly labeled
- ☐ Dispenser clearly labeled

33. ☐ Any spills must be directed to a point convenient for collection and recovery. Spills from storage tank facilities must be removed from the controlled drainage area for disposal within 24 hours of the spill.

- ☐ In the event of a spill, any spillage will be removed from the containment structure within 24 hours of the spill and disposed of properly.

- ☐ In the event of a spill, any spillage will be drained from the containment structure through a drain and valve within 24 hours of the spill and disposed of properly. The drain and valve system are shown in detail on the scaled drawing.

Site Plan Requirements

Items 34 - 46 must be included on the Site Plan.

34. ☒ The Site Plan must have a minimum scale of 1" = 400'.
Site Plan Scale: 1" = 40'.
35. 100-year floodplain boundaries:
- ☐ Some part(s) of the project site is located within the 100-year floodplain. The floodplain is shown and labeled.
- ☒ No part of the project site is located within the 100-year floodplain.
The 100-year floodplain boundaries are based on the following specific (including date of material) sources(s): 48029C0230G 9/29/2010.
36. ☒ The layout of the development is shown with existing and finished contours at appropriate, but not greater than ten-foot contour intervals. Lots, recreation centers, buildings, roads, etc. are shown on the site plan.
- ☐ The layout of the development is shown with existing contours at appropriate, but not greater than ten-foot contour intervals. Finished topographic contours will not differ from the existing topographic configuration and are not shown. Lots, recreation centers, buildings, roads, etc. are shown on the site plan.
37. ☒ A drainage plan showing all paths of drainage from the site to surface streams.
38. ☒ The drainage patterns and approximate slopes anticipated after major grading activities.
39. ☒ Areas of soil disturbance and areas which will not be disturbed.
40. ☒ Locations of major structural and nonstructural controls. These are the temporary and permanent best management practices.
41. ☒ Locations where soil stabilization practices are expected to occur.
42. ☐ Surface waters (including wetlands).
☒ N/A
43. ☐ Locations where stormwater discharges to surface water.
☒ There will be no discharges to surface water.
44. ☐ Temporary aboveground storage tank facilities.
☒ Temporary aboveground storage tank facilities will not be located on this site.

45. ☐ Permanent aboveground storage tank facilities.
☒ Permanent aboveground storage tank facilities will not be located on this site.
46. ☒ Legal boundaries of the site are shown.

Permanent Best Management Practices (BMPs)

Practices and measures that will be used during and after construction is completed.

47. ☒ Permanent BMPs and measures must be implemented to control the discharge of pollution from regulated activities after the completion of construction.
☐ N/A
48. ☒ These practices and measures have been designed, and will be constructed, operated, and maintained to insure that 80% of the incremental increase in the annual mass loading of total suspended solids (TSS) from the site caused by the regulated activity is removed. These quantities have been calculated in accordance with technical guidance prepared or accepted by the executive director.
☒ The TCEQ Technical Guidance Manual (TGM) was used to design permanent BMPs and measures for this site.
☐ A technical guidance other than the TCEQ TGM was used to design permanent BMPs and measures for this site. The complete citation for the technical guidance that was used is: _____.
☐ N/A
49. ☒ Owners must insure that permanent BMPs and measures are constructed and function as designed. A Texas Licensed Professional Engineer must certify in writing that the permanent BMPs or measures were constructed as designed. The certification letter must be submitted to the appropriate regional office within 30 days of site completion.
☐ N/A
50. Where a site is used for low density single-family residential development and has 20 % or less impervious cover, other permanent BMPs are not required. This exemption from permanent BMPs must be recorded in the county deed records, with a notice that if the percent impervious cover increases above 20% or land use changes, the exemption for the whole site as described in the property boundaries required by 30 TAC §213.4(g) (relating to Application Processing and Approval), may no longer apply and the property owner must notify the appropriate regional office of these changes.
☐ The site will be used for low density single-family residential development and has 20% or less impervious cover.
☐ The site will be used for low density single-family residential development but has more than 20% impervious cover.
☒ The site will not be used for low density single-family residential development.

51. The executive director may waive the requirement for other permanent BMPs for multi-family residential developments, schools, or small business sites where 20% or less impervious cover is used at the site. This exemption from permanent BMPs must be recorded in the county deed records, with a notice that if the percent impervious cover increases above 20% or land use changes, the exemption for the whole site as described in the property boundaries required by 30 TAC §213.4(g) (relating to Application Processing and Approval), may no longer apply and the property owner must notify the appropriate regional office of these changes.

☐ **Attachment I - 20% or Less Impervious Cover Waiver.** The site will be used for multi-family residential developments, schools, or small business sites and has 20% or less impervious cover. A request to waive the requirements for other permanent BMPs and measures is attached.

☒ The site will be used for multi-family residential developments, schools, or small business sites but has more than 20% impervious cover.

☐ The site will not be used for multi-family residential developments, schools, or small business sites.

52. ☒ **Attachment J - BMPs for Upgradient Stormwater.**

☐ A description of the BMPs and measures that will be used to prevent pollution of surface water, groundwater, or stormwater that originates upgradient from the site and flows across the site is attached.

☐ No surface water, groundwater or stormwater originates upgradient from the site and flows across the site, and an explanation is attached.

☒ Permanent BMPs or measures are not required to prevent pollution of surface water, groundwater, or stormwater that originates upgradient from the site and flows across the site, and an explanation is attached.

53. ☒ **Attachment K - BMPs for On-site Stormwater.**

☒ A description of the BMPs and measures that will be used to prevent pollution of surface water or groundwater that originates on-site or flows off the site, including pollution caused by contaminated stormwater runoff from the site is attached.

☐ Permanent BMPs or measures are not required to prevent pollution of surface water or groundwater that originates on-site or flows off the site, including pollution caused by contaminated stormwater runoff, and an explanation is attached.

54. ☐ **Attachment L - BMPs for Surface Streams.** A description of the BMPs and measures that prevent pollutants from entering surface streams is attached.

☒ N/A

55. ☒ **Attachment M - Construction Plans.** Construction plans and design calculations for the proposed permanent BMPs and measures have been prepared by or under the direct supervision of a Texas Licensed Professional Engineer, and are signed, sealed, and dated. Construction plans for the proposed permanent BMPs and measures are

attached and include: Design calculations, TCEQ Construction Notes, all proposed structural plans and specifications, and appropriate details.

☐ N/A

56. ☒ **Attachment N - Inspection, Maintenance, Repair and Retrofit Plan.** A site and BMP specific plan for the inspection, maintenance, repair, and, if necessary, retrofit of the permanent BMPs and measures is attached. The plan fulfills all of the following:

- ☒ Prepared and certified by the engineer designing the permanent BMPs and measures
- ☒ Signed by the owner or responsible party
- ☒ Outlines specific procedures for documenting inspections, maintenance, repairs, and, if necessary, retrofit.
- ☒ Contains a discussion of record keeping procedures

☐ N/A

57. ☐ **Attachment O - Pilot-Scale Field Testing Plan.** Pilot studies for BMPs that are not recognized by the Executive Director require prior approval from the TCEQ. A plan for pilot-scale field testing is attached.

☒ N/A

58. ☐ **Attachment P - Measures for Minimizing Surface Stream Contamination.** A description of the measures that will be used to avoid or minimize surface stream contamination and changes in the way in which water enters a stream as a result of the construction and development is attached. The measures address increased stream flashing, the creation of stronger flows and in-stream velocities, and other in-stream effects caused by the regulated activity, which increase erosion that result in water quality degradation.

☒ N/A

Responsibility for Maintenance of Permanent BMPs and Measures after Construction is Complete.

59. ☒ The applicant is responsible for maintaining the permanent BMPs after construction until such time as the maintenance obligation is either assumed in writing by another entity having ownership or control of the property (such as without limitation, an owner's association, a new property owner or lessee, a district, or municipality) or the ownership of the property is transferred to the entity. Such entity shall then be responsible for maintenance until another entity assumes such obligations in writing or ownership is transferred.
60. ☒ A copy of the transfer of responsibility must be filed with the executive director at the appropriate regional office within 30 days of the transfer if the site is for use as a multiple single-family residential development, a multi-family residential development,

or a non-residential development such as commercial, industrial, institutional, schools, and other sites where regulated activities occur.

Administrative Information

- 61. ☒ Submit one (1) original and one (1) copy of the application, plus additional copies as needed for each affected incorporated city, groundwater conservation district, and county in which the project will be located. The TCEQ will distribute the additional copies to these jurisdictions.
- 62. ☒ Any modification of this Contributing Zone Plan may require TCEQ review and Executive Director approval prior to construction, and may require submission of a revised application, with appropriate fees.
- 63. ☒ The site description, controls, maintenance, and inspection requirements for the storm water pollution prevention plan (SWPPP) developed under the EPA NPDES general permits for stormwater discharges have been submitted to fulfill paragraphs 30 TAC §213.24(1-5) of the technical report. All requirements of 30 TAC §213.24(1-5) have been met by the SWPPP document.
- ☒ The Temporary Stormwater Section (TCEQ-0602) is included with the application.



PROJECT NO. 1448-02

DATE: 10/07/24

DRAWN BY: JC DESIGNED BY: AB


SCALE: N.T.S.

VANCE JACKSON PARKING

VANCE JACKSON
SAN ANTONIO, TEXAS 78249

ATTACHMENT A - ROAD MAP

K Love
ENGINEERING
Site Development Engineering Services
Firm No. 11042
www.kloveengineering.com (210) 485-5683

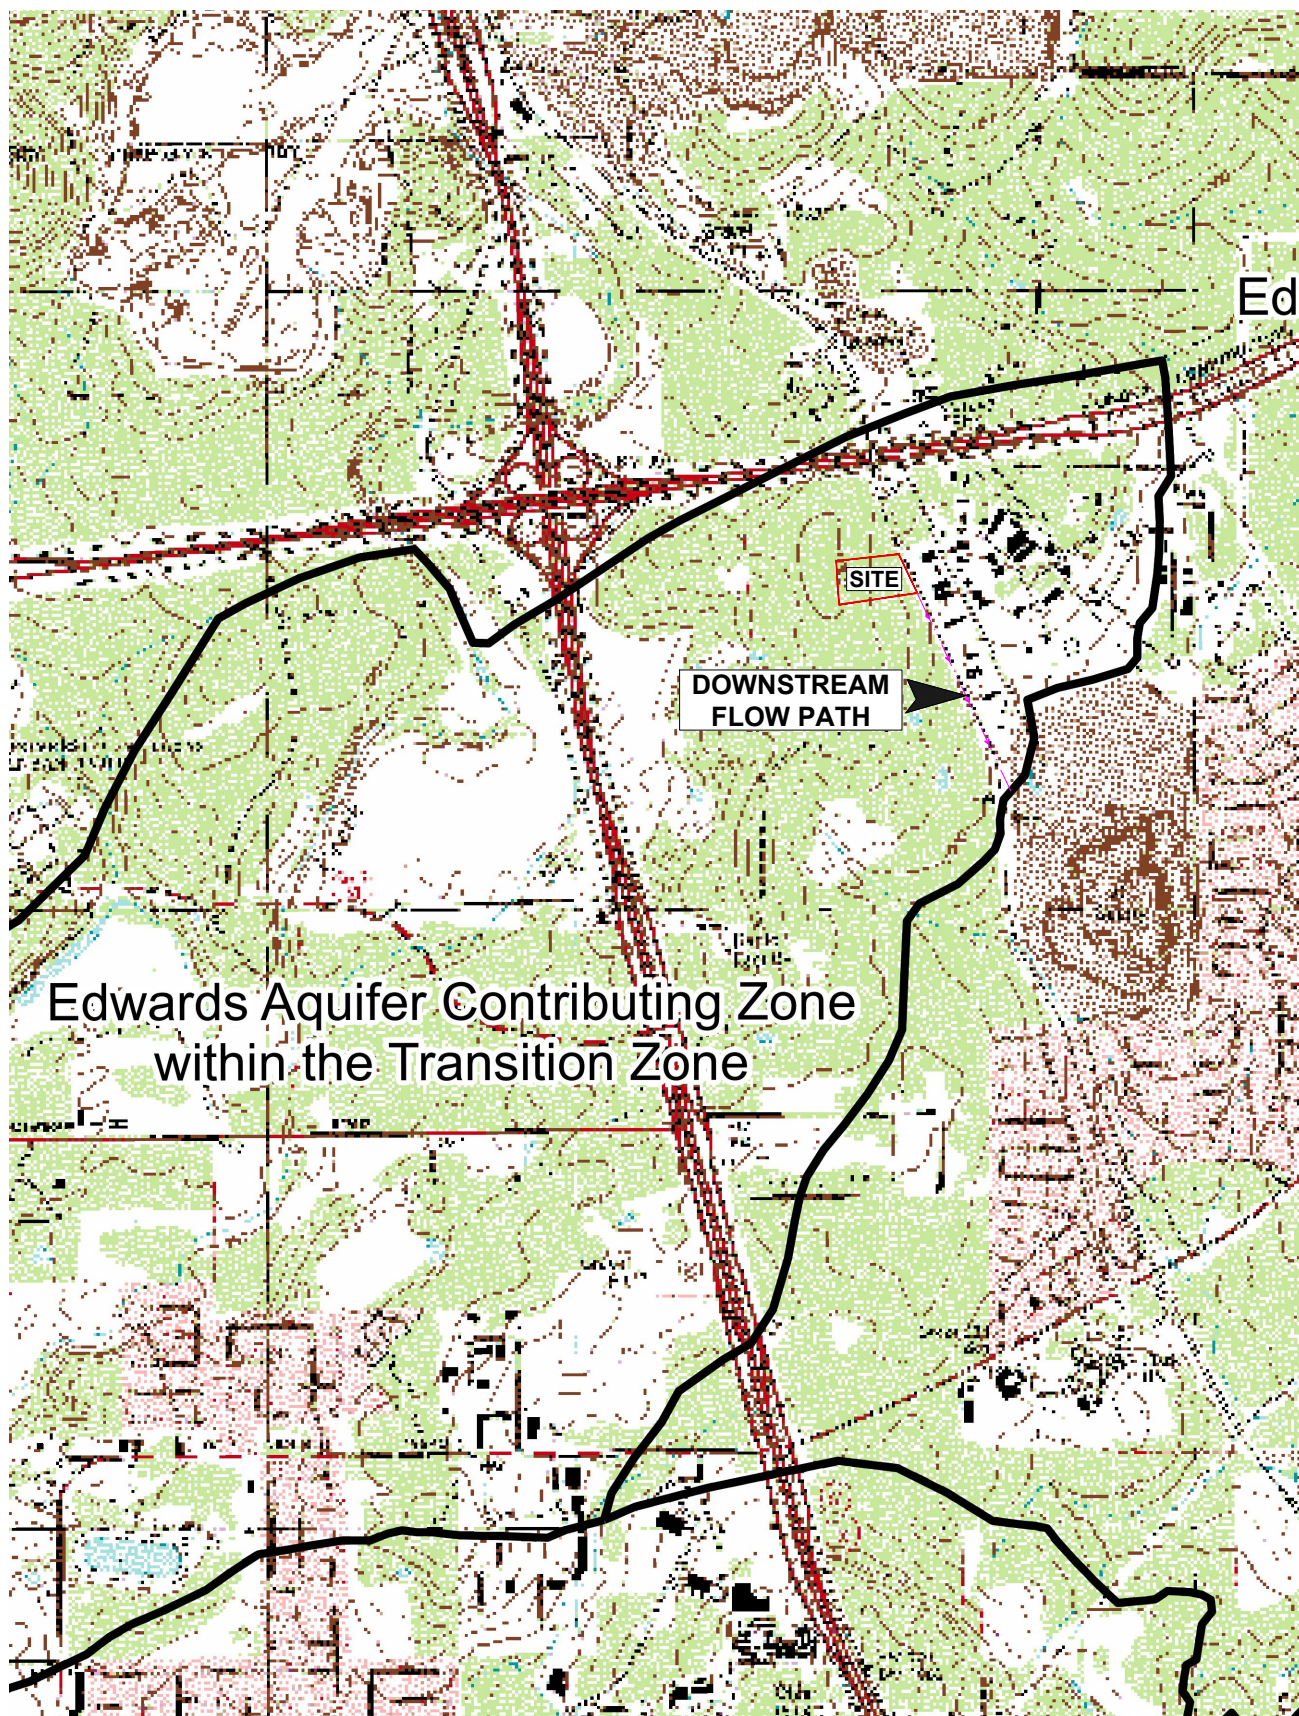

PROJECT NO. 1448-02

DATE: 10/07/24

DRAWN BY: JC DESIGNED BY: AB

SCALE: N.T.S.

VANCE JACKSON PARKING

VANCE JACKSON
SAN ANTONIO, TEXAS 78249

ATTACHMENT B - USGS MAP

K Love
ENGINEERING
Site Development Engineering Services
Firm No. 11042
www.kloveengineering.com (210) 485-5683

Attachment C – Project Narrative

The subject project is located northeast of the intersection Vance Jackson Rd and Presidio Pkwy. This location is within the city limits of the City of San Antonio and the Upper SAR Watershed. This area is not in a mandatory detention area and is currently undeveloped.

The Vance Jackson Parking project consists of 7.50 acres and will be used for commercial parking lot / storage. The proposed impervious cover for the development onsite is approximately 5.97 acres. The offsite area that will be going onto the proposed site is 0 acres with an existing offsite impervious cover of 0 acres. The proposed improvements addressed by this Contributing Zone Plan (CZP) are as follows:

- (1) One Access Driveway
- (2) Sidewalks
- (3) Parking Lot
- (4) Partial Sedimentation & Filtration System (Sand Basin)

To prevent pollution of storm water runoff originating on-site and potentially flowing across and off the site after construction, a Partial Sedimentation & Filtration System (Sand Basin) filter system is proposed to be built as the on-site permanent BMP. The Permanent Pollution Abatement Measures (BMPs) for the Vance Jackson Parking project will be designed in accordance with the TCEQ Technical Guidance Manual RG-348 (Revised July 2005) to remove 87% of the increased Total Suspended Solids (TSS) for the proposed improvements.

Potable water and wastewater disposal is provided by the San Antonio Water System (SAWS). Wastewater is disposed of by conveyance to the existing Leon Creek Water Recycling Center operated by SAWS.

Attachment D – Factors Affecting Surface Water Quality

Potential sources of pollution that may reasonably be expected to affect the quality of storm water discharges from the site during construction include:

- Soil erosion due to the clearing of the site
- Oil grease, fuel and hydraulic fluid contamination from construction equipment and vehicle drippings
- Hydrocarbons from asphalt paving operations
- Miscellaneous trash and litter from construction workers and material wrappings
- Concrete truck washout
- Spills/Overflow from portable toilets

Potential sources of pollution that may reasonably be expected to affect the quality of storm water discharges from the site after development include:

- Oil, grease, fuel and hydraulic fluid contamination from vehicle drippings
- Dirt and dust which may fall off vehicles
- Miscellaneous trash and litter

Attachment E – Volume and Character of Stormwater

The site is currently undeveloped with slopes ranging from 3% to 5%. The overall runoff coefficient prior to development of the 7.50 acres is estimated to be 0.49 based on the existing terrain and slopes. Storm water runoff drains southeast towards the Union Pacific Railroad.

The proposed use for this property will be commercial parking lot / storage and will consist of 5.97 acres (80%) of impervious cover for the entire site. A C-value of 0.87 was calculated based on the Table 504-1(b) of the City of San Antonio UDC. The site will generate approximately 64.4 cfs during the 25-year storm event. Values were calculated using the Modified Rational Method.

Attachment F – Suitability Letter from Authorized Agent

No OSSF will be used with this project.

Attachment G – Alternative Secondary Containment

No alternative secondary containment methods will be used with this project.

Attachment H – AST Containment Structure Drawing

No ASTs will be utilized in this project.

Attachment I – 20% or Less Impervious Cover Waiver

No impervious cover waiver is being requested with this project.

Attachment J – BMP for Upgradient Stormwater

The project site does not receive upgradient stormwater to the BMP.

Attachment K – BMP for On-Site Stormwater

In keeping with TCEQ rules, this development will employ a Partial Sedimentation & Filtration System (Sand Basin). The Best Management Practice used, Sand Basin filter system, for the project should achieve at least 87% reduction in the expected increase of suspended solids.

Attachment L – BMP for Surface Streams

No BMP for surface streams.

Attachment M – Construction Plans

See attached plans.

Additional information is provided for cells with a red triangle in the upper right corner. Place the cursor over the cell.

Text shown in blue indicate location of instructions in the Technical Guidance Manual - RG-348.

Characters shown in red are data entry fields.

Characters shown in black (Bold) are calculated fields. Changes to these fields will remove the equations used in the spreadsheet.

1. The Required Load Reduction for the total project:

Calculations from RG-348

Pages 3-27 to 3-30

Page 3-29 Equation 3.3: $L_M = 27.2(A_N \times P)$

where:

 L_M TOTAL PROJECT = Required TSS removal resulting from the proposed development = 80% of increased load A_N = Net increase in impervious area for the project P = Average annual precipitation, inches

Site Data: Determine Required Load Removal Based on the Entire Project

County =	Bexar	
Total project area included in plan *	7.50	acres
Predevelopment impervious area within the limits of the plan *	0.07	acres
Total post-development impervious area within the limits of the plan *	5.97	acres
Total post-development impervious cover fraction *	0.80	
P =	30	inches

 L_M TOTAL PROJECT = 4814 lbs.

* The values entered in these fields should be for the total project area.

Number of drainage basins / outfalls areas leaving the plan area = 1

2. Drainage Basin Parameters (This information should be provided for each basin):

Drainage Basin/Outfall Area No. = 1

Total drainage basin/outfall area =	7.15	acres
Predevelopment impervious area within drainage basin/outfall area =	0.07	acres
Post-development impervious area within drainage basin/outfall area =	5.97	acres
Post-development impervious fraction within drainage basin/outfall area =	0.83	
L_M THIS BASIN =	4814	lbs.

3. Indicate the proposed BMP Code for this basin.

Proposed BMP = Sand Filter
Removal efficiency = 89 percent

Aqualogic Cartridge Filter
Bioretention
Contech StormFilter
Constructed Wetland
Extended Detention
Grassy Swale
Retention / Irrigation
Sand Filter
Stormceptor
Vegetated Filter Strips
Vortechs
Wet Basin
Wet Vault

4. Calculate Maximum TSS Load Removed (L_R) for this Drainage Basin by the selected BMP Type.RG-348 Page 3-33 Equation 3.7: $L_R = (\text{BMP efficiency}) \times P \times (A_N \times 34.6 + A_P \times 0.54)$

where:

 A_C = Total On-Site drainage area in the BMP catchment area A_N = Impervious area proposed in the BMP catchment area A_P = Pervious area remaining in the BMP catchment area L_R = TSS Load removed from this catchment area by the proposed BMP

A_C =	7.15	acres
A_N =	5.97	acres
A_P =	1.18	acres
L_R =	5532	lbs

5. Calculate Fraction of Annual Runoff to Treat the drainage basin / outfall areaDesired L_M THIS BASIN = 4814 lbs. F = 0.87**6. Calculate Capture Volume required by the BMP Type for this drainage basin / outfall area.**

Calculations from RG-348

Pages 3-34 to 3-36

Rainfall Depth =	1.44	inches
Post Development Runoff Coefficient =	0.67	
On-site Water Quality Volume =	25221	cubic feet

Calculations from RG-348 Pages 3-36 to 3-37

Off-site area draining to BMP =	0.00	acres
Off-site Impervious cover draining to BMP =	0.00	acres
Impervious fraction of off-site area =	0	
Off-site Runoff Coefficient =	0.00	
Off-site Water Quality Volume =	0	cubic feet



Storage for Sediment = **5044**

Total Capture Volume (required water quality volume(s) x 1.20) = 30265 cubic feet

The following sections are used to calculate the required water quality volume(s) for the selected BMP.
The values for BMP Types not selected in cell C45 will show NA.

7. Retention/Irrigation System Designed as Required in RG-348 Pages 3-42 to 3-46

Required Water Quality Volume for retention basin = **NA** cubic feet

Irrigation Area Calculations:

Soil infiltration/permeability rate = **0.1** in/hr Enter determined permeability rate or assumed value of 0.1
Irrigation area = **NA** square feet
NA acres

8. Extended Detention Basin System Designed as Required in RG-348 Pages 3-46 to 3-51

Required Water Quality Volume for extended detention basin = **NA** cubic feet

9. Filter area for Sand Filters Designed as Required in RG-348 Pages 3-58 to 3-63

9A. Full Sedimentation and Filtration System

Water Quality Volume for sedimentation basin = **30265** cubic feet

Minimum filter basin area = **1401** square feet

Maximum sedimentation basin area = **12610** square feet For minimum water depth of 2 feet
Minimum sedimentation basin area = **3153** square feet For maximum water depth of 8 feet

9B. Partial Sedimentation and Filtration System

Water Quality Volume for combined basins = **30265** cubic feet

Minimum filter basin area = **2522** square feet

Maximum sedimentation basin area = **10088** square feet For minimum water depth of 2 feet
Minimum sedimentation basin area = **631** square feet For maximum water depth of 8 feet

10. Bioretention System Designed as Required in RG-348 Pages 3-63 to 3-65

Required Water Quality Volume for Bioretention Basin = **NA** cubic feet

11. Wet Basins Designed as Required in RG-348 Pages 3-66 to 3-71

Required capacity of Permanent Pool = **NA** cubic feet Permanent Pool Capacity is 1.20 times the WQV
Required capacity at WQV Elevation = **NA** cubic feet Total Capacity should be the Permanent Pool Capacity plus a second WQV.

12. Constructed Wetlands Designed as Required in RG-348 Pages 3-71 to 3-73

Required Water Quality Volume for Constructed Wetlands = **NA** cubic feet

13. AquaLogic™ Cartridge System Designed as Required in RG-348 Pages 3-74 to 3-78

** 2005 Technical Guidance Manual (RG-348) does not exempt the required 20% increase with maintenance contract with AquaLogic™.

Required Sedimentation chamber capacity = **NA** cubic feet
Filter canisters (FCs) to treat WQV = **NA** cartridges
Filter basin area (RIA_F) = **NA** square feet

14. Stormwater Management StormFilter® by CONTECH

Required Water Quality Volume for Contech StormFilter System = **NA** cubic feet

THE SIZING REQUIREMENTS FOR THE FOLLOWING BMPs / LOAD REMOVALS ARE BASED UPON FLOW RATES - NOT CALCULATED WATER QUALITY VOLUMES

15. Grassy Swales Designed as Required in RG-348 Pages 3-51 to 3-54

Design parameters for the swale:

Drainage Area to be Treated by the Swale = A = **8.00** acres
Impervious Cover in Drainage Area = **4.00** acres
Rainfall intensity = i = **1.1** in/hr
Swale Slope = **0.01** ft/ft
Side Slope (z) = **3**
Design Water Depth = y = **0.33** ft
Weighted Runoff Coefficient = C = **0.54**

A_{CS} = cross-sectional area of flow in Swale = **13.17** sf
P_W = Wetted Perimeter = **40.62** feet
R_H = hydraulic radius of flow cross-section = A_{CS}/P_W = **0.32** feet
n = Manning's roughness coefficient = **0.2**

15A. Using the Method Described in the RG-348

Manning's Equation: $Q = \frac{1.49}{n} A_{CS} R_H^{2/3} S^{0.5}$

Attachment N – Inspection, Maintenance, Repair and Retrofit Plan

See attached Plan.

PERMANENT STORMWATER SECTION

ATTACHMENT G

Inspection, Maintenance, Repair and Retrofit Plan

PROJECT NAME Vance Jackson Remote Parking Lot

ADDRESS 15480 Vance Jackson

CITY, STATE ZIP San Antonio, Texas 78249

SEDIMENTATION BASIN

Monthly The vegetative growth in the basin shall be checked. The growth shall not exceed 18 inches in height.

Quarterly The level of accumulated silt shall be checked. If depth of silt exceeds 6 inches, or is such that it impedes the capture volume of the basin, it shall be removed and disposed of.

The basin shall be checked for accumulation of debris and trash. The debris and trash shall be removed if excessive.

Bi-Annually The basin shall be inspected at least twice a year (once during or immediately following wet weather) to evaluate the facility operation. With each inspection, any damage to the structural elements of the system must be identified and repaired immediately.

All debris and trash shall be removed at least every six months.

Annually Sediment shall be removed from the inlet when it is impaired and at least once a year.

After Rainfall The basin shall be checked after each rainfall occurrence to insure that it drains within 48 hours after the storm is over. If it does not drain within this time, corrective measures shall be accomplished.

Five Years All sediment shall be removed at a minimum of every 5 years.

PERMANENT STORMWATER SECTION

FILTRATION AREA

Monthly

The filtration area shall be visually inspected for any areas of excessive surface deposits and/or disruptions in the uniformity of the sand layer. Such problem areas shall be promptly repaired or corrected.

The vegetative growth shall be checked and shall not exceed 18 inches in height.

Quarterly

The level of accumulated silt shall be checked. If depth of silt pollutants exceeds ½ inch, it shall be removed and disposed of “properly”.

The accumulation of pollutants/oils shall be checked. If the pollutants have significantly reduced the designed capacity of the sand filter, the pollutants shall be removed.

The basin shall be checked for accumulation of debris and trash. The debris and trash shall be removed if excessive.

Bi Annually

The basin shall be inspected at least twice a year (once during or immediately following wet weather) to evaluate the facility operation. With each inspection, any damage to the structural elements of the system must be identified and repaired immediately.

All debris and trash shall be removed at least every six months.

Two Years

The filter under drain network shall be cleaned at least every two years to remove any sediment buildup or cleaned to maintain design drawdown.

After Rainfall

The basin shall be checked after each rainfall occurrence to insure that it drains within 48 hours after the sedimentation basin has been emptied. If it does not drain within this time, corrective measures shall be undertaken. At a minimum such measures shall include removal of silt build-up on the surface of the sand. If draw-down time exceeds 72 hours, more extensive remediation measures are likely required and the condition of the filtration media should be investigated. In addition, if the basin fails to drain properly the owner must notify the SAWS Construction Section of the Resource Compliance Division at (210)-704-1158.

PERMANENT STORMWATER SECTION

Following any required maintenance, the surface of the filtration basin shall be raked and leveled to restore the system to its designed condition.

With each inspection, any damage to the structural elements of the system (pipes retaining walls, etc.) must be identified and repaired immediately.

“Proper” disposal of accumulated silt shall be accomplished following Texas Commission on Environmental Quality specifications. BMP maintenance frequently requires the disposal of accumulated sediment and other material. These materials are normally classified as special wastes when disposed of in municipal landfills. A Type 1 Municipal Solid Waste (MSW) landfill can accept household waste; anything else is a special waste as defined in 30TAC 330.2 (137). Special waste is a waste that requires special handling at a Type 1 MSW landfill. Labeling a filter media or sediment as a waste is not a waste characterization. The process to obtain authorization to dispose of a special waste begins with a request for approval called the “Request for Authorization for Disposal Waste, TCEQ Form 0152.” The request is completed by the generator and submitted to the MSW permits section of the TCEQ for Executive Director review/approval. The MSW permits section performs the review described in 30 TAC 330.136.

An amended copy of this document will be provided to the Texas Commission on Environmental Quality within thirty (30) days of any changes in the following information.

After all inspections results shall be written and records maintained and made available on request by TCEQ officials.

Upon transfer of ownership or maintenance responsibility: The seller must inform the buyer of all requirements of the basin maintenance. TCEQ must be notified and receive the form “TCEQ -10623 change in responsibility for maintenance on permanent Best Management Practices and Measures”. In addition, TCEQ and SAWS Resource Protection Division shall receive a signed, dated copy of this maintenance plan from the new owner.

Responsible Party for Maintenance Tessi Properties, LLC

Address 153 Treeline Park, Suite 100

City, State Zip San Antonio, TX 78209

Telephone Number 210-437-3961

Signature of Owner/Representative 
Abigail Kampmann (Dec 3, 2024 08:58 CST)

Print name of Owner/Representative Abigail Kampmann

Klove
ENGINEERING

PERMANENT STORMWATER SECTION

Permanent Stormwater Section Attachment "G" continued
Sample Maintenance Table

[illegible]

Attachment O – Pilot-Scale Field Testing Plan

The TCEQ's TGM was used to design the BMP's for this project.

Attachment P– Measures for Minimizing Surface Stream Contamination

Any points where discharge from this site is concentrated and erosive velocities exist will include appropriately sized energy dissipaters to reduce velocities to non-erosive levels.

Temporary Stormwater Section

Texas Commission on Environmental Quality

for Regulated Activities on the Edwards Aquifer Recharge Zone and Relating to 30 TAC §213.5(b)(4)(A), (B), (D)(I) and (G); Effective June 1, 1999

To ensure that the application is administratively complete, confirm that all fields in the form are complete, verify that all requested information is provided, consistently reference the same site and contact person in all forms in the application, and ensure forms are signed by the appropriate party.

Note: Including all the information requested in the form and attachments contributes to more streamlined technical reviews.

Signature

To the best of my knowledge, the responses to this form accurately reflect all information requested concerning the proposed regulated activities and methods to protect the Edwards Aquifer. This **Temporary Stormwater Section** is hereby submitted for TCEQ review and executive director approval. The application was prepared by:

Print Name of Customer/Agent: Kevin W. Love, P.E.

Date: _____

Signature of Customer/Agent:

 12/3/24

Regulated Entity Name: Vance Jackson Remote Parking Lot

Project Information

Potential Sources of Contamination

Examples: Fuel storage and use, chemical storage and use, use of asphaltic products, construction vehicles tracking onto public roads, and existing solid waste.

1. Fuels for construction equipment and hazardous substances which will be used during construction:

☐ The following fuels and/or hazardous substances will be stored on the site: _____

These fuels and/or hazardous substances will be stored in:

- ☐ Aboveground storage tanks with a cumulative storage capacity of less than 250 gallons will be stored on the site for less than one (1) year.

- ☐ Aboveground storage tanks with a cumulative storage capacity between 250 gallons and 499 gallons will be stored on the site for less than one (1) year.
- ☐ Aboveground storage tanks with a cumulative storage capacity of 500 gallons or more will be stored on the site. An Aboveground Storage Tank Facility Plan application must be submitted to the appropriate regional office of the TCEQ prior to moving the tanks onto the project.
- ☒ Fuels and hazardous substances will not be stored on the site.
- 2. ☒ **Attachment A - Spill Response Actions.** A site specific description of the measures to be taken to contain any spill of hydrocarbons or hazardous substances is attached.
- 3. ☒ Temporary aboveground storage tank systems of 250 gallons or more cumulative storage capacity must be located a minimum horizontal distance of 150 feet from any domestic, industrial, irrigation, or public water supply well, or other sensitive feature.
- 4. ☒ **Attachment B - Potential Sources of Contamination.** A description of any activities or processes which may be a potential source of contamination affecting surface water quality is attached.

Sequence of Construction

- 5. ☒ **Attachment C - Sequence of Major Activities.** A description of the sequence of major activities which will disturb soils for major portions of the site (grubbing, excavation, grading, utilities, and infrastructure installation) is attached.
 - ☒ For each activity described, an estimate (in acres) of the total area of the site to be disturbed by each activity is given.
 - ☒ For each activity described, include a description of appropriate temporary control measures and the general timing (or sequence) during the construction process that the measures will be implemented.
- 6. ☒ Name the receiving water(s) at or near the site which will be disturbed or which will receive discharges from disturbed areas of the project: Olmos Creek

Temporary Best Management Practices (TBMPs)

Erosion control examples: tree protection, interceptor swales, level spreaders, outlet stabilization, blankets or matting, mulch, and sod. Sediment control examples: stabilized construction exit, silt fence, filter dikes, rock berms, buffer strips, sediment traps, and sediment basins. Please refer to the Technical Guidance Manual for guidelines and specifications. All structural BMPs must be shown on the site plan.

- 7. ☒ **Attachment D – Temporary Best Management Practices and Measures.** TBMPs and measures will prevent pollution of surface water, groundwater, and stormwater. The construction-phase BMPs for erosion and sediment controls have been designed to retain sediment on site to the extent practicable. The following information is attached:

- ☒ A description of how BMPs and measures will prevent pollution of surface water, groundwater or stormwater that originates upgradient from the site and flows across the site.
 - ☒ A description of how BMPs and measures will prevent pollution of surface water or groundwater that originates on-site or flows off site, including pollution caused by contaminated stormwater runoff from the site.
 - ☒ A description of how BMPs and measures will prevent pollutants from entering surface streams, sensitive features, or the aquifer.
 - ☒ A description of how, to the maximum extent practicable, BMPs and measures will maintain flow to naturally-occurring sensitive features identified in either the geologic assessment, TCEQ inspections, or during excavation, blasting, or construction.
8. ☒ The temporary sealing of a naturally-occurring sensitive feature which accepts recharge to the Edwards Aquifer as a temporary pollution abatement measure during active construction should be avoided.
- ☐ **Attachment E - Request to Temporarily Seal a Feature.** A request to temporarily seal a feature is attached. The request includes justification as to why no reasonable and practicable alternative exists for each feature.
- ☒ There will be no temporary sealing of naturally-occurring sensitive features on the site.
9. ☒ **Attachment F - Structural Practices.** A description of the structural practices that will be used to divert flows away from exposed soils, to store flows, or to otherwise limit runoff discharge of pollutants from exposed areas of the site is attached. Placement of structural practices in floodplains has been avoided.
10. ☒ **Attachment G - Drainage Area Map.** A drainage area map supporting the following requirements is attached:
- ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin will be provided.
 - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a smaller sediment basin and/or sediment trap(s) will be used.
 - ☐ For areas that will have more than 10 acres within a common drainage area disturbed at one time, a sediment basin or other equivalent controls are not attainable, but other TBMPs and measures will be used in combination to protect down slope and side slope boundaries of the construction area.
 - ☐ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. A smaller sediment basin and/or sediment trap(s) will be used in combination with other erosion and sediment controls within each disturbed drainage area.

- ☒ There are no areas greater than 10 acres within a common drainage area that will be disturbed at one time. Erosion and sediment controls other than sediment basins or sediment traps within each disturbed drainage area will be used.
11. ☐ **Attachment H - Temporary Sediment Pond(s) Plans and Calculations.** Temporary sediment pond or basin construction plans and design calculations for a proposed temporary BMP or measure have been prepared by or under the direct supervision of a Texas Licensed Professional Engineer. All construction plans and design information must be signed, sealed, and dated by the Texas Licensed Professional Engineer. Construction plans for the proposed temporary BMPs and measures are attached.
- ☒ N/A
12. ☒ **Attachment I - Inspection and Maintenance for BMPs.** A plan for the inspection of each temporary BMP(s) and measure(s) and for their timely maintenance, repairs, and, if necessary, retrofit is attached. A description of the documentation procedures, recordkeeping practices, and inspection frequency are included in the plan and are specific to the site and/or BMP.
13. ☒ All control measures must be properly selected, installed, and maintained in accordance with the manufacturer's specifications and good engineering practices. If periodic inspections by the applicant or the executive director, or other information indicate a control has been used inappropriately, or incorrectly, the applicant must replace or modify the control for site situations.
14. ☒ If sediment escapes the construction site, off-site accumulations of sediment must be removed at a frequency sufficient to minimize offsite impacts to water quality (e.g., fugitive sediment in street being washed into surface streams or sensitive features by the next rain).
15. ☒ Sediment must be removed from sediment traps or sedimentation ponds not later than when design capacity has been reduced by 50%. A permanent stake will be provided that can indicate when the sediment occupies 50% of the basin volume.
16. ☒ Litter, construction debris, and construction chemicals exposed to stormwater shall be prevented from becoming a pollutant source for stormwater discharges (e.g., screening outfalls, picked up daily).

Soil Stabilization Practices

Examples: establishment of temporary vegetation, establishment of permanent vegetation, mulching, geotextiles, sod stabilization, vegetative buffer strips, protection of trees, or preservation of mature vegetation.

17. ☒ **Attachment J - Schedule of Interim and Permanent Soil Stabilization Practices.** A schedule of the interim and permanent soil stabilization practices for the site is attached.

- 18. ☒ Records must be kept at the site of the dates when major grading activities occur, the dates when construction activities temporarily or permanently cease on a portion of the site, and the dates when stabilization measures are initiated.
- 19. ☒ Stabilization practices must be initiated as soon as practicable where construction activities have temporarily or permanently ceased.

Administrative Information

- 20. ☒ All structural controls will be inspected and maintained according to the submitted and approved operation and maintenance plan for the project.
- 21. ☒ If any geologic or manmade features, such as caves, faults, sinkholes, etc., are discovered, all regulated activities near the feature will be immediately suspended. The appropriate TCEQ Regional Office shall be immediately notified. Regulated activities must cease and not continue until the TCEQ has reviewed and approved the methods proposed to protect the aquifer from any adverse impacts.
- 22. ☒ Silt fences, diversion berms, and other temporary erosion and sediment controls will be constructed and maintained as appropriate to prevent pollutants from entering sensitive features discovered during construction.

Temporary Stormwater Section

Attachment A – Spill Response Actions

Spill Prevention and Control

The objective of this section is to describe measures to prevent or reduce the discharge of pollutants to drainage systems or watercourses from leaks and spills by reducing the chance for spills, stopping the source of spills, containing and cleaning up spills, properly disposing of spill materials, and training employees.

The following steps will help reduce the storm water impacts of leaks and spills:

Education

- (1) Be aware that different materials pollute in different amounts. Make sure that each employee knows what a “significant spill” is for each material they use, and what is the appropriate response for “significant” and “insignificant” spills. Employees should also be aware of when spill must be reported to the TCEQ. Information available in 30 TAC 327.4 and 40 CFR 302.4.
- (2) Educate employees and subcontractors on potential dangers to humans and the environment from spills and leaks.
- (3) Hold regular meetings to discuss and reinforce appropriate disposal procedures (incorporate into regular safety meetings).
- (4) Establish a continuing education program to indoctrinate new employees.
- (5) Have contractor's superintendent or representative oversee and enforce proper spill prevention and control measures.

General Measures

- (1) To the extent that the work can be accomplished safely, spills of oil, petroleum products, and substances listed under 40 CFR parts 110,117, and 302, and sanitary and septic wastes should be contained and cleaned up immediately.
- (2) Store hazardous materials and wastes in covered containers and protect from vandalism.
- (3) Place a stockpile of spill cleanup materials where it will be readily accessible.
- (4) Train employees in spill prevention and cleanup.
- (5) Designate responsible individuals to oversee and enforce control measures.

- (6) Spills should be covered and protected from stormwater runoff during rainfall to the extent that it doesn't compromise cleanup activities.
- (7) Do not bury or wash spills with water.
- (8) Store and dispose of used clean up materials, contaminated materials, and recovered spill material that is no longer suitable for the intended purpose in conformance with the provisions in applicable BMPs.
- (9) Do not allow water used for cleaning and decontamination to enter storm drains or watercourses. Collect and dispose of contaminated water in accordance with applicable regulations.
- (10) Contain water overflow or minor water spillage and do not allow it to discharge into drainage facilities or watercourses.
- (11) Place Material Safety Data Sheets (MSDS), as well as proper storage, cleanup, and spill reporting instructions for hazardous materials stored or used on the project site in an open, conspicuous, and accessible location.
- (12) Keep waste storage areas clean, well organized, and equipped with ample cleanup supplies as appropriate for the materials being stored. Perimeter controls, containment structures, covers, and liners should be repaired or replaced as needed to maintain proper function.

Cleanup

- (1) Clean up leaks and spills immediately.
- (2) Use a rag for small spills on paved surfaces, a damp mop for general cleanup, and absorbent material for larger spills. If the spilled material is hazardous, then the used cleanup materials are also hazardous and must be disposed of as hazardous waste.
- (3) Never hose down or bury dry material spills. Clean up as much of the material as possible and dispose of properly. See the waste management BMPs in this section for specific information.

Minor Spills

- (1) Minor spills typically involve small quantities of oil, gasoline, paint, etc. which can be controlled by the first responder at the discovery of the spill.
- (2) Use absorbent materials on small spills rather than hosing down or burying the spill.
- (3) Absorbent materials should be promptly removed and disposed of properly.
- (4) Follow the practice below for a minor spill:

- a) Contain the spread of the spill.
- b) Recover spilled materials.
- c) Clean the contaminated area and properly dispose of contaminated materials.

Semi-significant Spills

Semi-significant spills still can be controlled by the first responder along with the aid of other personnel such as laborers and the foreman, etc. This response may require the cessation of all other activities.

Spills should be cleaned up immediately:

- (1) Contain spread of the spill.
- (2) Notify the project foreman immediately.
- (3) If the spill occurs on paved or impermeable surfaces, clean up using "dry" methods (absorbent materials, cat litter and/or rags). Contain the spill by encircling with absorbent materials and do not let the spill spread widely.
- (4) If the spill occurs in dirt areas, immediately contain the spill by constructing an earthen dike. Dig up and properly dispose of contaminated soil.
- (5) If the spill occurs during rain, cover spill with tarps or other material to prevent contaminating runoff.

Significant/Hazardous Spills

For significant or hazardous spills that are in reportable quantities:

- (1) Notify the TCEQ by telephone as soon as possible and within 24 hours at 512-339-2929 (Austin) or 210-490-3096 (San Antonio) between 8 AM and 5 PM. After hours, contact the Environmental Release Hotline at 1-800-832-8224. It is the contractor's responsibility to have all emergency phone numbers at the construction site.
- (2) For spills of federal reportable quantities, in conformance with the requirements in 40 CFR parts 110, 119, and 302, the contractor should notify the National Response Center at (800) 424-8802.
- (3) Notification should first be made by telephone and followed up with a written report.
- (4) The services of a spills contractor or a Haz-Mat team should be obtained immediately. Construction personnel should not attempt to clean up until the appropriate and qualified staffs have arrived at the job site.
- (5) Other agencies which may need to be consulted include, but are not limited to, the City Police Department, County Sheriff Office, Fire Departments, etc.

More information on spill rules and appropriate responses is available on the TCEQ website at:

http://www.tnrcc.state.tx.us/enforcement/emergency_response.html.

Vehicle and Equipment Maintenance

- (1) If maintenance must occur onsite, use a designated area and a secondary containment, located away from drainage courses, to prevent the runoff of stormwater and the runoff of spills.
- (2) Regularly inspect onsite vehicles and equipment for leaks and repair immediately.
- (3) Check incoming vehicles and equipment (including delivery trucks, and employee and subcontractor vehicles) for leaking oil and fluids. Do not allow leaking vehicles or equipment onsite.
- (4) Always use secondary containment, such as a drain pan or drop cloth, to catch spills or leaks when removing or changing fluids.
- (5) Place drip pans or absorbent materials under paving equipment when not in use.
- (6) Use absorbent materials on small spills rather than hosing down or burying the spill. Remove the absorbent materials promptly and dispose of properly.
- (7) Promptly transfer used fluids to the proper waste or recycling drums. Don't leave full drip pans or other open containers lying around.
- (8) Oil filters disposed of in trashcans or dumpsters can leak oil and pollute stormwater. Place the oil filter in a funnel over a waste oil-recycling drum to drain excess oil before disposal. Oil filters can also be recycled. Ask the oil supplier or recycler about recycling oil filters.
- (9) Store cracked batteries in a non-leaking secondary container. Do this with all cracked batteries even if you think all the acid has drained out. If you drop a battery, treat it as if it is cracked. Put it into the containment area until you are sure it is not leaking.

Vehicle and Equipment Fueling

- (1) If fueling must occur on site, use designated areas, located away from drainage courses, to prevent the runoff of stormwater and the runoff of spills.
- (2) Discourage "topping off" of fuel tanks.
- (3) Always use secondary containment, such as a drain pan, when fueling to catch spills/leaks.

Spill Response Actions

In the event that a spill of hydrocarbons or hazardous substances does occur, the contractor shall be required to maintain a sufficient stockpile of sand material in the staging area. This sand material shall be used to immediately isolate and provide containment of the spill by constructing dikes. Furthermore, this sand material shall act as an absorbent material that can be disposed of offsite and out of the Recharge Zone during clean-up operations. The contractor, in the event of a spill, shall also notify the owner who shall contact TCEQ. All contaminated soils resulting from an accidental release will be required to be removed and disposed of in accordance with all local, state and federal regulations.

Attachment B – Potential Sources Contamination

Potential Source	Oil, grease, fuel and hydraulic fluid contamination from construction equipment and vehicle dripping.
Preventive Measure	Vehicle maintenance, when possible, will be performed within a construction staging area specified by the General Contractor.
Potential Source	Miscellaneous trash and litter from construction workers and material wrappings.
Preventive Measure	Trash containers will be placed throughout the site to encourage proper trash disposal.
Potential Source	Construction debris.
Preventive Measure	Construction debris will be monitored daily by contractor. Debris will be collected weekly and placed in disposal bins. Situations requiring immediate attention will be addressed on a case by case basis.
Potential Source	Stormwater contamination from excess application of fertilizers, herbicides and pesticides.
Preventive Measure	Fertilizers, herbicides and pesticides will be applied only when necessary and in accordance with manufacturer's directions.
Potential Source	Soil and mud from construction vehicle tires as they leave the site.
Preventive Measure	A temporary construction entrance/exit shall be utilized as vehicles leave the site. Any soil, mud, etc. carried from the project onto public roads shall be cleaned up within 24 hours.
Potential Source	Sediment from soil, sand, gravel and excavated materials stockpiled on site.

Preventive Measure	Silt fence shall be installed on the down gradient side of all stockpiled materials. Reinforced rock berms shall be installed at all downstream discharge locations.
Potential Source	Portable toilet spill.
Preventive Measure	Toilets on the site will be emptied on a regular basis by the contracted toilet company.

Attachment C – Sequence of Major Activities

The sequence of major activities which disturb soil during construction on this site will be divided into stages. The first stage is site preparation that will include clearing and grubbing of vegetation, where applicable. This will disturb approximately 7.50 acres. The second is construction that will include installation of utilities, construction of the water quality basin and the proposed buildings, parking lot, landscaping and site cleanup. This will disturb approximately 7.50 acres.

Sequence Item	Description
1.	Install TBMP's as required. (Silt Fence, etc.)
2.	Clearing of Disturbed Areas
3.	Grading of Disturbed Areas
4.	Construction of Permanent BMP's
5.	Complete Construction
6.	Soil Stabilization and/or re-vegetation
7.	Clean site
8.	Remove TBMP's

Attachment D – Temporary Best Management Practices and Measures

1. Temporary Construction Entrance/Exit – A stabilized pad of crushed stone located at any point where traffic will be entering or leaving the construction site from a public R.O.W., street, alley, sidewalk or parking area. It shall be a minimum of 50 feet long, 12 feet wide and 8 inches thick. The rock shall be 4" to 8" in size.
2. Silt Fence – A barrier consisting of geotextile fabric supported by metal posts to prevent soil and sediment loss from a site. Silt fences shall be installed on the down gradient side of the proposed areas to be disturbed that have a drainage area of ¼ acres per 100 feet of fence.
3. Rock Berms – A sediment trap consisting of 3" to 5" diameter rock wrapped in a woven wire sheathing. The berm shall have a minimum height of 36" and a minimum top width

of 2 feet. A rock berm shall be placed at locations of the concentrated flows where the drainage area is between 2 and 5 acres.


4. Inlet Protection – Placed around inlets to catch and stop sediment from entering the storm drain system before filtration systems are in place.
5. Concrete Washout Pit – Designed to trap and store waste from concrete and similar activities. This allows for safe storage and removal from the site by not allowing contaminants to enter the storm water. Contaminants can be kept in a location that will not allow storm water to mix and flow off the site.

Sequence of installation during construction process



1. The Temporary Construction Entrance/Exit (Item 1) shall be installed prior to disturbing any soil except at the location of the Temporary Construction Entrance/Exit. It shall stay in place and be maintained until the end of the infrastructure construction.
2. Silt fence (Item 2) shall be installed along the western boundary of the site prior to any disturbance of the site
3. Rock berms (Item 4) shall be installed around the perimeter of the project at natural low points following rough grading of the site and shall be removed once grading to the on-site stormwater drainage system with bagged gravel inlet filters in sump is complete. Rock berms will also be utilized at the outlet of the pond while it is being constructed.

The TBMPs and measures utilized for the proposed project to prevent pollution of storm water, groundwater, and surface water during the construction phase are the following:

1. Temporary Construction Entrance/Exit
2. Silt Fence
3. Concrete Washout Pit
4. Rock Berm
5. Inlet Protection

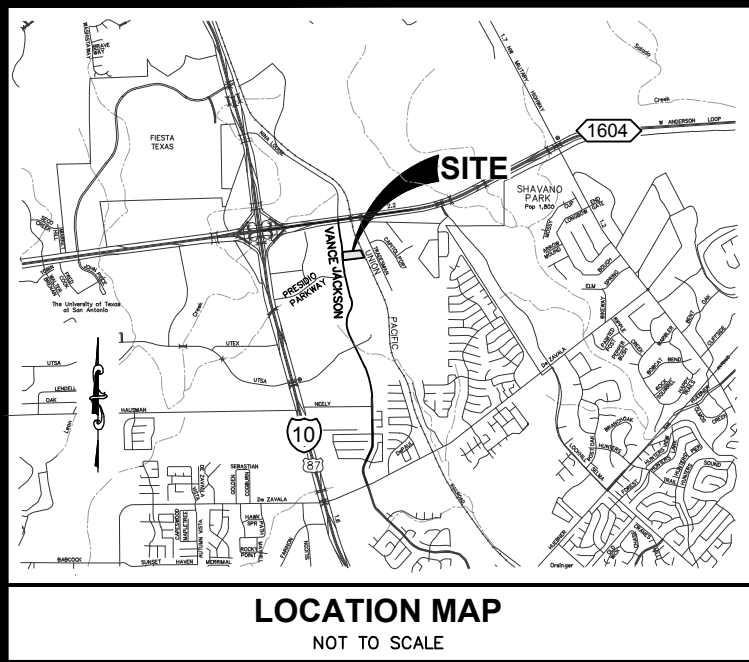

CURVE TABLE				
CURVE #	LENGTH	RADIUS	DELTA	CHORD BEARING
C1	213.96'	1,957.00'	06°15'51"	213.85' N 05°21'09" W

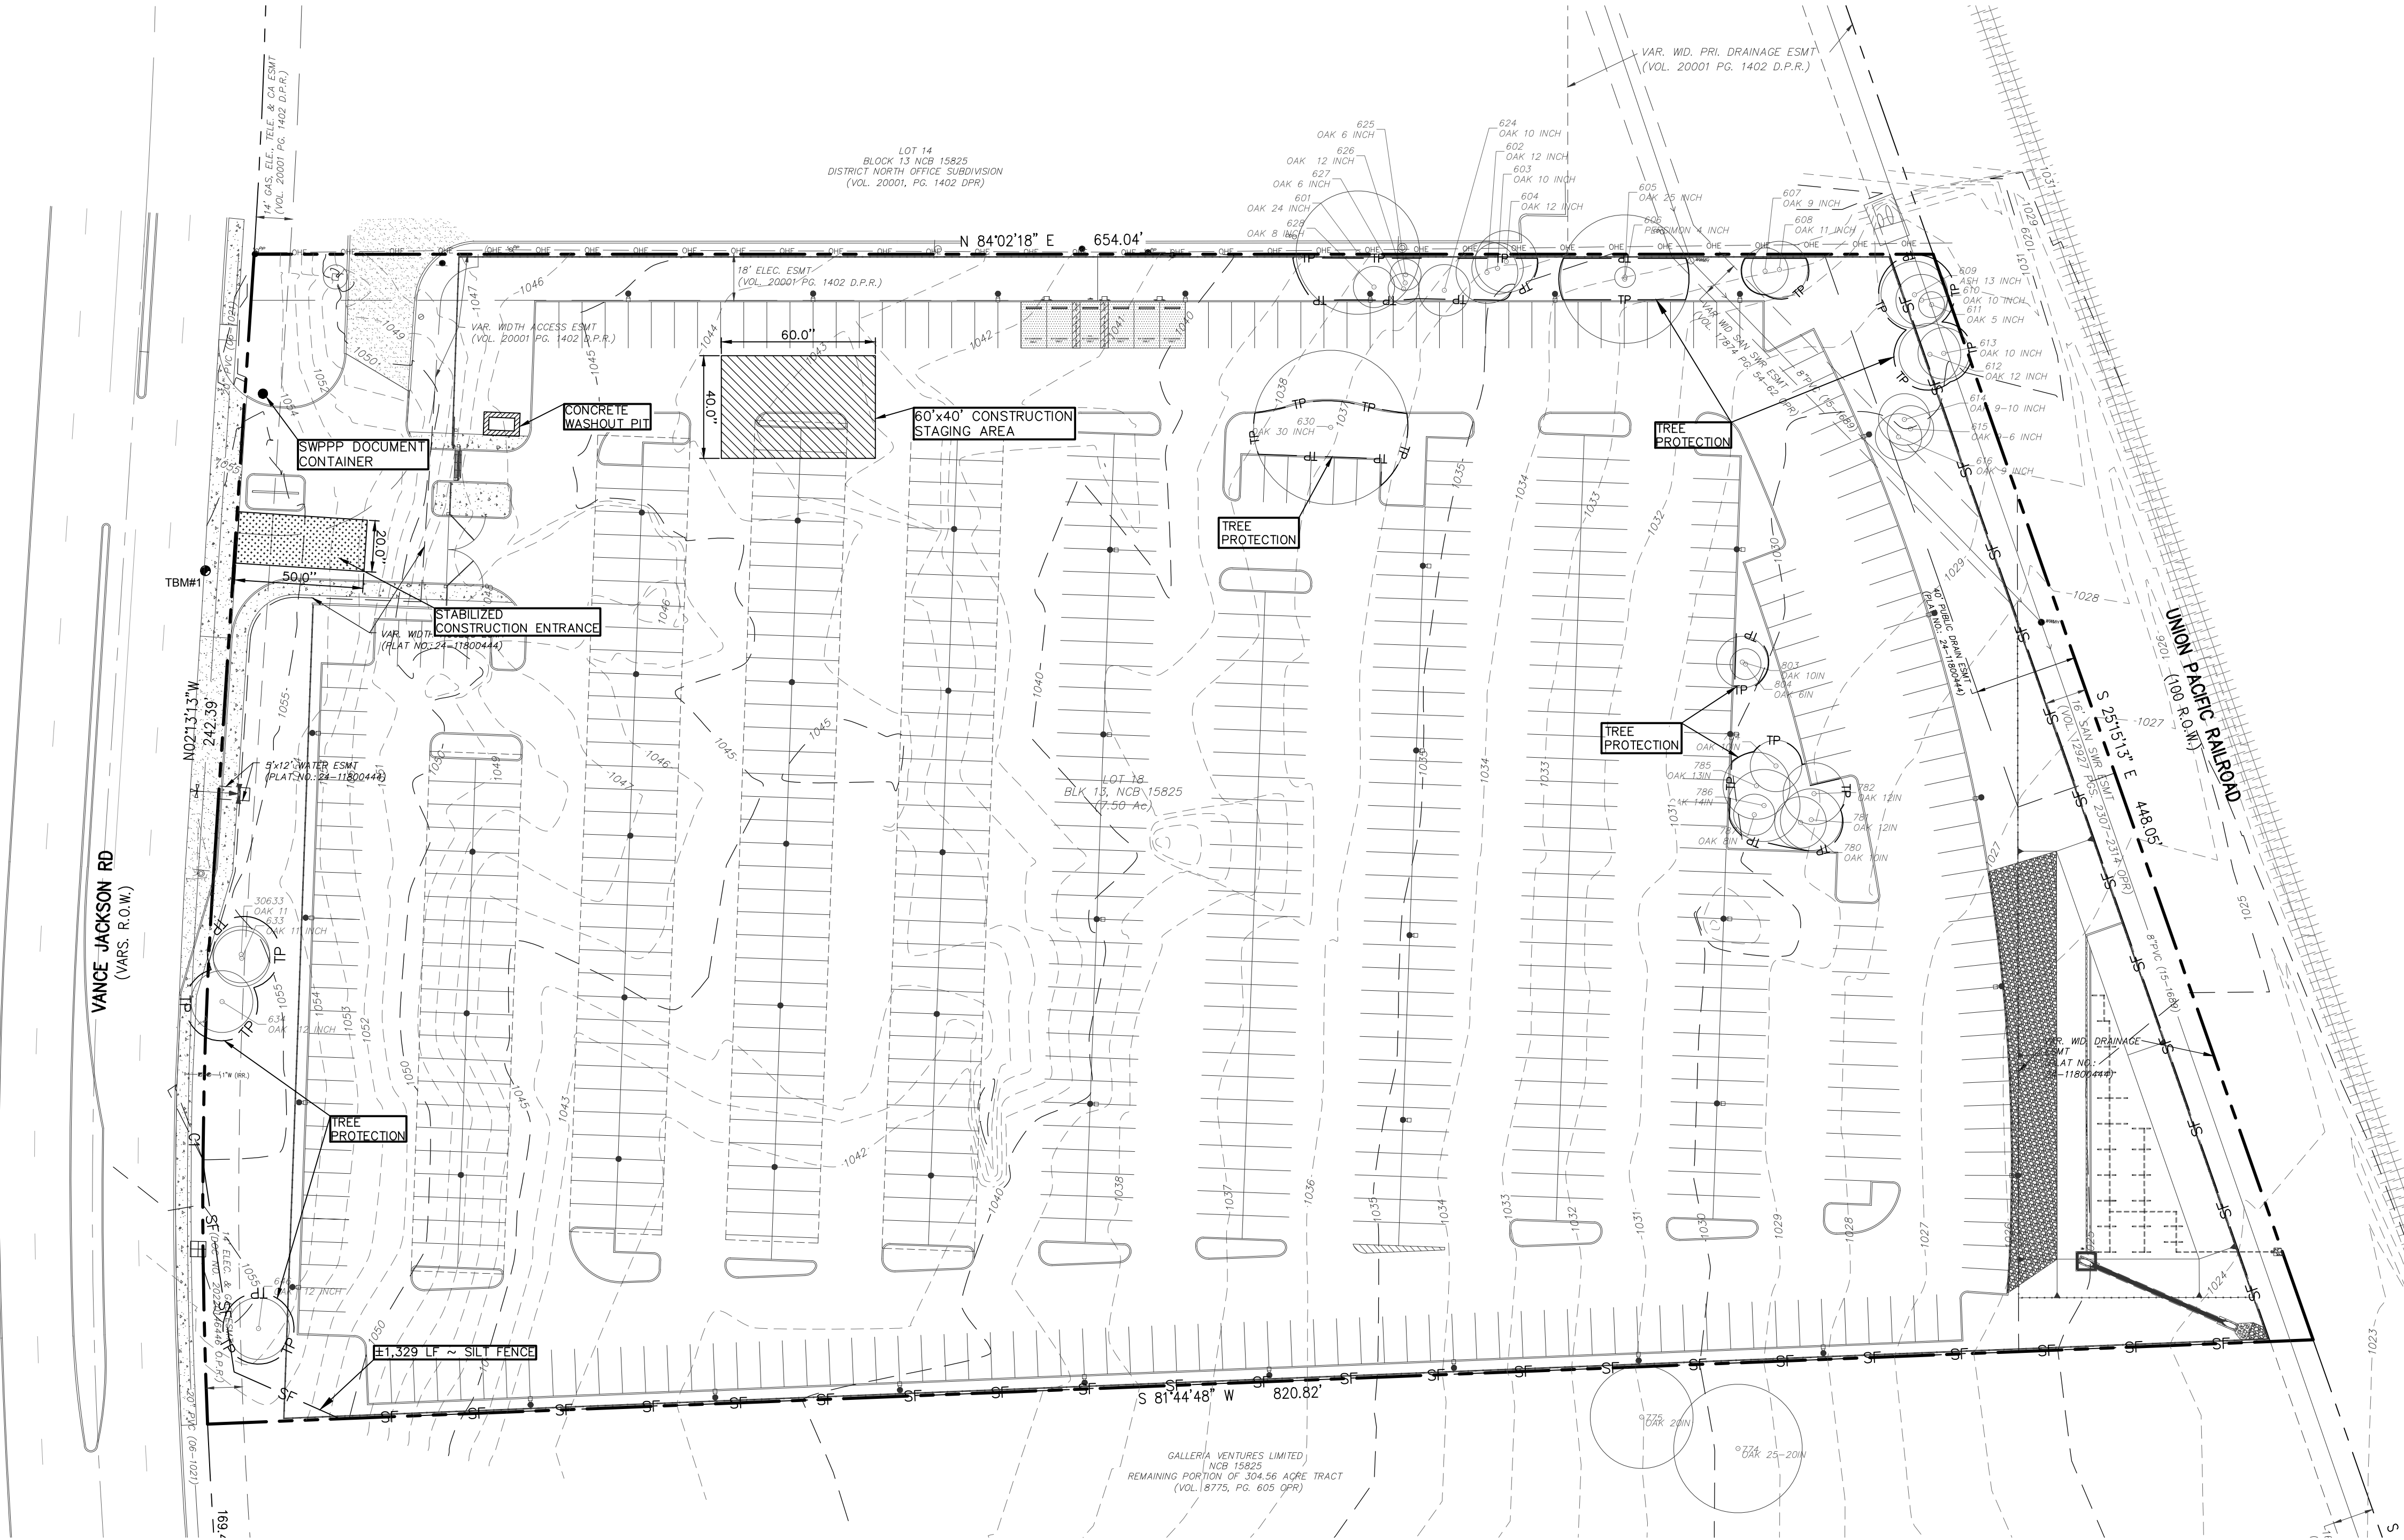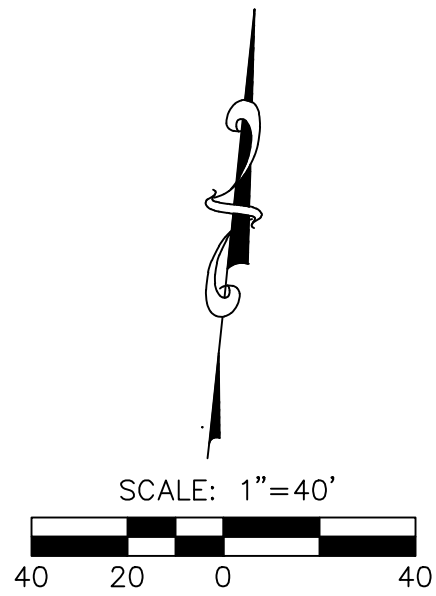

LEGEND		
EXISTING	PROPOSED	DESCRIPTION
(XXX)		PROPERTY (R.O.W.) LINE/ SUBDIVISION BOUNDARY
LP		ADJACENT PROPERTY RECORD INFORMATION
PP		BENCHMARK
E		LIGHT POLE
T		POWER POLE
W		DOWN GUY
TR		TRANSFORMER (SIZE VARIES)
FR		FIRE HYDRANT
WV		WATER VALVE
WM		WATER METER
WMV		WATER METER VAULT
WMH		WATER MANHOLE
WMH		TELEPHONE RISER
WMH		CABLE TV RISER
WMH		ELECTRIC BOX
WMH		ELECTRIC METER
WMH		GAS VALVE
WMH		GAS METER
WMH		TRAFFIC CONTROL BOX
WMH		TRAFFIC SIGNAL POST
WMH		UNDERGROUND GAS LINE MARKER
WMH		GREASE TRAP (SIZE VARIES)
WMH		STORMDRAIN LINE
WMH		WATER LINE
WMH		FIRE LINE
WMH		WASTEWATER LINE
WMH		GAS LINE
WMH		OVERHEAD ELECTRIC (PRIMARY)
WMH		UNDERGROUND ELECTRIC (PRIMARY)
WMH		UNDERGROUND ELECTRIC (SECONDARY)
WMH		UNDERGROUND TELEPHONE
WMH		UNDERGROUND CABLE
WMH		ELECTRIC MANHOLE (SIZE VARIES)
WMH		WASTEWATER MANHOLE (SIZE VARIES)
WMH		STORMDRAIN MANHOLE (SIZE VARIES)
WMH		TELEPHONE MANHOLE (SIZE VARIES)
WMH		FIRE DEPARTMENT CONNECTION
WMH		WASTEWATER CLEANOUT
WMH		CURB
WMH		HEADER CURB
WMH		SAWTOOTH CURB
WMH		RETAINING WALL
WMH		CHAINLINK FENCE
WMH		CONCRETE SIDEWALKS
WMH		CONTOUR
WMH		DIRECTION OF FLOW
WMH		SPOT ELEVATION/TOP OF CURB
WMH		SPOT ELEVATION
WMH		SWALE
WMH		CONCRETE PAVEMENT
WMH		ASPHALT PAVEMENT
WMH		TREE PROTECTION
WMH		SILT FENCE
WMH		ROCK BERM
WMH		STABILIZED CONSTRUCTION ENTRANCE
WMH		CONCRETE WASHOUT PIT

NOTES TO CONTRACTOR:

- THE LOCATIONS OF THE STABILIZED CONST. ENTRANCE, STAGING AREA AND CONC. WASHOUT PIT MAY BE CHANGED. IF NECESSARY ANY CHANGES TO THESE LOCATIONS MAY BE REDUCED BY THE CONTRACTOR AND KEPT ON SITE WITH THE TIDES.
- THE FLOODPLAIN IS TO BE STAKED ON SITE. (IF APPLICABLE)
- THE FLOODPLAIN PERMIT (IF APPLICABLE) AND/OR STORM WATER QUALITY PERMIT APPROVAL LETTER IS TO BE POSTED AT THE ENTRANCE OF THE SITE.
- PERMIT TO BE TERMINATED WITH A FINAL INSPECTION PERFORMED BY A TEXAS COUNTY STORM WATER QUALITY INSPECTOR BY APPOINTMENT. (IF APPLICABLE)
- SILT FENCE SHOWN IS TO BE PLACED ON PROPERTY LINE AND NOT TO ENCR OACH ONTO ADJACENT OWNERS PROPERTY.

THE LOCATION OF EXISTING UNDERGROUND UTILITIES ARE SHOWN IN AN APPROXIMATE WAY ONLY. THE CONTRACTOR SHALL DETERMINE THE EXACT LOCATION OF ALL EXISTING UTILITIES BEFORE COMMENCING WORK. HE AGREES TO BE FULLY RESPONSIBLE FOR ANY AND ALL DAMAGES WHICH MIGHT OCCUR BY HIS FAILURE TO EXACTLY LOCATE AND PRESERVE ANY AND ALL UNDERGROUND UTILITIES.





DATE	
REVISIONS:	

OWNER:
TESSI PROPERTIES, LLC
153 TREELINE PARK, SUITE 100
SAN ANTONIO, TEXAS 78209

VANCE JACKSON
REMOTE PARKING LOT
15480 VANCE JACKSON
SAN ANTONIO, TX 78249
STORM WATER POLLUTION PREVENTION PLAN


DESIGNED BY:	AB
DRAWN BY:	JAR
SCALE:	1"=40'
DATE:	11/27/24
SHEET NO.	C2.0



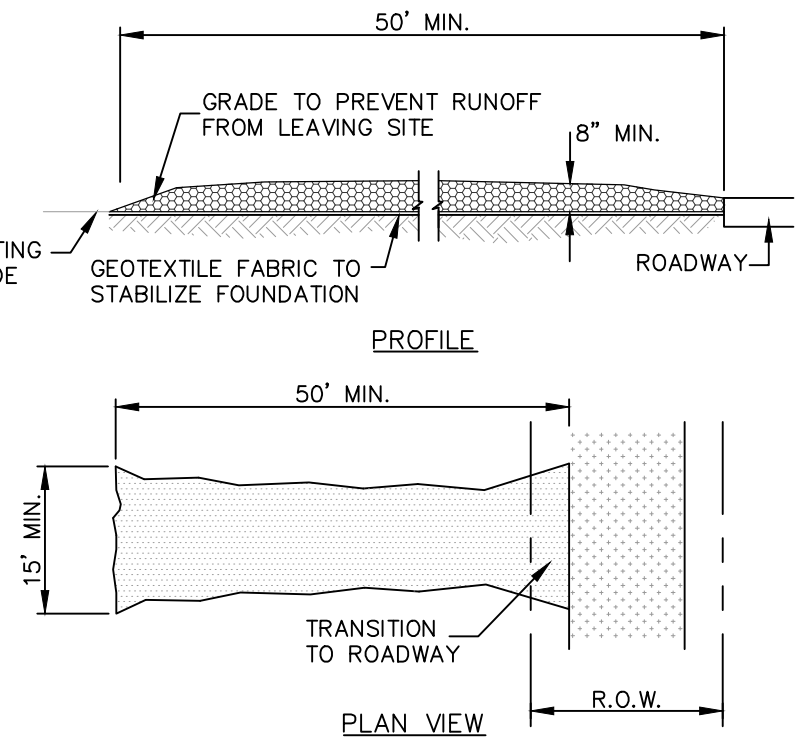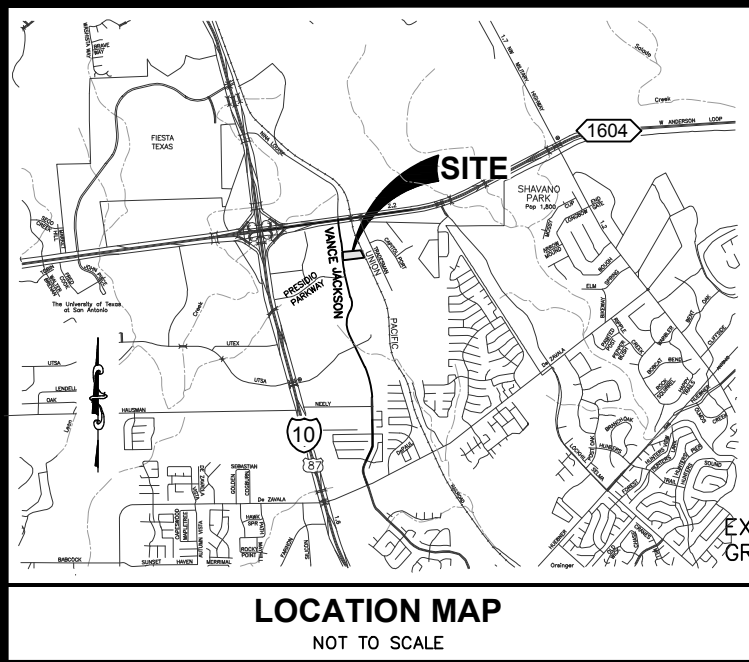


- GENERAL NOTES:
1. STONE SIZE- 4 TO 8 INCH OPEN GRADED ROCK.
 2. LENGTH- AS EFFECTIVE, BUT NOT LESS THAN 50 FEET.
 3. THICKNESS- NOT LESS THAN 8 INCHES.
 4. WIDTH- NOT LESS THAN FULL WIDTH OF ALL POINTS OF INGRESS OR EGRESS.
 5. GEOTEXTILE FABRIC- SOIL FILTRATION MEDIA WITH AN APPROXIMATE WEIGHT OF 6 oz/yd², A MULLEN BURST RATING OF 140 lb/in², AND AN EQUIVALENT OPENING SIZE GREATER THAN NUMBER 50 SIEVE.
 6. WASHING- WHEN NECESSARY, WHEELS SHALL BE CLEANED TO REMOVE SEDIMENT PRIOR TO ENTRANCE ONTO PUBLIC ROADWAY. WHEN WASHING IS REQUIRED, IT SHALL BE DONE ON AN AREA STABILIZED WITH CRUSHED STONE WHICH DRAINS INTO AN APPROVED TRAP OR SEDIMENT BASIN. ALL SEDIMENT SHALL BE PREVENTED FROM ENTERING ANY STORM DRAIN, DITCH, OR WATERCOURSE USING APPROVED METHODS.
 7. MAINTENANCE- THE ENTRANCE SHALL BE MAINTAINED IN A CONDITION WHICH WILL PREVENT TRACKING OR FLOWING OF SEDIMENT ONTO PUBLIC ROADWAYS. THIS MAY REQUIRE PERIODIC TOP DRESSING WITH ADDITIONAL STONE AS CONDITIONS DEMAND, AND REPAIR AND/OR CLEANOUT OF ANY MEASURES USED TO TRAP SEDIMENT. ALL SEDIMENT SPILLED, DROPPED, WASHED OR TRACKED ONTO PUBLIC ROADWAY MUST BE REMOVED IMMEDIATELY.
 8. DRAINAGE- ENTRANCE MUST BE PROPERLY GRADED OR INCORPORATE A DRAINAGE SWALE TO PREVENT RUNOFF FROM LEAVING THE CONSTRUCTION SITE.

STABILIZED CONSTRUCTION ENTRANCE
NOT TO SCALE

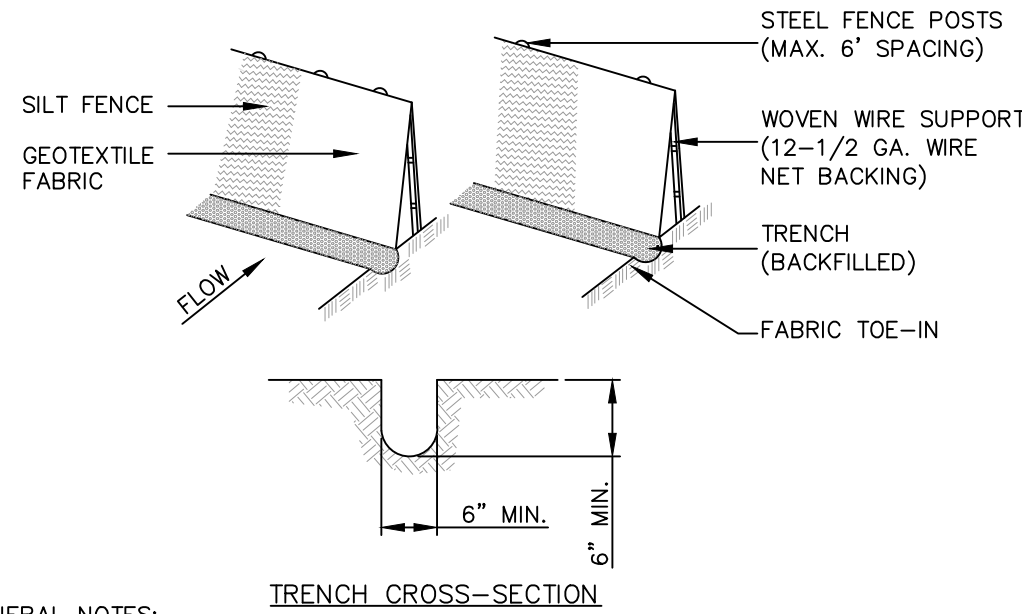


- GENERAL NOTES:
1. STEEL POSTS WHICH SUPPORT THE SILT FENCE SHALL BE INSTALLED ON A SLIGHT ANGLE TOWARD THE ANTICIPATED RUNOFF SOURCE. POST MUST BE EMBEDDED A MINIMUM OF ONE FOOT.
 2. THE TOE OF THE SILT FENCE SHALL BE TRENCHED IN WITH A SPADE OR MECHANICAL TRENCHER, SO THAT THE DOWNSLOPE FACE OF THE TRENCH IS FLAT AND PERPENDICULAR TO THE LINE OF FLOW. WHERE FENCE CAN NOT BE TREATED IN (e.g. pavement) WEIGHT FABRIC FLAP WITH WASHED GRAVEL ON UPHILL SIDE TO PREVENT FLOW UNDER FENCE.
 3. THE TRENCH MUST BE A MINIMUM OF 6 INCHES DEEP AND 6 INCHES WIDE TO ALLOW FOR THE SILT FENCE FABRIC TO BE LAID IN THE GROUND AND BACKFILLED WITH COMPACTED MATERIAL.
 4. SILT FENCE SHOULD BE SECURELY FASTENED TO EACH STEEL SUPPORT POSTS OR TO WOVEN WIRE, WHICH IS IN TURN ATTACHED TO THE STEEL FENCE POST.
 5. INSPECTION SHALL BE MADE WEEKLY OR AFTER EACH RAINFALL EVENT AND REPAIR OR REPLACEMENT SHALL BE MADE PROMPTLY AS NEEDED.
 6. SILT FENCE SHALL BE REMOVED WHEN THE SITE IS COMPLETELY STABILIZED SO AS NOT TO BLOCK OR IMPEDE STORM FLOW OR DRAINAGE.
 7. ACCUMULATED SILT SHALL BE REMOVED WHEN IT REACHES A DEPTH OF 6 INCHES. THE SILT SHALL BE DISPOSED OF IN AN APPROVED SITE AND IN SUCH A MANNER AS TO NOT CONTRIBUTE TO ADDITIONAL SILTATION.

SILT FENCE
NOT TO SCALE

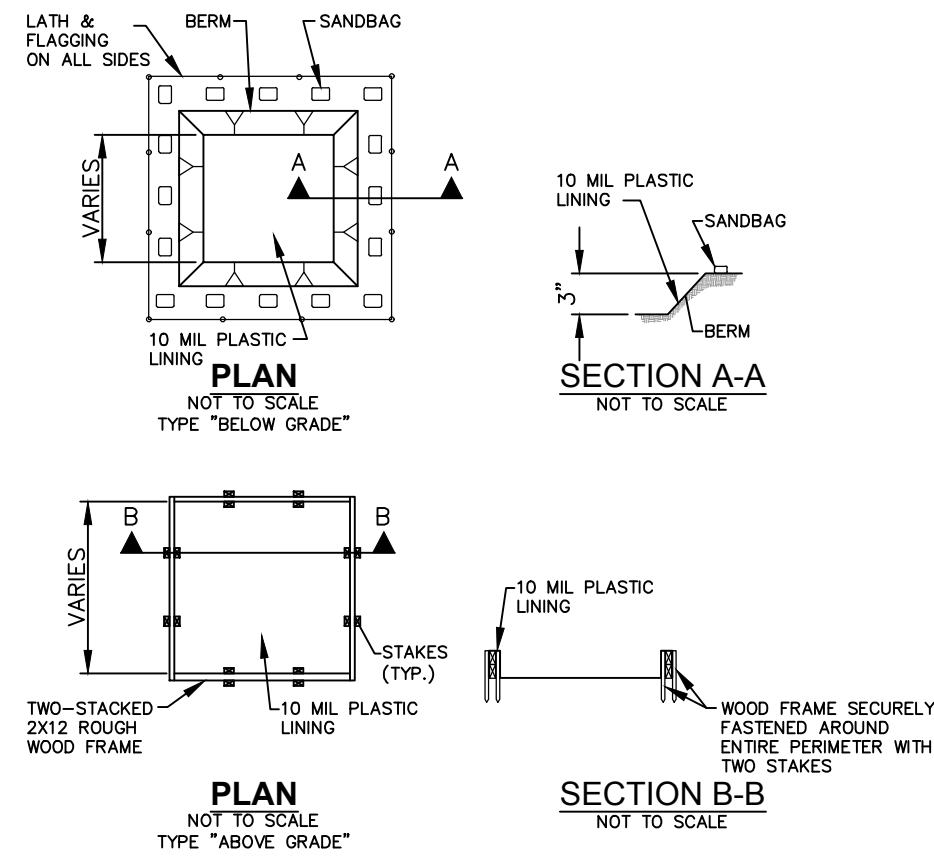


- GENERAL NOTES:
1. DETAIL ILLUSTRATES MINIMUM DIMENSIONS. PIT CAN BE INCREASED IN SIZE DEPENDING ON EXPECTED FREQUENCY OF USE.
 2. WASHOUT PIT SHALL BE LOCATED IN AN AREA EASILY ACCESSIBLE TO CONSTRUCTION TRAFFIC.
 3. WASHOUT PIT SHALL NOT BE LOCATED IN AREAS SUBJECT TO INUNDATION FROM STORM WATER RUNOFF.

CONCRETE TRUCK WASHOUT PIT
NOT TO SCALE

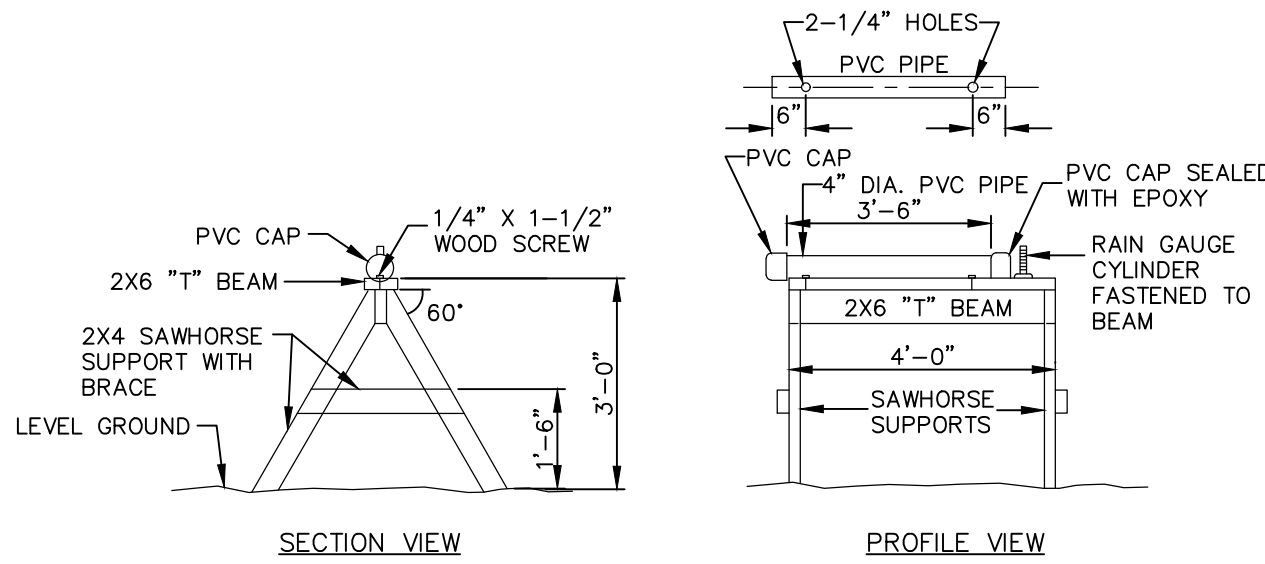


- NOTES:
1. THIS CANISTER SHALL BE USED TO STORE ALL STORMWATER POLLUTION PREVENTION PLAN (SWPPP) AND ALL OTHER RELATED DOCUMENTS SO THAT THEY ARE AVAILABLE ON SITE FOR THE INSPECTOR.
 2. THIS CANISTER SHALL BE LOCATED ON SOLID LEVEL GROUND ADJACENT TO THE CONSTRUCTION ENTRANCE AND ON THE OPPOSITE SIDE OF THE TRUCK WASH OUT PIT.

S.W.P.P.P. DOCUMENT CONTAINER
NOT TO SCALE

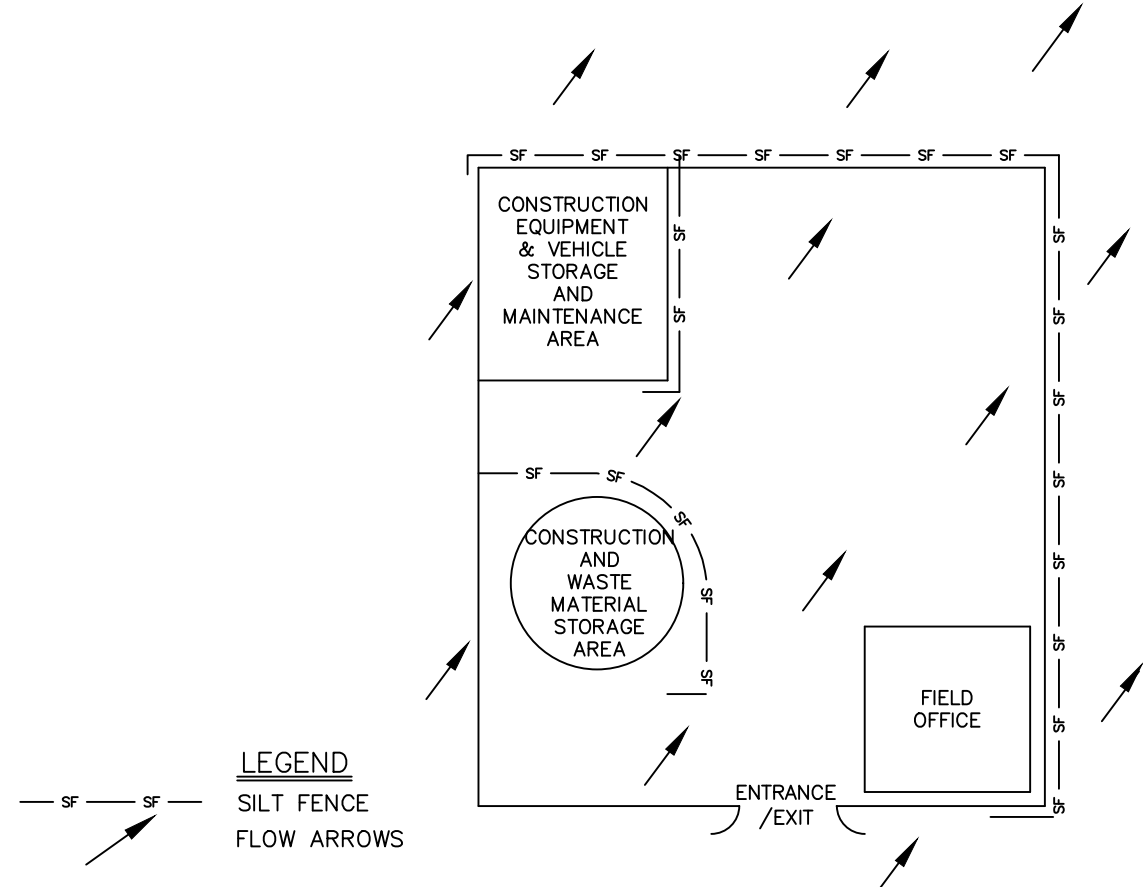

CONSTRUCTION STAGING AREA DETAIL
NOT TO SCALE

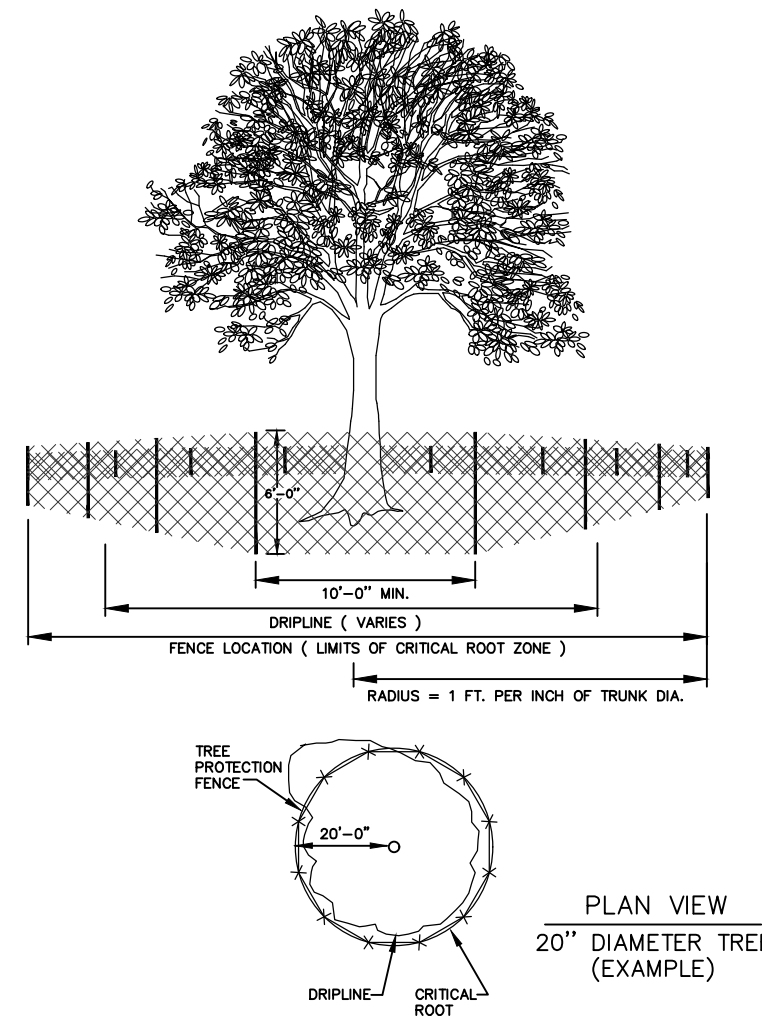

TREE PROTECTION CONSTRUCTION FENCE
NOT TO SCALE

DATE	
REVISIONS:	

OWNER:
TESSI PROPERTIES, LLC
153 TREELINE PARK, SUITE 100
SAN ANTONIO, TEXAS 78209

**VANCE JACKSON
REMOTE PARKING LOT**
15480 VANCE JACKSON
SAN ANTONIO, TX 78249

STORM WATER POLLUTION PREVENTION details

DESIGNED BY:	AB
DRAWN BY:	JAR
SCALE:	N"=50'
DATE:	11/27/24
SHEET NO.	

C2.1

Attachment E – Request to Temporarily Seal a Feature

No sensitive features will be sealed in this project site.

Attachment F – Structural Practices

The following structural measures will be installed prior to the initiation of site preparation activities:


- Erection of silt fences along the downgradient boundary of construction activities and rock berms with silt fence for secondary protection, as located on Exhibit 1 and illustrated in Exhibit 3.
- Installation of stabilized construction entrance/exit(s) and construction staging area(s), as located on Exhibit 1, and illustrated on Exhibit 3.

The following structural measures will be installed at the initiation of construction activities or as appropriate based on the construction sequencing:

- Installation of concrete truck washout pit(s), as required and located on Exhibit 1 and illustrated on Exhibit 3.

Attachment G – Drainage Area Map

See Exhibit 2 – Drainage Area Map attached at the end of these attachments.

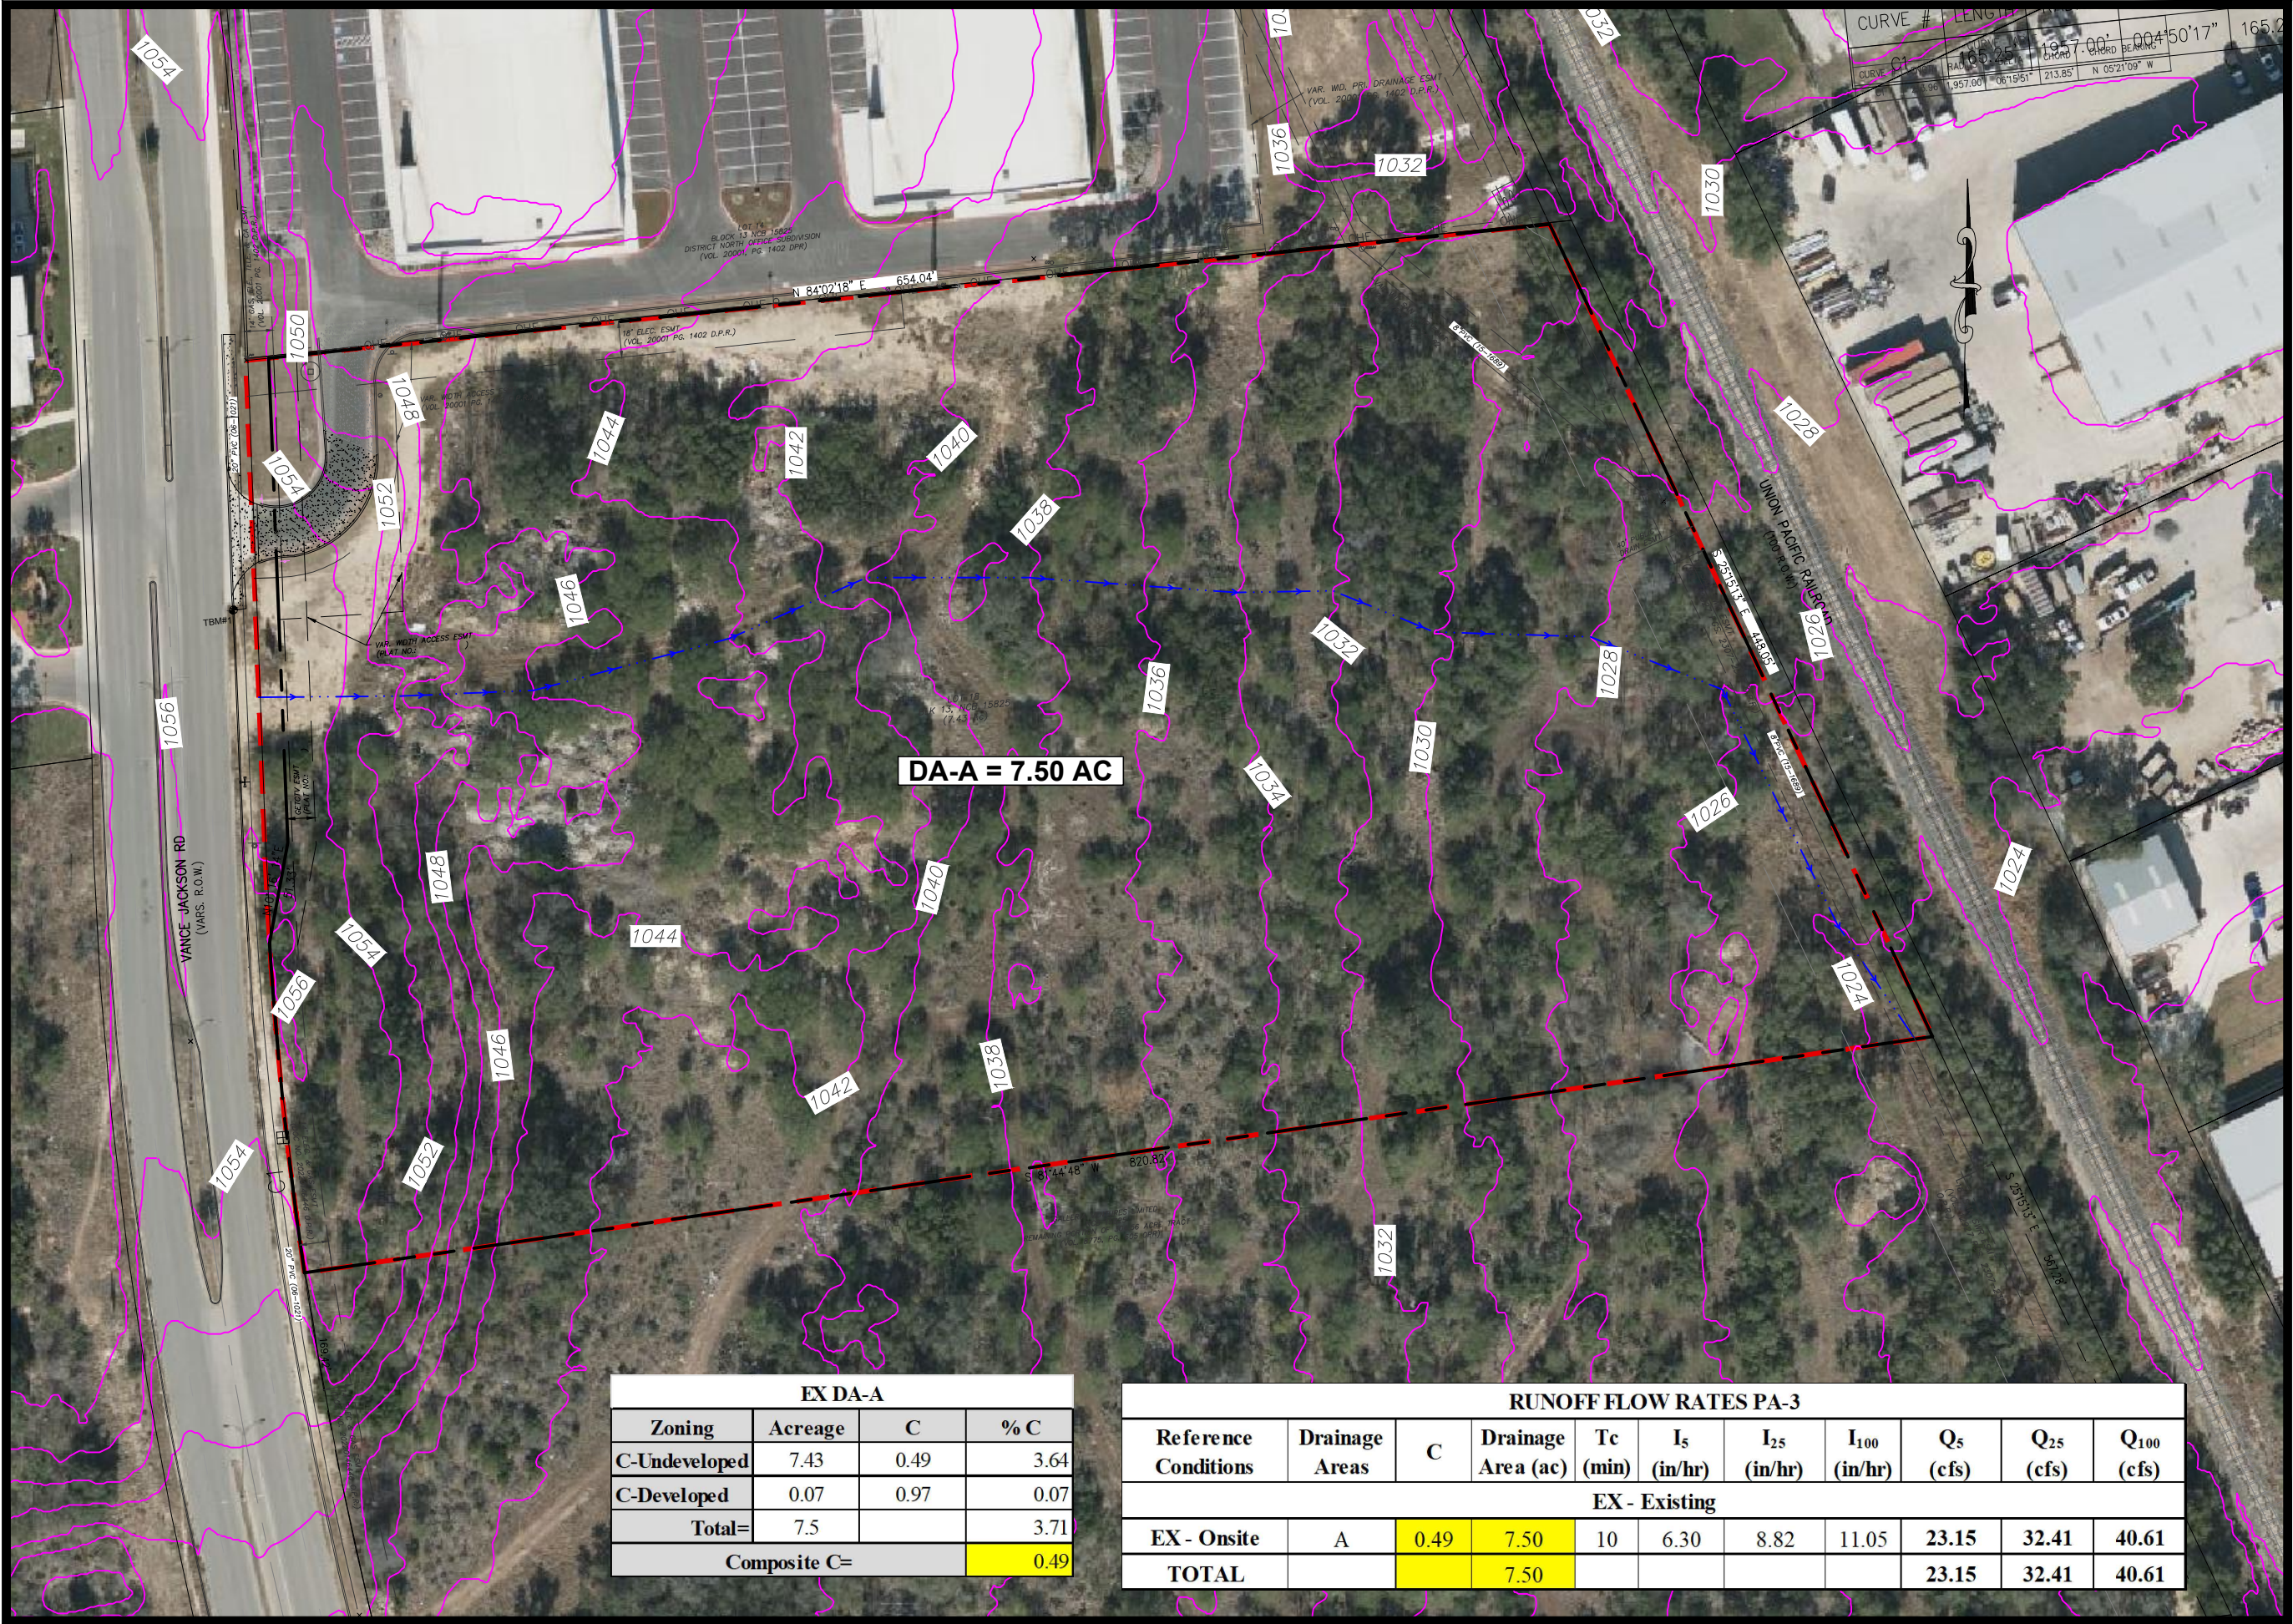

EX DA-A			
Zoning	Acreeage	C	% C
C-Undeveloped	7.43	0.49	3.64
C-Developed	0.07	0.97	0.07
Total=	7.5		3.71
Composite C=			0.49


RUNOFF FLOW RATES PA-3											
Reference Conditions	Drainage Areas	C	Drainage Area (ac)	Tc (min)	I _s (in/hr)	I ₂₅ (in/hr)	I ₁₀₀ (in/hr)	Q ₅ (cfs)	Q ₂₅ (cfs)	Q ₁₀₀ (cfs)	
EX - Existing											
EX - Onsite	A	0.49	7.50	10	6.30	8.82	11.05	23.15	32.41	40.61	
TOTAL			7.50					23.15	32.41	40.61	

TESSI PROPERTIES BUSINESS PARK

VANCE JACKSON
SAN ANTONIO, TEXAS 78249

EXISTING DRAINAGE AREA MAP

PROJECT NO.	1448-02
FILENAME:	
DESIGNED BY:	AB
DRAWN BY:	JC
SCALE:	1"=80'
DATE:	10/31/24
SHEET NO.	

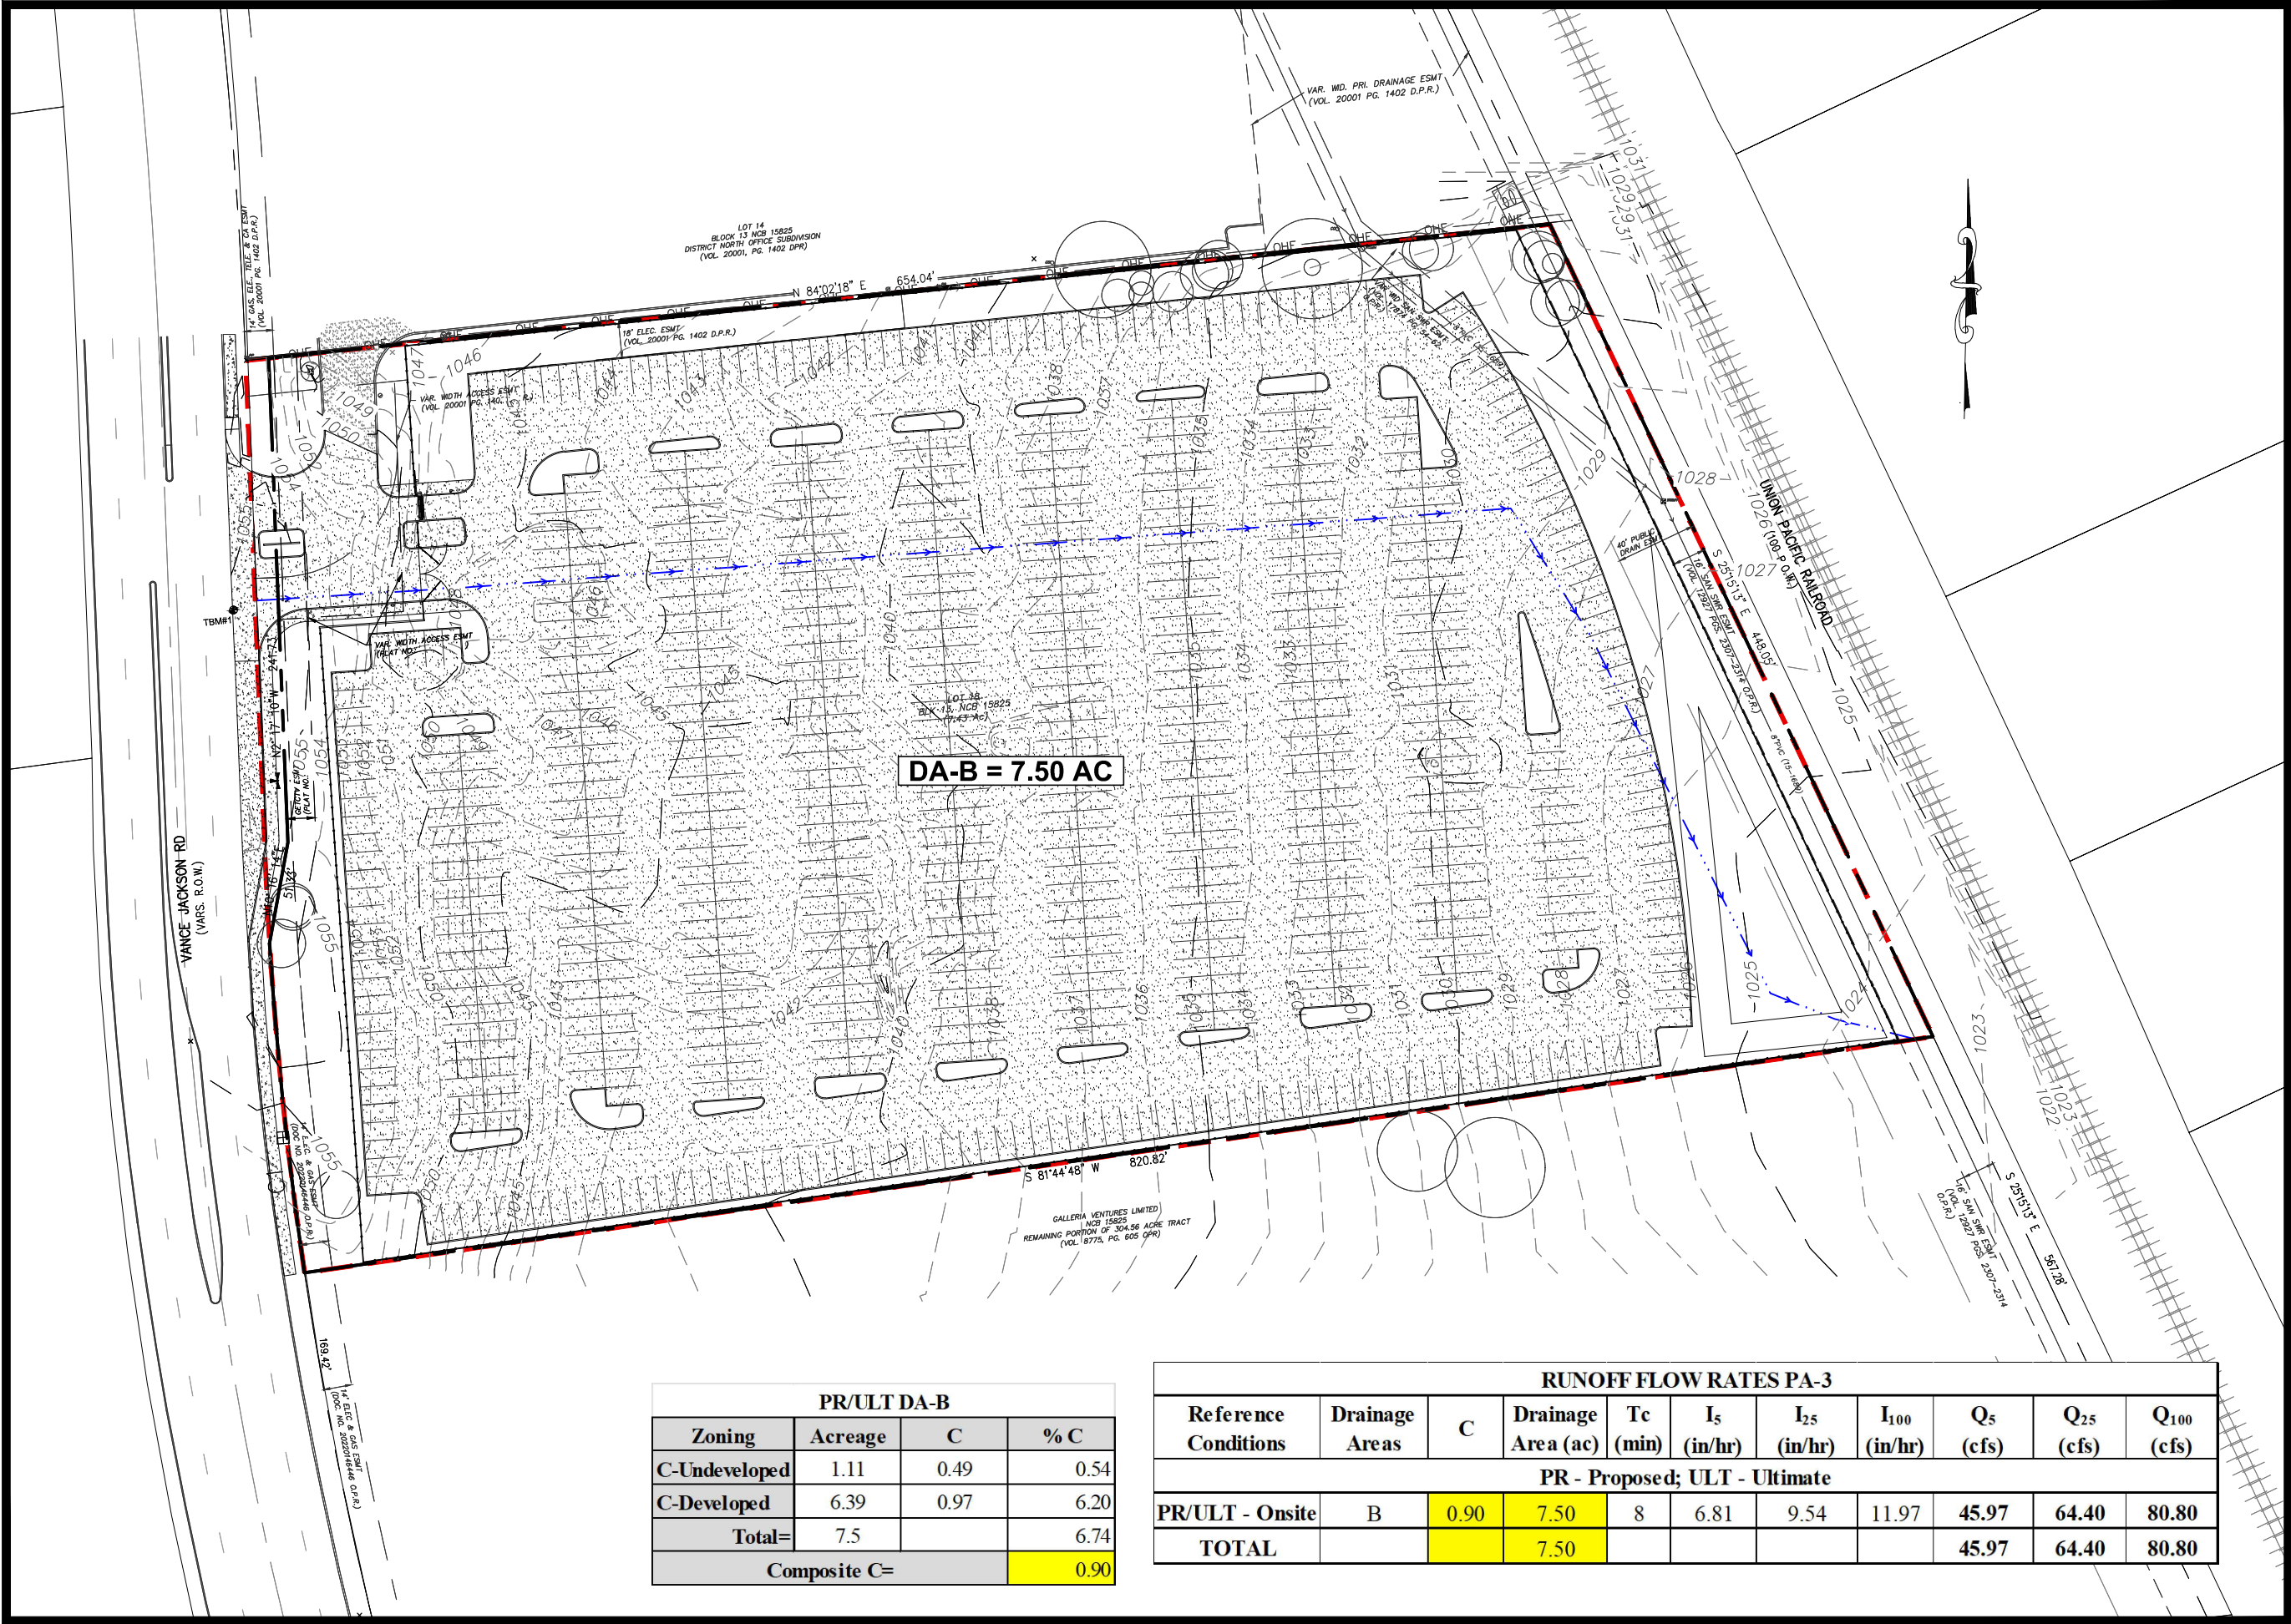

PR/ULT DA-B			
Zoning	Acreage	C	% C
C-Undeveloped	1.11	0.49	0.54
C-Developed	6.39	0.97	6.20
Total=	7.5		6.74
Composite C=			0.90

RUNOFF FLOW RATES PA-3										
Reference Conditions	Drainage Areas	C	Drainage Area (ac)	Tc (min)	I ₅ (in/hr)	I ₂₅ (in/hr)	I ₁₀₀ (in/hr)	Q ₅ (cfs)	Q ₂₅ (cfs)	Q ₁₀₀ (cfs)
PR - Proposed; ULT - Ultimate										
PR/ULT - Onsite	B	0.90	7.50	8	6.81	9.54	11.97	45.97	64.40	80.80
TOTAL			7.50					45.97	64.40	80.80

TESSI PROPERTIES BUSINESS PARK

VANCE JACKSON
SAN ANTONIO, TEXAS 78249

PROPOSED/ULTIMATE DRAINAGE AREA MAP

Klove
ENGINEERING
Site Development Engineering Services
Firm No. 11042
www.kloveengineering.com (210) 485-5683

PROJECT NO.	1448-02
FILENAME:	
DESIGNED BY:	AB
DRAWN BY:	JC & MV
SCALE:	1"=80'
DATE:	10/31/24
SHEET NO.	

Attachment H – Temporary Sediment Pond(s) Plans and Calculations

No temporary sediment pond required.

Attachment I – Inspection and Maintenance for TBMPs

Inspections

Designated and qualified person(s) shall inspect Pollution Control Measures weekly and within 24 hours after a storm event greater than 0.5 inches of rainfall. An inspection report that summarizes the scope of the inspection, names and qualifications of personnel conducting the inspection, date of the inspection, major observations, and actions taken as a result of the inspection shall be recorded and maintained as part of Storm Water TPDES data for a period of three years after the date of the inspection. A copy of the Inspection Report Form is provided in this Storm Water Pollution Prevention Plan.

As a minimum, the inspector shall observe: (1) significant disturbed areas for evidence of erosion, (2) storage areas for evidence of leakage from the exposed stored materials, (3) structural controls (rock berm outlets, silt fences, drainage swales, etc.) for evidence of failure or excess siltation (over 6 inches deep), (4) vehicle exit point for evidence of off-site sediment tracking, (5) vehicle storage areas for signs of leaking equipment or spills, and (6) concrete truck rinse-out pit for signs of potential failure. Deficiencies noted during the inspection will be corrected and documented within seven (7) calendar days following the inspection or before the next anticipated storm event if practicable.

Pollution Prevention Measure	Inspected	Corrective Action	
		Description	Date Completed
General			
Revegetation			
Erosion/Sediment Controls			
Vehicle Exits			
Material Areas			
Equipment Areas			
Concrete Rinse			
Construction Debris			
Trash Receptacles			
Infrastructure			
Roadway Clearing			
Utility Clearing			
Roadway Grading			
Utility Construction			
Drainage Construction			
Roadway Base			
Roadway Surfaces			
Site Cleanups			
Building			
Clearing for Building			
Foundation Grading			
Utility Construction			
Foundation Construction			
Building Construction			
Site Grading			
Site Cleanup			

**Indicate N/A where measure does not apply.*

By my signature below, I certify that all items are acceptable and the project site is in compliance with SWPPP.

Inspector's Name

Inspector's Signature

Name of Owner/Operator (Firm)

Date

Note: Inspector is to attach a brief statement of his qualifications to this report.

PROJECT MILESTONE DATES

Date when major site grading activities begin:

<u>Construction Activity</u>	<u>Date</u>

Dates when construction activities temporarily or permanently cease on all or a portion of the project:

<u>Construction Activity</u>	<u>Date</u>

Date when stabilization measures are initiated:

<u>Stabilization Activity</u>	<u>Date</u>

Attachment I (con't) – Inspection and Maintenance for TBMPs

Temporary Sediment Control Fences

1. Inspect all fencing weekly, and after any rainfall.
2. Remove sediment when buildup reaches 6 inches.
3. Replace any torn fabric or install a second line of fencing parallel to the torn section.
4. Replace or repair any sections crushed or collapsed in the course of construction activity. If a section of fence is obstructing vehicular access, consider relocating it to a spot where it will provide equal protection, but will not obstruct vehicles. A triangular filter dike may be preferable to a silt fence at common vehicle access points.
5. When construction is complete, the sediment should be disposed of in a manner that will not cause additional siltation and the prior location of silt fence should be revegetated. The fence itself should be disposed of in an approved landfill.

Rock Berm/High Service Rock Berm

1. Inspections should be made weekly and after each rainfall by the responsible party.
2. Remove sediment and other debris when buildup reaches 6 inches and dispose of the accumulated silt in an approved manner.
3. Repair any loose wire sheathing.
4. The berm should be reshaped as needed during inspection.
5. The berm should be replaced when the structure ceases to function as intended due to silt accumulation among the rocks, washout, construction traffic damage, etc.
6. The rock berm should be left in place until all upstream areas are stabilized and accumulated silt removed.

Temporary Construction Entrance and Exits

1. The entrance should be maintained in a condition, which will prevent tracking or following of sediment onto public rights-of-way. This may require periodic top dressing with additional stone as conditions demand and repair and/or cleanout of any measures used to trap sediment.
2. All sediment spilled, dropped, washed or tracked on to public rights-of-ways should be removed immediately by contractor.
3. When necessary, wheels should be cleaned to remove sediment prior to entrance onto public right-of-way.
4. When washing is required, it should be done on an area stabilized with crushed stone that drains into an approved sediment trap or sediment basin.
5. All sediment should be prevented from entering any storm drain, ditch, or water course by using approved methods.

Bagged Gravel Inlet Filters

1. Inspections should be made weekly and after each rainfall. Repair or replacement should be made promptly as needed by the contractor.
2. Remove sediment when buildup reached a depth of 3 inches. Removed sediment should be deposited in a suitable area and in such a manner that it will not erode.
3. Check placement of device to prevent gaps between device and curb.

4. Inspect filter fabric and patch or replace if torn or missing.
5. Structures should be removed and the area stabilized only after the remaining drainage area has been properly stabilized.

Temporary Sedimentation Basin

1. Inspection should be made weekly and after each rainfall. Check the embankment, spillways, and outlet for erosion damage, and inspect the embankment for piping and settlement. Repair should be made promptly as needed by contractor.
2. Trash and other debris should be removed after each rainfall to prevent clogging out of the outlet structure.
3. Accumulated silt should be removed and the basin should be re-graded to its original dimensions at such point that the capacity of the impoundment has been reduced to 75% of its original storage capacity.
4. The removed sediment should be stockpiled or redistributed in areas that are protected from erosion.


Documentation Procedures

1. A copy of the inspection report is located on the following page.
2. The inspection report must be maintained on site at all times.
3. The inspection report is incorporated as part of the WPAP. The contractor is responsible for completing and updating the form in compliance with TCEQ rules.

Attachment J – Schedule of Interim and Permanent Soil Stabilization

Interim on-site stabilization measures, which are continuous, will include minimizing soil disturbances by exposing only the smallest practical area of land required for the shortest period of time and maximizing use of natural vegetation. As soon as practical, all disturbed soil will be stabilized as per project specifications in accordance with pages 1-35 to 1-60 of TCEQ's Technical Guidance Manual (TGM) RG-348 (2005). Mulching, netting, erosion blankets and seeding are acceptable.


Stabilization measures will be initiated as soon as practicable in portions of the site where construction activities have temporarily or permanently ceased, and except as provided below, will be initiated no more than fourteen (14) days after the construction activity in that portion of the site has temporarily or permanently ceased. Where construction activity on a portion of the site is temporarily ceased, and earth disturbing activities will be resumed within twenty-one (21) days, temporary stabilization measures do not have to be initiated on that portion of site. In areas experiencing droughts where the initiation of stabilization measures by the 14th day after construction activity has temporarily or permanently ceased is precluded by seasonably arid conditions, stabilization measures must be initiated as soon as practicable.

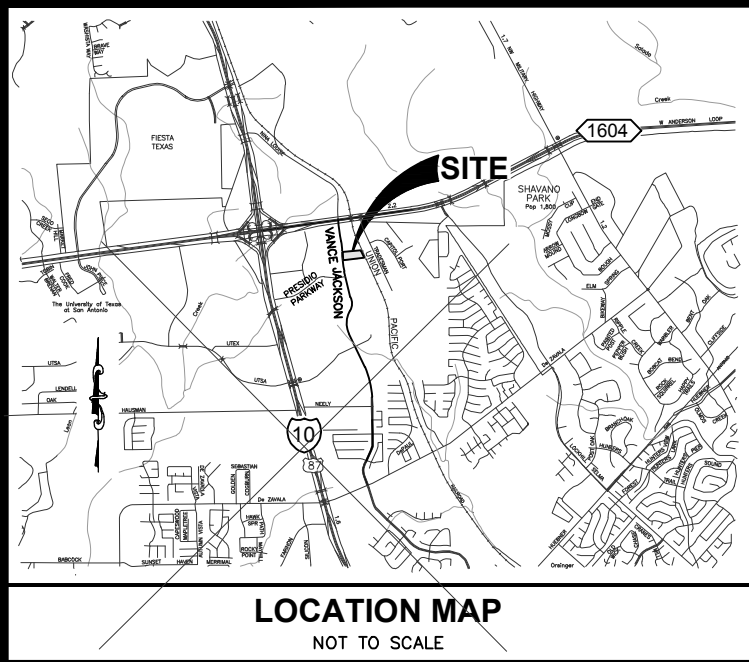

REQUIRED TSS REMOVAL FOR ENTIRE SITE			
TOTAL ACREAGE	PRE-DEVELOPMENT IMPERVIOUS COVER	POST-DEVELOPMENT IMPERVIOUS COVER	Lm-REQUIRED TSS REMOVAL
7.50 ac	0.07 ac	5.97 ac	4,814 lbs

BREAKDOWN OF TSS TREATED BY PERMANENT BMPS						
PROPOSED BMP	DRAINAGE AREA TO BMP	IMPERVIOUS COVER TO BMP	BMP EFFICIENCY	F	PERCENT OF TOTAL TSS BEING TREATED	TSS BEING REMOVED BY BMP
SAND BASIN	7.15 ac	5.97 ac	89%	0.87	100%	4,814 lbs



LEGEND		
EXISTING	PROPOSED	DESCRIPTION
-6.78-	-6.78-	CONTOUR
	→	FLOW ARROW
		UNCAPTURED AREA
		RETAINING WALL



UNCAPTURED AREA



CAPTURED AREA

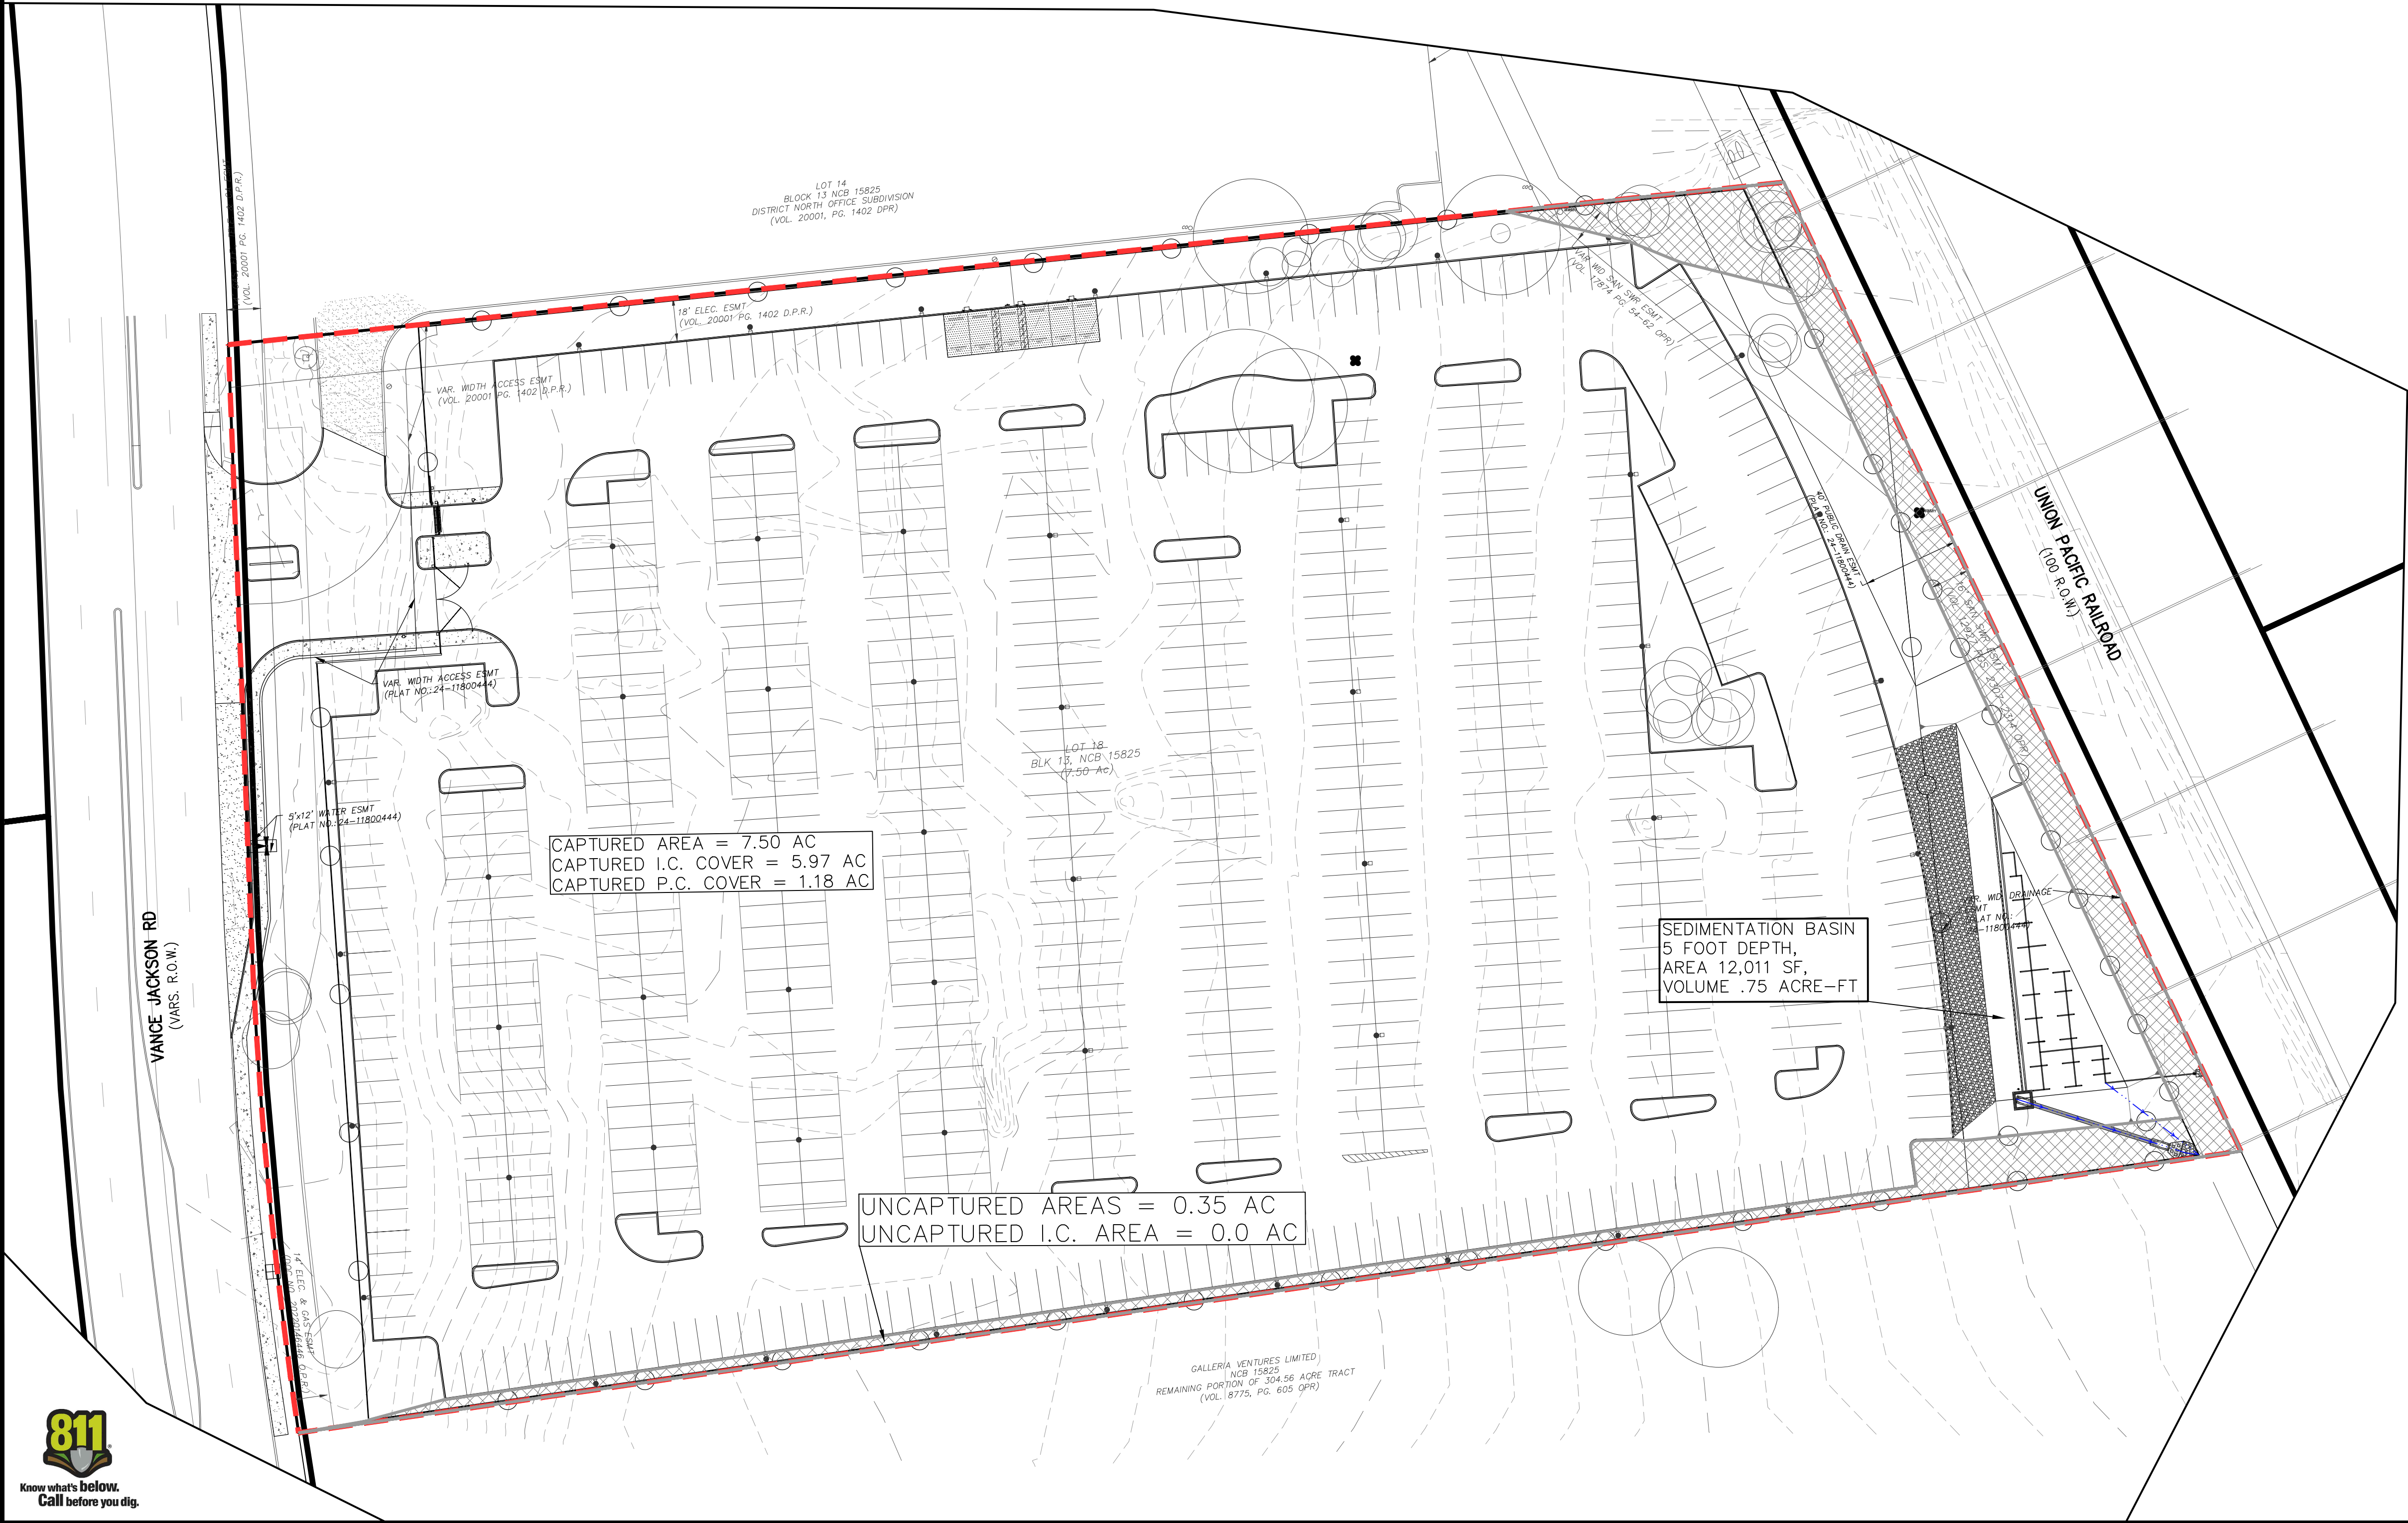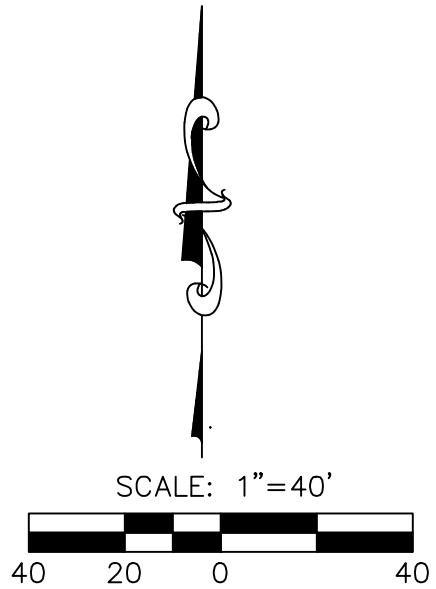

- Texas Commission on Environmental Quality
Contributing Zone Plan
General Construction Notes
- Edwards Aquifer Protection Program Construction Notes - Legal Disclaimer
- The following listed "construction notes" are intended to be advisory in nature only and do not constitute an approval or conditional approval by the Executive Director (ED), nor do they constitute a comprehensive listing of rules or conditions to be followed during construction. Further actions may be required to achieve compliance with TCEQ regulations found in Title 30, Texas Administrative Code (TAC), Chapters 213 and 217, as well as local ordinances and regulations providing for the protection of water quality. Additionally, nothing contained in the following listed "construction notes" restricts the powers of the ED, the commission or any other governmental entity to prevent, correct, or curtail activities that result or may result in pollution of the Edwards Aquifer or hydrologically connected surface waters. The holder of any Edwards Aquifer Protection Plan containing "construction notes" is still responsible for compliance with Title 30, TAC, Chapters 213 or any other applicable TCEQ regulation, as well as all conditions of an Edwards Aquifer Protection Plan through all phases of plan implementation. Failure to comply with any condition of the ED's approval, whether or not in contradiction of any "construction notes," is a violation of TCEQ regulations and any violation is subject to administrative rules, orders, and penalties as provided under Title 30, TAC § 213.10 (relating to Enforcement). Such violations may also be subject to civil penalties and injunction. The following listed "construction notes" in no way represent an approved exception by the ED to any part of Title 30 TAC, Chapters 213 and 217, or any other TCEQ applicable regulation.
- A written notice of construction must be submitted to the TCEQ regional office at least 48 hours prior to the start of any ground disturbance or construction activities. This notice must include:
 - the name of the approved project;
 - the activity start date; and
 - the contact information of the prime contractor.
 - All contractors conducting regulated activities associated with this project should be provided with complete copies of the approved Contributing Zone Plan (CZP) and the TCEQ letter indicating the specific conditions of its approval. During the course of these regulated activities, the contractor(s) should keep copies of the approved plan and approval letter on-site.
 - No hazardous substance storage tank shall be installed within 150 feet of a water supply source, distribution system, well, or sensitive feature.
 - Prior to beginning any construction activity, all temporary erosion and sedimentation (E&S) control measures must be properly installed and maintained in accordance with the manufacturers specifications. If inspections indicate a control has been used inappropriately, or incorrectly, the applicant must replace or modify the control for site situations. These controls must remain in place until the disturbed areas have been permanently stabilized.
 - Any sediment that escapes the construction site must be collected and properly disposed of before the next rain event to ensure it is not washed into surface streams, sensitive features, etc.
 - Sediment must be removed from the sediment traps or sedimentation basins when it occupies 50% of the basin's design capacity.
 - Litter, construction debris, and construction chemicals exposed to stormwater shall be prevented from being discharged offsite.
 - All excavated material that will be stored on-site must have proper E&S controls.
 - If portions of the site will have a cease in construction activity lasting longer than 14 days, soil
- TCEQ-0592A (Rev. July 15, 2015) Page 1 of 2

- stabilization in those areas shall be initiated as soon as possible prior to the 14th day of inactivity. If activity will resume prior to the 21st day, stabilization measures are not required. If drought conditions or inclement weather prevent action by the 14th day, stabilization measures shall be initiated as soon as possible.
- The following records should be maintained and made available to the TCEQ upon request:
 - the dates when major grading activities occur;
 - the dates when construction activities temporarily or permanently cease on a portion of the site; and
 - the dates when stabilization measures are initiated.
 - The holder of any approved CZP must notify the appropriate regional office in writing and obtain approval from the executive director prior to initiating any of the following:
 - A. any physical or operational modification of any best management practices (BMPs) or structure(s), including but not limited to temporary or permanent ponds, dams, berms, silt fences, and diversionary structures;
 - B. any change in the nature or character of the regulated activity from that which was originally approved;
 - C. any change that would significantly impact the ability to prevent pollution of the Edwards Aquifer; or
 - D. any development of land previously identified as undeveloped in the approved contributing zone plan.
- | | |
|--|---|
| Austin Regional Office
12100 Park 35 Circle, Building A
Austin, Texas 78755-1808
Phone (512) 339-2929
Fax (512) 339-3795 | San Antonio Regional Office
14250 Judson Road
San Antonio, Texas 78223-4480
Phone (210) 493-3096
Fax (210) 545-4329 |
|--|---|

THESE GENERAL CONSTRUCTION NOTES MUST BE INCLUDED ON THE CONSTRUCTION PLANS PROVIDED TO THE CONTRACTOR AND ALL SUBCONTRACTORS.

DATE	
REVISIONS:	

OWNER:
TESSI PROPERTIES, LLC
153 TREELINE PARK, SUITE 100
SAN ANTONIO, TEXAS 78209

VANCE JACKSON
REMOTE PARKING LOT
15480 VANCE JACKSON
SAN ANTONIO, TX 78249

DESIGNED BY:	AB
DRAWN BY:	JAR
SCALE:	1"=40'
DATE:	11/27/24
SHEET NO.	



Notice of Intent (NOI) for an Authorization for Stormwater Discharges Associated with Construction Activity under TPDES General Permit TXR150000

IMPORTANT INFORMATION

Please read and use the General Information and Instructions prior to filling out each question in the NOI form.

Use the NOI Checklist to ensure all required information is completed correctly.

Incomplete applications delay approval or result in automatic denial.

Once processed your permit authorization can be viewed by entering the following link into your internet browser: http://www2.tceq.texas.gov/wq_dpa/index.cfm or you can contact TCEQ Stormwater Processing Center at 512-239-3700.

ePERMITS

Effective September 1, 2018, this paper form must be submitted to TCEQ with a completed electronic reporting waiver form (TCEQ-20754).

To submit an NOI electronically, enter the following web address into your internet browser and follow the instructions: <https://www3.tceq.texas.gov/steers/index.cfm>

APPLICATION FEE AND PAYMENT

The application fee for submitting a paper NOI is \$325. The application fee for electronic submittal of a NOI through the TCEQ ePermits system (STEERS) is \$225.

Payment of the application fee can be submitted by mail or through the TCEQ ePay system. The payment and the NOI must be mailed to separate addresses. To access the TCEQ ePay system enter the following web address into your internet browser: <http://www.tceq.texas.gov/epay>.

Provide your payment information for verification of payment:

- If payment was mailed to TCEQ, provide the following:
 - Check/Money Order Number:
 - Name printed on Check:
- If payment was made via ePay, provide the following:
 - Voucher Number:
 - A copy of the payment voucher is attached to this paper NOI form.

RENEWAL (This portion of the NOI is not applicable after June 3, 2018)

Is this NOI for a renewal of an existing authorization? ☐ Yes ☐ No

If Yes, provide the authorization number here: TXR15

NOTE: If an authorization number is not provided, a new number will be assigned.

SECTION 1. OPERATOR (APPLICANT)

- a) If the applicant is currently a customer with TCEQ, what is the Customer Number (CN) issued to this entity? CN

(Refer to Section 1.a) of the Instructions)

- b) What is the Legal Name of the entity (applicant) applying for this permit? (The legal name must be spelled exactly as filed with the Texas Secretary of State, County, or in the legal document forming the entity.)

Tessi Properties, LLC

- c) What is the contact information for the Operator (Responsible Authority)?

Prefix (Mr. Ms. Miss): Ms.

First and Last Name: Abigail Kampmann

Suffix:

Title: Manager

Credentials:

Phone Number: 210-437-3961

Fax Number:

E-mail: akampmann@principleauto.com

Mailing Address: 153 Treeline Park, Suite 100

City, State, and Zip Code: San Antonio, TX 78209

Mailing Information if outside USA:

Territory:

Country Code:

Postal Code:

- d) Indicate the type of customer:

☐ Individual

☐ Federal Government

☐ Limited Partnership

☐ County Government

☐ General Partnership

☐ State Government

☐ Trust

☐ City Government

☐ Sole Proprietorship (D.B.A.)

☐ Other Government

☐ Corporation

☒ Other: LLC

☐ Estate

- e) Is the applicant an independent operator? ☒ Yes ☐ No

(If a governmental entity, a subsidiary, or part of a larger corporation, check No.)

f) Number of Employees. Select the range applicable to your company.

☒ 0-20

☐ 251-500

☐ 21-100

☐ 501 or higher

☐ 101-250

g) Customer Business Tax and Filing Numbers: (**Required** for Corporations and Limited Partnerships. **Not Required** for Individuals, Government, or Sole Proprietors.)

State Franchise Tax ID Number: 32064266227

Federal Tax ID:

Texas Secretary of State Charter (filing) Number: 0802764029

DUNS Number (if known):

SECTION 2. APPLICATION CONTACT

Is the application contact the same as the applicant identified above?

☒ Yes, go to Section 3

☐ No, complete this section

Prefix (Mr. Ms. Miss): Ms.

First and Last Name:

Suffix:

Title:

Credential:

Organization Name:

Phone Number:

Fax Number:

E-mail:

Mailing Address:

Internal Routing (Mail Code, Etc.):

City, State, and Zip Code:

Mailing information if outside USA:

Territory:

Country Code:

Postal Code:

SECTION 3. REGULATED ENTITY (RE) INFORMATION ON PROJECT OR SITE

a) If this is an existing permitted site, what is the Regulated Entity Number (RN) issued to this site? RN

(Refer to Section 3.a) of the Instructions)

b) Name of project or site (the name known by the community where it's located):

Vance Jackson Remote Parking Lot

- c) In your own words, briefly describe the type of construction occurring at the regulated site (residential, industrial, commercial, or other): Commercial Parking Lot / Storage
- d) County or Counties (if located in more than one): Bexar
- e) Latitude: 29.588281 Longitude: -98.587967
- f) Site Address/Location

If the site has a physical address such as 12100 Park 35 Circle, Austin, TX 78753, complete *Section A*.

If the site does not have a physical address, provide a location description in *Section B*. Example: located on the north side of FM 123, 2 miles west of the intersection of FM 123 and Highway 1.

Section A:

Street Number and Name: Vance Jackson

City, State, and Zip Code: San Antonio, TX 78249

Section B:

Location Description:

City (or city nearest to) where the site is located:

Zip Code where the site is located:

SECTION 4. GENERAL CHARACTERISTICS

- a) Is the project or site located on Indian Country Lands?
- ☐ Yes, do not submit this form. You must obtain authorization through EPA Region 6.
- ☒ No
- b) Is your construction activity associated with a facility that, when completed, would be associated with the exploration, development, or production of oil or gas or geothermal resources?
- ☐ Yes. Note: The construction stormwater runoff may be under jurisdiction of the Railroad Commission of Texas and may need to obtain authorization through EPA Region 6.
- ☒ No
- c) What is the Primary Standard Industrial Classification (SIC) Code that best describes the construction activity being conducted at the site? 7521
- d) What is the Secondary SIC Code(s), if applicable?
- e) What is the total number of acres to be disturbed? 7.50
- f) Is the project part of a larger common plan of development or sale?
- ☐ Yes
- ☒ No. The total number of acres disturbed, provided in e) above, must be 5 or more. If the total number of acres disturbed is less than 5, do not submit this form. See the requirements in the general permit for small construction sites.

- g) What is the estimated start date of the project? 06/15/25
- h) What is the estimated end date of the project? 12/15/26
- i) Will concrete truck washout be performed at the site? ☒ Yes ☐ No
- j) What is the name of the first water body(ies) to receive the stormwater runoff or potential runoff from the site? Olmos Creek
- k) What is the segment number(s) of the classified water body(ies) that the discharge will eventually reach? 1911A
- l) Is the discharge into a Municipal Separate Storm Sewer System (MS4)?
☐ Yes ☒ No

If Yes, provide the name of the MS4 operator:

Note: The general permit requires you to send a copy of this NOI form to the MS4 operator.

- m) Is the discharge or potential discharge from the site within the Recharge Zone, Contributing Zone, or Contributing Zone within the Transition Zone of the Edwards Aquifer, as defined in 30 TAC Chapter 213?
- ☒ Yes, complete the certification below.
- ☐ No, go to Section 5

I certify that the copy of the TCEQ-approved Plan required by the Edwards Aquifer Rule (30 TAC Chapter 213) that is included or referenced in the Stormwater Pollution Prevention Plan will be implemented.

☒ Yes

SECTION 5. NOI CERTIFICATION

- a) I certify that I have obtained a copy and understand the terms and conditions of the Construction General Permit (TXR150000). ☒ Yes
- b) I certify that the full legal name of the entity applying for this permit has been provided and is legally authorized to do business in Texas. ☒ Yes
- c) I understand that a Notice of Termination (NOT) must be submitted when this authorization is no longer needed. ☒ Yes
- d) I certify that a Stormwater Pollution Prevention Plan has been developed, will be implemented prior to construction and to the best of my knowledge and belief is compliant with any applicable local sediment and erosion control plans, as required in the Construction General Permit (TXR150000). ☒ Yes

Note: For multiple operators who prepare a shared SWP3, the confirmation of an operator may be limited to its obligations under the SWP3, provided all obligations are confirmed by at least one operator.

SECTION 6. APPLICANT CERTIFICATION SIGNATURE

Operator Signatory Name: Abigail Kampmann

Operator Signatory Title: Manager

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

I further certify that I am authorized under 30 Texas Administrative Code §305.44 to sign and submit this document, and can provide documentation in proof of such authorization upon request.

Signature (use blue ink):  Abigail Kampmann (Dec 3, 2024 09:02 CST) Date: Dec 3, 2024

NOTICE OF INTENT CHECKLIST (TXR150000)

Did you complete everything? Use this checklist to be sure!

Are you ready to mail your form to TCEQ? Go to the General Information Section of the Instructions for mailing addresses.

Confirm each item (or applicable item) in this form is complete. This checklist is for use by the applicant to ensure a complete application is being submitted. **Missing information may result in denial of coverage under the general permit.** (See NOI process description in the General Information and Instructions.)

APPLICATION FEE

If paying by check:

- ☐ Check was mailed **separately** to the TCEQs Cashier's Office. (See Instructions for Cashier's address and Application address.)
- ☐ Check number and name on check is provided in this application.

If using ePay:

- ☐ The voucher number is provided in this application and a copy of the voucher is attached.

RENEWAL

- ☐ If this application is for renewal of an existing authorization, the authorization number is provided.

OPERATOR INFORMATION

- ☐ Customer Number (CN) issued by TCEQ Central Registry
- ☐ Legal name as filed to do business in Texas. (Call TX SOS 512-463-5555 to verify.)
- ☐ Name and title of responsible authority signing the application.
- ☐ Phone number and e-mail address
- ☐ Mailing address is complete & verifiable with USPS. www.usps.com
- ☐ Type of operator (entity type). Is applicant an independent operator?
- ☐ Number of employees.
- ☐ For corporations or limited partnerships - Tax ID and SOS filing numbers.
- ☐ Application contact and address is complete & verifiable with USPS. <http://www.usps.com>

REGULATED ENTITY (RE) INFORMATION ON PROJECT OR SITE

- ☐ Regulated Entity Number (RN) (if site is already regulated by TCEQ)
- ☐ Site/project name and construction activity description
- ☐ County
- ☐ Latitude and longitude <http://www.tceq.texas.gov/gis/sqmaview.html>
- ☐ Site Address/Location. Do not use a rural route or post office box.

GENERAL CHARACTERISTICS

- ☐ Indian Country Lands -the facility is not on Indian Country Lands.
- ☐ Construction activity related to facility associated to oil, gas, or geothermal resources
- ☐ Primary SIC Code that best describes the construction activity being conducted at the site.
www.osha.gov/oshstats/sicser.html
- ☐ Estimated starting and ending dates of the project.
- ☐ Confirmation of concrete truck washout.
- ☐ Acres disturbed is provided and qualifies for coverage through a NOI.
- ☐ Common plan of development or sale.
- ☐ Receiving water body or water bodies.
- ☐ Segment number or numbers.
- ☐ MS4 operator.
- ☐ Edwards Aquifer rule.

CERTIFICATION

- ☐ Certification statements have been checked indicating Yes.
- ☐ Signature meets 30 Texas Administrative Code (TAC) §305.44 and is original.

Instructions for Notice of Intent (NOI) for Stormwater Discharges Associated with Construction Activity under TPDES General Permit (TXR150000)

GENERAL INFORMATION

Where to Send the Notice of Intent (NOI):

By Regular Mail:

TCEQ

Stormwater Processing Center (MC228)

P.O. Box 13087

Austin, Texas 78711-3087

By Overnight or Express Mail:

TCEQ

Stormwater Processing Center (MC228)

12100 Park 35 Circle

Austin, TX

Application Fee:

The application fee of \$325 is required to be paid at the time the NOI is submitted. Failure to submit payment at the time the application is filed will cause delays in acknowledgment or denial of coverage under the general permit. Payment of the fee may be made by check or money order, payable to TCEQ, or through EPAY (electronic payment through the web).

Mailed Payments:

Use the attached General Permit Payment Submittal Form. The application fee is submitted to a different address than the NOI. Read the General Permit Payment Submittal Form for further instructions, including the address to send the payment.

ePAY Electronic Payment: <http://www.tceq.texas.gov/epay>

When making the payment you must select Water Quality, and then select the fee category "General Permit Construction Storm Water Discharge NOI Application". You must include a copy of the payment voucher with your NOI. Your NOI will not be considered complete without the payment voucher.

TCEQ Contact List:

Application – status and form questions:

512-239-3700, swpermit@tceq.texas.gov

Technical questions:

512-239-4671, swgp@tceq.texas.gov

Environmental Law Division:

512-239-0600

Records Management - obtain copies of forms:

512-239-0900

Reports from databases (as available):

512-239-DATA (3282)

Cashier's office:

512-239-0357 or 512-239-0187

Notice of Intent Process:

When your NOI is received by the program, the form will be processed as follows:

- **Administrative Review:** Each item on the form will be reviewed for a complete response. In addition, the operator's legal name must be verified with Texas Secretary of State as valid and active (if applicable). The address(es) on the form must be verified with the US Postal service as receiving regular mail delivery. Do not give an overnight/express mailing address.
- **Notice of Deficiency:** If an item is incomplete or not verifiable as indicated

above, a notice of deficiency (NOD) will be mailed to the operator. The operator will have 30 days to respond to the NOD. The response will be reviewed for completeness.

- **Acknowledgment of Coverage:** An Acknowledgment Certificate will be mailed to the operator. This certificate acknowledges coverage under the general permit.

or

Denial of Coverage: If the operator fails to respond to the NOD or the response is inadequate, coverage under the general permit may be denied. If coverage is denied, the operator will be notified.

General Permit (Your Permit)

For NOIs submitted **electronically** through ePermits, provisional coverage under the general permit begins immediately following confirmation of receipt of the NOI form by the TCEQ.

For **paper** NOIs, provisional coverage under the general permit begins **7 days after a completed NOI is postmarked for delivery** to the TCEQ.

You should have a copy of your general permit when submitting your application. You may view and print your permit for which you are seeking coverage, on the TCEQ web site <http://www.tceq.texas.gov>. Search using keyword TXR150000.

Change in Operator

An authorization under the general permit is not transferable. If the operator of the regulated project or site changes, the present permittee must submit a Notice of Termination and the new operator must submit a Notice of Intent. The NOT and NOI must be submitted no later than 10 days prior to the change in Operator status.

TCEQ Central Registry Core Data Form

The Core Data Form has been incorporated into this form. Do not send a Core Data Form to TCEQ. After final acknowledgment of coverage under the general permit, the program will assign a Customer Number and Regulated Entity Number, if one has not already been assigned to this customer or site.

For existing customers and sites, you can find the Customer Number and Regulated Entity Number by entering the following web address into your internet browser:

<http://www15.tceq.texas.gov/crpub/> or you can contact the TCEQ Stormwater Processing Center at 512-239-3700 for assistance. On the website, you can search by your permit number, the Regulated Entity (RN) number, or the Customer Number (CN). If you do not know these numbers, you can select "Advanced Search" to search by permittee name, site address, etc.

The Customer (Permittee) is responsible for providing consistent information to the TCEQ, and for updating all CN and RN data for all authorizations as changes occur. For this permit, a Notice of Change form must be submitted to the program area.

INSTRUCTIONS FOR FILLING OUT THE NOI FORM

Renewal of General Permit. Dischargers holding active authorizations under the expired General Permit are required to submit a NOI to continue coverage. The existing permit

number is required. If the permit number is not provided or has been terminated, expired, or denied, a new permit number will be issued.

Section 1. OPERATOR (APPLICANT)

a) Customer Number (CN)

TCEQ's Central Registry will assign each customer a number that begins with CN, followed by nine digits. **This is not a permit number, registration number, or license number.**

If the applicant is an existing TCEQ customer, the Customer Number is available at the following website: <http://www15.tceq.texas.gov/crpub/>. If the applicant is not an existing TCEQ customer, leave the space for CN blank.

b) Legal Name of Applicant

Provide the current legal name of the applicant. The name must be provided exactly as filed with the Texas Secretary of State (SOS), or on other legal documents forming the entity, as filed in the county. You may contact the SOS at 512-463-5555, for more information related to filing in Texas. If filed in the county, provide a copy of the legal documents showing the legal name.

c) Contact Information for the Applicant (Responsible Authority)

Provide information for the person signing the application in the Certification section. This person is also referred to as the Responsible Authority.

Provide a complete mailing address for receiving mail from the TCEQ. The mailing address must be recognized by the US Postal Service. You may verify the address on the following website: <https://tools.usps.com/go/ZipLookupAction!input.action>.

The phone number should provide contact to the applicant.

The fax number and e-mail address are optional and should correspond to the applicant.

d) Type of Customer (Entity Type)

Check only one box that identifies the type of entity. Use the descriptions below to identify the appropriate entity type. Note that the selected entity type also indicates the name that must be provided as an applicant for an authorization.

Individual

An individual is a customer who has not established a business, but conducts an activity that needs to be regulated by the TCEQ.

Partnership

A customer that is established as a partnership as defined by the Texas Secretary of State Office (TX SOS). If the customer is a 'General Partnership' or 'Joint Venture' filed in the county (not filed with TX SOS), the legal name of each partner forming the 'General Partnership' or 'Joint Venture' must be provided. Each 'legal entity' must apply as a co-applicant.

Trust or Estate

A trust and an estate are fiduciary relationships governing the trustee/executor with respect to the trust/estate property.

Sole Proprietorship (DBA)

A sole proprietorship is a customer that is owned by only one person and has not been incorporated. This business may:

1. be under the person's name
2. have its own name (doing business as or DBA)
3. have any number of employees.

If the customer is a Sole Proprietorship or DBA, the 'legal name' of the individual business 'owner' must be provided. The DBA name is not recognized as the 'legal name' of the entity. The DBA name may be used for the site name (regulated entity).

Corporation

A customer that meets all of these conditions:

1. is a legally incorporated entity under the laws of any state or country
2. is recognized as a corporation by the Texas Secretary of State
3. has proper operating authority to operate in Texas

The corporation's 'legal name' as filed with the Texas Secretary of State must be provided as applicant. An 'assumed' name of a corporation is not recognized as the 'legal name' of the entity.

Government

Federal, state, county, or city government (as appropriate)

The customer is either an agency of one of these levels of government or the governmental body itself. The government agency's 'legal name' must be provided as the applicant. A department name or other description of the organization is not recognized as the 'legal name'.

Other

This may include a utility district, water district, tribal government, college district, council of governments, or river authority. Provide the specific type of government.

e) Independent Entity

Check No if this customer is a subsidiary, part of a larger company, or is a governmental entity. Otherwise, check Yes.

f) Number of Employees

Check one box to show the number of employees for this customer's entire company, at all locations. This is not necessarily the number of employees at the site named in the application.

g) Customer Business Tax and Filing Numbers

These are required for Corporations and Limited Partnerships. These are not required for Individuals, Government, and Sole Proprietors.

State Franchise Tax ID Number

Corporations and limited liability companies that operate in Texas are issued a franchise tax identification number. If this customer is a corporation or limited liability company, enter the Tax ID number.

Federal Tax ID

All businesses, except for some small sole proprietors, individuals, or general partnerships should have a federal taxpayer identification number (TIN). Enter this number here. Use no prefixes, dashes, or hyphens. Sole proprietors, individuals, or general partnerships do not need to provide a federal tax ID.

TX SOS Charter (filing) Number

Corporations and Limited Partnerships required to register with the Texas Secretary of State are issued a charter or filing number. You may obtain further information by calling SOS at 512-463-5555.

DUNS Number

Most businesses have a DUNS (Data Universal Numbering System) number issued by Dun and Bradstreet Corp. If this customer has one, enter it here.

Section 2. APPLICATION CONTACT

Provide the name and contact information for the person that TCEQ can contact for additional information regarding this application.

Section 3. REGULATED ENTITY (RE) INFORMATION ON PROJECT OR SITE

a) Regulated Entity Number (RN)

The RN is issued by TCEQ's Central Registry to sites where an activity is regulated by TCEQ. This is not a permit number, registration number, or license number. Search TCEQ's Central Registry to see if the site has an assigned RN at <http://www15.tceq.texas.gov/crpub/>. If this regulated entity has not been assigned an RN, leave this space blank.

If the site of your business is part of a larger business site, an RN may already be assigned for the larger site. Use the RN assigned for the larger site.

If the site is found, provide the assigned RN and provide the information for the site to be authorized through this application. The site information for this authorization may vary from the larger site information.

An example is a chemical plant where a unit is owned or operated by a separate corporation that is accessible by the same physical address of your unit or facility. Other examples include industrial parks identified by one common address but different corporations have control of defined areas within the site. In both cases, an RN would be assigned for the physical address location and the permitted sites would be identified separately under the same RN.

b) Name of the Project or Site

Provide the name of the site or project as known by the public in the area where the site is located. The name you provide on this application will be used in the TCEQ Central Registry as the Regulated Entity name.

c) Description of Activity Regulated

In your own words, briefly describe the primary business that you are doing that requires this authorization. Do not repeat the SIC Code description.

d) County

Provide the name of the county where the site or project is located. If the site or project is located in more than one county, provide the county names as secondary.

e) Latitude and Longitude

Enter the latitude and longitude of the site in degrees, minutes, and seconds or decimal form. For help obtaining the latitude and longitude, go to:

<http://www.tceq.texas.gov/gis/sqmapview.html>.

f) Site Address/Location

If a site has an address that includes a street number and street name, enter the complete address for the site in *Section A*. If the physical address is not recognized as a USPS delivery address, you may need to validate the address with your local police (911 service) or through an online map site used to locate a site. Please confirm this to be a complete and valid address. Do not use a rural route or post office box for a site location.

If a site does not have an address that includes a street number and street name, provide a complete written location description in *Section B*. For example: "The site is located on the north side of FM 123, 2 miles west of the intersection of FM 123 and Highway 1."

Provide the city (or nearest city) and zip code of the site location.

Section 4. GENERAL CHARACTERISTICS

a) Indian Country Lands

If your site is located on Indian Country Lands, the TCEQ does not have authority to process your application. You must obtain authorization through EPA Region 6, Dallas. Do not submit this form to TCEQ.

b) Construction activity associated with facility associated with exploration, development, or production of oil, gas, or geothermal resources

If your activity is associated with oil and gas exploration, development, or production, you may be under jurisdiction of the Railroad Commission of Texas (RRC) and may need to obtain authorization from EPA Region 6.

Construction activities associated with a facility related to oil, gas or geothermal resources may include the construction of a well site; treatment or storage facility; underground hydrocarbon or natural gas storage facility; reclamation plant; gas processing facility; compressor station; terminal facility where crude oil is stored prior to refining and at which refined products are stored solely for use at the facility; a carbon dioxide geologic storage facility; and a gathering, transmission, or distribution pipeline that will transport crude oil or natural gas, including natural gas liquids, prior to refining of such oil or the use of the natural gas in any manufacturing process or as a residential or industrial fuel.

Where required by federal law, discharges of stormwater associated with construction activities under the RRC's jurisdiction must be authorized by the EPA and the RRC, as applicable. Activities under RRC jurisdiction include construction of a facility that, when completed, would be associated with the exploration, development, or production of oil or gas or geothermal resources, such as a well site; treatment or storage facility; underground hydrocarbon or natural gas storage facility; reclamation plant; gas processing facility; compressor station; terminal facility where crude oil is stored prior to refining and at which refined products are stored solely for use at the facility; a carbon dioxide geologic storage facility under the jurisdiction of the RRC; and a gathering, transmission, or distribution pipeline that will transport crude oil or natural gas, including natural gas liquids, prior to refining of such oil or the use of the natural gas in any manufacturing process or as a residential or industrial fuel. The RRC also has jurisdiction over stormwater from land disturbance associated with a site survey that is conducted prior to construction of a facility that would be regulated by the RRC. Under 33 U.S.C. §1342(l)(2) and §1362(24), EPA cannot require a permit for discharges of stormwater from field activities or operations associated with {oil and gas} exploration, production, processing, or treatment operations, or transmission facilities, including activities necessary to prepare a site for drilling and for the movement and placement of drilling equipment, whether or not such field activities or operations may be considered to be construction activities unless the discharge is contaminated by contact with any overburden, raw material, intermediate product, finished product, byproduct, or waste product located on the site of the facility. Under §3.8 of this title (relating to Water Protection), the RRC prohibits operators from causing or allowing pollution of surface or subsurface water. Operators are encouraged to implement and maintain best management practices (BMPs) to minimize discharges of pollutants, including sediment, in stormwater during construction activities to help ensure protection of surface water quality during storm events.

For more information about the jurisdictions of the RRC and the TCEQ, read the Memorandum of Understanding (MOU) between the RRC and TCEQ at 16 Texas Administrative Code, Part 1, Chapter 3, Rule 3.30, by entering the following link into an internet browser:

[http://texreg.sos.state.tx.us/public/readtac\\$ext.TacPage?sl=R&app=9&p_dir=&p_rloc=&p_tloc=&p_ploc=&pg=1&p_tac=&ti=16&pt=1&ch=3&rl=30](http://texreg.sos.state.tx.us/public/readtac$ext.TacPage?sl=R&app=9&p_dir=&p_rloc=&p_tloc=&p_ploc=&pg=1&p_tac=&ti=16&pt=1&ch=3&rl=30) or contact the TCEQ Stormwater Team at 512-239-4671 for additional information.

c) Primary Standard Industrial Classification (SIC) Code

Provide the SIC Code that best describes the construction activity being conducted at this site.

Common SIC Codes related to construction activities include:

- 1521 - Construction of Single Family Homes
- 1522 - Construction of Residential Buildings Other than Single Family Homes
- 1541 - Construction of Industrial Buildings and Warehouses
- 1542 - Construction of Non-residential Buildings, other than Industrial Buildings and Warehouses
- 1611 - Highway and Street Construction, except Highway Construction
- 1622 - Bridge, Tunnel, and Elevated Highway Construction

- 1623 - Water, Sewer, Pipeline and Communications, and Power Line Construction

For help with SIC Codes, enter the following link into your internet browser:

<http://www.osha.gov/pls/imis/sicsearch.html> or you can contact the TCEQ Small Business and Local Government Assistance Section at 800-447-2827 for assistance.

d) Secondary SIC Code

Secondary SIC Code(s) may be provided. Leave this blank if not applicable. For help with SIC Codes, enter the following link into your internet browser:

<http://www.osha.gov/pls/imis/sicsearch.html> or you can contact the TCEQ Small Business and Environmental Assistance Section at 800-447-2827 for assistance.

e) Total Number of Acres Disturbed

Provide the approximate number of acres that the construction site will disturb. Construction activities that disturb less than one acre, unless they are part of a larger common plan that disturbs more than one acre, do not require permit coverage. Construction activities that disturb between one and five acres, unless they are part of a common plan that disturbs more than five acres, do not require submission of an NOI. Therefore, the estimated area of land disturbed should not be less than five, unless the project is part of a larger common plan that disturbs five or more acres. Disturbed means any clearing, grading, excavating, or other similar activities.

If you have any questions about this item, please contact the stormwater technical staff by phone at 512-239-4671 or by email at swgp@tceq.texas.gov.

f) Common Plan of Development

Construction activities that disturb less than five acres do not require submission of an NOI unless they are part of a common plan of development or for sale where the area disturbed is five or more acres. Therefore, the estimated area of land disturbed should not be less than five, unless the project is part of a larger common plan that disturbs five or more acres. Disturbed means any clearing, grading, excavating, or other similar activities.

For more information on what a common plan of development is, refer to the definition of “Common Plan of Development” in the Definitions section of the general permit or enter the following link into your internet browser:

www.tceq.texas.gov/permitting/stormwater/common_plan_of_development_steps.html

For further information, go to the TCEQ stormwater construction webpage enter the following link into your internet browser: www.tceq.texas.gov/goto/construction and search for “Additional Guidance and Quick Links”. If you have any further questions about the Common Plan of Development you can contact the TCEQ Stormwater Team at 512-239-4671 or the TCEQ Small Business and Environmental Assistance at 800-447-2827.

g) Estimated Start Date of the Project

This is the date that any construction activity or construction support activity is initiated at the site. If renewing the permit provide the original start date of when construction activity for this project began.

h) Estimated End Date of the Project

This is the date that any construction activity or construction support activity will end and final stabilization will be achieved at the site.

i) Will concrete truck washout be performed at the site?

Indicate if you expect that operators of concrete trucks will washout concrete trucks at the construction site.

j) Identify the water body(s) receiving stormwater runoff

The stormwater may be discharged directly to a receiving stream or through a MS4 from your site. It eventually reaches a receiving water body such as a local stream or lake, possibly via a drainage ditch. You must provide the name of the water body that receives the discharge from the site (a local stream or lake).

If your site has more than one outfall you need to include the name of the first water body for each outfall, if they are different.

k) Identify the segment number(s) of the classified water body(s)

Identify the classified segment number(s) receiving a discharge directly or indirectly. Enter the following link into your internet browser to find the segment number of the classified water body where stormwater will flow from the site:

www.tceq.texas.gov/waterquality/monitoring/viewer.html or by contacting the TCEQ Water Quality Division at (512) 239-4671 for assistance.

You may also find the segment number in TCEQ publication GI-316 by entering the following link into your internet browser: www.tceq.texas.gov/publications/gi/gi-316 or by contacting the TCEQ Water Quality Division at (512) 239-4671 for assistance.

If the discharge is into an unclassified receiving water and then crosses state lines prior to entering a classified segment, select the appropriate watershed:

- 0100 (Canadian River Basin)
- 0200 (Red River Basin)
- 0300 (Sulfur River Basin)
- 0400 (Cypress Creek Basin)
- 0500 (Sabine River Basin)

Call the Water Quality Assessments section at 512-239-4671 for further assistance.

l) Discharge into MS4 – Identify the MS4 Operator

The discharge may initially be into a municipal separate storm sewer system (MS4). If the stormwater discharge is into an MS4, provide the name of the entity that operates the MS4 where the stormwater discharges. An MS4 operator is often a city, town, county, or utility district, but possibly can be another form of government. Please note that the Construction General Permit requires the Operator to supply the MS4 with a copy of the NOI submitted to TCEQ. For assistance, you may call the technical staff at 512-239-4671.

m) Discharges to the Edwards Aquifer Recharge Zone and Certification

The general permit requires the approved Contributing Zone Plan or Water Pollution Abatement Plan to be included or referenced as a part of the Stormwater Pollution Prevention Plan.

See maps on the TCEQ website to determine if the site is located within the Recharge Zone, Contributing Zone, or Contributing Zone within the Transition Zone of the Edwards Aquifer by entering the following link into an internet browser: www.tceq.texas.gov/field/eapp/viewer.html or by contacting the TCEQ Water Quality Division at 512-239-4671 for assistance.

If the discharge or potential discharge is within the Recharge Zone, Contributing Zone, or Contributing Zone within the Transition Zone of the Edwards Aquifer, a site-specific authorization approved by the Executive Director under the Edwards Aquifer Protection Program (30 TAC Chapter 213) is required before construction can begin.

For questions regarding the Edwards Aquifer Protection Program, contact the appropriate TCEQ Regional Office. For projects in Hays, Travis and Williamson Counties: Austin Regional Office, 12100 Park 35 Circle, Austin, TX 78753, 512-339-2929. For Projects in Bexar, Comal, Kinney, Medina and Uvalde Counties: TCEQ San Antonio Regional Office, 14250 Judson Rd., San Antonio, TX 78233-4480, 210-490-3096.

Section 5. NOI CERTIFICATION

Note: Failure to indicate Yes to all of the certification items may result in denial of coverage under the general permit.

a) Certification of Understanding the Terms and Conditions of Construction General Permit (TXR150000)

Provisional coverage under the Construction General Permit (TXR150000) begins 7 days after the completed paper NOI is postmarked for delivery to the TCEQ. Electronic applications submitted through ePermits have immediate provisional coverage. You must obtain a copy and read the Construction General Permit before submitting your application. You may view and print the Construction General Permit for which you are seeking coverage at the TCEQ web site by entering the following link into an internet browser: www.tceq.texas.gov/goto/construction or you may contact the TCEQ Stormwater processing Center at 512-239-3700 for assistance.

b) Certification of Legal Name

The full legal name of the applicant as authorized to do business in Texas is required. The name must be provided exactly as filed with the Texas Secretary of State (SOS), or on other legal documents forming the entity, that is filed in the county where doing business. You may contact the SOS at 512-463 5555, for more information related to filing in Texas.

c) Understanding of Notice of Termination

A permittee shall terminate coverage under the Construction General Permit through the submittal of a NOT when the operator of the facility changes, final stabilization has been reached, the discharge becomes authorized under an individual permit, or the construction activity never began at this site.

d) Certification of Stormwater Pollution Prevention Plan

The SWP3 identifies the areas and activities that could produce contaminated runoff at your site and then tells how you will ensure that this contamination is mitigated. For example, in describing your mitigation measures, your site's plan might identify the devices that collect and filter stormwater, tell how those devices are to be maintained, and tell how frequently that maintenance is to be carried out. You must develop this plan in accordance with the TCEQ general permit requirements. This plan must be developed and implemented before you complete this NOI. The SWP3 must be available for a TCEQ investigator to review on request.

Section 6. APPLICANT CERTIFICATION SIGNATURE

The certification must bear an original signature of a person meeting the signatory requirements specified under 30 Texas Administrative Code (TAC) §305.44.

If you are a corporation:

The regulation that controls who may sign an NOI or similar form is 30 Texas Administrative Code §305.44(a)(1) (see below). According to this code provision, any corporate representative may sign an NOI or similar form so long as the authority to sign such a document has been delegated to that person in accordance with corporate procedures. By signing the NOI or similar form, you are certifying that such authority has been delegated to you. The TCEQ may request documentation evidencing such authority.

If you are a municipality or other government entity:

The regulation that controls who may sign an NOI or similar form is 30 Texas Administrative Code §305.44(a)(3) (see below). According to this code provision, only a ranking elected official or principal executive officer may sign an NOI or similar form. Persons such as the City Mayor or County Commissioner will be considered ranking elected officials. In order to identify the principal executive officer of your government entity, it may be beneficial to consult your city charter, county or city ordinances, or the Texas statute(s) under which your government entity was formed. An NOI or similar document that is signed by a government official who is not a ranking elected official or principal executive officer does not conform to §305.44(a)(3). The signatory requirement may not be delegated to a government representative other than those identified in the regulation. By signing the NOI or similar form, you are certifying that you are either a ranking elected official or principal executive officer as required by the administrative code. Documentation demonstrating your position as a ranking elected official or principal executive officer may be requested by the TCEQ.

If you have any questions or need additional information concerning the signatory requirements discussed above, please contact the TCEQ's Environmental Law Division at 512-239-0600.

30 Texas Administrative Code

§305.44. Signatories to Applications

(a) All applications shall be signed as follows.

(1) For a corporation, the application shall be signed by a responsible corporate officer. For purposes of this paragraph, a responsible corporate officer means a president, secretary, treasurer, or vice-president of the corporation in charge of a principal business function, or any other person who performs similar policy or decision-making functions for the

corporation; or the manager of one or more manufacturing, production, or operating facilities employing more than 250 persons or having gross annual sales or expenditures exceeding \$25 million (in second-quarter 1980 dollars), if authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures. Corporate procedures governing authority to sign permit or post-closure order applications may provide for assignment or delegation to applicable corporate positions rather than to specific individuals.

(2) For a partnership or sole proprietorship, the application shall be signed by a general partner or the proprietor, respectively.

(3) For a municipality, state, federal, or other public agency, the application shall be signed by either a principal executive officer or a ranking elected official. For purposes of this paragraph, a principal executive officer of a federal agency includes the chief executive officer of the agency, or a senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency (e.g., regional administrator of the EPA).

Texas Commission on Environmental Quality General Permit Payment Submittal Form

Use this form to submit your Application Fee only if you are mailing your payment.

Instructions:

- Complete items 1 through 5 below:
- Staple your check in the space provided at the bottom of this document.
- *Do not mail this form with your NOI form.*
- *Do not mail this form to the same address as your NOI.*

Mail this form and your check to either of the following:

By Regular U.S. Mail

Texas Commission on Environmental Quality
Financial Administration Division
Cashier's Office, MC-214
P.O. Box 13088
Austin, TX 78711-3088

By Overnight or Express Mail

Texas Commission on Environmental Quality
Financial Administration Division
Cashier's Office, MC-214
12100 Park 35 Circle
Austin, TX 78753

Fee Code: GPA General Permit: TXR150000

1. Check or Money Order No:
2. Amount of Check/Money Order:
3. Date of Check or Money Order:
4. Name on Check or Money Order:
5. NOI Information:

If the check is for more than one NOI, list each Project or Site (RE) Name and Physical Address exactly as provided on the NOI. **Do not submit a copy of the NOI with this form, as it could cause duplicate permit application entries!**

If there is not enough space on the form to list all of the projects or sites the authorization will cover, then attach a list of the additional sites.

Project/Site (RE) Name:

Project/Site (RE) Physical Address:

Staple the check or money order to this form in this space.



LARGE CONSTRUCTION SITE NOTICE

FOR THE
Texas Commission on Environmental Quality (TCEQ)
Stormwater Program
TPDES GENERAL PERMIT TXR150000

“PRIMARY OPERATOR” NOTICE

This notice applies to construction sites operating under Part II.E.3. of the TPDES General Permit Number TXR150000 for discharges of stormwater runoff from construction sites equal to or greater than five acres, including the larger common plan of development. The information on this notice is required in Part III.D.2. of the general permit. Additional information regarding the TCEQ stormwater permit program may be found on the internet at:

<https://www.tceq.texas.gov/permitting/stormwater/construction>

Site-Specific TPDES Authorization Number:	
Operator Name:	
Contact Name and Phone Number:	
Project Description: <i>Physical address or description of the site's location, and estimated start date and projected end date, or date that disturbed soils will be stabilized.</i>	15480 Vance Jackson San Antonio, TX 78249
Location of Stormwater Pollution Prevention Plan:	Job Site

Agent Authorization Form
For Required Signature
Edwards Aquifer Protection Program
Relating to 30 TAC Chapter 213
Effective June 1, 1999

I _____ Abigail Kampmann _____,
Print Name

Manager _____,
Title - Owner/President/Other
of _____ Tessi Properties, LLC _____,
Corporation/Partnership/Entity Name
have authorized _____ Kevin W. Love, P.E. _____
Print Name of Agent/Engineer
of _____ KLove Engineering, LLC _____
Print Name of Firm

to represent and act on the behalf of the above named Corporation, Partnership, or Entity for the purpose of preparing and submitting this plan application to the Texas Commission on Environmental Quality (TCEQ) for the review and approval consideration of regulated activities.

I also understand that:

1. The applicant is responsible for compliance with 30 Texas Administrative Code Chapter 213 and any condition of the TCEQ's approval letter. The TCEQ is authorized to assess administrative penalties of up to \$10,000 per day per violation.
2. For those submitting an application who are not the property owner, but who have the right to control and possess the property, additional authorization is required from the owner.
3. Application fees are due and payable at the time the application is submitted. The application fee must be sent to the TCEQ cashier or to the appropriate regional office. The application will not be considered until the correct fee is received by the commission.
4. A notarized copy of the Agent Authorization Form must be provided for the person preparing the application, and this form must accompany the completed application.
5. No person shall commence any regulated activity on the Edwards Aquifer Recharge Zone, Contributing Zone or Transition Zone until the appropriate application for the activity has been filed with and approved by the Executive Director.

SIGNATURE PAGE:

Abigail G. Kampmann
Abigail Kampmann (Dec 2, 2024 15:54 CST)
Applicant's Signature

Dec 2, 2024
Date

THE STATE OF Texas §

County of Bexar §


BEFORE ME, the undersigned authority, on this day personally appeared Abigail Kampmann known to me to be the person whose name is subscribed to the foregoing instrument, and acknowledged to me that (s)he executed same for the purpose and consideration therein expressed.

GIVEN under my hand and seal of office on this 2nd day of December, 2024

[Signature]
NOTARY PUBLIC

Stephanie Perez
Typed or Printed Name of Notary

MY COMMISSION EXPIRES: September 4, 2028



NOTICE OF CONFIDENTIALITY RIGHTS: IF YOU ARE A NATURAL PERSON, YOU MAY REMOVE OR STRIKE ANY OF THE FOLLOWING INFORMATION FROM THIS INSTRUMENT BEFORE IT IS FILED FOR RECORD IN THE PUBLIC RECORDS: YOUR SOCIAL SECURITY NUMBER OR YOUR DRIVER'S LICENSE NUMBER.

SPECIAL WARRANTY DEED

DATE: Effective September 20, 2024

GRANTOR: Galleria Ventures Limited, a Texas limited partnership

GRANTOR'S ADDRESS:

1100 NW Loop 410, # 260, San Antonio, TX 78213

GRANTEE: Tessi Properties LLC, a Texas limited liability company (95%)
Abigail G. Kampmann and George A. Kampmann Jr. as community
Property (5%)

GRANTEE'S ADDRESS: 153 Treeline Park, Ste 100, San Antonio TX 78209

CONSIDERATION: TEN DOLLARS (\$10.00) and other good and valuable consideration, the sufficiency of which is confirmed.

PROPERTY: As described on Exhibit "A" attached hereto


RESERVATIONS FROM AND EXCEPTIONS TO CONVEYANCE AND WARRANTY:
See Exhibit "B" attached hereto and made a part hereof for all purposes.

Grantor, for the consideration and subject to the reservations from and exceptions to conveyance and warranty, grants, sells and conveys to Grantee the property, together with all and singular the rights and appurtenances thereto in anywise belonging, to have and hold it to Grantee, Grantee's heirs, executors, administrators, successors, or assigns forever. Grantor hereby binds Grantor and Grantor's heirs, executors, administrators, and successors to warrant and forever defend all and singular the property to Grantee and Grantee's heirs, executors, administrators, successors, and assigns, against every person whomsoever lawfully claiming or to claim the same or any part thereof, except as to the reservations from and exceptions to warranty, by and through the undersigned but not otherwise.

CHICAGO TITLE GF# 4300172400554 (MB)

GALLERIA VENTURES LIMITED

BY: GALLERIA GENERAL PARTNER LLC,
ITS GENERAL PARTNER

BY: 
AMIN GUINDI COHEN
MANAGER

THE STATE OF TEXAS

*

*

COUNTY OF BEXAR

*

This instrument was acknowledged before me on the 10th day of Sept, 2024, by Amin Guindi Cohen, Manager of Galleria General Partner LLC, a limited liability company, on behalf of said company, and the company acknowledged this instrument as General Partner on behalf of Galleria Ventures Limited, a limited partnership.


NOTARY PUBLIC, STATE OF TEXAS




EXHIBIT "B"


1. The following restrictive covenants of record itemized below: Volume 11972, Page 1764, Volume 16815, Page 401, Volume 17804, Page 2022, Volume 17804, Page 2069, Real Property Records, Bexar County, Texas.
 2. Sewer Easement granted to Laredo 98 Development, Ltd., a Texas limited partnership, Potranco Partners, Ltd., a Texas limited partnership, and I-10 Ventures, Ltd., a Texas limited partnership dated June 1, 2007 re recorded June 16, 2007 in Volume 12905, Page 575, and rerecorded in Volume 12927, Page 2307, Real Property Records, Bexar County, Texas.
 3. Sewer Easement recorded July 16, 2018 in Volume 17874, Page 54, Real Property Records, Bexar County, Texas.
 4. Electric and Gas Lines Easement to the City of San Antonio recorded June 13, 2022 in Document Number 20220146446, Official Public Records, Bexar County, Texas.
 5. Variable Width Access Easement 18' Electric Easement as shown in the instrument of record at Volume 20001, Page 1402, Plat Records of Bexar County, Texas.
 6. Consent Agreement between Galleria Ventures, Terrasota, UTSA352, and the City of San Antonio for the purpose(s) provided in instrument recorded in Volume 15300, Page 1100, Real Property Records, Bexar County, Texas.
- 

EXHIBIT "A"

A 7.500 ACRE TRACT OF LAND LYING IN THE R.C. HAWKINS SURVEY NUMBER 337, ABSTRACT NUMBER 329, NEW CITY BLOCK 15825, IN THE CITY OF SAN ANTONIO, BEXAR COUNTY, TEXAS, AND BEING A PORTION OF A 21.583 ACRE TRACT DESCRIBED IN DOCUMENT NUMBER 20180206640, OFFICIAL PUBLIC RECORDS, BEXAR COUNTY, TEXAS, AND BEING MORE PARTICULARLY DESCRIBED AS FOLLOWS:

BEGINNING: at a found 1/2 inch iron rod found on the existing east right-of-way line of Vance Jackson Road (a variable width public right-of-way), at the southwest corner of Lot 14, Block 13, New City Block 15825, DISTRICT NORTH OFFICE SUBDIVISION, recorded in Volume 20001, Page 1402, Deed and Plat Records, Bexar County Texas, at the northwest corner of said 21.583 acres, having Texas State Plane coordinates N=13,761,958.51 and E= 2,099,149.62, South Central Zone 4204, Grid, for the northwest corner of this 7.500 acre tract;

THENCE: North 84°02'18" East 654.04 feet departing the existing east right-of-way of Vance Jackson Road, with the north line of said 21.583 acres, the north line of this 7.500 acre tract and the south line of Lot 14, Block 13, to a 1/2 inch iron rod found on the existing west right-of-way of the Union Pacific Railroad (a 100-foot right-of-way), at the southeast corner of Lot 14, Block 13, at the northeast corner of said 21.583 acres, for the northeast corner of this 7.500 acre tract;

THENCE: South 25°15'13" East 448.06 feet along the existing west right-of-way of the Union Pacific Railroad, with the east line of said 21.583 acres, and the east line of this 7.500 acre tract to a 1/2 inch iron rod set with cap stamped "ALLIANCE LAND SURVEYORS RPLS 4716" for the southeast of this 7.500 acre tract;

THENCE: South 81°44'49" West 820.82 feet leaving the existing west right-of-way of the Union Pacific Railroad, crossing said 21.853 acres, to a 1/2 inch iron rod set with cap stamped "ALLIANCE LAND SURVEYORS RPLS 4716" on the existing east right-of-way of Vance Jackson Road, on the west boundary of said 21.583 acres, at the beginning of a curve to the right, for the southwest corner of this 7.500 acre tract;

THENCE: with the existing east right-of-way of Vance Jackson Road, the west boundary of said 21.583 acres and the west boundary of this 7.500 acre tract, the following two (2) calls:

1) 213.96 feet along said curve to the right having a radius of **1,957.00 feet**, a delta of **06°15'51"**, and a chord that bears: **North 05°21'09" West 213.86 feet** to a 1/2 inch iron rod set with cap stamped "ALLIANCE LAND SURVEYORS RPLS 4716" for angle;

2) North 02°13'13" West 242.39 feet to the **POINT OF BEGINNING** of this 7.500 acre (326,711 square feet) tract of land in Bexar County, Texas.

File Information

**eFILED IN THE OFFICIAL PUBLIC eRECORDS OF BEXAR COUNTY
LUCY ADAME-CLARK, BEXAR COUNTY CLERK**

Document Number: 20240173275
Recorded Date: September 20, 2024
Recorded Time: 4:34 PM
Total Pages: 5
Total Fees: \$37.00

**** THIS PAGE IS PART OF THE DOCUMENT ****

**** Do Not Remove ****

Any provision herein which restricts the sale or use of the described real property because of race is invalid and unenforceable under Federal law

STATE OF TEXAS, COUNTY OF BEXAR

I hereby Certify that this instrument was eFILED in File Number Sequence on this date and at the time stamped hereon by me and was duly eRECORDED in the Official Public Record of Bexar County, Texas on: 9/20/2024 4:34 PM



Lucy Adame-Clark
Lucy Adame-Clark
Bexar County Clerk

Application Fee Form

Texas Commission on Environmental Quality

Name of Proposed Regulated Entity: Vance Jackson Remote Parking Lot

Regulated Entity Location: 15480 Vance Jackson, San Antonio, TX 78249

Name of Customer: Tessi Properties, LLC

Contact Person: Abigail Kampmann

Phone: 210-437-3961

Customer Reference Number (if issued): CN _____

Regulated Entity Reference Number (if issued): RN _____

Austin Regional Office (3373)

☐ Hays

☐ Travis

☐ Williamson

San Antonio Regional Office (3362)

☒ Bexar

☐ Medina

☐ Uvalde

☐ Comal

☐ Kinney

Application fees must be paid by check, certified check, or money order, payable to the **Texas Commission on Environmental Quality**. Your canceled check will serve as your receipt. **This form must be submitted with your fee payment.** This payment is being submitted to:

☐ Austin Regional Office

☒ San Antonio Regional Office

☐ Mailed to: TCEQ - Cashier

☐ Overnight Delivery to: TCEQ - Cashier

Revenues Section

Mail Code 214

P.O. Box 13088

Austin, TX 78711-3088

12100 Park 35 Circle

Building A, 3rd Floor

Austin, TX 78753

(512)239-0357

Site Location (Check All That Apply):

☐ Recharge Zone

☒ Contributing Zone

☐ Transition Zone

Type of Plan	Size	Fee Due
Water Pollution Abatement Plan, Contributing Zone Plan: One Single Family Residential Dwelling	Acres	\$
Water Pollution Abatement Plan, Contributing Zone Plan: Multiple Single Family Residential and Parks	Acres	\$
Water Pollution Abatement Plan, Contributing Zone Plan: Non-residential	7.50 Acres	\$ 5,000
Sewage Collection System	L.F.	\$
Lift Stations without sewer lines	Acres	\$
Underground or Aboveground Storage Tank Facility	Tanks	\$
Piping System(s)(only)	Each	\$
Exception	Each	\$
Extension of Time	Each	\$

Signature: 
Abigail Kampmann (Dec 2, 2024 15:54 CST)

Date: Dec 2, 2024

Application Fee Schedule

Texas Commission on Environmental Quality

Edwards Aquifer Protection Program 30 TAC Chapter 213 (effective 05/01/2008)

Water Pollution Abatement Plans and Modifications

Contributing Zone Plans and Modifications

<i>Project</i>	<i>Project Area in Acres</i>	<i>Fee</i>
One Single Family Residential Dwelling	< 5	\$650
Multiple Single Family Residential and Parks	< 5	\$1,500
	5 < 10	\$3,000
	10 < 40	\$4,000
	40 < 100	\$6,500
	100 < 500	\$8,000
	≥ 500	\$10,000
Non-residential (Commercial, industrial, institutional, multi-family residential, schools, and other sites where regulated activities will occur)	< 1	\$3,000
	1 < 5	\$4,000
	5 < 10	\$5,000
	10 < 40	\$6,500
	40 < 100	\$8,000
	≥ 100	\$10,000

Organized Sewage Collection Systems and Modifications

<i>Project</i>	<i>Cost per Linear Foot</i>	<i>Minimum Fee- Maximum Fee</i>
Sewage Collection Systems	\$0.50	\$650 - \$6,500

Underground and Aboveground Storage Tank System Facility Plans and Modifications

<i>Project</i>	<i>Cost per Tank or Piping System</i>	<i>Minimum Fee- Maximum Fee</i>
Underground and Aboveground Storage Tank Facility	\$650	\$650 - \$6,500

Exception Requests

<i>Project</i>	<i>Fee</i>
Exception Request	\$500

Extension of Time Requests

<i>Project</i>	<i>Fee</i>
Extension of Time Request	\$150



TCEQ Use Only

TCEQ Core Data Form

For detailed instructions regarding completion of this form, please read the Core Data Form Instructions or call 512-239-5175.

SECTION I: General Information

1. Reason for Submission (If other is checked please describe in space provided.)		
<input checked="" type="checkbox"/> New Permit, Registration or Authorization (Core Data Form should be submitted with the program application.)		
<input type="checkbox"/> Renewal (Core Data Form should be submitted with the renewal form)	<input type="checkbox"/> Other	
2. Customer Reference Number (if issued)	Follow this link to search for CN or RN numbers in Central Registry**	3. Regulated Entity Reference Number (if issued)
CN		RN

SECTION II: Customer Information

4. General Customer Information		5. Effective Date for Customer Information Updates (mm/dd/yyyy)	
<input checked="" type="checkbox"/> New Customer		<input type="checkbox"/> Update to Customer Information	<input type="checkbox"/> Change in Regulated Entity Ownership
<input type="checkbox"/> Change in Legal Name (Verifiable with the Texas Secretary of State or Texas Comptroller of Public Accounts)			
The Customer Name submitted here may be updated automatically based on what is current and active with the Texas Secretary of State (SOS) or Texas Comptroller of Public Accounts (CPA).			
6. Customer Legal Name (If an individual, print last name first: eg: Doe, John)		If new Customer, enter previous Customer below:	
Tessi Properties, LLC			
7. TX SOS/CPA Filing Number	8. TX State Tax ID (11 digits)	9. Federal Tax ID (9 digits)	10. DUNS Number (if applicable)
0802764029	32064266227		
11. Type of Customer:	<input type="checkbox"/> Corporation	<input type="checkbox"/> Individual	Partnership: <input type="checkbox"/> General <input type="checkbox"/> Limited
Government: <input type="checkbox"/> City <input type="checkbox"/> County <input type="checkbox"/> Federal <input type="checkbox"/> State <input type="checkbox"/> Other	<input type="checkbox"/> Sole Proprietorship	<input checked="" type="checkbox"/> Other: Limited liability Company	
12. Number of Employees		13. Independently Owned and Operated?	
<input checked="" type="checkbox"/> 0-20 <input type="checkbox"/> 21-100 <input type="checkbox"/> 101-250 <input type="checkbox"/> 251-500 <input type="checkbox"/> 501 and higher		<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
14. Customer Role (Proposed or Actual) – as it relates to the Regulated Entity listed on this form. Please check one of the following			
<input checked="" type="checkbox"/> Owner <input type="checkbox"/> Operator <input type="checkbox"/> Owner & Operator			
<input type="checkbox"/> Occupational Licensee <input type="checkbox"/> Responsible Party <input type="checkbox"/> Voluntary Cleanup Applicant <input type="checkbox"/> Other:			
15. Mailing Address:	153 Treeline Park, Suite 100		
	City	San Antonio	State TX ZIP 78209 ZIP + 4
16. Country Mailing Information (if outside USA)		17. E-Mail Address (if applicable)	
		akampmann@principleauto.com	
18. Telephone Number	19. Extension or Code	20. Fax Number (if applicable)	
(210) 437-3961		() -	

SECTION III: Regulated Entity Information

21. General Regulated Entity Information (If 'New Regulated Entity' is selected below this form should be accompanied by a permit application)	
<input checked="" type="checkbox"/> New Regulated Entity <input type="checkbox"/> Update to Regulated Entity Name <input type="checkbox"/> Update to Regulated Entity Information	
The Regulated Entity Name submitted may be updated in order to meet TCEQ Agency Data Standards (removal of organizational endings such as Inc, LP, or LLC).	
22. Regulated Entity Name (Enter name of the site where the regulated action is taking place.)	
Vance Jackson Parking	

23. Street Address of the Regulated Entity: (No PO Boxes)	15480 Vance Jackson							
	City	San Antonio	State	TX	ZIP	78249	ZIP + 4	
24. County	Bexar							

Enter Physical Location Description if no street address is provided.

25. Description to Physical Location:	450 LF North of Vance Jackson Rd and Presidio Pkwy intersection							
26. Nearest City	State				Nearest ZIP Code			
San Antonio	TX				78249			
27. Latitude (N) In Decimal:	29.588281			28. Longitude (W) In Decimal:	-98.587967			
Degrees	Minutes	Seconds	Degrees	Minutes	Seconds			
29	35	17.81	-98	35	16.68			
29. Primary SIC Code (4 digits)	30. Secondary SIC Code (4 digits)		31. Primary NAICS Code (5 or 6 digits)		32. Secondary NAICS Code (5 or 6 digits)			
7521								
33. What is the Primary Business of this entity? (Do not repeat the SIC or NAICS description.)								
Parking Lot / Storage								
34. Mailing Address:	153 Treeline Park, Suite 100							
	City	San Antonio	State	TX	ZIP	78209	ZIP + 4	
35. E-Mail Address:								
36. Telephone Number			37. Extension or Code			38. Fax Number (if applicable)		
() -						() -		

39. TCEQ Programs and ID Numbers Check all Programs and write in the permits/registration numbers that will be affected by the updates submitted on this form. See the Core Data Form instructions for additional guidance.


<input type="checkbox"/> Dam Safety	<input type="checkbox"/> Districts	<input checked="" type="checkbox"/> Edwards Aquifer	<input type="checkbox"/> Emissions Inventory Air	<input type="checkbox"/> Industrial Hazardous Waste
		Contributing Zone Plan		
<input type="checkbox"/> Municipal Solid Waste	<input type="checkbox"/> New Source Review Air	<input type="checkbox"/> OSSF	<input type="checkbox"/> Petroleum Storage Tank	<input type="checkbox"/> PWS
<input type="checkbox"/> Sludge	<input type="checkbox"/> Storm Water	<input type="checkbox"/> Title V Air	<input type="checkbox"/> Tires	<input type="checkbox"/> Used Oil
<input type="checkbox"/> Voluntary Cleanup	<input type="checkbox"/> Waste Water	<input type="checkbox"/> Wastewater Agriculture	<input type="checkbox"/> Water Rights	<input type="checkbox"/> Other:

SECTION IV: Preparer Information

40. Name:	KLove Engineering		41. Title:	Engineer
42. Telephone Number	43. Ext./Code	44. Fax Number	45. E-Mail Address	
(210) 485-5683		() -	klove@kloveengineering.com	

SECTION V: Authorized Signature

46. By my signature below, I certify, to the best of my knowledge, that the information provided in this form is true and complete, and that I have signature authority to submit this form on behalf of the entity specified in Section II, Field 6 and/or as required for the updates to the ID numbers identified in field 39.

Company:	KLove Engineering, LLC	Job Title:	Engineer
Name (In Print):	Kevin W. Love	Phone:	(210) 485- 5683
Signature:		Date:	12/3/24
