

EXIDE FRISCO MASTER SCHEDULE SUMMARY

(Current as of 5/2/13 and Subject to Change)

Exide Frisco Recycling Center Closure


Main Components:

- **Former Operating Plant Decontamination and Demolition** (clean and remove certain structures)
- **Active Landfill Remediation** (retreat certain waste in open cells)
- **Undeveloped Buffer Property Investigation and Remediation** (also known as the VCP Parcel; investigate, remediate, and certify result to obtain TCEQ Voluntary Cleanup Program (VCP) Certificate of Completion)
- **Undeveloped Buffer Property Transfer to the Frisco EDC and CDC**
- **Former Operating Plant Investigation and Remediation** (investigate, remediate, and certify result for Exide retained property)
- **Long Term Maintenance of Former Operating Plant** (Exide retained property)

An overview of the current project schedule along with public participation milestones and tasks can be found on page 2.


The closure of the Recycling Center will follow established regulatory processes with each step building upon the previous step and impacting the next. A simplified overview is depicted to the right. The individual task schedules are estimated based on current information and are subject to change as the process proceeds.

This project schedule will be reviewed on a weekly basis and updated as necessary.

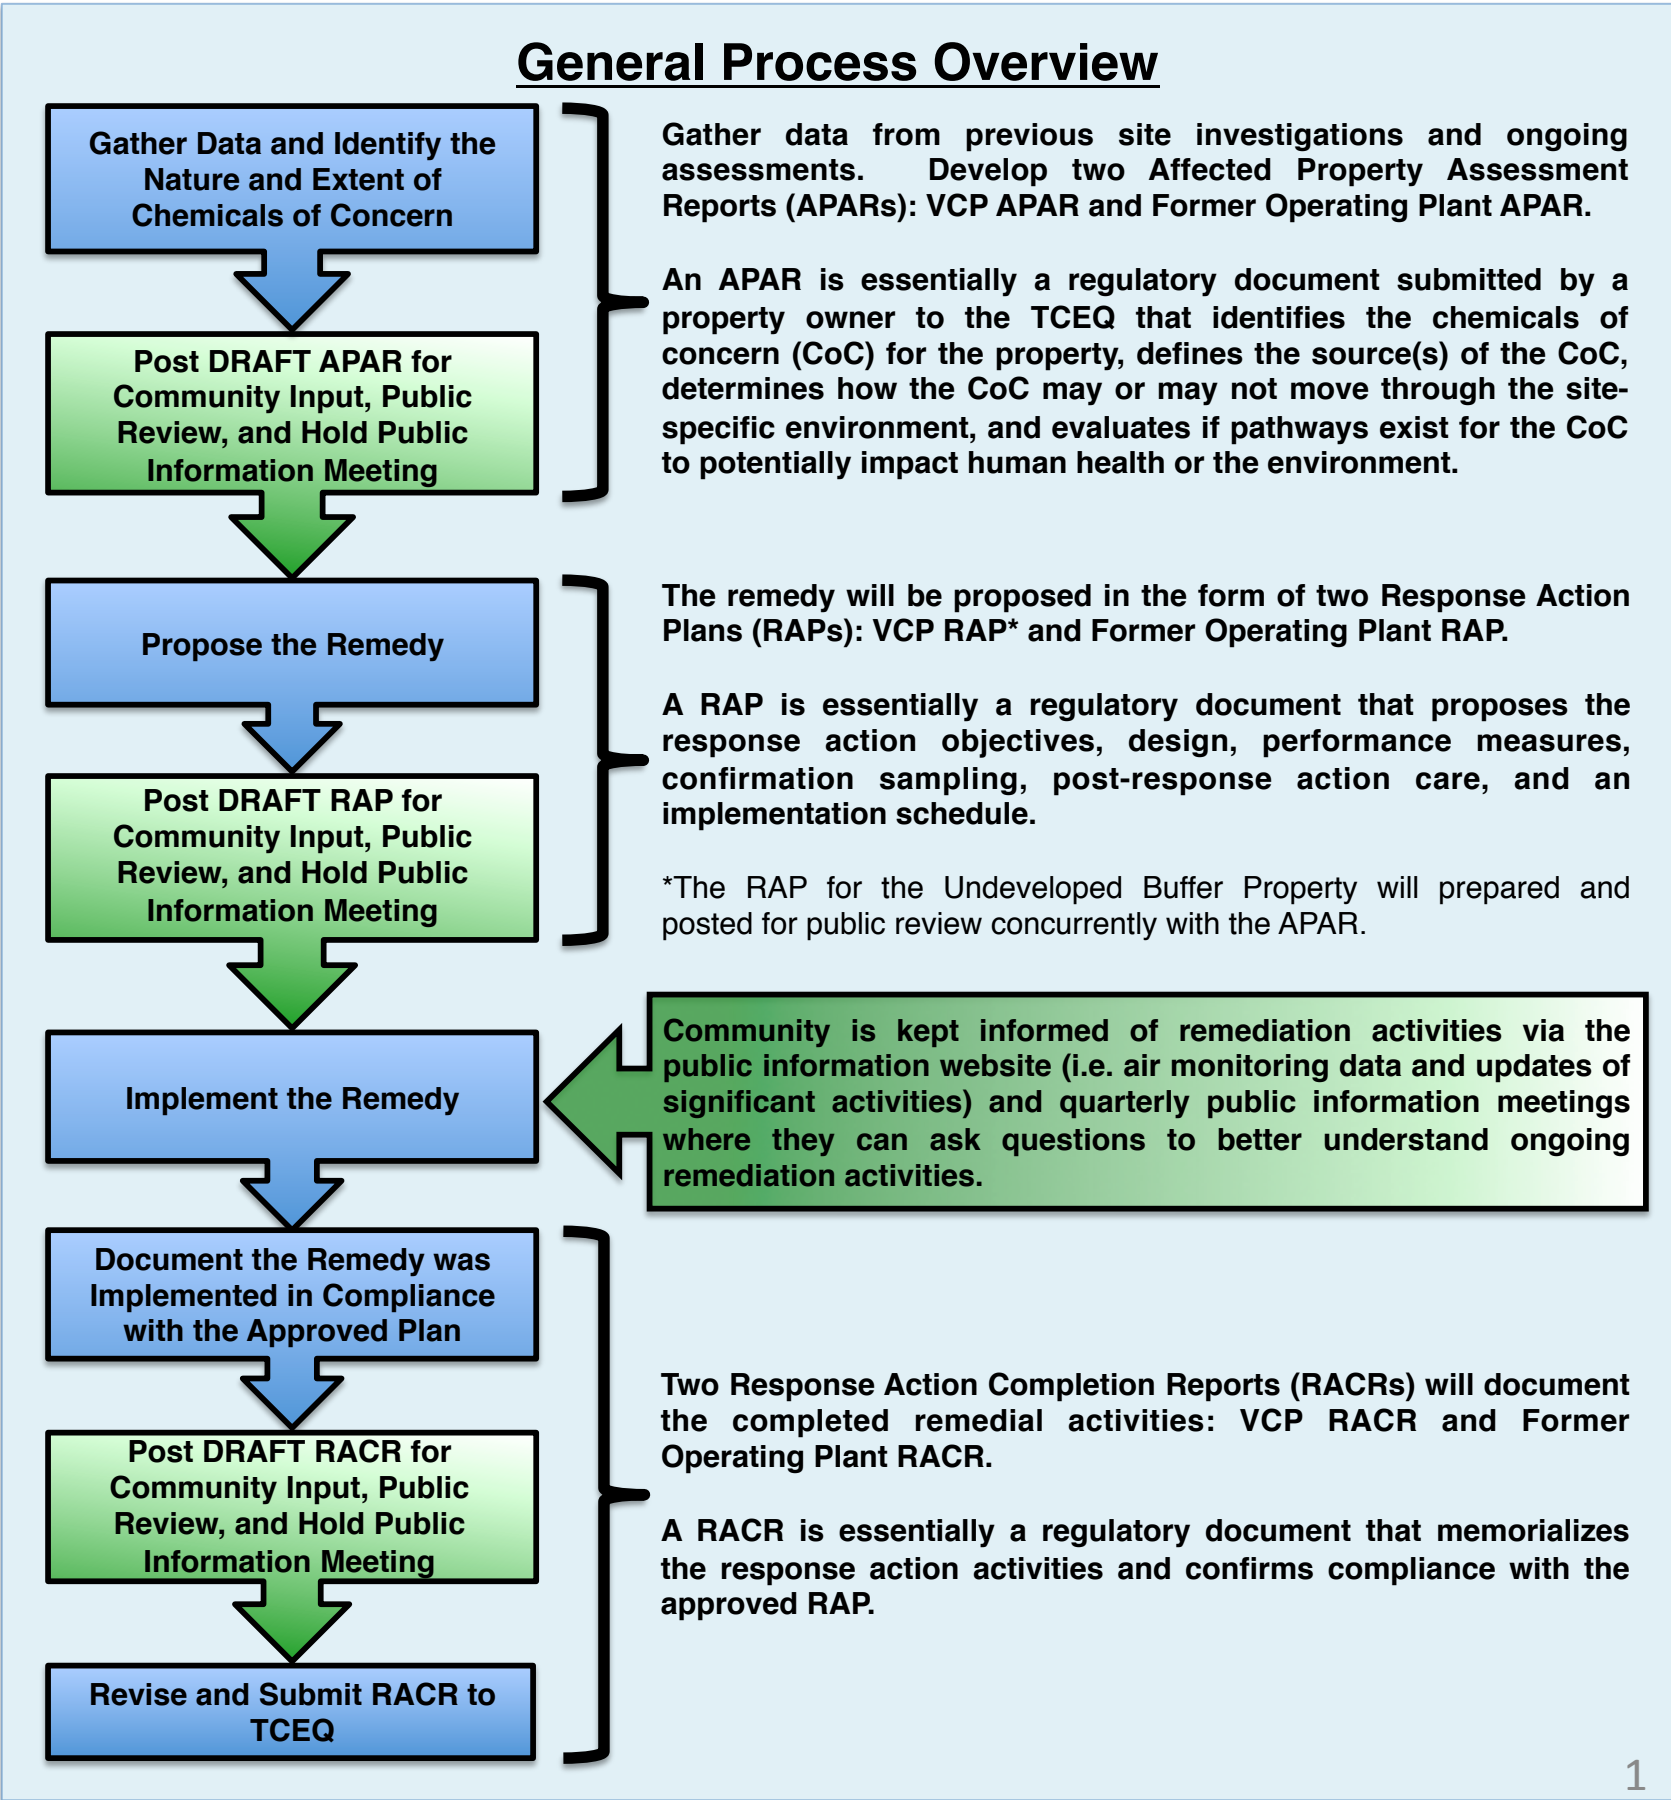

EXIDE FRISCO MASTER SCHEDULE SUMMARY

(Current as of 5/2/13 and Subject to Change)

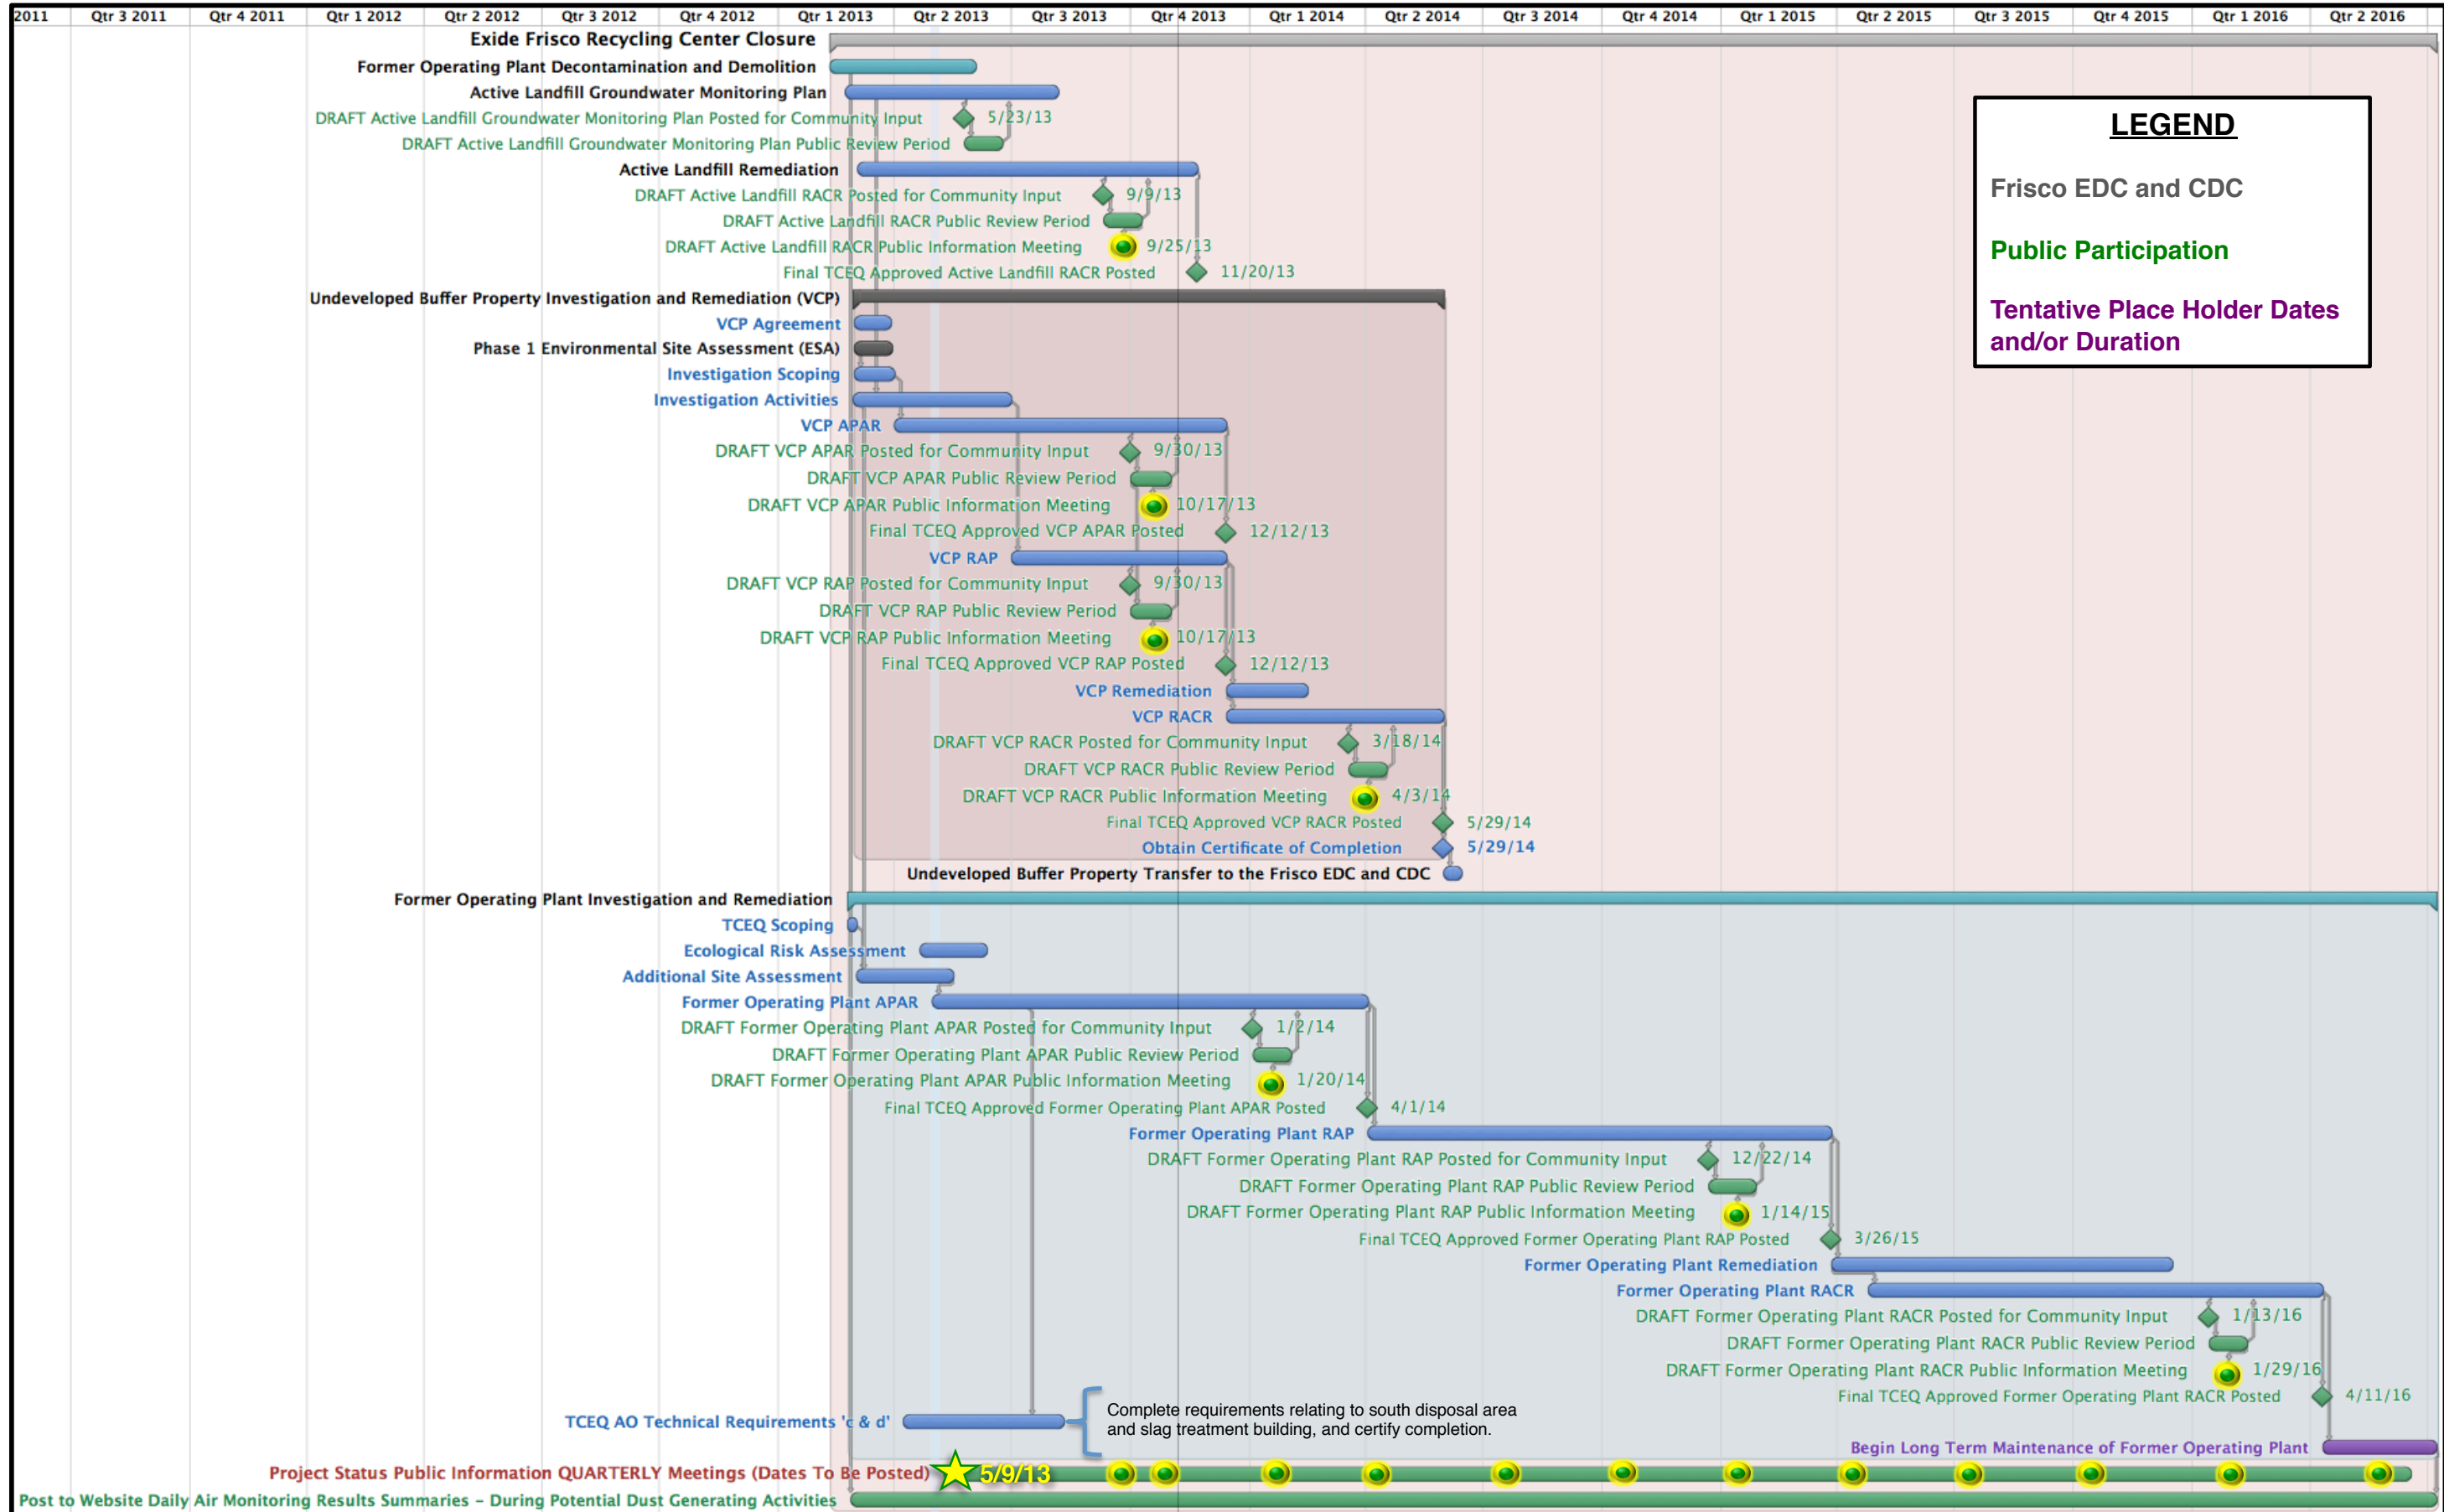

LEGEND

- Frisco EDC and CDC
- Public Participation
- Tentative Place Holder Dates and/or Duration

*APAR = Identify the nature & extent of Chemicals of Concern (CoC)

*RAP = Propose the remedy

*RACR = Document successful implementation of the approved remedy
